


Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float							
						2025				2026		2027
						2028				2029		2030
						J	J	J	J	J	J	J
						A	S	O	N	D	F	M
EM1721	Single line diagrams of the DC and UPS systems (62)	0d		13-Jan-26 17:00	477d							
EM1580	Final consolidated equipment, valve, instrument, etc. lists (135)	0d		26-Jan-26 17:00	468d							
EM1918	Instrument installation drawings (Loose supplied instruments only) (63)	0d		11-Feb-26 17:00	456d							
EM1760	Electrical metering and protective relaying one line and three line diagrams (97)	0d		13-Feb-26 17:00	454d							
EM1761	Three line diagrams (Phasing&voltage vector). Equipment shall be shown on the drawings based c	0d		13-Feb-26 17:00	454d							
EM1548	Valve drawings (including weights) (81)	0d		16-Feb-26 08:00	454d							
PL3060	Valves - Final Vendor Drawings Received	0d		16-Feb-26 08:00*	161d							
PL3080	Electrical PDPs - Final Vendor Drawings Received	0d		16-Feb-26 17:00*	0d							
EM1639	Large bore pipe support drawings (93)	0d		24-Feb-26 17:00	447d							
EM1921	Plant DCS Datalink Table (66)	0d		25-Feb-26 17:00	446d							
EM1941	Control narratives (BOP systems) (80)	0d		27-Feb-26 17:00	204d							
EM1949	Control logic diagrams and logic schematics in ISA S5.1 (SAMA) format (86)	0d		27-Feb-26 17:00	444d							
EM1951	Preliminary HMI graphics sketches (88)	0d		27-Feb-26 17:00	444d							
EM1550	Spare Parts Lists (startup/commissioning and recommended): See "Spare Parts" Section A5.0 (84)	0d		02-Mar-26 17:00	443d							
EM1529	HVAC Equipment General Arrangements, Datasheets, calculations, etc. (69)	0d		06-Mar-26 17:00	439d							
EM1638	Piping Isometrics (92)	0d		16-Mar-26 17:00	433d							
EM1920	Instrument, Valve and Equipment Location Drawing (65)	0d		16-Mar-26 17:00	433d							
EM1758	Electrical cable and raceway lists, including fiber optic and communication cabling (95)	0d		26-Mar-26 17:00	425d							
EM1765	Electrical bills of material (102)	0d		26-Mar-26 17:00	425d							
EM1766	Electrical calcs including short circuit, running & starting voltage drops (Load Flow), and arc flash (1	0d		30-Mar-26 17:00	423d							
EM1530	System and Equipment Description Documents (70)	0d		03-Apr-26 17:00	419d							
EM1950	Final Control logic diagrams and logic schematics in ISA S5.1 (SAMA) format (87)	0d		03-Apr-26 17:00	419d							
EM1952	HMI graphics sketches (89)	0d		03-Apr-26 17:00	17d							
EM1260	Final Electrical Load List (To Be Updated after Equipment Data becomes available) (40)	0d		20-Apr-26 17:00	408d							
EM1953	Preliminary Alarm list in Owner's standard format, including Contractor's recommended alarm value	0d		08-May-26 17:00	394d							
EM1954	Alarm list in Owner's standard format, including Contractor's recommended alarm value setting(s) (9	0d		08-May-26 17:00	394d							
EM1728	Electrical raceway plans (67)	0d		28-May-26 17:00	381d							
EM1763	Underground raceway and grounding requirements (100)	0d		07-Jul-26 17:00	354d							
EM1768	Electrical system stability study (105)	0d		21-Jul-26 17:00	344d							
EM1741	Electrical panel schedules (75)	0d		22-Jul-26 17:00	343d							
EM1740	Final grounding and cathodic protection survey reports (74)	0d		11-Aug-26 09:00	330d							
EM1770	Schematics and wiring diagrams of all Contractor supplied equipment requiring electrical connector	0d		28-Aug-26 17:00	316d							
EM1640	Lubricating oil/Grease list: (94)	0d		22-Feb-27 10:00	196d							
00373.3 ENGINEERING												
00373.3.19 Common												
00373.3.19.20 General												
UE0530	Prepare 30% Design ReviewAgenda	0d	23-May-25 08:00 A	30-May-25 17:00 A								
UE0535	30% Design Review Meeting	0d		04-Jun-25 08:00 A								
UE0560	Prepare 60% Design ReviewAgenda	0d	05-Nov-25 08:00 A	12-Nov-25 17:00 A								
UE0565	60% Design Review Meeting	0d		12-Nov-25 17:00 A								
UE0590	Prepare 90% Design ReviewAgenda	5d	13-Mar-26 08:00	19-Mar-26 17:00	72d							

[illegible]

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float												
						2025			2026			2027			2028		
						J	J	J	J	J	J	J	J	J	J	J	J
	UE130509-05	Prep & Check Structural Calc Foundation - Fuel Gas Yard Equipment	15d	09-Feb-26 08:00	27-Feb-26 17:00	58d											
	UE131109-05	Prep, Check, and Issue IDR Foundation Dwgs.- Fuel Gas Yard Equipment	20d	02-Mar-26 08:00	27-Mar-26 17:00	58d											
	UE131109-10	IDR Foundation Dwgs - Fuel Gas Yard Equipment	5d	30-Mar-26 08:00	03-Apr-26 17:00	58d											
	UE131109-15	Address IDR Foundation Dwgs. & Issue for CR -Fuel Gas Yard Equipment	10d	06-Apr-26 08:00	17-Apr-26 17:00	58d											
	UE131109-20	Client Review Foundation Dwgs - Foundation - Fuel Gas Yard Equipment	15d	20-Apr-26 08:00	08-May-26 17:00	58d											
	UE131109-25	Address Client Comments and Issue IFC Foundation Dwgs. & Calculation - Fuel Gas Yard Equipme	5d	11-May-26 08:00	15-May-26 17:00	58d											
	00373.3.19.5.1.1.7 GE Supplied Equipment Skids																
	UE130510-05	Prep & Check Structural Calc Foundation - GE Supplied Equipment Skids	0d	28-May-25 08:00 A	12-Sep-25 17:00 A												
	UE131110-05	Prep, Check, and Issue IDR Foundation Dwgs.- GE Supplied Equipment Skids	0d	28-May-25 08:00 A	12-Sep-25 17:00 A												
	UE131110-10	IDR Foundation Dwgs - GE Supplied Equipment Skids	0d	15-Sep-25 08:00 A	19-Sep-25 17:00 A												
	UE131110-15	Address IDR Foundation Dwgs. & Issue for CR - GE Supplied Equipment Skids	0d	22-Sep-25 08:00 A	13-Oct-25 17:00 A												
	UE131110-20	Client Review Foundation Dwgs - Foundation - GE Supplied Equipment Skids	0d	14-Oct-25 08:00 A	27-Oct-25 17:00 A												
	UE131110-25	Address Client Comments and Issue IFC Foundation Dwgs. & Calculation - GE Supplied Equipmen	0d	28-Oct-25 08:00 A	19-Nov-25 17:00 A												
	00373.3.19.5.1.1.8 Misc. Foundations																
	UE130511-05	Prep & Check Structural Calc Foundation - Misc. Foundations	0d	21-Nov-25 08:00 A	22-Dec-25 17:00 A												
	UE131111-10	IDR Foundation Dwgs - Misc. Foundations ***Delete all task below**	0d	15-Dec-25 08:00 A	15-Dec-25 17:00 A												
	UE131111-15	Address IDR Foundation Dwgs. & Issue for CR - Misc. Foundations	0d	16-Dec-25 08:00 A	16-Dec-25 17:00 A												
	UE131111-25	Address Client Comments and Issue IFC Foundation Dwgs. & Calculation - Misc. Foundations	0d	16-Dec-25 08:00 A	16-Dec-25 17:00 A												
	UE131111-20	Client Review Foundation Dwgs - Foundation - Misc. Foundations	0d	17-Dec-25 08:00 A	17-Dec-25 17:00 A												
	UE131111-05	Prep, Check, and Issue IFC Foundation Dwgs.- Misc. Foundations	10d	05-Jan-26 08:00 A	30-Jan-26 17:00	19d											
	00373.3.19.5.1.1.27 Pipe Support Foundations																
	UE130511-5	Prep & Check Structural Calc Foundation - Pipe Support Foundations	5d	05-Jan-26 08:00 A	23-Jan-26 17:00	167d											
	UE131111-35	Prep, Check, and Issue IDR Foundation Dwgs- Pipe Support Foundations	10d	05-Jan-26 08:00 A	30-Jan-26 17:00	167d											
	UE131111-45	IDR Foundation Dwgs - Pipe Support Foundations	5d	02-Feb-26 08:00	06-Feb-26 17:00	167d											
	UE131111-55	Address IDR Foundation Dwgs. & Issue for CR - Pipe Support Foundations	5d	09-Feb-26 08:00	13-Feb-26 17:00	167d											
	UE131111-65	Client Review Foundation Dwgs - Foundation - Pipe Support Foundations	15d	16-Feb-26 08:00	06-Mar-26 17:00	167d											
	UE131111-75	Address Client Comments and Issue IFC Foundation Dwgs. & Calculation - Pipe Support Foundatio	5d	09-Mar-26 08:00	13-Mar-26 17:00	167d											
	00373.3.19.5.1.1.28 Demin Trailer Area																
	UE130511-15	Prep & Check Structural Calc Foundation - Demin Trailer Area Foundations	20d	22-Jan-26 08:00	18-Feb-26 17:00	132d											
	UE131111-85	Prep, Check, and Issue IDR Foundation Dwgs.- Demin Trailer Area Foundations	20d	29-Jan-26 08:00	25-Feb-26 17:00	132d											
	UE131111-95	IDR Foundation Dwgs - Demin Trailer Area Foundations	5d	26-Feb-26 08:00	04-Mar-26 17:00	132d											
	UE131111-105	Address IDR Foundation Dwgs. & Issue for CR - Demin Trailer Area Foundations	5d	05-Mar-26 08:00	11-Mar-26 17:00	132d											
	UE131111-115	Client Review Foundation Dwgs - Foundation - Demin Trailer Area Foundations	15d	12-Mar-26 08:00	01-Apr-26 17:00	132d											
	UE131111-125	Address Client Comments and Issue IFC Foundation Dwgs. & Calculation - Demin Trailer Area Four	5d	02-Apr-26 08:00	08-Apr-26 17:00	132d											
	00373.3.19.5.1.1.29 Hydrogen Trailer Area																
	UE130511-25	Prep & Check Structural Calc Foundation - Hydrogen Trailer Area Foundations	20d	22-Jan-26 08:00	18-Feb-26 17:00	133d											
	UE131111-135	Prep, Check, and Issue IDR Foundation Dwgs.- Hydrogen Trailer Area Foundations	20d	29-Jan-26 08:00	25-Feb-26 17:00	133d											
	UE131111-145	IDR Foundation Dwgs - Hydrogen Trailer Area Foundations	5d	26-Feb-26 08:00	04-Mar-26 17:00	133d											
	UE131111-155	Address IDR Foundation Dwgs. & Issue for CR - Hydrogen Trailer Area Foundations	5d	05-Mar-26 08:00	11-Mar-26 17:00	133d											
	UE131111-165	Client Review Foundation Dwgs - Foundation - Hydrogen Trailer Area Foundations	15d	12-Mar-26 08:00	01-Apr-26 17:00	133d											
	UE131111-175	Address Client Comments and Issue IFC Foundation Dwgs. & Calculation - Hydrogen Trailer Area F	5d	02-Apr-26 08:00	08-Apr-26 17:00	133d											
	00373.3.19.5.1.1.30 Building HVAC																
	UE130511-35	Prep & Check Structural Calc Foundation - Building HVAC Foundations	20d	23-Feb-26 08:00	20-Mar-26 17:00	105d											
	UE131111-185	Prep, Check, and Issue IDR Foundation Dwgs.- Building HVAC Foundations	20d	02-Mar-26 08:00	27-Mar-26 17:00	105d											
	UE131111-195	IDR Foundation Dwgs - Building HVAC Foundations	5d	30-Mar-26 08:00	03-Apr-26 17:00	105d											
	UE131111-205	Address IDR Foundation Dwgs. & Issue for CR - Building HVAC Foundations	5d	06-Apr-26 08:00	10-Apr-26 17:00	105d											
	UE131111-215	Client Review Foundation Dwgs - Foundation - Building HVAC Foundations	15d	13-Apr-26 08:00	01-May-26 17:00	105d											
	UE131111-225	Address Client Comments and Issue IFC Foundation Dwgs. & Calculation - Building HVAC Foundati	5d	04-May-26 08:00	08-May-26 17:00	105d											
	00373.3.19.5.1.1.9 Diesel Generator																
	PL3096	Diesel Generator - Final Vendor Drawings Received	0d		12-Jan-26 08:00*	0d											
	UE130512-05	Prep & Check Structural Calc Foundation - Diesel Generator	15d	26-Jan-26 08:00	13-Feb-26 17:00	154d											
	Legend: Remaining Level of Effort (Green bar), Actual Work (Blue bar), Milestone (Diamond), Actual Level of Effort (Green bar), Primary Baseline (Yellow bar), Critical Remaining Work (Red bar)																

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	2025												2026												2027												2028												2029												2030																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
	UE131112-05	Prep, Check, and Issue IDR Foundation Dwgs.- Diesel Generator	20d	23-Feb-26 08:00	20-Mar-26 17:00	154d																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						

[illegible]

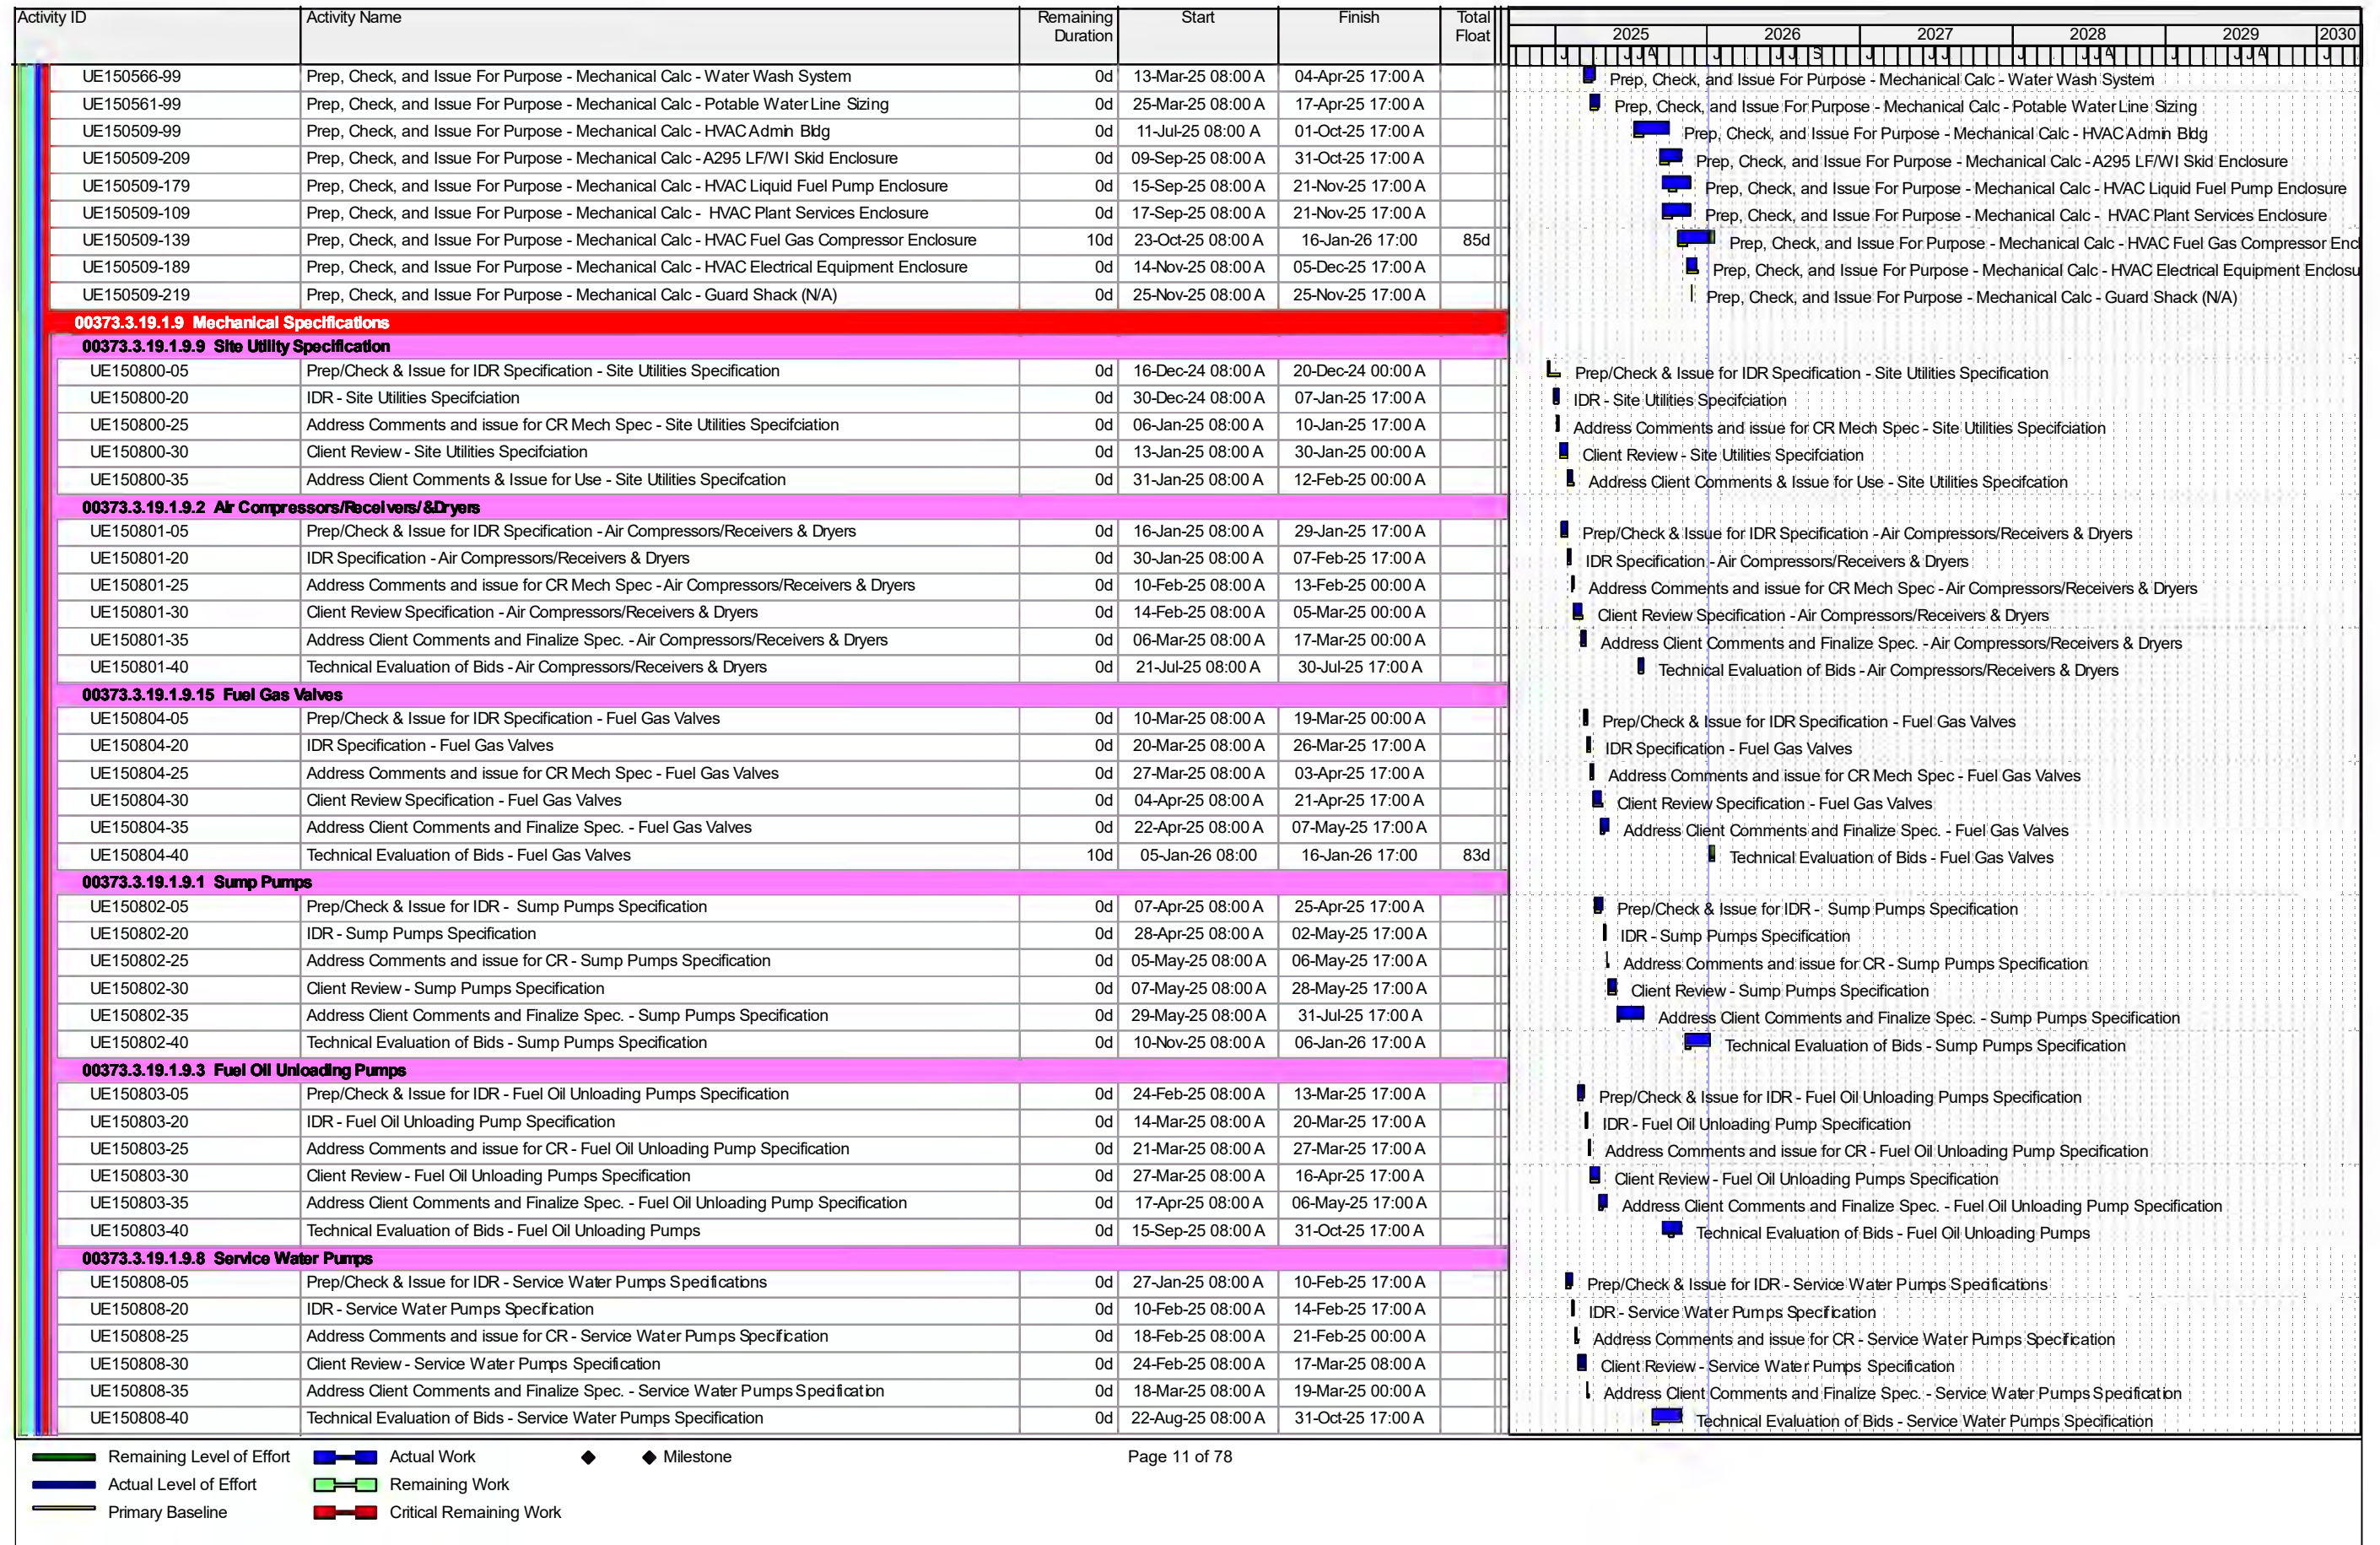

[illegible]

[illegible]

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float												
						2025			2026			2027			2028		
						J	J	A	J	J	S	J	J		J	J	A
	UE161113-20	Client Review P&ID's - Water Mist System	0d	17-Apr-25 08:00 A	28-Apr-25 17:00 A												
	UE161113-25	Address Client Comments and Issue IFD P&ID's - Water Mist System	0d	29-Apr-25 08:00 A	07-May-25 17:00 A												
	00373.3.19.3.4.4.14 Fire Protection																
	UE161114-05	Prep, Check, and Issue IDR P&ID's - Fire Protection	0d	19-Feb-25 08:00 A	07-Mar-25 00:00 A												
	UE161114-10	IDR P&ID's - Fire Protection	0d	10-Mar-25 08:00 A	17-Mar-25 00:00 A												
	UE161114-15	Address Comments and Issue for CR P&ID's - Fire Protection	0d	18-Mar-25 08:00 A	21-Mar-25 00:00 A												
	UE161114-20	Client Review P&ID's - Fire Protection	0d	24-Mar-25 08:00 A	08-Apr-25 00:00 A												
	UE161114-25	Address Client Comments and Issue IFD P&ID's - Fire Protection	0d	09-Apr-25 08:00 A	29-Apr-25 17:00 A												
	00373.3.19.3.4.4.15 Sanitary System (Riser Diagrams)																
	UE161115-05	Prep, Check, and Issue IDR P&ID's - Sanitary System & Potable Water Riser Diagrams	0d	06-Mar-25 08:00 A	25-Mar-25 17:00 A												
	UE161115-10	IDR P&ID's - Sanitary System & Potable Water Riser Diagrams	0d	26-Mar-25 08:00 A	01-Apr-25 17:00 A												
	UE161115-15	Address Comments and Issue for CR P&ID's - Sanitary System & Potable Water Riser Diagrams	0d	02-Apr-25 08:00 A	14-Apr-25 00:00 A												
	UE161115-20	Client Review P&ID's - Sanitary System & Potable Water Riser Diagrams	0d	15-Apr-25 08:00 A	05-May-25 17:00 A												
	UE161115-25	Address Client Comments and Issue IFD P&ID's - Sanitary System & Potable Water Riser Diagrams	0d	06-May-25 08:00 A	16-May-25 17:00 A												
	00373.3.19.3.4.5 Isometrics & Pipe Supports																
	UE100-95	IDR Pipe Supports - All Systems	10d	26-Jan-26 08:00	06-Feb-26 17:00	102d											
	UE100-97	Address IDR comments & Backcheck Pipe Supports - All Systems	10d	09-Feb-26 08:00	20-Feb-26 17:00	102d											
	UE100-99	Issue IFC Pipe Support Drawings- All Systems	2d	23-Feb-26 08:00	24-Feb-26 17:00	102d											
	00373.3.19.3.4.5.1 Fuel Gas																
	UE161101-35	Model Piping - Fuel Gas	0d	23-Jun-25 08:00 A	01-Dec-25 17:00 A												
	UE161101-75	Model Pipe Supports - Fuel Gas	0d	04-Aug-25 08:00 A	01-Dec-25 17:00 A												
	UE161101-40	Prep & Extract Isos. - Fuel Gas	0d	15-Oct-25 08:00 A	29-Dec-25 17:00 A												
	UE161101-80	Prepare Pipe Support Drawings- Fuel Gas	0d	20-Oct-25 08:00 A	03-Dec-25 08:00 A												
	UE161101-85	Check Pipe Support Drawings- Fuel Gas	0d	04-Dec-25 08:00 A	17-Dec-25 17:00 A												
	UE161101-95	IDR Pipe Support Drawings- Fuel Gas **Close Out**	0d	15-Dec-25 08:00 A	15-Dec-25 17:00 A												
	UE161101-99	Issue IFC Pipe Support Drawings- Fuel Gas **Close out**	0d	16-Dec-25 08:00 A	17-Dec-25 17:00 A												
	UE161101-90	Address Comments & Prepare for IDR Pipe Supports - Fuel Gas	0d	18-Dec-25 08:00 A	31-Dec-25 17:00 A												
	UE161101-45	Check Isos. - Fuel Gas	6d	30-Dec-25 08:00 A	12-Jan-26 17:00	52d											
	UE161101-50	Address comments & Issue for IDR - Fuel Gas	5d	13-Jan-26 08:00	19-Jan-26 17:00	52d											
	UE161101-60	IDR - Fuel Gas	10d	20-Jan-26 08:00	02-Feb-26 17:00	52d											
	UE161101-65	Address Comments & Backcheck Isos. - Fuel Gas	5d	03-Feb-26 08:00	09-Feb-26 17:00	52d											
	UE161101-70	Issue Iso. IFC - Fuel Gas	1d	10-Feb-26 08:00	10-Feb-26 17:00	52d											
	00373.3.19.3.4.5.17 Fuel Gas Yard Piping																
	UE161101-109	Model Piping - Fuel Gas Yard Piping	10d	09-Feb-26 08:00	20-Feb-26 17:00	220d											
	UE161101-119	Prep & Extract Isos. - Fuel Gas Yard Piping	5d	23-Feb-26 08:00	27-Feb-26 17:00	220d											
	UE161101-129	Check Isos. - Fuel Gas Yard Piping	5d	02-Mar-26 08:00	06-Mar-26 17:00	220d											
	UE161101-179	Model Pipe Supports - Fuel Gas Yard Piping	5d	02-Mar-26 08:00	06-Mar-26 17:00	225d											
	UE161101-189	Prepare Pipe Support Drawings- Fuel Gas Yard Piping	5d	02-Mar-26 08:00	06-Mar-26 17:00	225d											
	UE161101-139	Address comments & Issue for IDR - Fuel Gas Yard Piping	5d	09-Mar-26 08:00	13-Mar-26 17:00	220d											
	UE161101-199	Check Pipe Support Drawings- Fuel Gas Yard Piping	5d	09-Mar-26 08:00	13-Mar-26 17:00	225d											
	UE161101-149	IDR - Fuel Gas Yard Piping	5d	16-Mar-26 08:00	20-Mar-26 17:00	220d											
	UE161101-209	Address Comments & Prepare for IFC Pipe Supports - Fuel Gas Yard Piping	5d	16-Mar-26 08:00	20-Mar-26 17:00	225d											
	UE161101-229	Issue IFC Pipe Support Drawings- Fuel Gas Yard Piping	1d	23-Mar-26 08:00	23-Mar-26 17:00	225d											
	UE161101-159	Address Comments & Backcheck Isos. - Fuel Gas Yard Piping	5d	23-Mar-26 08:00	27-Mar-26 17:00	220d											
	UE161101-169	Issue Iso. IFC - Fuel Gas Yard Piping	1d	30-Mar-26 08:00	30-Mar-26 17:00	220d											
	00373.3.19.3.4.5.2 Fuel Oil																
	UE161102-35	Model Piping - Fuel Oil	0d	23-Jun-25 08:00 A	01-Dec-25 17:00 A												
	UE161102-75	Model Pipe Supports - Fuel Oil	0d	04-Aug-25 08:00 A	01-Dec-25 17:00 A												
	UE161102-80	Prepare Pipe Support Drawings- Fuel Oil	0d	20-Oct-25 08:00 A	03-Dec-25 08:00 A												
	UE161102-40	Prep & Extract Isos. - Fuel Oil	10d	20-Oct-25 08:00 A	16-Jan-26 17:00	42d											
	UE161102-95	IDR Pipe Support Drawings- Fuel Oil	0d	01-Dec-25 08:00 A	01-Dec-25 17:00 A												
Remaining Level of Effort Actual Level of Effort Primary Baseline Actual Work Remaining Work Critical Remaining Work Milestone																	

[illegible]

[illegible]

[illegible]

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float																																																																				
						2025												2026												2027												2028												2029												2030							
						J J J A												J J J S												J J J												J J J A												J J J A												J							
UE170809-35	Address Client Comments and Finalize Spec. - 125VDC/120VAC	10d	04-Feb-26 08:00	17-Feb-26 17:00	35d																																																																				
UE170809-40	Technical Evaluation of Bids - 125VDC/120VAC	15d	04-May-26 08:00	22-May-26 17:00	7d																																																																				
00373.3.19.2.8.10 Heat Trace Specification																																																																									
UE170810-05	Prep/Check & Issue for IDR Specification - Heat Trace	20d	17-Mar-26 08:00	13-Apr-26 17:00	28d																																																																				
UE170810-20	IDR Procurement Specification - Heat Trace	5d	14-Apr-26 08:00	20-Apr-26 17:00	28d																																																																				
UE170810-25	Address Comments and issue for CR Spec - Heat Trace	5d	21-Apr-26 08:00	27-Apr-26 17:00	28d																																																																				
UE170810-30	Client Review Procurement Specification - Heat Trace	15d	28-Apr-26 08:00	18-May-26 17:00	28d																																																																				
UE170810-35	Address Client Comments and Finalize Spec. - Heat Trace	10d	19-May-26 08:00	02-Jun-26 17:00	28d																																																																				
UE170810-40	Technical Evaluation of Bids - Heat Trace	15d	09-Jul-26 08:00	29-Jul-26 17:00	28d																																																																				
00373.3.19.2.8.12 Electrical Installation Specification																																																																									
UE170901-05	Prep/Check & Issue for IDR Specification - Electrical Installation Requirements **** Close out****	0d	11-Aug-25 08:00 A	11-Aug-25 17:00 A																																																																					
UE170901-20	IDR Procurement Specification - Electrical Installation Requirements	0d	11-Aug-25 08:00 A	11-Aug-25 17:00 A																																																																					
UE170901-25	Address Comments and issue for CR Spec - Electrical Installation Requirements	0d	11-Aug-25 08:00 A	11-Aug-25 17:00 A																																																																					
UE170901-30	Client Review Procurement Specification - Electrical Installation Requirements	0d	11-Aug-25 08:00 A	11-Aug-25 17:00 A																																																																					
UE170901-35	Address Client Comments and Issue Final - Electrical Installation Requirements	0d	11-Aug-25 08:00 A	11-Aug-25 17:00 A																																																																					
00373.3.19.2.1 Calculations & Studies																																																																									
00373.3.19.2.1.1 Electrical LF/SC Calculation																																																																									
UE170501-05	Prepare & Issue CR - Preliminary Electrical LF/SC Calculations	0d	03-Jan-25 08:00 A	07-Feb-25 17:00 A																																																																					
Ue170501-20	Client Review - Preliminary Electrical LF/SC Calculations	0d	10-Feb-25 08:00 A	28-Feb-25 17:00 A																																																																					
UE170501-25	Address CR Comments & Issue Preliminary Electrical LF/SC Calculations	0d	03-Mar-25 08:00 A	21-Mar-25 17:00 A																																																																					
Ue170501-30	Prepare & Issue CR - Final Electrical LF/SC Calculations	26d	19-Jan-26 08:00	23-Feb-26 17:00	71d																																																																				
UE170501-35	Client Review - Final Electrical LF/SC Calculations	15d	24-Feb-26 08:00	16-Mar-26 17:00	71d																																																																				
Ue170501-40	Address CR Comments & Issue Final Electrical LF/SC Calculations	10d	17-Mar-26 08:00	30-Mar-26 17:00	71d																																																																				
00373.3.19.2.1.2 Electrical Isophase Bus Sizing Calculation																																																																									
UE170502-05	Prepare Preliminary Isophase Bus Sizing Calculation	0d	30-Dec-24 08:00 A	14-Feb-25 17:00 A																																																																					
UE170502-10	Issue Preliminary Electrical Isophase Bus Sizing Calculation	0d	14-Feb-25 08:00 A	14-Feb-25 17:00 A																																																																					
UE170502-15	Review & Revise Isophase Bus Sizing Calculation	0d	11-Apr-25 08:00 A	28-Apr-25 17:00 A																																																																					
UE170502-20	Issue Final Isophase Bus Sizing Calculation	0d	29-Apr-25 08:00 A	29-Apr-25 17:00 A																																																																					
00373.3.19.2.1.3 125VDC/120VAC Load Calculation																																																																									
UE170503-05	Prepare & Issue Preliminary 125VDC/120VAC Load Calculation for IDR	0d	13-Nov-25 08:00 A	29-Dec-25 17:00 A																																																																					
UE170503-10	Issue Preliminary 125VDC/120VAC Load Calculation	0d	29-Dec-25 08:00 A	29-Dec-25 17:00 A																																																																					
UE170503-15	Address Comments & Issue for CR 125VDC/120VAC Load Calculation	35d	30-Dec-25 08:00 A	20-Feb-26 17:00	7d																																																																				
UE170503-30	Client Review 125VDC/120VAC Load Calculation	15d	23-Feb-26 08:00	13-Mar-26 17:00	7d																																																																				
UE170503-20	Address Client Comments & Finalize Spec 125VDC/120VAC Load Calculation	10d	16-Mar-26 08:00	27-Mar-26 17:00	7d																																																																				
00373.3.19.2.1.4 Lightning Protection Calculation																																																																									
UE170504-05	Prepare Preliminary Lightning Protection Calculation & Issue for IDR	0d	07-Aug-25 08:00 A	13-Oct-25 17:00 A																																																																					
UE170504-10	IDR Preliminary Lightning Protection Calculation	0d	14-Oct-25 08:00 A	20-Oct-25 17:00 A																																																																					
UE170504-15	Address IDR Comments & Issue for CR - Lightning Protection Calculation	0d	21-Oct-25 08:00 A	27-Oct-25 17:00 A																																																																					
UE170504-30	Client Review - Lightning Protection Calculation	0d	28-Oct-25 08:00 A	10-Nov-25 17:00 A																																																																					
UE170504-20	Address Client Comments & Issue IFC - Lightning Protection Calculation	0d	11-Nov-25 08:00 A	01-Dec-25 08:00 A																																																																					
00373.3.19.2.1.5 Relay Setting & Coordination Study																																																																									
UE170505-05	Prepare Preliminary Relay Setting & Coordination Study	40d	26-May-26 08:00	21-Jul-26 17:00	61d																																																																				
UE170505-10	Issue for CR - Preliminary Relay Setting & Coordination Study	1d	21-Jul-26 08:00	21-Jul-26 17:00	61d																																																																				
UE170505-15	Client Review - Preliminary Relay Setting & Coordination Study	15d	22-Jul-26 08:00	11-Aug-26 17:00	66d																																																																				
UE170505-20	Review & Revise Relay Setting & Coordination Study	15d	19-Aug-26 08:00	09-Sep-26 17:00	61d																																																																				
UE170505-25	Issue Final Relay Setting & Coordination Study	1d	09-Sep-26 08:00	09-Sep-26 17:00	61d																																																																				
00373.3.19.2.1.8 Cable Take Off																																																																									
UE171182-3																																																																									

[illegible]

[illegible]

Activity ID		Activity Name		Remaining Duration	Start	Finish	Total Float																														
								2025				2026				2027				2028				2029				2030									
								J	J	J	A	J	J	J	S	J	J	J	J	J	A	J	J	J	A	J	J	J	A	J							
00373.3.19.2.7.1 Schematics & Wiring Diagrams - Fuel Gas																																					
UE171115-07		Prepare Wiring & Schematic Diagrams - Fuel Gas		30d	05-Jun-26 08:00	17-Jul-26 17:00	105d																							Prepare Wiring & Schematic Diagrams - Fuel Gas							
UE171115-10		Receive vendor Information - Wiring & Schematic Diagrams - Fuel Gas		10d	20-Jul-26 08:00	31-Jul-26 17:00	105d																							Receive vendor Information - Wiring & Schematic Diagrams - Fuel Gas							
UE171115-15		Incorporate information & Issue for CR - Wiring & Schematic Diagrams - Fuel Gas		20d	03-Aug-26 08:00	28-Aug-26 17:00	105d																							Incorporate information & Issue for CR - Wiring & Schematic Diagrams - Fuel Gas							
UE171115-20		Client Review - Wiring & Schematic Diagrams - Fuel Gas		15d	31-Aug-26 08:00	21-Sep-26 17:00	105d																							Client Review - Wiring & Schematic Diagrams - Fuel Gas							
UE171115-25		Address Client Comments & Update with Final Vendor info & Issue IFC - Wiring & Schematics - Fuel Gas		10d	22-Sep-26 08:00	05-Oct-26 17:00	105d																							Address Client Comments & Update with Final Vendor info & Issue IFC - Wiring & Schematics - Fuel Gas							
00373.3.19.2.7.6 Schematics & Wiring Diagrams - Demineralized Water																																					
UE171117-07		Prepare Wiring & Schematic Diagrams - Demin Water		15d	17-Mar-26 08:00	06-Apr-26 17:00	64d																							Prepare Wiring & Schematic Diagrams - Demin Water							
UE171117-12		Receive vendor Information - Wiring & Schematic Diagrams - Demin Water		10d	07-Apr-26 08:00	20-Apr-26 17:00	64d																							Receive vendor Information - Wiring & Schematic Diagrams - Demin Water							
UE171117-17		Incorporate information & Issue for CR - Wiring & Schematic Diagrams - Demin Water		12d	21-Apr-26 08:00	06-May-26 17:00	64d																							Incorporate information & Issue for CR - Wiring & Schematic Diagrams - Demin Water							
UE171117-22		Client Review - Wiring & Schematic Diagrams - Demin Water		15d	07-May-26 08:00	28-May-26 17:00	124d																							Client Review - Wiring & Schematic Diagrams - Demin Water							
UE171117-27		Address Client Comments & Update with Final Vendor info & Issue IFC - Wiring & Schematics - Demin Water		10d	29-May-26 08:00	11-Jun-26 17:00	124d																							Address Client Comments & Update with Final Vendor info & Issue IFC - Wiring & Schematics - Demin Water							
00373.3.19.2.7.9 Schematics & Wiring Diagrams - Fuel Oil																																					
UE171107-05		Prepare Wiring & Schematic Diagrams - Fuel Oil		15d	07-May-26 08:00	28-May-26 17:00	79d																							Prepare Wiring & Schematic Diagrams - Fuel Oil							
UE171107-12		Receive vendor Information - Wiring & Schematic Diagrams - Fuel Gas		10d	29-May-26 08:00	11-Jun-26 17:00	79d																							Receive vendor Information - Wiring & Schematic Diagrams - Fuel Gas							
UE171107-17		Incorporate information & Issue for CR - Wiring & Schematic Diagrams - Fuel Gas		20d	12-Jun-26 08:00	10-Jul-26 17:00	79d																							Incorporate information & Issue for CR - Wiring & Schematic Diagrams - Fuel Gas							
UE171107-22		Client Review - Wiring & Schematic Diagrams - Fuel Gas		15d	13-Jul-26 08:00	31-Jul-26 17:00	79d																							Client Review - Wiring & Schematic Diagrams - Fuel Gas							
UE171107-27		Address Client Comments & Update with Final Vendor info & Issue IFC - Wiring & Schematics - Fuel Gas		10d	03-Aug-26 08:00	14-Aug-26 17:00	79d																							Address Client Comments & Update with Final Vendor info & Issue IFC - Wiring & Schematics - Fuel Gas							
00373.3.19.2.7.7 Schematics & Wiring Diagrams - Closed Cooling Water																																					
UE171127-07		Prepare Wiring & Schematic Diagrams - Closed Cooling Water		15d	05-Jun-26 08:00	25-Jun-26 17:00	59d																							Prepare Wiring & Schematic Diagrams - Closed Cooling Water							
UE171127-12		Receive vendor Information - Wiring & Schematic Diagrams - Closed Cooling Water		10d	26-Jun-26 08:00	10-Jul-26 17:00	59d																							Receive vendor Information - Wiring & Schematic Diagrams - Closed Cooling Water							
UE171127-17		Incorporate information & Issue for CR - Wiring & Schematic Diagrams - Closed Cooling Water		20d	13-Jul-26 08:00	07-Aug-26 17:00	59d																							Incorporate information & Issue for CR - Wiring & Schematic Diagrams - Closed Cooling Water							
UE171127-22		Client Review - Wiring & Schematic Diagrams - Closed Cooling Water		15d	10-Aug-26 08:00	28-Aug-26 17:00	59d																							Client Review - Wiring & Schematic Diagrams - Closed Cooling Water							
UE171127-27		Address Client Comments & Update with Final Vendor info & Issue IFC - Wiring & Schematics - Closed Cooling Water		10d	31-Aug-26 08:00	14-Sep-26 17:00	59d																							Address Client Comments & Update with Final Vendor info & Issue IFC - Wiring & Schematics - Closed Cooling Water							
00373.3.19.2.7.10 Schematics & Wiring Diagrams - Service Water																																					
UE171119-07		Prepare Wiring & Schematic Diagrams - Service Water		20d	07-May-26 08:00	04-Jun-26 17:00	74d																							Prepare Wiring & Schematic Diagrams - Service Water							
UE171119-12		Receive vendor Information - Wiring & Schematic Diagrams - Service Water		10d	05-Jun-26 08:00	18-Jun-26 17:00	74d																							Receive vendor Information - Wiring & Schematic Diagrams - Service Water							
UE171119-17		Incorporate information & Issue for CR - Wiring & Schematic Diagrams - Service Water		20d	19-Jun-26 08:00	17-Jul-26 17:00																															


[illegible]

[illegible]


Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	202520262027202820292030																																																			
PL130803-40	Proc to check spec, MR, Load SPM, Issue for Bid - Platforms	0d	15-Oct-25 08:00 A	28-Oct-25 17:00 A		Proc to check spec, MR, Load SPM, Issue for Bid - Platforms																																																			
PL130803-45	Receive Bids - Platforms	0d	29-Oct-25 08:00 A	04-Nov-25 17:00 A		Receive Bids - Platforms																																																			
PL130803-50	Comm Bid Evaluation and Conform Tech Documents - Platforms	0d	31-Oct-25 08:00 A	06-Nov-25 17:00 A		Comm Bid Evaluation and Conform Tech Documents - Platforms																																																			
PL130803-55	Award Package - Platforms	0d	05-Nov-25 08:00 A	05-Nov-25 17:00 A		Award Package - Platforms																																																			
PL130803-60	Receive/Approve Supplier Documents - Platforms	0d	10-Nov-25 08:00 A	15-Dec-25 08:00 A		Receive/Approve Supplier Documents - Platforms																																																			
PL130803-65	Fabricate and Deliver- Platforms	91d	15-Dec-25 08:00 A	11-May-26 17:00	88d	Fabricate and Deliver- Platforms																																																			
PL130803-70	Deliver to Site - Platforms	5d	12-May-26 08:00	18-May-26 17:00	88d	Deliver to Site - Platforms																																																			
00373.4.22 Embedments & Anchor Bolts																																																									
PL130805-40	Proc to check spec, MR, Load SPM, Issue for Bid - Embedments & Anchor Bolts	0d	18-Aug-25 08:00 A	02-Sep-25 08:00 A		Proc to check spec, MR, Load SPM, Issue for Bid - Embedments & Anchor Bolts																																																			
PL130805-45	Receive Bids - Embedments & Anchor Bolts	0d	02-Sep-25 08:00 A	15-Sep-25 08:00 A		Receive Bids - Embedments & Anchor Bolts																																																			
PL130805-50	Tech/Comm Bid Evaluation and Conform Tech Documents - Embedments & Anchor Bolts	0d	15-Sep-25 08:00 A	15-Sep-25 17:00 A		Tech/Comm Bid Evaluation and Conform Tech Documents - Embedments & Anchor Bolts																																																			
PL130805-55	Award Package - Embedments & Anchor Bolts	0d	16-Sep-25 08:00 A	16-Sep-25 17:00 A		Award Package - Embedments & Anchor Bolts																																																			
PL130805-60	Receive/Approve Supplier Documents - Embedments & Anchor Bolts	0d	17-Sep-25 08:00 A	19-Nov-25 17:00 A		Receive/Approve Supplier Documents - Embedments & Anchor Bolts																																																			
PL130805-65	Fabricate and Deliver- CTG Base Slab Anchor Bolts	0d	20-Nov-25 08:00 A	15-Dec-25 08:00 A		Fabricate and Deliver- CTG Base Slab Anchor Bolts																																																			
PL130805-80	Fabricate and Deliver- CTG Pedestals Embedments & Anchor Bolts	0d	20-Nov-25 08:00 A	22-Dec-25 17:00 A		Fabricate and Deliver- CTG Pedestals Embedments & Anchor Bolts																																																			
00373.4.22.1 Deliver to Site - Base Slab Anchor Bolts																																																									
PL130805-100	Deliver to Site - U2 CTG Base Slab Anchor Bolts	0d	15-Dec-25 08:00 A	15-Dec-25 17:00 A		Deliver to Site - U2 CTG Base Slab Anchor Bolts																																																			
PL130805-120	Deliver to Site - U3 CTG Base Slab Anchor Bolts	0d	15-Dec-25 08:00 A	15-Dec-25 17:00 A		Deliver to Site - U3 CTG Base Slab Anchor Bolts																																																			
PL130805-140	Deliver to Site - U4 CTG Base Slab Anchor Bolts	0d	15-Dec-25 08:00 A	15-Dec-25 17:00 A		Deliver to Site - U4 CTG Base Slab Anchor Bolts																																																			
PL130805-70	Deliver to Site - U1 CTG Base Slab Anchor Bolts	0d	15-Dec-25 08:00 A	15-Dec-25 17:00 A		Deliver to Site - U1 CTG Base Slab Anchor Bolts																																																			
00373.4.22.2 Deliver to Site - Pedestal Embedments & Anchor Bolts																																																									
PL130805-110	Deliver to Site - U2 CTG Pedestals Embedments & Anchor Bolts	0d	29-Dec-25 08:00 A	29-Dec-25 17:00 A		Deliver to Site - U2 CTG Pedestals Embedments & Anchor Bolts																																																			
PL130805-130	Deliver to Site - U3 CTG Pedestals Embedments & Anchor Bolts	0d	29-Dec-25 08:00 A	29-Dec-25 17:00 A		Deliver to Site - U3 CTG Pedestals Embedments & Anchor Bolts																																																			
PL130805-150	Deliver to Site - U4 CTG Pedestals Embedments & Anchor Bolts	0d	29-Dec-25 08:00 A	29-Dec-25 17:00 A		Deliver to Site - U4 CTG Pedestals Embedments & Anchor Bolts																																																			
PL130805-90	Deliver to Site - U1 CTG Pedestals Embedments & Anchor Bolts *Close out all units**	0d	29-Dec-25 08:00 A	29-Dec-25 17:00 A		Deliver to Site - U1 CTG Pedestals Embedments & Anchor Bolts *Close out all units**																																																			
00373.4.2 Air Compressors/Receivers/&Dryers																																																									
PL150801-40	Proc to check spec, MR, Load SPM, Issue for Bid - Air Compressors/Receivers & Dryers	0d	18-Jun-25 08:00 A	01-Jul-25 17:00 A		Proc to check spec, MR, Load SPM, Issue for Bid - Air Compressors/Receivers & Dryers																																																			
PL150801-45	Receive Bids - Air Compressors/Receivers & Dryers	0d	02-Jul-25 08:00 A	07-Jul-25 17:00 A		Receive Bids - Air Compressors/Receivers & Dryers																																																			
PL150801-50	Comm Bid Evaluation and Conform Tech Documents - Air Compressors/Receivers & Dryers	0d	08-Jul-25 08:00 A	09-Jul-25 17:00 A		Comm Bid Evaluation and Conform Tech Documents - Air Compressors/Receivers & Dryers																																																			
PL150801-55	Award Package - Air Compressors/Receivers & Dryers	0d	10-Jul-25 08:00 A	16-Jul-25 17:00 A		Award Package - Air Compressors/Receivers & Dryers																																																			
PL150801-60	Receive/Approve Supplier Documents - Air Compressors/Receivers & Dryers	0d	17-Jul-25 08:00 A	17-Jul-25 17:00 A		Receive/Approve Supplier Documents - Air Compressors/Receivers & Dryers																																																			
PL150801-65	Fabricate and Deliver- Air Compressors/Receivers & Dryers	0d	18-Jul-25 08:00 A	18-Jul-25 17:00 A		Fabricate and Deliver- Air Compressors/Receivers & Dryers																																																			
PL150801-70	Deliver to Site - Air Compressors/Receivers & Dryers	0d	21-Jul-25 08:00 A	21-Jul-25 17:00 A		Deliver to Site - Air Compressors/Receivers & Dryers																																																			
00373.4.7 Sump Pumps																																																									
PL150802-40	Proc to check spec, MR, Load SPM, Issue for Bid - Sump Pumps	0d	08-Sep-25 08:00 A	19-Sep-25 17:00 A		Proc to check spec, MR, Load SPM, Issue for Bid - Sump Pumps																																																			
PL150802-45	Receive Bids - Sump Pumps	0d	22-Sep-25 08:00 A	30-Sep-25 17:00 A		Receive Bids - Sump Pumps																																																			
PL150802-50	Comm Bid Evaluation and Conform Tech Documents - Sump Pumps	0d	01-Oct-25 08:00 A	28-Oct-25 08:00 A		Comm Bid Evaluation and Conform Tech Documents - Sump Pumps																																																			
PL150802-55	Award Package - Sump Pumps	0d	03-Nov-25 08:00 A	07-Nov-25 17:00 A		Award Package - Sump Pumps																																																			
PL150802-60	Receive/Approve Supplier Documents - Sump Pumps	0d	10-Nov-25 08:00 A	05-Jan-26 08:00 A		Receive/Approve Supplier Documents - Sump Pumps																																																			
PL150802-65	Fabricate and Deliver- Sump Pumps	180d	05-Jan-26 08:00 A	16-Sep-26 17:00	66d	Fabricate and Deliver- Sump Pumps																																																			
PL15																																																									

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
						2025													2026													2027													2028													2029													2030																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																													
						J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J

[illegible]

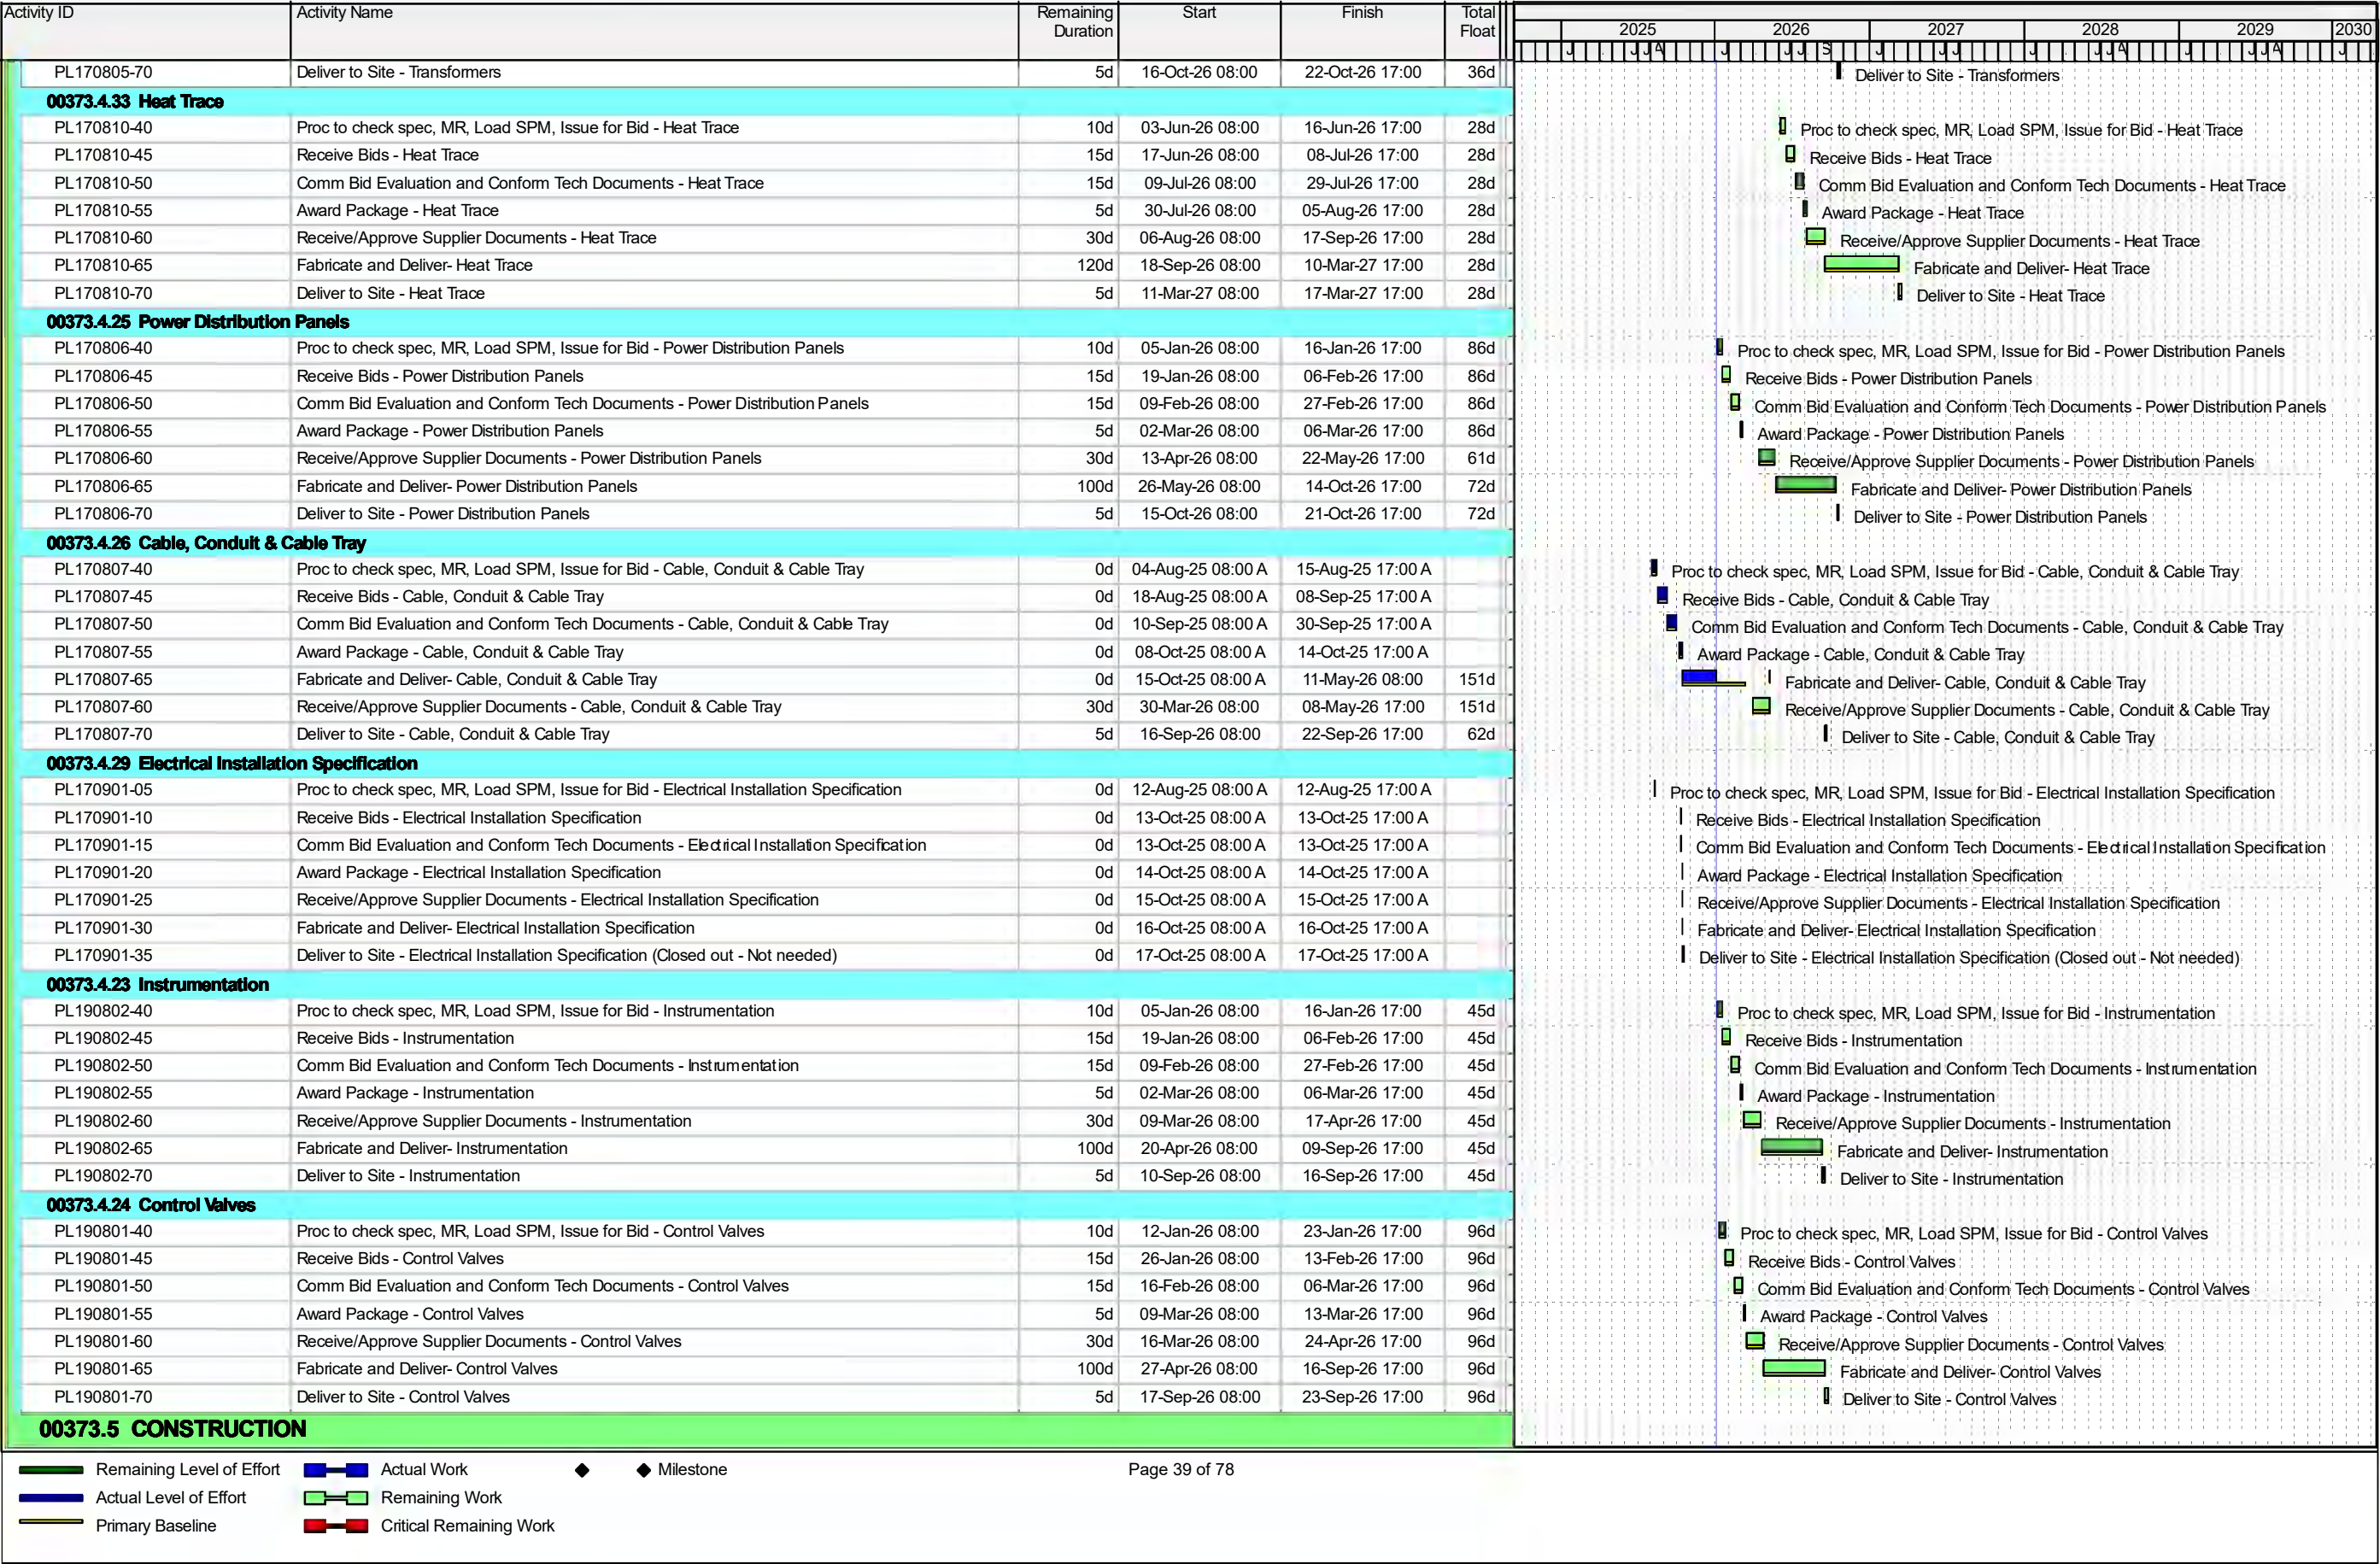

Page 39 of 78

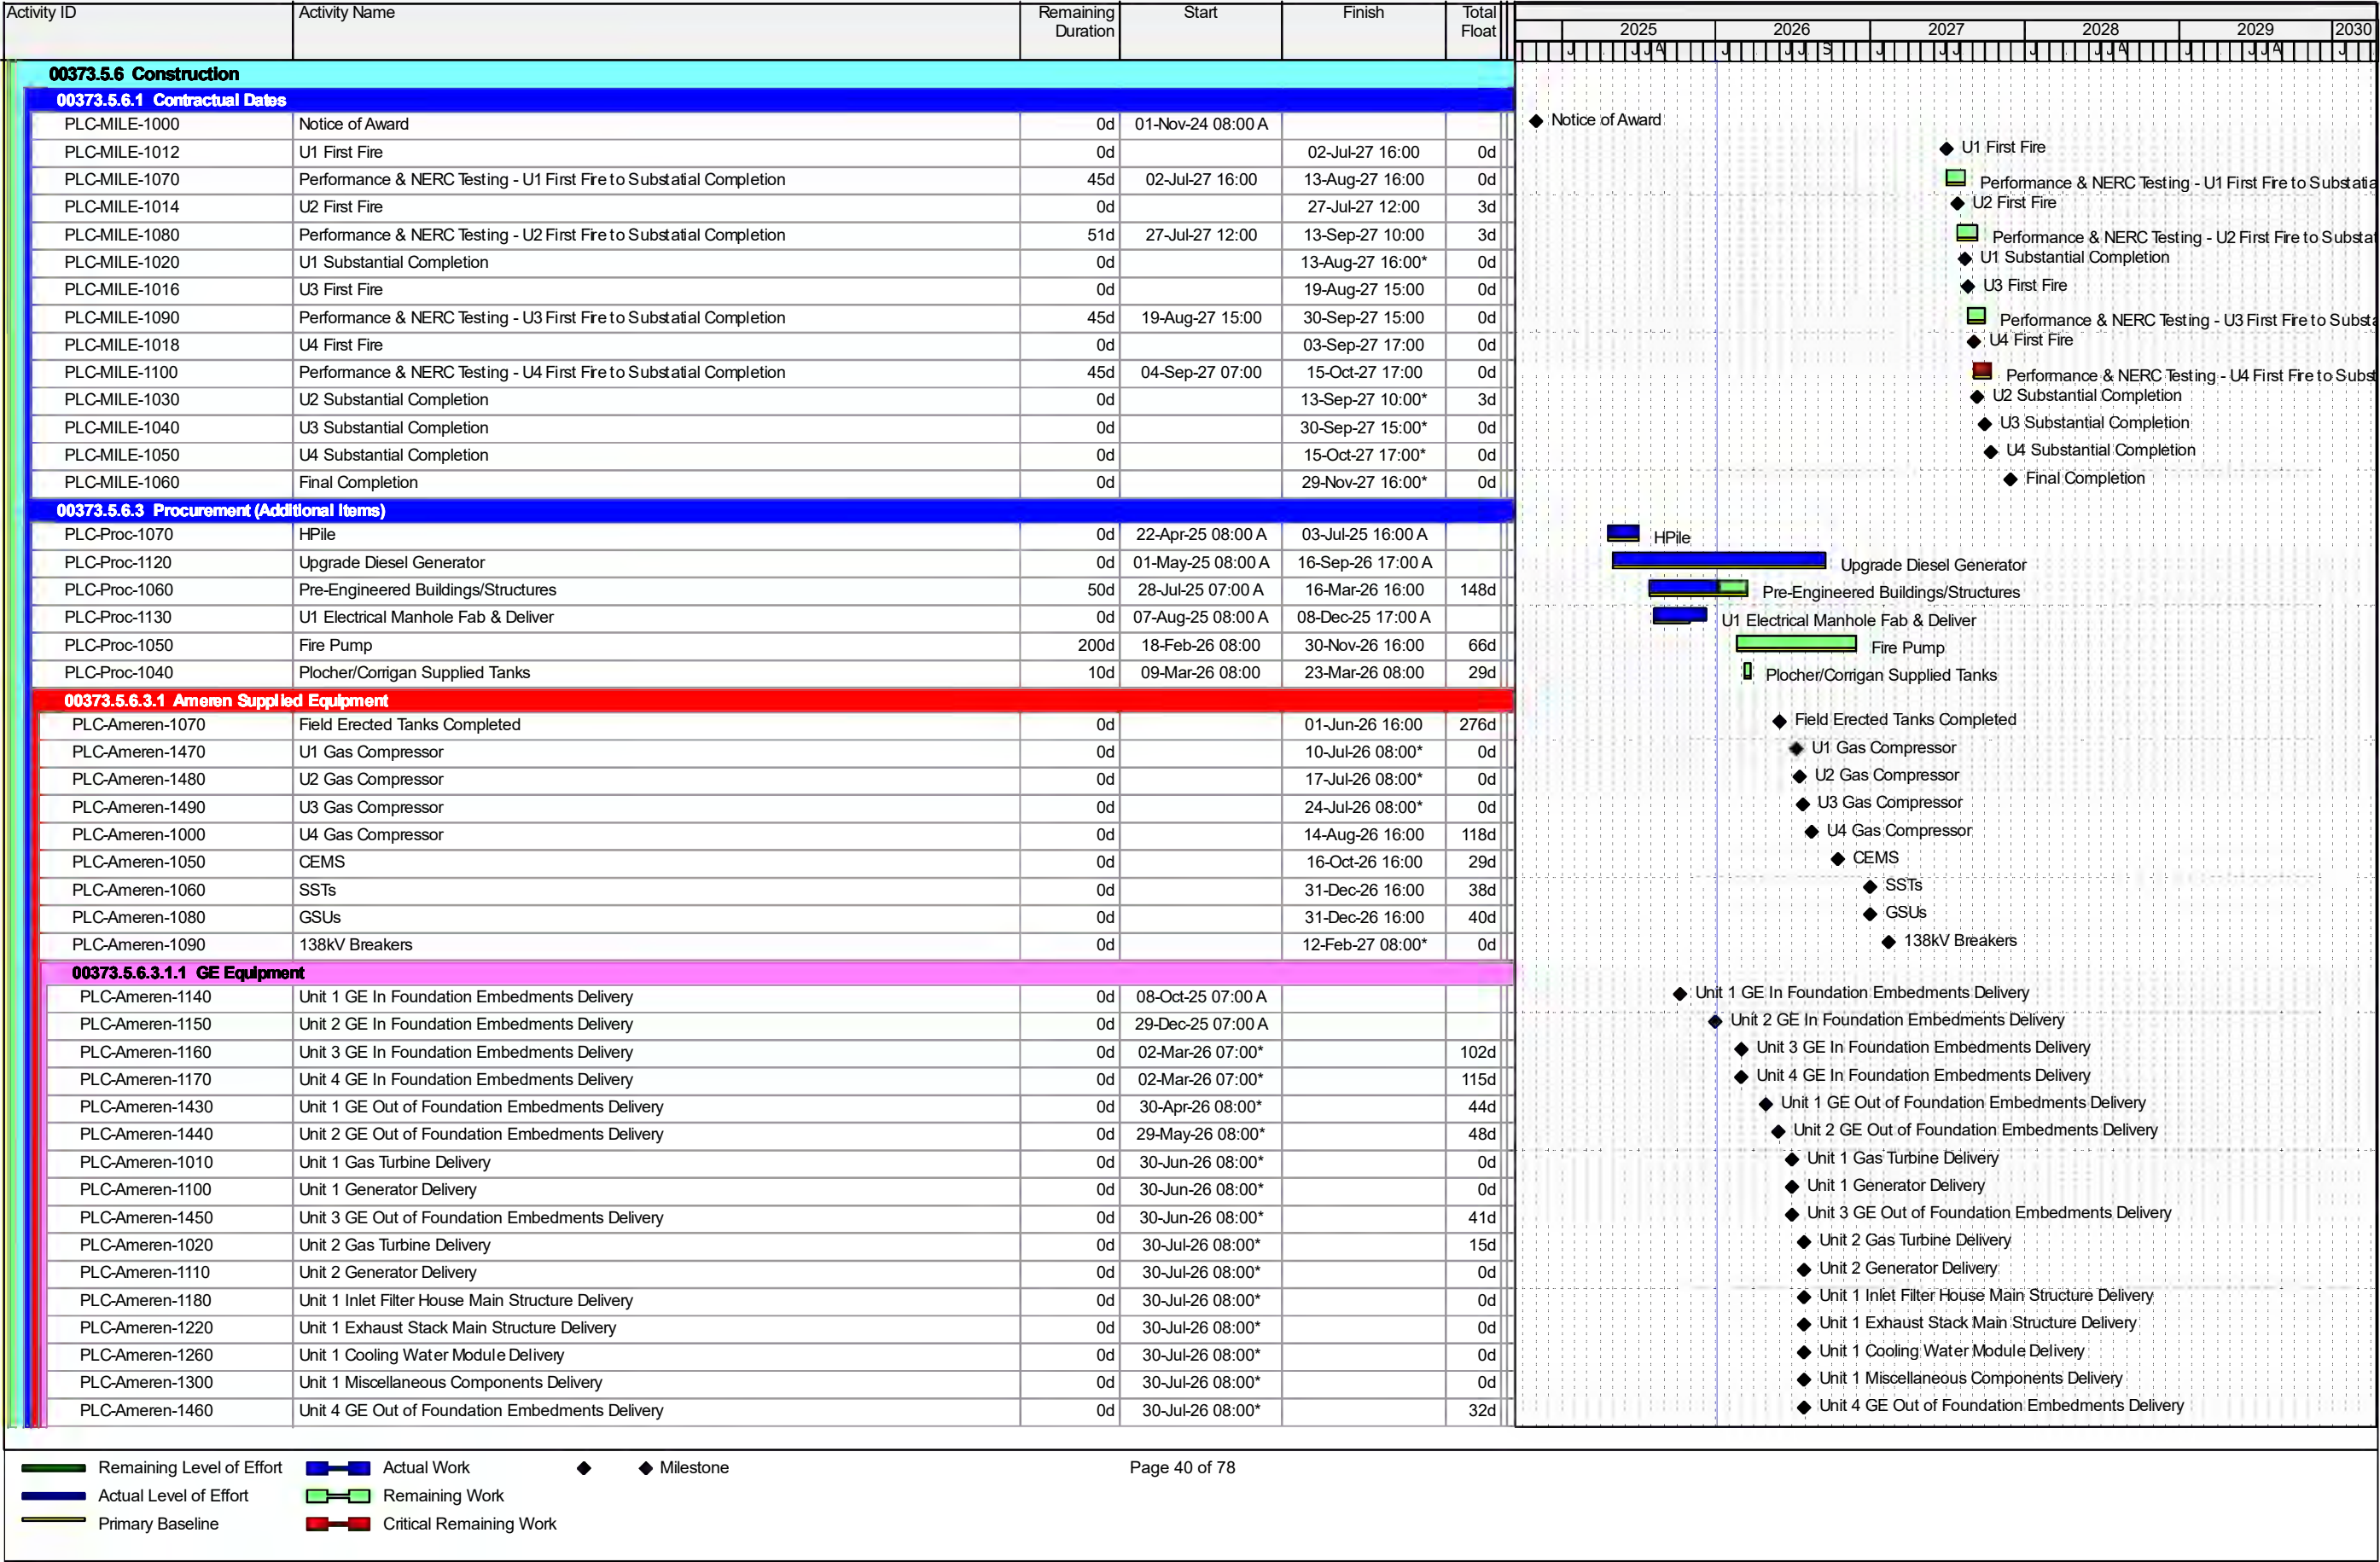

[illegible]

[illegible]

[illegible]

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float	202520262027202820292030																																																					
00373.5.6.01.0044 Diesel Generator	PL-FGC-1120	Set Fuel Gas Compressor #3	3d	23-Nov-26 07:00	25-Nov-26 11:00	58d																																																					
	PL-FGC-1130	SRT Fuel Gas Compressor #4	3d	25-Nov-26 11:00	30-Nov-26 15:00	58d																																																					
	PL-FGC-1140	Set Fuel Gas Compressor Cooler #1	1d	30-Nov-26 15:00	01-Dec-26 13:00	58d																																																					
	PL-FGC-1150	Set Fuel Gas Compressor Cooler #2	1d	01-Dec-26 13:00	02-Dec-26 11:00	58d																																																					
	PL-FGC-1160	Set Fuel Gas Compressor Cooler #3	1d	02-Dec-26 11:00	03-Dec-26 09:00	58d																																																					
	PL-FGC-1170	Set Fuel Gas Compressor Cooler #4	1d	03-Dec-26 09:00	03-Dec-26 17:00	58d																																																					
	PL-FGC-1070	Set Fuel Gas Compressors Air Receiver	1d	04-Dec-26 07:00	04-Dec-26 15:00	58d																																																					
	PL-FGC-1080	Set Fuel Gas Chromatograph	1d	04-Dec-26 15:00	07-Dec-26 13:00	166d																																																					
	PL-FGC-1180	Set Fuel Gas Nitrogen Generator #1	1d	04-Dec-26 15:00	07-Dec-26 13:00	58d																																																					
	PL-FGC-1190	Set Fuel Gas Nitrogen Generator #2	1d	07-Dec-26 13:00	08-Dec-26 11:00	58d																																																					
	PL-ADWH-1240	Fuel Gas Building Drywall & Wall Finishes	20d	09-Dec-26 09:00	05-Jan-27 09:00	144d																																																					
	PL-ADWH-1250	MEP Finishes	15d	05-Jan-27 09:00	21-Jan-27 09:00	144d																																																					
	00373.5.6.01.044 Diesel Generator																																																										
	PL-DG-1000	Drive Pile (5) DG	1d	11-May-26 07:00	11-May-26 15:00	194d																																																					
	PL-DG-1010	Excavate DG	1d	11-May-26 15:00	12-May-26 13:00	194d																																																					
	PL-DG-1020	Underground Rough-In DG	3d	12-May-26 13:00	14-May-26 17:00	194d																																																					
	PL-DG-1030	Mud Mat DG	1d	15-May-26 07:00	15-May-26 15:00	253d																																																					
	PL-DG-1040	Base Slab Forming and Embeds DG	5d	15-May-26 15:00	21-May-26 15:00	253d																																																					
	PL-DG-1050	Base Slab Reinforcement DG	5d	21-May-26 15:00	28-May-26 15:00	253d																																																					
	PL-DG-1080	Grounding	2d	28-May-26 15:00	01-Jun-26 11:00	253d																																																					
	PL-DG-1060	Pour and Wreck Base Slab DG	3d	01-Jun-26 11:00	03-Jun-26 15:00	253d																																																					
	PL-DG-1070	Backfill DG	2d	03-Jun-26 15:00	05-Jun-26 11:00	253d																																																					
	00373.5.6.01.010 Fire Protection Pump House																																																										
	PL-FPPH-1000	Drive Pile (6) Fire Pump House	2d	06-Jul-26 16:00	08-Jul-26 12:00	194d																																																					
	PL-FPPH-1010	Excavate Fire Pump House	1d	08-Jul-26 12:00	09-Jul-26 10:00	194d																																																					
	PL-FPPH-1020	Underground Rough-In Fire Pump House	3d	09-Jul-26 10:00	13-Jul-26 14:00	194d																																																					
	PL-FPPH-1030	Base Slab Forming and Embeds Fire Pump House	4d	13-Jul-26 14:00	16-Jul-26 16:00	194d																																																					
	PL-FPPH-1040	Base Slab Reinforcement Fire Pump House	2d	16-Jul-26 16:00	20-Jul-26 12:00	194d																																																					
	PL-FPPH-1070	Grounding	3d	20-Jul-26 12:00	22-Jul-26 16:00	194d																																																					
	PL-FPPH-1050	Pour and Wreck Base Slab Fire Pump House	2d	22-Jul-26 16:00	24-Jul-26 12:00	194d																																																					
	PL-FPPH-1060	Backfill Fire Pump House	2d	30-Nov-26 16:00	02-Dec-26 12:00	82d																																																					
	00373.5.6.01.043 Hydrogen Trailers																																																										
	PL-HT-1000	Form, Reinforce and Pour Slab Hydrogen Trailers	5d	27-May-26 13:00	02-Jun-26 13:00	244d																																																					
	00373.5.6.01.019 Fuel Gas Metering Yard Area																																																										
	PL-FGMY-1000	Place Holder for Gas Metering Yard	185d	01-Dec-25 11:00 A	15-Dec-26 17:00	73d																																																					
	00373.5.6.01.050 Proposed New Gas Line - (AMEREN)																																																										
	PL-NGL-1000	MRT Gas Line Completion Milestone	0d		15-Dec-26 17:00*	73d																																																					
	00373.5.6.01.060 Liquid Fuel Pump Enclosure Building																																																										
	PL-FOU-1000	Excavate Liquid Fuel Pump Encloser	1d	24-Apr-26 14:00	27-Apr-26 12:00	152d																																																					
	PL-FOU-1010	Underground Rough-In Liquid Fuel Pump Encloser	3d	07-May-26 07:00	11-May-26 11:00	142d																																																					
	PL-FOU-1020	Mud Mat Liquid Fuel Pump Encloser	1d	11-May-26 11:00	12-May-26 09:00	142d																																																					
	PL-FOU-1030	Base Slab Forming and Embeds Liquid Fuel Pump Encloser	5d	12-May-26 09:00	18-May-26 09:00	142d																																																					
PL-FOU-1140	Grounding	4d	18-May-26 09:00	21-May-26 11:00	143d																																																						
PL-FOU-1040	Base Slab Reinforcement Liquid Fuel Pump Encloser	5d	18-May-26 09:00	22-May-26 09:00	142d																																																						
PL-FOU-1050	Pour and Wreck Base Slab Liquid Fuel Pump Encloser	3d	22-May-26 09:00	27-May-26 13:00	142d																																																						
PL-FOU-1060	Backfill Liquid Fuel Pump Encloser	2d	27-May-26 13:00	29-May-26 09:00	142d																																																						
PL-ADWH-1260	Erect Pre-Engineered Structure	35d	29-May-26 09:00	09-Jul-26 09:00	142d																																																						
PL-ADWH-1270	Frame Fuel Oil Unloading Building Walls	15d	09-Jul-26 09:00	27-Jul-26 09:00	142d																																																						
PL-FOU-1070																																																											

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
						2025													2026													2027													2028													2029													2030																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
						J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J	J

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float												
						2025			2026			2027			2028		
						J	J	J	J	J	J	J	J	J	J	J	J
	PLU3-SST3-1060	Pour and Wreck Base Slab SST3	3d	28-Sep-26 08:00	30-Sep-26 12:00	158d											
	PLU3-SST3-1070	Backfill SST3	3d	30-Sep-26 12:00	02-Oct-26 16:00	158d											
00373.5.6.5.23A Air Processing Unit Foundation-3 Civil/Structural																	
	PLU3-FP3-1000	Form, Reinforce and Pour Slab Air Processing Unit Foundation	4d	20-Jul-26 10:00	23-Jul-26 12:00	89d											
00373.5.6.5.24A Compressed Air Receiver Foundation-3 Civil/Structural																	
	PLU3-WMFP3-1000	Form, Reinforce and Pour Slab Compressed Air Receiver	4d	23-Jul-26 12:00	28-Jul-26 14:00	89d											
00373.5.6.5.25A CTG Electrical PDC-3 Civil/Structural																	
	PLU3-EPDC-1130	Excavate Electrical Building	1d	22-Jul-26 14:00	23-Jul-26 12:00	111d											
	PLU3-EPDC-1140	Excavate AUX Transformer Foundations	1d	23-Jul-26 12:00	24-Jul-26 10:00	111d											
	PLU3-EPDC-1060	Underground Rough-In Electrical Building & AUX Transformers	5d	23-Jul-26 12:00	29-Jul-26 12:00	111d											
	PLU3-EPDC-1070	Mud Mat Electrical Building	2d	29-Jul-26 12:00	31-Jul-26 08:00	111d											
	PLU3-EPDC-1080	Base Slab Forming Electrical Building	1d	31-Jul-26 08:00	31-Jul-26 16:00	111d											
	PLU3-EPDC-1090	Base Slab Reinforcement Electrical Building	3d	31-Jul-26 16:00	05-Aug-26 10:00	111d											
	PLU3-EPDC-1120	Grounding	2d	05-Aug-26 10:00	06-Aug-26 16:00	111d											
	PLU3-EPDC-1150	AUX Transformer Slab Reinforcement	3d	05-Aug-26 10:00	07-Aug-26 14:00	114d											
	PLU3-EPDC-1100	Pour and Wreck Base Slab Electrical Building	3d	06-Aug-26 16:00	11-Aug-26 10:00	111d											
	PLU3-EPDC-1160	Pour & Wreck AUX Transformer Foundations	2d	11-Aug-26 10:00	12-Aug-26 16:00	112d											
	PLU3-EPDC-1110	Backfill Electrical Building	3d	11-Aug-26 10:00	13-Aug-26 14:00	111d											
00373.5.6.5.29A Gas Fuel Filtering Skid-3 Civil/Structural																	
	PLU3-FGC3-1060	Excavate Gas Fuel Filtering Skid	1d	13-Aug-26 14:00	14-Aug-26 12:00	111d											
	PLU3-FGC3-1010	Underground Rough-In Gas Fuel Filtering Skid	5d	14-Aug-26 12:00	20-Aug-26 12:00	111d											
	PLU3-FGC3-1020	Mud Mat Gas Fuel Filtering Skid	2d	20-Aug-26 12:00	24-Aug-26 08:00	145d											
	PLU3-FGC3-1030	Base Slab Forming and Embeds Gas Fuel Filtering Skid	10d	24-Aug-26 08:00	04-Sep-26 08:00	145d											
	PLU3-FGC3-1040	Base Slab Reinforcement Gas Fuel Filtering Skid	10d	04-Sep-26 08:00	16-Sep-26 08:00	145d											
	PLU3-FGC3-1050	Pour and Wreck Base Slab Gas Fuel Filtering Skid	3d	16-Sep-26 08:00	18-Sep-26 12:00	145d											
00373.5.6.5.33A AC Reactor-3 Civil/Structural																	
	PLU3-VTC3-1010	Excavate AC Reactor	1d	24-Aug-26 16:00	25-Aug-26 14:00	111d											
	PLU3-VTC3-1020	Underground Rough-In AC Reactor	3d	25-Aug-26 14:00	28-Aug-26 08:00	111d											
	PLU3-VTC3-1030	Mud Mat AC Reactor	1d	28-Aug-26 08:00	28-Aug-26 16:00	111d											
	PLU3-VTC3-1040	Base Slab Forming and Embeds AC Reactor	5d	28-Aug-26 16:00	04-Sep-26 16:00	111d											
	PLU3-VTC3-1050	Base Slab Reinforcement AC Reactor	5d	04-Sep-26 16:00	10-Sep-26 16:00	111d											
	PLU3-VTC3-1060	Pour and Wreck Base Slab AC Reactor	3d	10-Sep-26 16:00	15-Sep-26 10:00	111d											
	PLU3-VTC3-1070	Backfill AC Reactor	2d	15-Sep-26 10:00	16-Sep-26 16:00	111d											
00373.5.6.5.34A DC Link Reactor-3 Civil/Structural																	
	PLU3-GTET3-1010	Excavate DC Link Reactor	1d	16-Sep-26 16:00	17-Sep-26 14:00	111d											
	PLU3-GTET3-1020	Underground Rough-In DC Link Reactor	3d	17-Sep-26 14:00	22-Sep-26 08:00	156d											
	PLU3-GTET3-1030	Mud Mat DC Link Reactor	1d	22-Sep-26 08:00	22-Sep-26 16:00	156d											
	PLU3-GTET3-1040	Base Slab Forming and Embeds DC Link Reactor	5d	22-Sep-26 16:00	28-Sep-26 16:00	156d											
	PLU3-GTET3-1050	Base Slab Reinforcement DC Link Reactor	5d	28-Sep-26 16:00	02-Oct-26 16:00	156d											
	PLU3-GTET3-1060	Pour and Wreck Base Slab DC Link Reactor	3d	02-Oct-26 16:00	07-Oct-26 10:00	156d											
	PLU3-GTET3-1070	Backfill DC Link Reactor	2d	07-Oct-26 10:00	08-Oct-26 16:00	156d											
00373.5.6.5.36A CT Isolation-3 Civil/Structural																	
	PLU3-IT3-1010	Excavate CT Isolation	1d	17-Sep-26 14:00	18-Sep-26 12:00	111d											
	PLU3-IT3-1020	Underground Rough-In CT Isolation	3d	18-Sep-26 12:00	22-Sep-26 16:00	111d											
	PLU3-IT3-1030	Mud Mat CT Isolation	1d	22-Sep-26 16:00	23-Sep-26 14:00	111d											
	PLU3-IT3-1040	Base Slab Forming and Embeds CT Isolation	5d	23-Sep-26 14:00	29-Sep-26 14:00	111d											
	PLU3-IT3-1050	Base Slab Reinforcement CT Isolation	5d	29-Sep-26 14:00	05-Oct-26 14:00	111d											
	PLU3-IT3-1060	Pour and Wreck Base Slab CT Isolation	3d	05-Oct-26 14:00	08-Oct-26 08:00	111d											
	PLU3-IT3-1070	Backfill CT Isolation	2d	08-Oct-26 08:00	09-Oct-26 14:00	111d											
00373.5.6.5.35A LEC & PEC-3 Civil/Structural																	
	PLU3-LEC3-1010	Excavate LEC & PEC	1d	18-Sep-26 12:00	21-Sep-26 10:00	168d											
Legend: Remaining Level of Effort (Green), Actual Work (Blue), Actual Level of Effort (Dark Blue), Primary Baseline (Yellow), Critical Remaining Work (Red), Milestone (Diamond)																	

[illegible]

[illegible]

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float												
						2025				2026				2027			
						J	J	J	J	J	J	J	J	J	J	J	J
	PLU3-CT3-2350	Equipment Rough-in	15d	03-Feb-27 12:00	22-Feb-27 12:00	46d											
	PLU3-CT3-2390	Equipment Disconnects	5d	22-Feb-27 12:00	26-Feb-27 12:00	46d											
	PLU3-CT3-2370	Equipment Wire Pulls	5d	26-Feb-27 12:00	04-Mar-27 12:00	46d											
	PLU3-CT3-2410	Equipment /Motor Terminations	5d	04-Mar-27 12:00	10-Mar-27 12:00	46d											
00373.5.6.5.98A.10 Fire Alarm & Fiber Pulls																	
	PLU3-CT3-2400	Fire Alarm Cabling	2d	25-Feb-27 11:00	26-Feb-27 17:00	47d											
	PLU3-CT3-2420	Fiber Cable Pulls	3d	01-Mar-27 07:00	03-Mar-27 11:00	47d											
	PLU3-CT3-2440	Fiber Terminations	5d	03-Mar-27 11:00	09-Mar-27 11:00	47d											
00373.5.6.5.98A.11 Instrumentation Install																	
	PLU3-CT3-2430	Instrumentation Rough-In	35d	25-Sep-26 13:00	04-Nov-26 13:00	92d											
	PLU3-CT3-2450	Instrumentaltion Cable Pulls	20d	04-Nov-26 13:00	26-Nov-26 13:00	92d											
	PLU3-CT3-2460	Inst Device Installation & Field Terminations	30d	26-Nov-26 13:00	05-Jan-27 13:00	92d											
	PLU3-CT3-2480	HeadEnd Terminations	10d	05-Jan-27 13:00	15-Jan-27 13:00	92d											
00373.5.6.5.98A.12 CTG Area Lighting																	
	PLU3-CT3-2470	Site Lighting Rough-in	15d	23-Feb-27 07:00	10-Mar-27 17:00	36d											
	PLU3-CT3-2500	Site Ltg Fixture Installation	6d	11-Mar-27 07:00	17-Mar-27 15:00	36d											
	PLU3-CT3-2490	Site Ltg Branch Wire	3d	17-Mar-27 15:00	22-Mar-27 09:00	36d											
00373.5.6.5.00373.5.6.5.99A Startup																	
	PLU3-CT3-2560	Startup Prior to First Fire	80d	29-Apr-27 15:00	19-Aug-27 15:00	0d											
00373.5.6.6 Unit 4																	
00373.5.6.6.01 Pile Driving Throughout CTG Area																	
	PLU4-CT4-1000	Drive Pile (72) CT4	0d	27-Oct-25 07:00 A	14-Nov-25 07:00 A												
	PLU4-ES4-1000	Drive Pile (20) Exhaust Stack	0d	19-Nov-25 07:00 A	20-Nov-25 11:00 A												
	PLU4-VTC4-1000	Drive Pile (6) AC Reactor	0d	08-Dec-25 12:00 A	09-Dec-25 10:00 A												
	PLU4-SST4-1000	Drive Pile (6) SST4	0d	08-Dec-25 14:00 A	09-Dec-25 12:00 A												
	PLU4-LEC4-1000	Drive Pile (6) LEC & PEC 4	0d	10-Dec-25 10:00 A	11-Dec-25 08:00 A												
	PLU4-IT4-1000	Drive Pile (6) IT4	0d	11-Dec-25 08:00 A	11-Dec-25 16:00 A												
	PLU4-LOCM4-1000	Drive Pile (8) LOCM4	0d	15-Dec-25 16:00 A	16-Dec-25 14:00 A												
	PLU4-CEMS4-1000	Drive Pile (5) CEMS4	0d	18-Dec-25 08:00 A	18-Dec-25 16:00 A												
	PLU4-GTSU4-1000	Drive Pile (6) GTSU4	0d	18-Dec-25 16:00 A	19-Dec-25 14:00 A												
	PLU4-GSUTW4-1000	Drive Pile (8) GSUTW4	0d	19-Dec-25 14:00 A	22-Dec-25 12:00 A												
	PLU4-EPDC4-1000	Drive Pile (20) Closed Cooling Water Skid (PECC)	0d	22-Dec-25 12:00 A	29-Dec-25 16:00 A												
	PLU4-CTGEPDC4-1000	Drive Pile (32) Electrical Building	4d	05-Feb-26 10:00	10-Feb-26 12:00	167d											
00373.5.6.6.54A Water Wash / False Start Drains Tank-4 Civil/Structural																	
	PLU4-WWDT-1000	Excavate WWDT (13.5 ft deep)	2d	23-Mar-26 08:00	24-Mar-26 14:00	36d											
00373.5.6.6.01A CTG-4 CM/Structural																	
	PLU4-CT4-1005	Underground Rough-In Under CTG4 (All Electrical)	7d	16-Feb-26 07:00	24-Feb-26 13:00	63d											
	PLU4-CT4-1010	Mud Mat CT4	4d	26-Mar-26 10:00	31-Mar-26 12:00	36d											
	PLU4-CT4-1015	Base Slab Forming and Embeds CT4	25d	31-Mar-26 12:00	28-Apr-26 12:00	57d											
	PLU4-CT4-1020	Base Slab Reinforcement & Mechanical Rough-In CT4	25d	28-Apr-26 12:00	27-May-26 12:00	57d											
	PLU4-CT4-1290	Grounding	5d	27-May-26 12:00	02-Jun-26 12:00	57d											
	PLU4-CT4-2600	Underground Rough-In Around CTG4 (All MEPS)	60d	27-May-26 12:00	04-Aug-26 12:00	112d											
	PLU4-CT4-1025	Pour and Wreck Base Slab CT4	5d	02-Jun-26 12:00	08-Jun-26 12:00	57d											
	PLU4-CT4-1030	Pedestal Forming and Embeds CT4	20d	08-Jun-26 12:00	30-Jun-26 12:00	57d											
	PLU4-CT4-1035	Pedestal Reinforcement CT4	20d	30-Jun-26 12:00	23-Jul-26 12:00	57d											
	PLU4-CT4-1040	Pour and Wreck Pedestals CT4	4d	23-Jul-26 12:00	28-Jul-26 14:00	57d											
	PLU4-CT4-2590	Install Above Ground Foundation (Embeds) CT4	15d	30-Jul-26 08:00	17-Aug-26 08:00	40d											
00373.5.6.6.02A Exhaust Stack-4 Civil/Structural																	
	PLU4-ES4-1010	Underground Rough-In Exhaust Stack	2d	31-Mar-26 12:00	02-Apr-26 08:00	36d											
	PLU4-ES4-1020	Mud Mat Exhaust Stack	2d	02-Apr-26 08:00	03-Apr-26 14:00	36d											
	PLU4-ES4-1030	Base Slab Forming and Embeds Exhaust Stack	10d	03-Apr-26 14:00	15-Apr-26 14:00	36d											
Legend																	
Remaining Level of Effort Actual Work Milestone Milestone																	
Actual Level of Effort Remaining Work																	
Primary Baseline Critical Remaining Work																	

[illegible]

[illegible]

[illegible]

[illegible]

[illegible]

Activity ID		Activity Name	Remaining Duration	Start	Finish	Total Float																																																																														
							2025													2026													2027													2028													2029													2030												
	PLU4-CT4-1510	Erect Inlet Bleed Heat Piping and Supports	10d	13-Nov-26 12:00	23-Nov-26 12:00	187d																																																																														
	PLU4-CT4-1620	Erect Generator Lube Oil / Cooling Water / Vents Piping and Supports	21d	17-Nov-26 10:00	07-Dec-26 08:00	17d																																																																														
	PLU4-CT4-1540	Erect Cooling / Sealing / Atomizing Air Piping and Supports	36d	17-Nov-26 10:00	21-Dec-26 08:00	2d																																																																														
	PLU4-CT4-1070	Erect Cooling Water/Impingement Cooling Piping	29d	21-Dec-26 08:00	16-Jan-27 10:00	2d																																																																														
	PLU4-CT4-1560	Erect Water wash system Piping and Supports	10d	16-Jan-27 10:00	26-Jan-27 10:00	2d																																																																														
	PLU4-CT4-1520	Erect Plenum Drains Piping and Supports	5d	26-Jan-27 10:00	30-Jan-27 10:00	2d																																																																														
	PLU4-CT4-1550	Erect CO2 / H2 Manifolds	3d	30-Jan-27 10:00	02-Feb-27 14:00	2d																																																																														
	PLU4-CT4-1570	Erect Lube Oil Piping and Supports	26d	02-Feb-27 14:00	26-Feb-27 12:00	2d																																																																														
	PLU4-CT4-1590	Erect Hydraulic Piping / Tubing and Supports	40d	26-Feb-27 12:00	05-Apr-27 12:00	2d																																																																														
	PLU4-CT4-1600	Erect Spray Wash Pping and Supports	28d	05-Apr-27 12:00	30-Apr-27 16:00	2d																																																																														
	PLU4-CT4-1610	Erect Water Mist Pping and Supports	10d	30-Apr-27 16:00	10-May-27 16:00	2d																																																																														
	PLU4-CT4-1630	Erect Performance Monitoring / Pressure Transducer /Misc. tubing	35d	10-May-27 16:00	11-Jun-27 16:00	2d																																																																														
	PLU4-CT4-1660	CT4 GE/OEM Pipe Insulation	18d	18-Aug-27 10:00	03-Sep-27 14:00	0d																																																																														
	00373.5.6.6.98A CTG Electrical Work-4																																																																																			
	00373.5.6.6.98A.1 MV Ductbanks																																																																																			
	PLU4-CT4-2190	DB SECTION WIP4 ROUGH IN	5d	21-Jul-26 07:00	24-Jul-26 17:00	236d																																																																														
	PLU4-CT4-2180	DB SECTION D1-D1 ROUGH IN	10d	21-Jul-26 07:00	30-Jul-26 17:00	231d																																																																														
	PLU4-CT4-2170	ELECTRICAL BLDG DB TO D-D ROUGH IN	10d	23-Jul-26 12:00	04-Aug-26 12:00	228d																																																																														
	PLU4-CT4-2510	DB SECTION Z-Z ROUGH IN	5d	18-Sep-26 12:00	24-Sep-26 12:00	183d																																																																														
00373.5.6.6.98A.3 CTG Electrical Equipment Install																																																																																				
	PLU4-CT4-2160	Iso-Phase Bus Welding - Mobilize & Setup	5d	07-Oct-26 07:00	12-Oct-26 17:00	76d																																																																														
	PLU4-CT4-2070	ISOLATION XFMR - 3500KVA 4.16 -2.08KV	2d	08-Oct-26 08:00	09-Oct-26 14:00	173d																																																																														
	PLU4-CT4-2060	EXCITATION XFMR - 1800KVA 4.16 - 64KV	4d	08-Oct-26 16:00	14-Oct-26 08:00	170d																																																																														
	PLU4-CT4-2090	PEECC Bldg	15d	09-Oct-26 08:00	27-Oct-26 08:00	35d																																																																														
	PLU4-CT4-2520	AUX Transformers	2d	27-Oct-26 08:00	28-Oct-26 14:00	141d																																																																														
	PLU4-CG4-MBS-1150	CTG4 Set LEC Cubicle	1d	17-Nov-26 16:00	18-Nov-26 14:00	13d																																																																														
	PLU4-CT4-2000	89SS -100 Amp MTR Disconnect Switch	5d	18-Nov-26 14:00	24-Nov-26 14:00	38d																																																																														
	PLU4-CT4-2120	Iso-Phase Bus -Receiving & Handling	20d	24-Nov-26 14:00	17-Dec-26 14:00	38d																																																																														
	PLU4-CT4-2080	LCI'S	2d	30-Nov-26 07:00	01-Dec-26 13:00	143d																																																																														
	PLU4-CT4-2130	Iso-Phase Bus Installation & Welding - A Phase	30d	17-Dec-26 14:00	25-Jan-27 14:00	38d																																																																														
	PLU4-CT4-2050	SST XFMR Installation	5d	31-Dec-26 16:00	07-Jan-27 16:00	105d																																																																														
	PL-PGE-1200	Install MV Switchgear	25d	07-Jan-27 07:00	03-Feb-27 17:00	70d																																																																														
	PL-PGE-1230	Install LV Switchgear	25d	07-Jan-27 07:00	03-Feb-27 17:00	28d																																																																														
	PLU4-CT4-2030	GSU Step Up XFMR	4d	07-Jan-27 16:00	13-Jan-27 08:00	102d																																																																														
	PLU4-CT4-1990	Electrical Equipment Anchoring	5d	13-Jan-27 08:00	19-Jan-27 08:00	104d																																																																														
	PLU4-CT4-2140	Iso-Phase Bus Installation & Welding - B Phase	30d	25-Jan-27 14:00	01-Mar-27 14:00	38d																																																																														
	PLU4-CT4-2100	DC LINK REACTOR 560A	3d	26-Jan-27 13:00	28-Jan-27 17:00	91d																																																																														
	PLU4-CT4-2110	AC REACTOR	3d	29-Jan-27 07:00	02-Feb-27 11:00	91d																																																																														
	PLU4-CT4-2040	138Kva 3000Amp GSU Breaker	7d	12-Feb-27 08:00	22-Feb-27 14:00	74d																																																																														
	PLU4-CT4-2020	SST Breaker	8d	12-Feb-27 08:00	23-Feb-27 12:00	73d																																																																														
	PLU4-CT4-2150	Iso-Phase Bus Installation & Welding - C-Phase	30d	01-Mar-27 14:00	02-Apr-27 14:00	38d																																																																														
	PLU4-CT4-2210	Heat Trace Panel + Devices Install	20d	11-Jun-27 16:00	06-Jul-27 16:00	0d																																																																														
	PLU4-CT4-2530	Heat Trace Cable Install	20d	06-Jul-27 16:00	28-Jul-27 16:00	0d																																																																														
	PLU4-CT4-2540	Heat																																																																																		

[illegible]
