Big Hollow Simple Cycle Schedule

Printed on 10/14/26
Data Date 10/9/26

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
BH CNN-KPJV-MAST-LIVE BIG HOLLOW CNN KPJV MASTER - LIVE					
BH CNN-KPJV-MAST-LIVE,01 MILESTONES					
BH CNN-KPJV-MAST-LIVE,01,10 MS - Contractual					
KP.MC.07	MM 07 - Gas Turbine & Generator Foundation Complete [FO 09	0		4/7/27 5:00 PM*	103
KP.MC.10	MM 10 - Gas Turbine & Generator Foundation Complete [FO 12	0		4/15/27 5:00 PM*	160
KP.MC.09	MM 09 - Gas Turbine & Generator Foundation Complete [FO 11	0		5/14/27 5:00 PM*	118
KP.MC.08	MM 08 - Gas Turbine & Generator Foundation Complete [FO 10	0		7/6/27 5:00 PM*	62
KP.MC.22	MM 22 - Ready for First Fire [SO 05/31/2028] LD Milestone - Tra	0	5/31/28 7:00 AM*		0
KP.MC.23	MM 23 - Ready for First Fire [SO 06/23/2028] LD Milestone - Tra	0	6/23/28 7:00 AM*		0
KP.MC.24	MM 24 - Ready for First Fire [SO 07/11/2028] LD Milestone - Tra	0	7/10/28 7:00 AM*		1
KP.MC.35	MM 25 - Ready for First Fire [SO 08/01/2028] LD Milestone - Tra	0	7/31/28 7:00 AM*		1
BH CNN-KPJV-MAST-LIVE,01,20 MS - Major Milestones					
KP.MC.00	MM 00 - LNTP [SO 01/30/2026] Milestone	0	1/30/26 7:00 AM A		
KP.MC.01	MM 01 - FNTP [SO 03/16/2026] Milestone	0	3/16/26 7:00 AM A		
KP.MC.02	MM 02 - Site Mobilization [SO 05/04/2026] Milestone	0	5/4/26 7:00 AM A		
KP.MC.06	MM 06 - Train 4 SCR & Stack Foundation Complete [FO 02/01/2	0		12/3/26 5:00 PM*	64
KP.MC.03	MM 03 - Train 1 SCR & Stack Foundation Complete [FO 11/02/2	0		4/21/27 5:00 PM*	7
KP.MC.05	MM 05 - Train 3 SCR & Stack Foundation Complete [FO 01/04/2	0		5/28/27 5:00 PM*	2
KP.MC.16	MM 16 - PDC Piers/Foundation Complete Milestone	0		6/7/27 5:00 PM	371
KP.MC.19	MM 19 - PDC Installation Complete Milestone	0		6/11/27 5:00 PM	274
KP.MC.04	MM 04 - Train 2 SCR & Stack Foundation Complete [FO 12/01/2	0		7/20/27 5:00 PM*	19
KP.MC.11	MM 11 - All Other Foundations Complete [FO 01/04/2028] Miles	0		8/5/27 5:00 PM*	104
KP.MC.12	MM 12 - Civil Work Complete Milestone	0		8/5/27 5:00 PM	329
KP.MC.14	MM 14 - Administrative Building Complete [FO 12/01/2027 Miles	0		9/8/27 5:00 PM*	59
KP.MC.15	MM 15 - Gas Compressor Building Complete [FO 07/01/2027] M	0		10/15/27 5:00 PM*	0
KP.MC.13	MM 13 - U/G Pipe & Conduit Complete Milestone	0		11/2/27 5:00 PM	267
KP.MC.18	MM 18 - Gas Compressors Complete Milestone	0		12/6/27 5:00 PM	189
KP.MC.20	MM 20 - Backfeed Available [SO 01/31/2028] Milestone	0	1/31/28 7:00 AM*		207
KP.MC.17	MM 17 - Gas Turbine Auxiliaries Complete Milestone	0		5/31/28 7:00 AM	132
KP.MC.28	MM 28 - Substantial Completion [FO 07/01/2028] Milestone - Tr	0		5/31/28 7:00 AM*	23
KP.MC.29	MM 29 - Substantial Completion [FO 07/15/2028] Milestone - Tr	0		6/23/28 7:00 AM*	15
KP.MC.30	MM 30 - Substantial Completion [FO 08/01/2028] Milestone - Tr	0		7/10/28 7:00 AM*	17
KP.MC.21	MM 21 - Plant Manuals/Operating Procedures Complete Milesto	0		7/31/28 7:00 AM	18
KP.MC.26	MM 26 - Training Completed by OFE Manufacture [FO 08/22/2(	0		7/31/28 7:00 AM*	17
KP.MC.31	MM 31 - Substantial Completion [FO 08/15/2028] Milestone - Tr	0		7/31/28 7:00 AM*	12
KP.MC.27	MM 27 - Commissioning Complete (In-Service) - Milestone	0		8/8/28 5:00 PM	5
KP.MC.32	MM 32 - Final Completion [FO 04/11/2029] Milestone	0		11/30/28 5:00 PM*	3
BH CNN-KPJV-MAST-LIVE,01,01 MS - Project Milestones					
KPA.CTG4.MSDF	MS - Drive Pile - Complete - Train 4	0		1/6/27 5:00 PM	20
KPA.CTG3.MSDF	MS - Drive Pile - Complete - Train 3	0		3/5/27 5:00 PM	2
KP.MC.27.BP.0	MM 20.BP.0 - Backfeed Complete	0	7/1/27 7:00 AM*		354
BH CNN-KPJV-MAST-LIVE,01,01,02 MS - JV Provided Final Design Data					
JV8000	Received - Final Vendor Drawings - PEMB - Fuel Gas Compress	0		10/23/26 5:00 PM*	2
JV5000	Received - Final Vendor Drawings - Field Erected Tanks	0		10/23/26 5:00 PM*	542
JV5025	Received - Final Vendor Drawings - Fuel Oil Truck Unloading Pu	0		11/16/26 5:00 PM*	66
JV5040	Received - Final Vendor Drawings - Air Compressors. Receivers,	0		11/16/26 5:00 PM*	66
JV5010	Received - Final Vendor Drawings - Piping Specialities	0		11/18/26 5:00 PM*	525


24
2025
2026
2027
2028
2029
30
J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
JV5030	Received - Final Vendor Drawings - Service Water Pumps	0		11/18/26 5:00 PM*	327
JV5045	Received - Final Vendor Drawings - Oily Water Separator	0		11/18/26 5:00 PM*	525
JV5050	Received - Final Vendor Drawings - Sump Pumps	0		11/18/26 5:00 PM*	206
JV5055	Received - Final Vendor Drawings - Shop Fabricated Tanks	0		11/18/26 5:00 PM*	525
JV5060	Received - Final Vendor Drawings - Valves	0		11/18/26 5:00 PM*	525
JV7000	Received - Final Vendor Drawings - Electrical PDPs	0		11/18/26 5:00 PM*	525
JV7010	Received - Final Vendor Drawings - Non-Segregated Bus Duct	0		11/18/26 5:00 PM*	525
JV7020	Received - Final Vendor Drawings - Isophase Bus Duct	0		11/18/26 5:00 PM*	525
JV7030	Received - Final Vendor Drawings - Relay Protection Control Cat	0		11/18/26 5:00 PM*	525
JV8010	Received - Final Vendor Drawings - PEMB - Admin/Warehouse	0		11/18/26 5:00 PM*	525
JV8020	Received - Final Vendor Drawings - PEMB - Liquid Fuel Pump E	0		11/18/26 5:00 PM*	525
JV8030	Received - Final Vendor Drawings - PEMB - A295 Liquid Fuel Er	0		11/18/26 5:00 PM*	525
JV8075	Received - Final Vendor Drawings - PEMB - Plant Services Bldg	0		11/18/26 5:00 PM*	145
JV5020	Received - Final Vendor Drawings - Fire Protection Pumps/Enclc	0		3/16/27 5:00 PM*	448
BH CNN-KPJV-MAST-LIVE,01,01,03 MS - Document Submittals					
ANTP	ANTP	0	3/2/26 7:00 AM A		
EM1665X	Issue - Final P&IDs (42) was 6/15/26	0		6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,01,01,04 MS - Ameren Provided Final Design Data					
GE2030	Received - P&ID's - GE Equipment	0		3/6/26 7:00 AM A	
GE2020	Received - Final Vendor Drawings & Model - GE Equipment - Fu	0		3/6/26 5:00 PM A	
GE2000	Received - Final Vendor Drawings & Model - GE Equipment - CT	0		3/13/26 5:00 PM A	
GE2005	Received - Final Vendor Drawings & Model - GE Equipment - Cl	0		3/13/26 5:00 PM A	
GE2015	Received - Final Vendor Drawings & Model - GE Equipment - Fu	0		3/13/26 5:00 PM A	
GE2035	Received - Terminal Point Lists - GE Equipment (MLI 40363)	0		3/13/26 5:00 PM A	
GE2010	Received - Final Vendor Drawings & Model - GE Equipment - Lu	0		3/20/26 5:00 PM A	
GE1030	Software - Acceptance Test (SWAT) Start	11	1/6/27 7:00 AM	1/21/27 5:00 PM	480
GE1040	Software - Acceptance Test (SWAT) Complete	0		1/21/27 5:00 PM	480
GE1050	Software - Ship to Site	5	1/22/27 7:00 AM	1/28/27 5:00 PM	480
GE1000	Software - Freeze 100% - BOP - DCS Software	0		4/9/27 5:00 PM	431
BH CNN-KPJV-MAST-LIVE,01,01,05 MS - Nooter Erikson Deliverables					
NOOTER3000	Provide Exhaust Duct Foundation	0		1/15/26 5:00 PM A	
NOOTER53100	Provide Stack Foundation	0		1/15/26 5:00 PM A	
NOOTER53110	Provide SCR Blowers Foundation	0		1/15/26 5:00 PM A	
NOOTER5000	SCR Initial Vendor Drawings & Model Received	0		5/5/26 5:00 PM A	
NOOTER5100	Develop & Issue Tie-in Point List	0	5/8/26 7:00 AM A	8/4/26 5:00 PM A	
NOOTER5200	Develop & Issue Equipment Data Sheets	0	5/4/26 7:00 AM A	8/4/26 5:00 PM A	
NOOTER5099	Received - Final Vendor Drawings & Model - SCR	0		10/5/26 7:00 AM A	
BH CNN-KPJV-MAST-LIVE,01,01,06 MS - Engineering Milestones					
AEC1000	Start Engineering Milestone	0	2/6/26 7:00 AM A		
AEC-M1000	LNTP (Limited Notice from KPII)	0	2/27/26 7:00 AM A		
AEC-M2000	Final BOP P&IDs Issued for Design	0		6/3/26 5:00 PM A	
AEC-M4500	Issue - Spec. - Major Equipment	0		10/26/26 5:00 PM	541
AEC-M5500	All Foundations Design IFC	0		3/15/27 5:00 PM	33
AEC-M9999	Engineering - Completed	0		11/1/27 5:00 PM	289
BH CNN-KPJV-MAST-LIVE,03 ENGINEERING					
BH CNN-KPJV-MAST-LIVE,03,20 ENG - General					
AEC0530	Prepare - 30% Design Review Agenda	0	7/27/26 7:00 AM A	8/18/26 5:00 PM A	
AEC0535	Review - Meeting - 30% Design	0		8/19/26 5:00 PM A	
AEC0560	Prepare - 60% Design Review Agenda	6	2/12/27 7:00 AM	2/22/27 5:00 PM*	6
AEC0565	Review - Meeting - 60% Design	0		2/22/27 5:00 PM	6



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC0590	Prepare - 90% Design Review Agenda	5	4/30/27 7:00 AM	5/6/27 5:00 PM*	6
AEC0595	Review - Meeting - 90% Design	0		5/6/27 5:00 PM	412
BH CNN-KPJV-MAST-LIVE,03,20,01 ENG - General - Design Criteria					
BH CNN-KPJV-MAST-LIVE,03,20,01,01 ENG - General - Design Criteria - C/S/A Design Criteria					
AEC13GEN-05	Prep & Check & IDR - C/S/A Design Criteria	0	2/17/26 7:00 AM A	2/18/26 5:00 PM A	
AEC13GEN-10	IDR - C/S/A Design Criteria	0	2/17/26 7:00 AM A	2/18/26 5:00 PM A	
AEC13GEN-15	Address IDR - Comments & Issue for Client Review - C/S/A Desi	0	2/17/26 7:00 AM A	2/18/26 5:00 PM A	
AEC13GEN-20	Client Review - C/S/A. Design Criteria	0	3/11/26 7:00 AM A	3/30/26 5:00 PM A	
AEC13GEN-25	Address Client Comments & Issue Final - C/S/A Design Criteria	0	3/31/26 7:00 AM A	4/15/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,20,01,02 ENG - General - Design Criteria - Mechanical Design Criteria					
AEC15GEN-05	Prep & Check & IDR - Mech. Design Criteria	0	3/9/26 7:00 AM A	3/13/26 5:00 PM A	
AEC15GEN-10	IDR - Mech. Design Criteria	0	3/16/26 7:00 AM A	4/6/26 5:00 PM A	
AEC15GEN-15	Address IDR - Comments & Issue for Client Review - Mech. Des	0	4/6/26 7:00 AM A	4/17/26 5:00 PM A	
AEC15GEN-20	Client Review - Mech. Design Criteria	0	4/20/26 7:00 AM A	6/8/26 5:00 PM A	
AEC15GEN-25	Address Client Comments & Issue Final - Mech. Design Criteria	0	6/8/26 7:00 AM A	8/27/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,20,01,03 ENG - General - Design Criteria - Electrical Design Criteria					
AEC17GEN-05	Prep & Check & IDR - Electrical. Design Criteria	0	3/9/26 7:00 AM A	3/27/26 5:00 PM A	
AEC17GEN-10	IDR - Electrical. Design Criteria	0	3/30/26 7:00 AM A	4/13/26 5:00 PM A	
AEC17GEN-15	Address IDR - Comments & Issue for Client Review - Electrical D	0	4/14/26 7:00 AM A	4/22/26 5:00 PM A	
AEC17GEN-20	Client Review - Electrical Design Criteria	0	4/22/26 7:00 AM A	5/18/26 5:00 PM A	
AEC17GEN-25	Address Client Comments & Issue Final - Electrical. Design Crite	0	5/19/26 7:00 AM A	6/12/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,04 ENG - Site Preparation					
BH CNN-KPJV-MAST-LIVE,03,04,01 ENG - Site Preparation - Civil					
BH CNN-KPJV-MAST-LIVE,03,04,01,08 ENG - Site Preparation - Civil - Site Permitting					
AEC121100-05	Prepare & Issue Jefferson County Site Development Plan & Flo	0	3/2/26 7:00 AM A	4/3/26 5:00 PM A	
AEC121100-12	Jefferson County Review of Site Development Plan	0	4/6/26 7:00 AM A	4/10/26 5:00 PM A	
AEC121100-10	Prepare - Jefferson County Land Disturbance & Stormwater Dra	0	4/6/26 7:00 AM A	4/20/26 5:00 PM A	
AEC121100-12	Client Review - Site Development Plan	0	4/7/26 7:00 AM A	4/21/26 5:00 PM A	
AEC121100-15	Jefferson County Review of Flood Plain Development Permit	0	4/6/26 7:00 AM A	5/4/26 5:00 PM A	
AEC121100-25	Jefferson County Review of Land Disturbance & Stormwater/Dra	0	4/17/26 7:00 AM A	6/19/26 5:00 PM A	
AEC121100-85	Building Permit - Admin Building (Full Permit Incl. Sanitary/Septi	40	11/25/26 7:00 AM	1/27/27 5:00 PM	98
BH CNN-KPJV-MAST-LIVE,03,04,01,01 ENG - Site Preparation - Civil - SWPPP Drawings					
AEC121101-05	Prep & Check & IDR & Client Review & Jefferson County Reviev	0	4/6/26 7:00 AM A	4/20/26 5:00 PM A	
AEC121101-20	Client Review - SWPPP Civil Drawings	0	4/21/26 7:00 AM A	5/4/26 5:00 PM A	
AEC121101-10	IDR - SWPPP Civil Drawings	0	4/20/26 7:00 AM A	5/20/26 5:00 PM A	
AEC121101-15	Jefferson County Review of SWPPP Civil Drawings	0	4/20/26 7:00 AM A	6/3/26 5:00 PM A	
AEC121101-25	Address IDR - Client Review & Jefferson County Comments & IF	0	5/20/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,04,01,04 ENG - Site Preparation - Civil - Septic Design Drawings					
AEC121104-05	Prep & Check & IDR - Civil Drawings - Septic Design	0	6/18/26 7:00 AM A	7/10/26 5:00 PM A	
AEC121104-10	IDR - Civil Drawings - Septic Design	0	7/17/26 7:00 AM A	7/27/26 5:00 PM A	
AEC121104-15	Address Comments & Issue for Client Review - Civil Drawings - S	0	7/27/26 7:00 AM A	8/5/26 5:00 PM A	
AEC121104-20	Client Review - Civil Drawings - Septic Design	0	8/6/26 7:00 AM A	8/21/26 5:00 PM A	
AEC121104-25	Address Client Comments & IFC - Civil Drawings - Septic Design	0	9/8/26 7:00 AM A	9/10/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,04,01,02 ENG - Site Preparation - Civil - Rough Grading					
AEC121102-05	Prep & Check & IDR & Client Review - Rough Grading Drawings	0	4/6/26 7:00 AM A	5/4/26 5:00 PM A	
AEC121102-10	IDR - Civil Drawings - Rough Grading	0	5/5/26 7:00 AM A	5/28/26 5:00 PM A	
AEC121102-20	Client Review - Civil Drawings - Rough Grading	0	5/5/26 7:00 AM A	5/28/26 5:00 PM A	
AEC121102-35	Address IDR - Client Review & IFC - Rough Grading Drawings	0	5/29/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,04,01,03 ENG - Site Preparation - Civil - Roadway Plans & Sections & Details					
AEC121103-05	Prep & Check & IDR - Civil Drawings - Road Plans / Sections/De	0	4/27/26 7:00 AM A	5/4/26 5:00 PM A	
AEC121103-10	IDR - Civil Drawings - Road Plan/Sections/Details	0	5/5/26 7:00 AM A	5/12/26 5:00 PM A	




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC121103-15	Address Comments & Issue for Client Review - Civil Drawings - F	0	5/5/26 7:00 AM A	5/12/26 5:00 PM A	
AEC121103-20	Client Review - Civil Drawings - Road Profile/Sections/Details	0	5/12/26 7:00 AM A	5/26/26 5:00 PM A	
AEC121103-25	Address Client Comments & IFC - Civil Drawings - Road Profile/S	0	6/8/26 7:00 AM A	6/12/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,04,01,05 ENG - Site Preparation - Civil - Permanent Storm Drainage and Collection					
AEC121105-05	Prep & Check & IDR & Client Review & Jefferson County Reviev	0	4/6/26 7:00 AM A	4/17/26 5:00 PM A	
AEC121105-20	Client Review - Civil Drawings - Permanent Storm Drainage & Cc	0	4/21/26 7:00 AM A	5/4/26 5:00 PM A	
AEC121105-10	IDR - Permanent Storm Drainage & Collections Drawings	0	4/20/26 7:00 AM A	5/20/26 5:00 PM A	
AEC121105-15	Jefferson County Review - Permanent Storm Drainage & Collect	0	4/21/26 7:00 AM A	5/20/26 5:00 PM A	
AEC121105-25	Address IDR - Client Review & Jefferson County Comments & IF	0	5/21/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,04,01,06 ENG - Site Preparation - Civil - Fuel Oil Tank Berm					
AEC121106-05	Prep & Check & IDR - Civil Drawings - Fuel Oil Tank Berm	0	5/18/26 7:00 AM A	6/19/26 5:00 PM A	
AEC121106-10	IDR - Civil Drawings - Fuel Oil Tank Berm	0	6/22/26 7:00 AM A	6/26/26 5:00 PM A	
AEC121106-15	Address Comments & Issue for Client Review - Civil Drawings - F	0	6/29/26 7:00 AM A	7/14/26 5:00 PM A	
AEC121106-20	Client Review - Civil Drawings - Fuel Oil Tank Berm	0	7/15/26 7:00 AM A	8/7/26 5:00 PM A	
AEC121106-25	Address Client Comments & IFC - Civil Drawings - Fuel Oil Tank	0	8/10/26 7:00 AM A	8/11/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,04,01,11 ENG - Site Preparation - Civil - Transformer SPCCC					
AEC121110-05	Prep & Check & IDR - Civil Drawings - Transformer SPCCC	0	6/5/26 7:00 AM A	6/25/26 5:00 PM A	
AEC121110-10	IDR Civil Drawings - Transformer SPCCC	0	6/30/26 7:00 AM A	7/28/26 5:00 PM A	
AEC121110-15	Address Comments & Issue for CR Civil Drawings - Transformer	0	7/28/26 7:00 AM A	8/5/26 5:00 PM A	
AEC121110-20	Client Review Civil Drawings - Transformer SPCCC	0	8/6/26 7:00 AM A	8/31/26 5:00 PM A	
AEC121110-25	Address Client Comments & Issue IFC Civil Drawings - Transfom	0	9/8/26 7:00 AM A	9/10/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,04,01,10 ENG - Site Preparation - Civil - Gas Metering Yard					
AEC121109-05	Prep & Check & IDR - Civil Drawings - Gas Metering Yard	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
AEC121109-15	IDR & CR ReviewCivil Drawings - Gas Metering Yard	0	6/3/26 7:00 AM A	6/29/26 5:00 PM A	
AEC121109-20	Address IDR & CR Comments & Issue IFC Civil Drawings - Gas I	0	6/30/26 7:00 AM A	7/8/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,04,01,07 ENG - Site Preparation - Civil - Final/Finish Grading					
AEC121107-05	Prep & Check & IDR - Civil Drawings - Final/Finish Grading	0	8/10/26 7:00 AM A	9/11/26 5:00 PM A	
AEC121107-10	IDR - Civil Drawings - Final/Finish Grading	0	9/11/26 7:00 AM A	9/23/26 5:00 PM A	
AEC121107-15	Address Comments & Issue for Client Review - Civil Drawings - F	0	9/23/26 7:00 AM A	10/1/26 5:00 PM A	
AEC121107-20	Client Review - Civil Drawings - Final/Finish Grading	9	10/1/26 7:00 AM A	10/22/26 5:00 PM	328
AEC121107-25	Address Client Comments & IFC - Civil Drawings - Final/Finish G	5	10/23/26 7:00 AM	10/29/26 5:00 PM	328
BH CNN-KPJV-MAST-LIVE,03,04,01,20 ENG - Site Preparation - Civil - Fuel Oil Unloading Containment					
AEC121108-05	Prep & Check & IDR - Civil Drawings - Fuel Oil Unloading Contai	0	8/6/26 7:00 AM A	8/25/26 5:00 PM A	
AEC121108-10	IDR Civil Drawings - Fuel Oil Unloading Containment	0	8/25/26 7:00 AM A	9/8/26 5:00 PM A	
AEC121108-15	Address Comments & Issue for CR Civil Drawings - Fuel Oil Unlc	0	9/8/26 7:00 AM A	9/9/26 5:00 PM A	
AEC121108-20	Client Review Civil Drawings - Fuel Oil Unloading Containment	0	9/9/26 7:00 AM A	9/23/26 5:00 PM A	
AEC121108-25	Address Client Comments & Issue IFC Civil Drawings - Fuel Oil U	0	9/24/26 7:00 AM A	10/2/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,04,01,09 ENG - Site Preparation - Civil - Miscellaneous					
AEC121107-35	Prep & Check & IDR - Civil Drawings - Miscellaneous	2	8/18/26 7:00 AM A	10/13/26 5:00 PM	132
AEC121107-45	IDR - Civil Drawings - Miscellaneous	5	10/14/26 7:00 AM	10/20/26 5:00 PM	132
AEC121107-55	Address Comments & Issue for Client Review - Civil Drawings - M	10	10/21/26 7:00 AM	11/3/26 5:00 PM	132
AEC121107-65	Client Review - Civil Drawings - Miscellaneous	15	11/4/26 7:00 AM	11/25/26 5:00 PM	132
AEC121107-75	Address Client Comments & IFC - Civil Drawings - Miscellaneous	5	11/27/26 7:00 AM	12/3/26 5:00 PM	132
BH CNN-KPJV-MAST-LIVE,03,05 ENG - Structural					
BH CNN-KPJV-MAST-LIVE,03,05,06 ENG - Structural - Specifications					
BH CNN-KPJV-MAST-LIVE,03,05,06,01 ENG - Structural - Specifications - Supply of Concrete Materials Specifications					
AEC130802-05	Prep & Check & IDR - Supply of Concrete Materials Specs.	0	2/23/26 7:00 AM A	3/24/26 5:00 PM A	
AEC130802-20	IDR - Supply of Concrete Materials Specs.	0	3/25/26 7:00 AM A	3/30/26 5:00 PM A	
AEC130802-25	Address Comments & Issue for Client Review - Supply of Concr	0	4/1/26 7:00 AM A	4/7/26 5:00 PM A	
AEC130802-30	Client Review - Supply of Concrete Materials Specs.	0	4/7/26 7:00 AM A	4/21/26 5:00 PM A	
AEC130802-35	Address Client Comments & IFC - Supply of Concrete Materials	0	4/23/26 7:00 AM A	4/29/26 5:00 PM A	

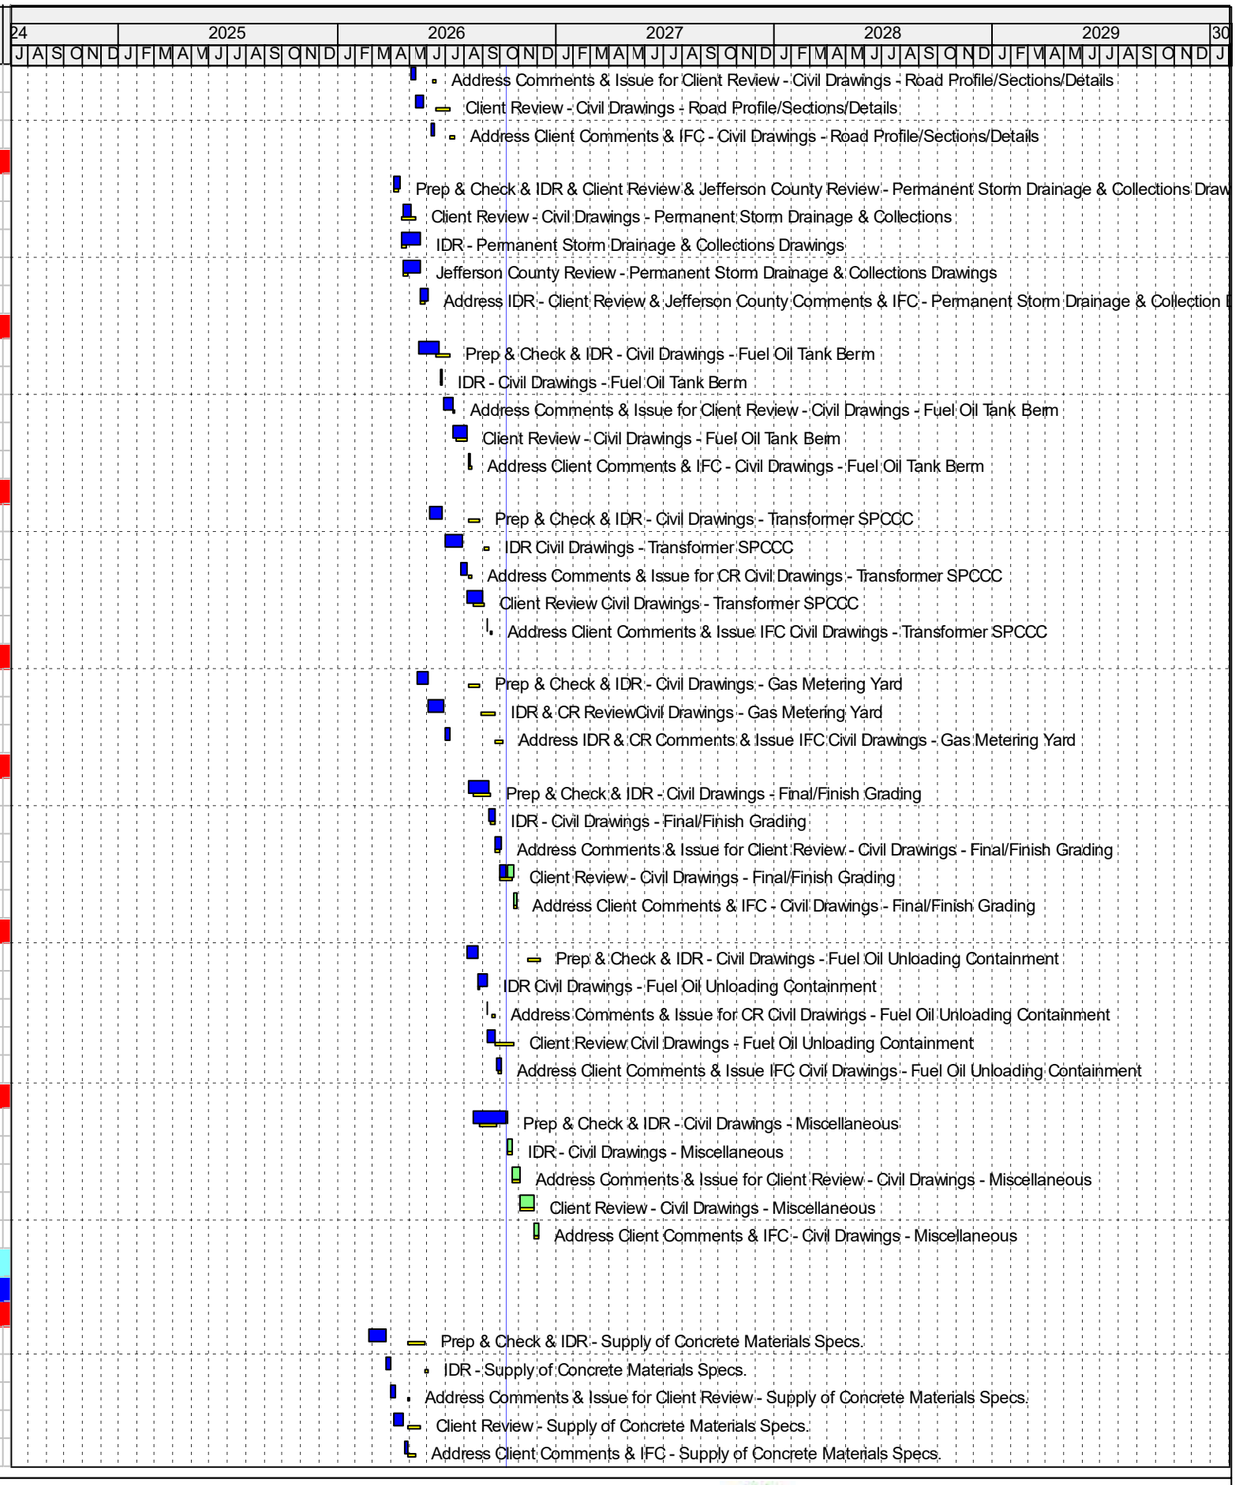


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
BH CNN-KPJV-MAST-LIVE,03,05,06,02 ENG - Structural - Specifications - Structural Steel Supply Specification					
AEC130801-05	Prep & Check & IDR - Structural Steel Supply Spec.	0	2/23/26 7:00 AM A	3/24/26 5:00 PM A	
AEC130801-20	IDR - Structural Steel Supply Spec.	0	3/25/26 7:00 AM A	3/30/26 5:00 PM A	
AEC130801-25	Address Comments & Issue for Client Review - Structural Steel :	0	3/31/26 7:00 AM A	4/7/26 5:00 PM A	
AEC130801-30	Client Review - Structural Steel Supply Spec.	0	4/7/26 7:00 AM A	4/21/26 5:00 PM A	
AEC130801-35	Address Client Comments & IFC - Structural Steel Supply Spec.	0	4/23/26 7:00 AM A	4/30/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,06,03 ENG - Structural - Specifications - Supply & Fabrication of Concrete Reinforcing Steel					
AEC130803-05	Prep & Check & IDR - Supply & Fabrication of Concrete Reinforc	0	2/23/26 7:00 AM A	3/24/26 5:00 PM A	
AEC130803-10	IDR - Supply & Fabrication of Concrete Reinforcing Steel	0	3/25/26 7:00 AM A	3/31/26 5:00 PM A	
AEC130803-15	Address Comments & Issue for Client Review - Supply & Fabric	0	4/1/26 7:00 AM A	4/7/26 5:00 PM A	
AEC130803-20	Client Review - Supply & Fabrication of Concrete Reinforcing Ste	0	4/7/26 7:00 AM A	4/21/26 5:00 PM A	
AEC130803-25	Address Client Comments & IFC - Supply & Fabrication of Conc	0	4/23/26 7:00 AM A	4/28/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,06,04 ENG - Structural - Specifications - Supply & Fabrication of Concrete Embedded Steel					
AEC130804-05	Prep & Check & IDR - Supply & Fabrication of Concrete Embed	0	2/23/26 7:00 AM A	3/24/26 5:00 PM A	
AEC130804-10	IDR - Supply & Fabrication of Concrete Embedded Steel	0	3/25/26 7:00 AM A	3/31/26 5:00 PM A	
AEC130804-15	Address Comments & Issue for Client Review - Supply & Fabric	0	4/1/26 7:00 AM A	4/7/26 5:00 PM A	
AEC130804-20	Client Review - Supply & Fabrication of Concrete Embedded Ste	0	4/7/26 7:00 AM A	4/21/26 5:00 PM A	
AEC130804-25	Address Client Comments & IFC - Supply & Fabrication of Conc	0	4/23/26 7:00 AM A	4/29/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,07 ENG - Structural - Structural Steel Calculations/Drawings					
BH CNN-KPJV-MAST-LIVE,03,05,07,01 ENG - Structural - Structural Steel Calculations/Drawings - Isophase Bus Duct					
AEC131130-00	Model - 3D Modeling - Isophase Structural Steel	0	4/6/26 7:00 AM A	4/29/26 5:00 PM A	
AEC131130-02	Prep & Check & Issue Structural Calc - Isophase Steel	0	5/7/26 7:00 AM A	8/31/26 5:00 PM A	
AEC131130-05	Prep & Check & IDR - Plan / Section Drawings - Isophase Steel	0	7/6/26 7:00 AM A	9/11/26 5:00 PM A	
AEC131130-10	IDR - Structural Drawings - Isophase Steel	5	10/12/26 7:00 AM	10/16/26 5:00 PM	289
AEC131130-15	Address IDR - Comments & Issue for Client Review Steel - Isopl	4	10/19/26 7:00 AM	10/22/26 5:00 PM	289
AEC131130-20	Client Review - Structural Drawings - Isophase Steel	15	10/23/26 7:00 AM	11/13/26 5:00 PM	289
AEC131130-25	Address Client Comments & IFC - Structural Drawings & Calcs -	10	11/16/26 7:00 AM	11/30/26 5:00 PM	289
BH CNN-KPJV-MAST-LIVE,03,05,07,02 ENG - Structural - Structural Steel Calculations/Drawings - Platforms					
AEC131140-02	Prep & Check & Issue Calc - Platforms	20	12/30/26 7:00 AM	1/29/27 5:00 PM	451
AEC131140-05	Prep & Check & IDR - Plan / Section Drawings - Platforms	25	1/8/27 7:00 AM	2/12/27 5:00 PM	451
AEC131140-10	IDR - Structural Drawings - Platforms	5	2/16/27 7:00 AM	2/22/27 5:00 PM	451
AEC131140-15	Address IDR - Comments & Issue for Client Review Steel - Platf	3	2/23/27 7:00 AM	2/25/27 5:00 PM	451
AEC131140-20	Client Review - Structural Drawings - Platforms	5	2/26/27 7:00 AM	3/4/27 5:00 PM	451
AEC131140-25	Address Client Comments & IFC - Structural Drawings & Calcs -	5	3/5/27 7:00 AM	3/11/27 5:00 PM	451
BH CNN-KPJV-MAST-LIVE,03,05,07,04 ENG - Structural - Structural Steel Calculations/Drawings - Pipe Support Steel Calculations					
AEC130531-00	Model - 3D Modeling - Pipe Support Steel Calculations	20	1/4/27 7:00 AM	2/1/27 5:00 PM	423
AEC131131-05	Prep & Check & Issue Structural Calc - Pipe Support Steel Calcu	20	5/13/27 7:00 AM	6/10/27 5:00 PM	328
AEC131131-10	Prep & Check & IDR - Plan / Section Drawings - Pipe Support St	25	6/21/27 7:00 AM	7/26/27 5:00 PM	328
AEC131131-15	IDR - Structural Drawings - Pipe Support Steel Calculations	5	7/27/27 7:00 AM	8/2/27 5:00 PM	328
AEC131131-20	Address IDR - Comments & Issue for Client Review Steel - Pipe	5	8/3/27 7:00 AM	8/9/27 5:00 PM	328
AEC131131-25	Client Review - Structural Drawings - Pipe Support Steel Calcula	15	8/10/27 7:00 AM	8/30/27 5:00 PM	328
AEC131131-30	Address Client Comments & IFC - Structural Drawings & Calcs -	5	8/31/27 7:00 AM	9/7/27 5:00 PM	328
BH CNN-KPJV-MAST-LIVE,03,05,07,03 ENG - Structural - Structural Steel Calculations/Drawings - Misc. Steel/Cable Tray Supports Calcs.					
AEC131132-35	Prep & Check & Issue Structural Calc - Misc. Steel/Cable Tray S	20	11/27/26 7:00 AM	12/28/26 5:00 PM	199
AEC131132-30	Model - 3D Modeling - Misc. Steel/Cable Tray Supports Calcs.	20	1/4/27 7:00 AM	2/1/27 5:00 PM	182
AEC131132-40	Prep & Check & IDR - Plan / Section Drawings - Misc. Steel/Cab	25	2/2/27 7:00 AM	3/9/27 5:00 PM	182
AEC131132-45	IDR - Structural Drawings - Misc. Steel/Cable Tray Supports Calc	5	3/10/27 7:00 AM	3/16/27 5:00 PM	182
AEC131132-50	Address IDR - Comments & Issue for Client Review Steel - Misc	5	3/17/27 7:00 AM	3/23/27 5:00 PM	182
AEC131132-65	Client Review - Structural Drawings - Misc. Steel/Cable Tray Sup	15	3/24/27 7:00 AM	4/14/27 5:00 PM	182
AEC131132-60	Address Client Comments & IFC - Structural Drawings & Calcs -	5	4/15/27 7:00 AM	4/21/27 5:00 PM	182
BH CNN-KPJV-MAST-LIVE,03,05,07,05 ENG - Structural - Structural Steel Calculations/Drawings - Sump Steel & Grating					

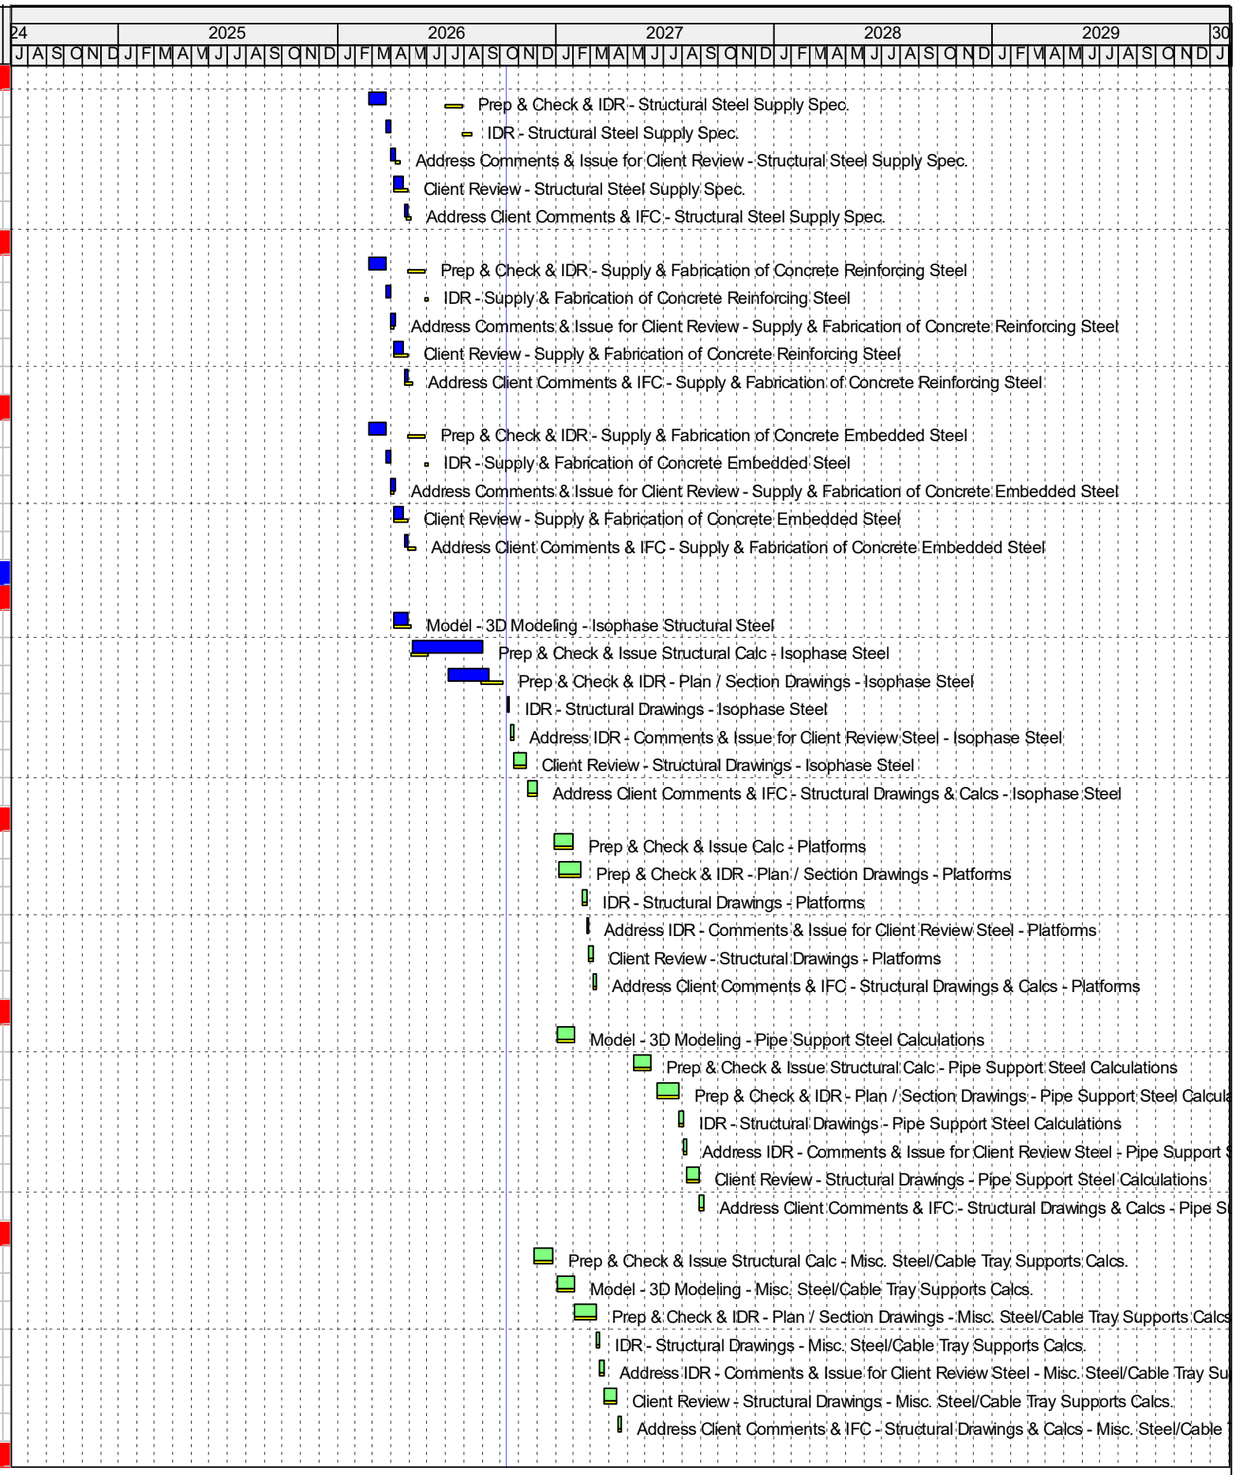


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC130533-00	Model - 3D Modeling - Sump Steel & Grating	0	8/7/26 7:00 AM A	9/8/26 5:00 PM A	
AEC130533-05	Prep & Check & Issue Structural Calc - Sump Steel & Grating	2	9/9/26 7:00 AM A	10/13/26 5:00 PM	288
AEC131133-10	Prep & Check & IDR - Plan / Section Drawings - Sump Steel & (	5	9/21/26 7:00 AM A	10/16/26 5:00 PM	288
AEC131133-15	IDR - Structural Drawings - Sump Steel & Grating	5	10/19/26 7:00 AM	10/23/26 5:00 PM	288
AEC131133-20	Address IDR - Comments & Issue for Client Review Steel - Sum	5	10/26/26 7:00 AM	10/30/26 5:00 PM	288
AEC131133-25	Client Review - Structural Drawings - Sump Steel & Grating	15	11/2/26 7:00 AM	11/23/26 5:00 PM	288
AEC131133-30	Address Client Comments & IFC - Structural Drawings & Calcs -	5	11/24/26 7:00 AM	12/1/26 5:00 PM	288
BH CNN-KPJV-MAST-LIVE,03,05,07,06 ENG - Structural - Structural Steel Calculations/Drawings - GSU & SST Transformer Steel					
AEC130534-00	Model - 3D Modeling - GSU (Generator Step Up) & SST Transfo	0	5/11/26 7:00 AM A	6/8/26 5:00 PM A	
AEC130534-05	Prep & Check & Issue Structural Calc - GSU (Generator Step Up	0	6/9/26 7:00 AM A	9/8/26 5:00 PM A	
AEC131134-05	Prep & Check & IDR - Plan / Section Drawings - GSU (Generato	0	6/30/26 7:00 AM A	9/8/26 5:00 PM A	
AEC131134-10	IDR - Structural Drawings - GSU (Generator Step Up) & SST Tra	1	9/9/26 7:00 AM A	10/12/26 5:00 PM	285
AEC131134-15	Address IDR - Comments & Issue for Client Review Steel - GSU	5	10/13/26 7:00 AM	10/19/26 5:00 PM	285
AEC131134-20	Client Review - Structural Drawings - GSU (Generator Step Up) &	15	10/20/26 7:00 AM	11/9/26 5:00 PM	285
AEC131134-25	Address Client Comments & IFC - Structural Drawings & Calcs -	5	11/10/26 7:00 AM	11/17/26 5:00 PM	285
BH CNN-KPJV-MAST-LIVE,03,05,01 ENG - Structural - Foundation Drawings					
BH CNN-KPJV-MAST-LIVE,03,05,01,01 ENG - Structural - Calcs/Foundation Drawings					
BH CNN-KPJV-MAST-LIVE,03,05,01,01,14 ENG - Structural - Calcs/Foundation Drawings - Fuel Oil Tanks					
AEC130517-0	Prep & Check Structural Calc Foundation - Fuel Oil Tanks	0	4/13/26 7:00 AM A	6/11/26 5:00 PM A	
AEC131117-0	Prep & Check & IDR - Foundation Drawings - Fuel Oil Tanks	0	4/13/26 7:00 AM A	6/11/26 5:00 PM A	
AEC131117-1	IDR - Foundation Drawings - Fuel Oil Tanks	0	6/11/26 7:00 AM A	6/18/26 5:00 PM A	
AEC131117-1	Address IDR - Foundation Drawings & Issue for Client Review - I	0	6/19/26 7:00 AM A	6/23/26 5:00 PM A	
AEC131117-2	Client Review - Foundation Drawings - Fuel Oil Tanks	0	6/24/26 7:00 AM A	7/17/26 5:00 PM A	
AEC131117-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	7/20/26 7:00 AM A	7/30/26 5:00 PM A	
AEC131117-3	Address Client Comments & IFC - Pile Foundation Drawings - Fu	0	7/20/26 7:00 AM A	7/30/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,27 ENG - Structural - Calcs/Foundation Drawings - SCR Foundations					
AEC131100-0	Prep & Check & IDR - Foundation Drawings - SCR Foundation	0	4/13/26 7:00 AM A	6/12/26 5:00 PM A	
AEC130500-0	Prep & Check Structural Calc Foundation - SCR	0	4/13/26 7:00 AM A	6/22/26 5:00 PM A	
AEC131100-1	IDR - Foundation Drawings - SCR Foundation	0	6/15/26 7:00 AM A	6/22/26 5:00 PM A	
AEC131100-1	Address IDR - Foundation Drawings & Issue for Client Review - S	0	6/22/26 7:00 AM A	6/24/26 5:00 PM A	
AEC131100-2	Client Review - Foundation Drawings - SCR	0	6/25/26 7:00 AM A	7/14/26 5:00 PM A	
AEC131100-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	7/15/26 7:00 AM A	9/3/26 5:00 PM A	
AEC131100-3	Address Client Comments & IFC - Pile Foundation Drawings - S	0	8/10/26 7:00 AM A	9/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,28 ENG - Structural - Calcs/Foundation Drawings - Ammonia Unloading & Storage Equipment					
AEC130550-0	Prep & Check Structural Calc Foundation - Ammonia Unloading	25	10/12/26 7:00 AM	11/16/26 5:00 PM	39
AEC131150-0	Prep & Check & IDR - Foundation Drawings - Ammonia Unloadir	25	10/12/26 7:00 AM	11/16/26 5:00 PM	39
AEC131150-1	IDR - Foundation Drawings - Ammonia Unloading & Storage Eq	5	11/17/26 7:00 AM	11/23/26 5:00 PM	39
AEC131150-1	Address IDR - Foundation Drawings & Issue for Client Review - A	3	11/24/26 7:00 AM	11/27/26 5:00 PM	39
AEC131150-2	Client Review - Foundation Drawings - Ammonia Unloading & St	15	11/30/26 7:00 AM	12/18/26 5:00 PM	39
AEC131150-3	Address Client Comments & IFC - Pile Foundation Drawings - Ar	4	12/21/26 7:00 AM	12/28/26 5:00 PM	39
AEC131150-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	12/21/26 7:00 AM	12/29/26 5:00 PM	83
BH CNN-KPJV-MAST-LIVE,03,05,01,01,29 ENG - Structural - Calcs/Foundation Drawings - Unit Auxiliary Transformers					
AEC130555-0	Prep & Check Structural Calc Foundation - Unit Auxiliary Transfo	0	7/6/26 7:00 AM A	9/11/26 5:00 PM A	
AEC131155-0	Prep & Check & IDR - Foundation Drawings - Unit Auxiliary Trans	0	7/2/26 7:00 AM A	10/6/26 5:00 PM A	
AEC131155-1	IDR - Foundation Drawings - Unit Auxiliary Transformers (GA036	11	10/7/26 7:00 AM A	10/26/26 5:00 PM	46
AEC131155-1	Address IDR - Foundation Drawings & Issue for Client Review - U	3	10/27/26 7:00 AM	10/29/26 5:00 PM	46
AEC131155-2	Client Review - Foundation Drawings - Unit Auxiliary Transformer	15	10/30/26 7:00 AM	11/20/26 5:00 PM	46
AEC131155-2	Address Client Comments & IFC - Foundation Drawings & Calcs	4	11/23/26 7:00 AM	11/27/26 5:00 PM	103
AEC131155-3	Address Client Comments & IFC - Pile Layout Drawings & Calc -	4	11/23/26 7:00 AM	11/27/26 5:00 PM	46
BH CNN-KPJV-MAST-LIVE,03,05,01,01,01 ENG - Structural - Calcs/Foundation Drawings - Demineralized Water Tanks					
AEC131101-0	Prep & Check & IDR - Foundation Drawings - Demineralized Wa	0	6/1/26 7:00 AM A	6/19/26 5:00 PM A	

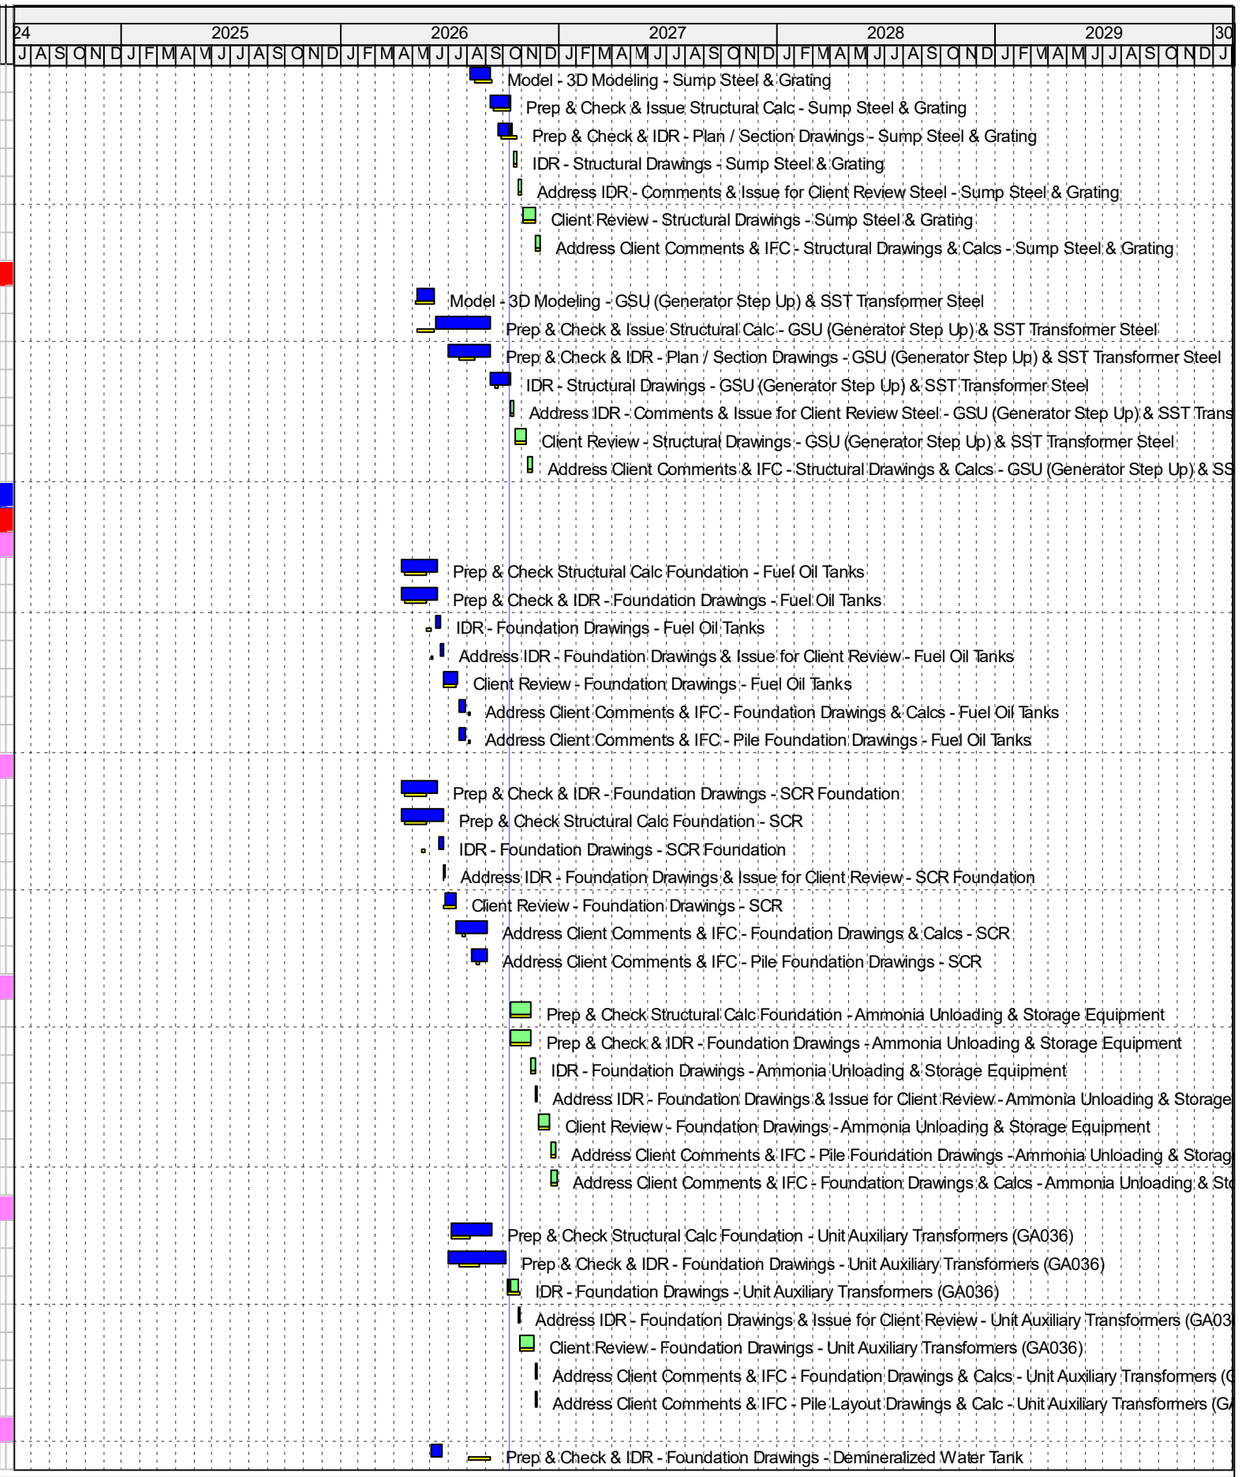


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC131101-1	IDR - Structural Drawings Issue for Client Review Foundation - D	0	7/20/26 7:00 AM A	7/31/26 5:00 PM A	
AEC131101-1	Address IDR - Comments & Issue for Client Review Foundation	0	8/3/26 7:00 AM A	8/27/26 5:00 PM A	
AEC131101-2	Client Review - Structural Drawings - Building - Foundation - Den	0	8/28/26 7:00 AM A	9/11/26 5:00 PM A	
AEC131101-2	Address Client Comments & IFC - Structural Drawings & Calcs F	0	9/28/26 7:00 AM A	10/6/26 5:00 PM A	
AEC131101-3	Address Client Comments & IFC - Pile Layout Drawings & Calc -	0	9/28/26 7:00 AM A	10/6/26 5:00 PM A	
AEC130501-0	Prep & Check Structural Calc Foundation - Demineralized Wate	4	6/1/26 7:00 AM A	10/15/26 5:00 PM	95
BH CNN-KPJV-MAST-LIVE,03,05,01,01,19 ENG - Structural - Calcs/Foundation Drawings - Service/Fire Water Tank					
AEC130545-0	Prep & Check Structural Calc Foundation - Service/Fire Water Ta	0	4/13/26 7:00 AM A	5/8/26 5:00 PM A	
AEC131145-0	Prep & Check & IDR - Foundation Drawings - Service/Fire Wate	0	4/13/26 7:00 AM A	6/5/26 5:00 PM A	
AEC131145-1	IDR - Foundation Drawings - Service/Fire Water Tank	0	6/5/26 7:00 AM A	6/8/26 5:00 PM A	
AEC131145-1	Address IDR - Comments & Issue for Client Review Foundation	0	6/9/26 7:00 AM A	6/30/26 5:00 PM A	
AEC131145-2	Client Review - Structural Drawings - Building - Foundation - Ser	0	7/1/26 7:00 AM A	7/13/26 5:00 PM A	
AEC131145-2	Address Client Comments & IFC - Structural Drawings & Calcs F	0	7/14/26 7:00 AM A	7/30/26 5:00 PM A	
AEC131145-3	Address Client Comments & IFC - Pile Layout Drawings & Calc -	0	7/14/26 7:00 AM A	7/30/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,02 ENG - Structural - Calcs/Foundation Drawings - Crane Pads					
AEC130505-0	Prep & Check Structural Calc Foundation - Crane Pads	0	6/12/26 7:00 AM A	7/14/26 5:00 PM A	
AEC131105-0	Prep & Check & IDR - Foundation Drawings - Crane Pads	0	6/26/26 7:00 AM A	7/16/26 5:00 PM A	
AEC131105-1	IDR - Foundation Drawings - Crane Pads	0	7/14/26 7:00 AM A	7/17/26 5:00 PM A	
AEC131105-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	7/20/26 7:00 AM A	7/23/26 5:00 PM A	
AEC131105-2	Client Review - Foundation Drawings - Crane Pads	0	7/23/26 7:00 AM A	8/10/26 5:00 PM A	
AEC131105-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	8/11/26 7:00 AM A	8/12/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,03 ENG - Structural - Calcs/Foundation Drawings - Station Service Transformers (138/345 kV)					
AEC130506-0	Prep & Check Structural Calc Foundation - Station Service Trans	0	8/13/26 7:00 AM A	9/11/26 5:00 PM A	
AEC131106-0	Prep & Check & IDR - Foundation Drawings - Station Service Tra	0	9/11/26 7:00 AM A	9/23/26 5:00 PM A	
AEC131106-1	IDR - Foundation Drawings - Station Service Transformers	0	9/24/26 7:00 AM A	9/30/26 5:00 PM A	
AEC131106-1	Address IDR - Foundation Drawings & Issue for Client Review - S	0	10/1/26 7:00 AM A	10/2/26 5:00 PM A	
AEC131106-2	Client Review - Foundation Drawings - Station Service Transforr	11	10/5/26 7:00 AM A	10/26/26 5:00 PM	54
AEC131106-3	Address Client Comments & IFC - Pile Layout Drawings & Calc -	5	10/27/26 7:00 AM	11/2/26 5:00 PM	54
AEC131106-2	Address Client Comments & IFC - Foundation Drawings & Calcs	10	10/27/26 7:00 AM	11/9/26 5:00 PM	115
BH CNN-KPJV-MAST-LIVE,03,05,01,01,04 ENG - Structural - Calcs/Foundation Drawings - Fuel Gas Compressor Coolers					
AEC131107-0	Prep & Check & IDR - Foundation Drawings - Fuel Gas Compres	0	5/4/26 7:00 AM A	6/12/26 5:00 PM A	
AEC130507-0	Prep & Check Structural Calc Foundation - Fuel Gas Compressc	0	4/20/26 7:00 AM A	6/23/26 5:00 PM A	
AEC131107-1	IDR - Foundation Drawings - Fuel Gas Compressor Coolers	0	7/2/26 7:00 AM A	8/3/26 5:00 PM A	
AEC131107-1	Address IDR - Foundation Drawings & Issue for Client Review - I	0	8/4/26 7:00 AM A	8/14/26 5:00 PM A	
AEC131107-2	Client Review - Foundation Drawings - Fuel Gas Compressor Co	0	8/14/26 7:00 AM A	9/10/26 5:00 PM A	
AEC131107-2	Address Client Comments & IFC - Foundation Drawings & Calcs	3	9/10/26 7:00 AM A	10/14/26 5:00 PM	133
AEC131107-3	Address Client Comments & IFC - Pile Foundation Drawings - Fu	4	9/10/26 7:00 AM A	10/15/26 5:00 PM	132
BH CNN-KPJV-MAST-LIVE,03,05,01,01,43 ENG - Structural - Calcs/Foundation Drawings - Isophase Bus/Generator Circuit Breaker Supports					
AEC130504-0	Prep & Check Structural Calc Foundation - Isophase Bus/Gener	0	7/8/26 7:00 AM A	9/11/26 5:00 PM A	
AEC131104-0	Prep & Check & IDR - Foundation Drawings - Isophase Bus/Ger	0	9/21/26 7:00 AM A	10/5/26 5:00 PM A	
AEC131104-1	IDR - Foundation Drawings - Isophase Bus/Generator Circuit Bre	5	10/12/26 7:00 AM	10/16/26 5:00 PM	98
AEC131104-1	Address IDR - Foundation Drawings & Issue for Client Review - I	10	10/19/26 7:00 AM	10/30/26 5:00 PM	98
AEC131104-2	Client Review - Foundation Drawings - Isophase Bus/Generator	15	11/2/26 7:00 AM	11/23/26 5:00 PM	98
AEC131104-2	Address Client Comments & IFC - Foundation Drawings & Calcs	8	11/24/26 7:00 AM	12/4/26 5:00 PM	98
BH CNN-KPJV-MAST-LIVE,03,05,01,01,20 ENG - Structural - Calcs/Foundation Drawings - Fuel Oil Unloading Pumps					
AEC130527-0	Prep & Check Structural Calc Foundation - Fuel Oil Unloading P	0	9/10/26 7:00 AM A	10/1/26 5:00 PM A	
AEC131127-0	Prep & Check & IDR - Foundation Drawings - Fuel Oil Unloading	10	11/17/26 7:00 AM	12/1/26 5:00 PM	66
AEC131127-1	IDR - Foundation Drawings - Fuel Oil Unloading Pumps	5	12/2/26 7:00 AM	12/8/26 5:00 PM	66
AEC131127-1	Address IDR - Foundation Drawings & Issue for Client Review - I	10	12/9/26 7:00 AM	12/22/26 5:00 PM	66
AEC131127-2	Client Review - Foundation Drawings - Fuel Oil Unloading Pump	15	12/23/26 7:00 AM	1/19/27 5:00 PM	66
AEC131127-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	1/20/27 7:00 AM	1/26/27 5:00 PM	66

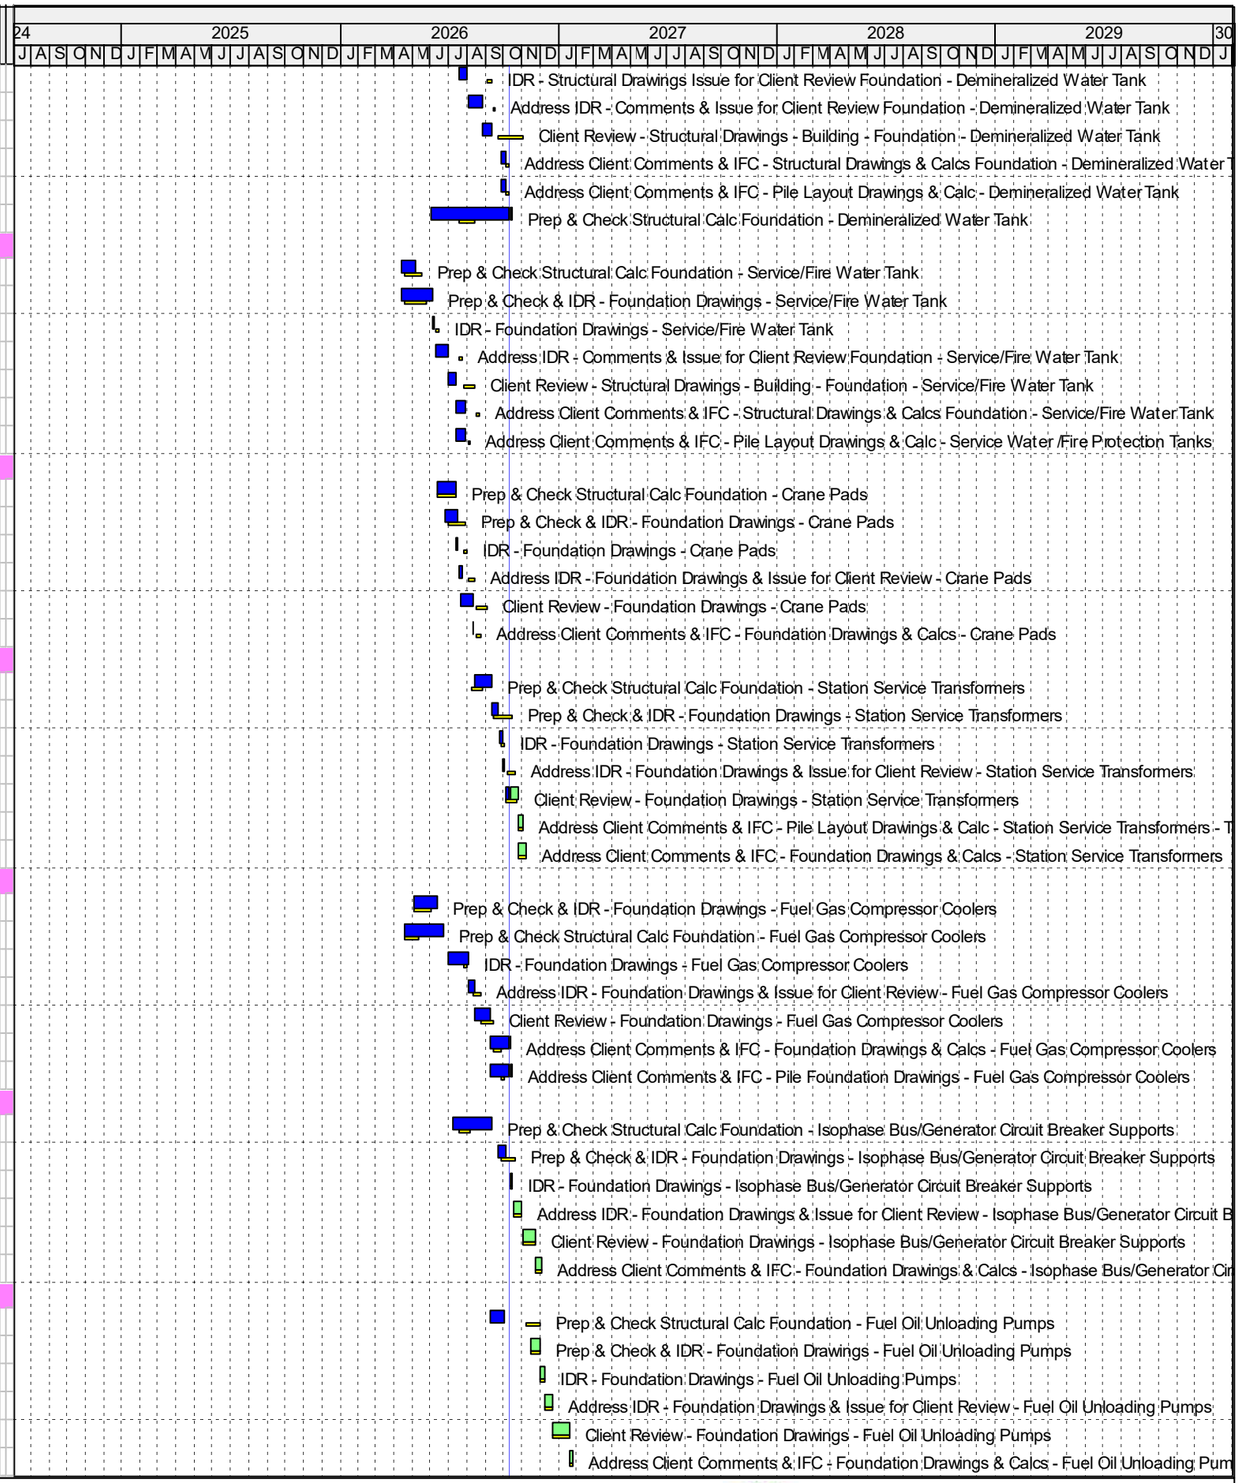


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
BH CNN-KPJV-MAST-LIVE,03,05,01,01,21 ENG - Structural - Calcs/Foundation Drawings - GE Cooling Water Module					
AEC130528-0	Prep & Check Structural Calc Foundation - GE Cooling Water M	0	4/30/26 7:00 AM A	6/18/26 5:00 PM A	
AEC131128-0	Prep & Check & IDR - Foundation Drawings - GE Cooling Water	0	5/11/26 7:00 AM A	6/30/26 5:00 PM A	
AEC131128-1	IDR - Foundation Drawings - GE Cooling Water Module	0	7/1/26 7:00 AM A	7/8/26 5:00 PM A	
AEC131128-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	7/9/26 7:00 AM A	7/14/26 5:00 PM A	
AEC131128-2	Client Review - Foundation Drawings - GE Cooling Water Modul	0	7/15/26 7:00 AM A	8/7/26 5:00 PM A	
AEC131128-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	8/10/26 7:00 AM A	9/11/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,05 ENG - Structural - Calcs/Foundation Drawings - CEMS Building					
AEC130508-0	Prep & Check Structural Calc Foundation - CEMS Building	0	4/9/26 7:00 AM A	5/8/26 5:00 PM A	
AEC131108-0	Prep & Check & IDR - Foundation Drawings - CEMS Building	0	4/27/26 7:00 AM A	6/26/26 5:00 PM A	
AEC131108-1	IDR - Foundation Drawings - CEMS Building	0	6/30/26 7:00 AM A	7/7/26 5:00 PM A	
AEC131108-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	7/8/26 7:00 AM A	7/14/26 5:00 PM A	
AEC131108-2	Client Review - Foundation Drawings - CEMS Building	0	7/15/26 7:00 AM A	7/23/26 5:00 PM A	
AEC131108-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	8/3/26 7:00 AM A	9/2/26 5:00 PM A	
AEC131108-3	Address Client Comments & IFC - Pile Foundation Drawings - C	0	8/3/26 7:00 AM A	9/2/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,06 ENG - Structural - Calcs/Foundation Drawings - Knockout Drums					
AEC130509A	Prep & Check Structural Calc Foundation - Knockout Drums	10	10/12/26 7:00 AM	10/23/26 5:00 PM	52
AEC131109A	Prep & Check & IDR - Foundation Drawings - Knockout Drums	10	10/12/26 7:00 AM	10/23/26 5:00 PM	52
AEC131109A	IDR - Foundation Drawings - Knockout Drums	4	10/26/26 7:00 AM	10/29/26 5:00 PM	52
AEC131109A	Address IDR - Foundation Drawings & Issue for Client Review - I	5	10/30/26 7:00 AM	11/5/26 5:00 PM	52
AEC131109A	Client Review - Foundation Drawings - Knockout Drums	15	11/6/26 7:00 AM	11/30/26 5:00 PM	52
AEC131109A	Address Client Comments & IFC - Foundation Drawings & Calcs	5	12/1/26 7:00 AM	12/7/26 5:00 PM	52
BH CNN-KPJV-MAST-LIVE,03,05,01,01,09 ENG - Structural - Calcs/Foundation Drawings - Fuel Gas Yard Drain Tank					
AEC130509B	Prep & Check Structural Calc Foundation - Fuel Gas Yard Drain	10	12/1/26 7:00 AM	12/14/26 5:00 PM	52
AEC131109B	Prep & Check & IDR - Foundation Drawings - Fuel Gas Yard Dra	10	12/15/26 7:00 AM	12/30/26 5:00 PM	52
AEC131109B	IDR - Foundation Drawings - Fuel Gas Yard Drain Tank	5	1/4/27 7:00 AM	1/8/27 5:00 PM	52
AEC131109B	Address IDR - Foundation Drawings & Issue for Client Review -F	5	1/11/27 7:00 AM	1/15/27 5:00 PM	52
AEC131109B	Client Review - Foundation Drawings - Fuel Gas Yard Drain Tank	15	1/19/27 7:00 AM	2/8/27 5:00 PM	52
AEC131109B	Address Client Comments & IFC - Foundation Drawings & Calcs	5	2/9/27 7:00 AM	2/16/27 5:00 PM	52
BH CNN-KPJV-MAST-LIVE,03,05,01,01,13 ENG - Structural - Calcs/Foundation Drawings - Weather Station					
AEC131109C	Prep & Check & IDR - Foundation Drawings - Weather Station	0	8/3/26 7:00 AM A	8/27/26 5:00 PM A	
AEC130509C	Prep & Check Structural Calc Foundation - Weather Station	0	8/3/26 7:00 AM A	8/28/26 5:00 PM A	
AEC131109C	IDR - Foundation Drawings - Weather Station	0	9/1/26 7:00 AM A	9/8/26 5:00 PM A	
AEC131109C	Address IDR - Foundation Drawings & Issue for Client Review -V	0	9/8/26 7:00 AM A	9/11/26 5:00 PM A	
AEC131109C	Client Review - Foundation Drawings - Weather Station	0	9/11/26 7:00 AM A	9/25/26 5:00 PM A	
AEC131109C	Address Client Comments & IFC - Foundation Drawings & Calcs	0	9/28/26 7:00 AM A	10/5/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,22 ENG - Structural - Calcs/Foundation Drawings - Fuel Gas Enclosure Auxiliary Transformer					
AEC131109D	Prep & Check Structural Foundation Drawing - Aux Transformer	0	8/20/26 7:00 AM A	8/27/26 5:00 PM A	
AEC131109D	IDR - Foundation Drawings - Aux Transformer - Fuel Gas Enclos	0	8/27/26 7:00 AM A	9/4/26 5:00 PM A	
AEC130509D	Prep & Check Structural Calc Foundation - Aux Transformer - Fu	0	8/10/26 7:00 AM A	9/8/26 5:00 PM A	
AEC131109D	Address IDR - Foundation Drawings & Issue for Client Review - /	0	9/8/26 7:00 AM A	9/11/26 5:00 PM A	
AEC131109D	Client Review - Foundation Drawings - Aux Transformer - Fuel G	5	9/11/26 7:00 AM A	10/16/26 5:00 PM	126
AEC131109D	Address Client Comments & IFC - Foundation Drawings & Calcs	5	10/19/26 7:00 AM	10/23/26 5:00 PM	126
BH CNN-KPJV-MAST-LIVE,03,05,01,01,31 ENG - Structural - Calcs/Foundation Drawings - GE Supplied Gas Fuel Filtering Skid					
AEC130571-0	Prep & Check Structural Calc Foundation - GE Supplied Fuel Ga	0	3/30/26 7:00 AM A	4/23/26 5:00 PM A	
AEC131171-0	Prep & Check & IDR - Foundation Drawings - GE Supplied Fuel	0	3/25/26 7:00 AM A	4/23/26 5:00 PM A	
AEC131171-1	IDR - Foundation Drawings - GE Supplied Fuel Gas Filtering Ski	0	4/23/26 7:00 AM A	4/30/26 5:00 PM A	
AEC131171-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	5/1/26 7:00 AM A	5/1/26 5:00 PM A	
AEC131171-2	Client Review - Foundation Drawings - GE Supplied Fuel Gas Fil	0	5/1/26 7:00 AM A	5/22/26 5:00 PM A	
AEC131171-3	Address Client Comments & IFC - Foundation Drawings & Calcs	0	5/26/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,32 ENG - Structural - Calcs/Foundation Drawings - Fuel Gas CTG Drain Tank					

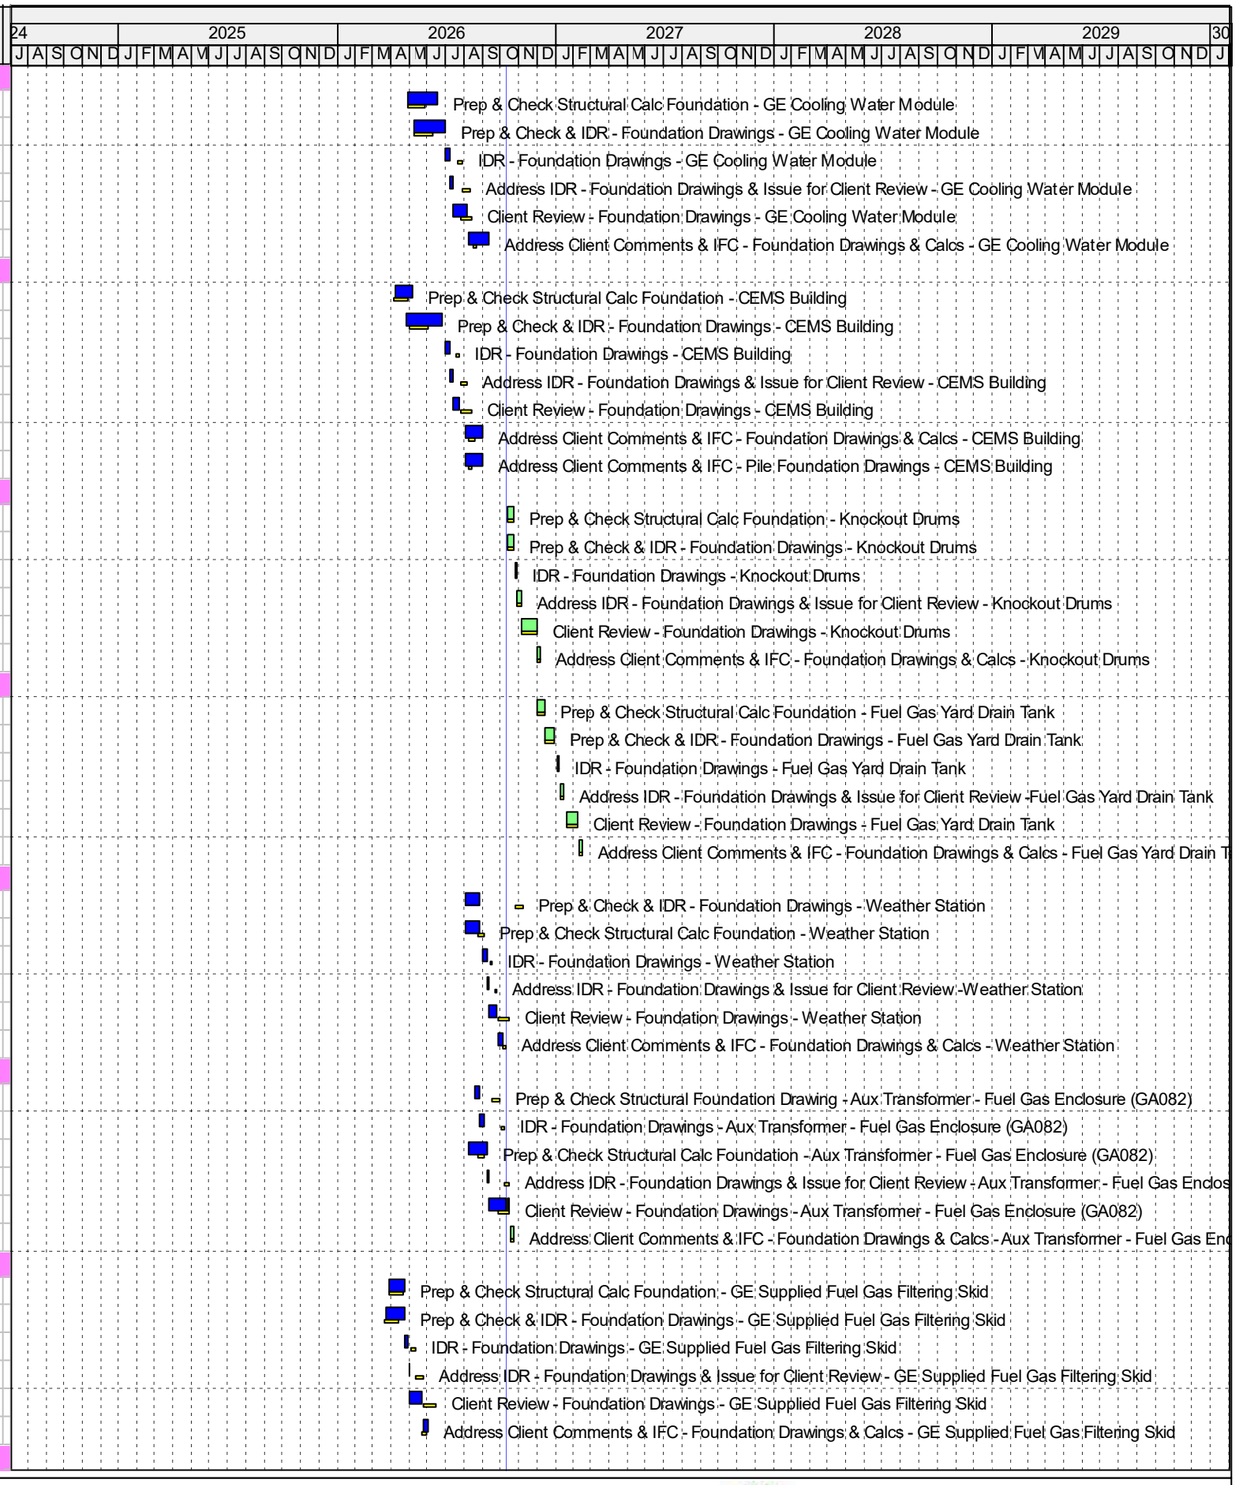


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC130572-0	Prep & Check Structural Calc Foundation - Fuel Gas CTG Drain	15	10/12/26 7:00 AM	10/30/26 5:00 PM	86
AEC131172-0	Prep & Check & IDR - Foundation Drawings - Fuel Gas CTG Dra	15	10/12/26 7:00 AM	10/30/26 5:00 PM	86
AEC131172-1	IDR - Foundation Drawings - Fuel Gas CTG Drain Tank	5	11/2/26 7:00 AM	11/6/26 5:00 PM	86
AEC131172-1	Address IDR - Foundation Drawings & Issue for Client Review - I	10	11/9/26 7:00 AM	11/23/26 5:00 PM	86
AEC131172-2	Client Review - Foundation Drawings - Fuel Gas CTG Drain Tank	15	11/24/26 7:00 AM	12/15/26 5:00 PM	86
AEC131172-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	12/16/26 7:00 AM	12/22/26 5:00 PM	86
BH CNN-KPJV-MAST-LIVE,03,05,01,01,38 ENG - Structural - Calcs/Foundation Drawings - GE PEECC/LEC Foundations					
AEC131177-0	Prep & Check & IDR - Foundation Drawings - GE PEECC/LEC F	0	9/1/26 7:00 AM A	9/4/26 5:00 PM A	
AEC131177-1	IDR - Foundation Drawings - GE PEECC/LEC Foundations (GA(	0	9/7/26 7:00 AM A	9/11/26 5:00 PM A	
AEC131177-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	9/14/26 7:00 AM A	9/18/26 5:00 PM A	
AEC130577-0	Prep & Check Structural Calc Foundation - GE PEECC/LEC Fou	3	9/1/26 7:00 AM A	10/14/26 5:00 PM	77
AEC131177-2	Client Review - Foundation Drawings - GE PEECC/LEC Foundat	6	9/8/26 7:00 AM A	10/19/26 5:00 PM	77
AEC131177-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	10/20/26 7:00 AM	10/26/26 5:00 PM	125
AEC131177-3	Address Client Comments & IFC - Pile Foundation Drawings - G	5	10/20/26 7:00 AM	10/26/26 5:00 PM	77
BH CNN-KPJV-MAST-LIVE,03,05,01,01,50 ENG - Structural - Calcs/Foundation Drawings - CT Oil Containing Sump					
AEC131180-0	Prep & Check & IDR - Foundation Drawings - CT Oil Containing	0	5/4/26 7:00 AM A	6/3/26 5:00 PM A	
AEC131180-1	IDR - Foundation Drawings - CT Oil Containing Sump	0	6/3/26 7:00 AM A	6/8/26 5:00 PM A	
AEC130580-0	Prep & Check Structural Calc Foundation - CT Oil Containing Su	0	5/4/26 7:00 AM A	6/15/26 5:00 PM A	
AEC131180-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	6/9/26 7:00 AM A	6/18/26 5:00 PM A	
AEC131180-2	Client Review - Foundation Drawings - CT Oil Containing Sump	0	6/18/26 7:00 AM A	7/8/26 5:00 PM A	
AEC-131180-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	7/9/26 7:00 AM A	8/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,51 ENG - Structural - Calcs/Foundation Drawings - GE Dehumidification Skid Foundation					
AEC130581-0	Prep & Check Structural Calc Foundation - GE Dehumidification	0	4/29/26 7:00 AM A	5/19/26 5:00 PM A	
AEC131181-0	Prep & Check & IDR - Foundation Drawings - GE Dehumidificati	0	4/29/26 7:00 AM A	6/1/26 5:00 PM A	
AEC131181-1	IDR - Foundation Drawings - GE Dehumidification Skid Foundati	0	6/1/26 7:00 AM A	6/5/26 5:00 PM A	
AEC131181-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	6/8/26 7:00 AM A	6/12/26 5:00 PM A	
AEC131181-2	Client Review - Foundation Drawings - GE Dehumidification Skic	0	6/15/26 7:00 AM A	6/29/26 5:00 PM A	
AEC131181-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	6/29/26 7:00 AM A	6/30/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,52 ENG - Structural - Calcs/Foundation Drawings - GE DC Link Reactor Foundation					
AEC131182-0	Prep & Check & IDR - Foundation Drawings - GE DC Link React	0	5/11/26 7:00 AM A	6/1/26 5:00 PM A	
AEC131182-1	IDR - Foundation Drawings - GE DC Link Reactor Foundation	0	6/1/26 7:00 AM A	6/8/26 5:00 PM A	
AEC130582-0	Prep & Check Structural Calc Foundation - GE DC Link Reactor	0	6/8/26 7:00 AM A	6/12/26 5:00 PM A	
AEC131182-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	6/9/26 7:00 AM A	6/15/26 5:00 PM A	
AEC131182-2	Client Review - Foundation Drawings - GE DC Link Reactor Fou	0	6/16/26 7:00 AM A	6/29/26 5:00 PM A	
AEC131182-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	6/29/26 7:00 AM A	7/1/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,53 ENG - Structural - Calcs/Foundation Drawings - GE CT Excitation Transformer Foundation					
AEC13118305	Prep & Check & IDR - Foundation Drawings - GE CT Excitation T	0	5/11/26 7:00 AM A	6/1/26 5:00 PM A	
AEC130583-0	Prep & Check Structural Calc Foundation - GE CT Excitation Tra	0	6/1/26 7:00 AM A	6/8/26 5:00 PM A	
AEC131183-1	IDR - Foundation Drawings - GE CT Excitation Transformer Fou	0	6/1/26 7:00 AM A	6/8/26 5:00 PM A	
AEC131183-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	6/9/26 7:00 AM A	6/15/26 5:00 PM A	
AEC131183-2	Client Review - Foundation Drawings - GE CT Excitation Transfo	0	6/16/26 7:00 AM A	6/29/26 5:00 PM A	
AEC131183-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	6/29/26 7:00 AM A	7/1/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,54 ENG - Structural - Calcs/Foundation Drawings - GE CT Isolation Transformer Foundation					
AEC131184-0	Prep & Check & IDR - Foundation Drawings - GE CT Isolation Tr	0	5/11/26 7:00 AM A	6/1/26 5:00 PM A	
AEC131184-1	IDR - Foundation Drawings - GE CT Isolation Transformer Foun	0	6/1/26 7:00 AM A	6/5/26 5:00 PM A	
AEC131184-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	6/8/26 7:00 AM A	6/12/26 5:00 PM A	
AEC131184-2	Client Review - Foundation Drawings - GE CT Isolation Transfor	0	6/15/26 7:00 AM A	6/29/26 5:00 PM A	
AEC131184-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	6/29/26 7:00 AM A	7/1/26 5:00 PM A	
AEC130584-0	Prep & Check Structural Calc Foundation - GE CT Isolation Tran	0	6/22/26 7:00 AM A	7/27/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,55 ENG - Structural - Calcs/Foundation Drawings - Aux Transformer Foundation					
AEC130585-0	Prep & Check Structural Calc Foundation - Aux Transformer Fou	0	7/15/26 7:00 AM A	8/26/26 5:00 PM A	

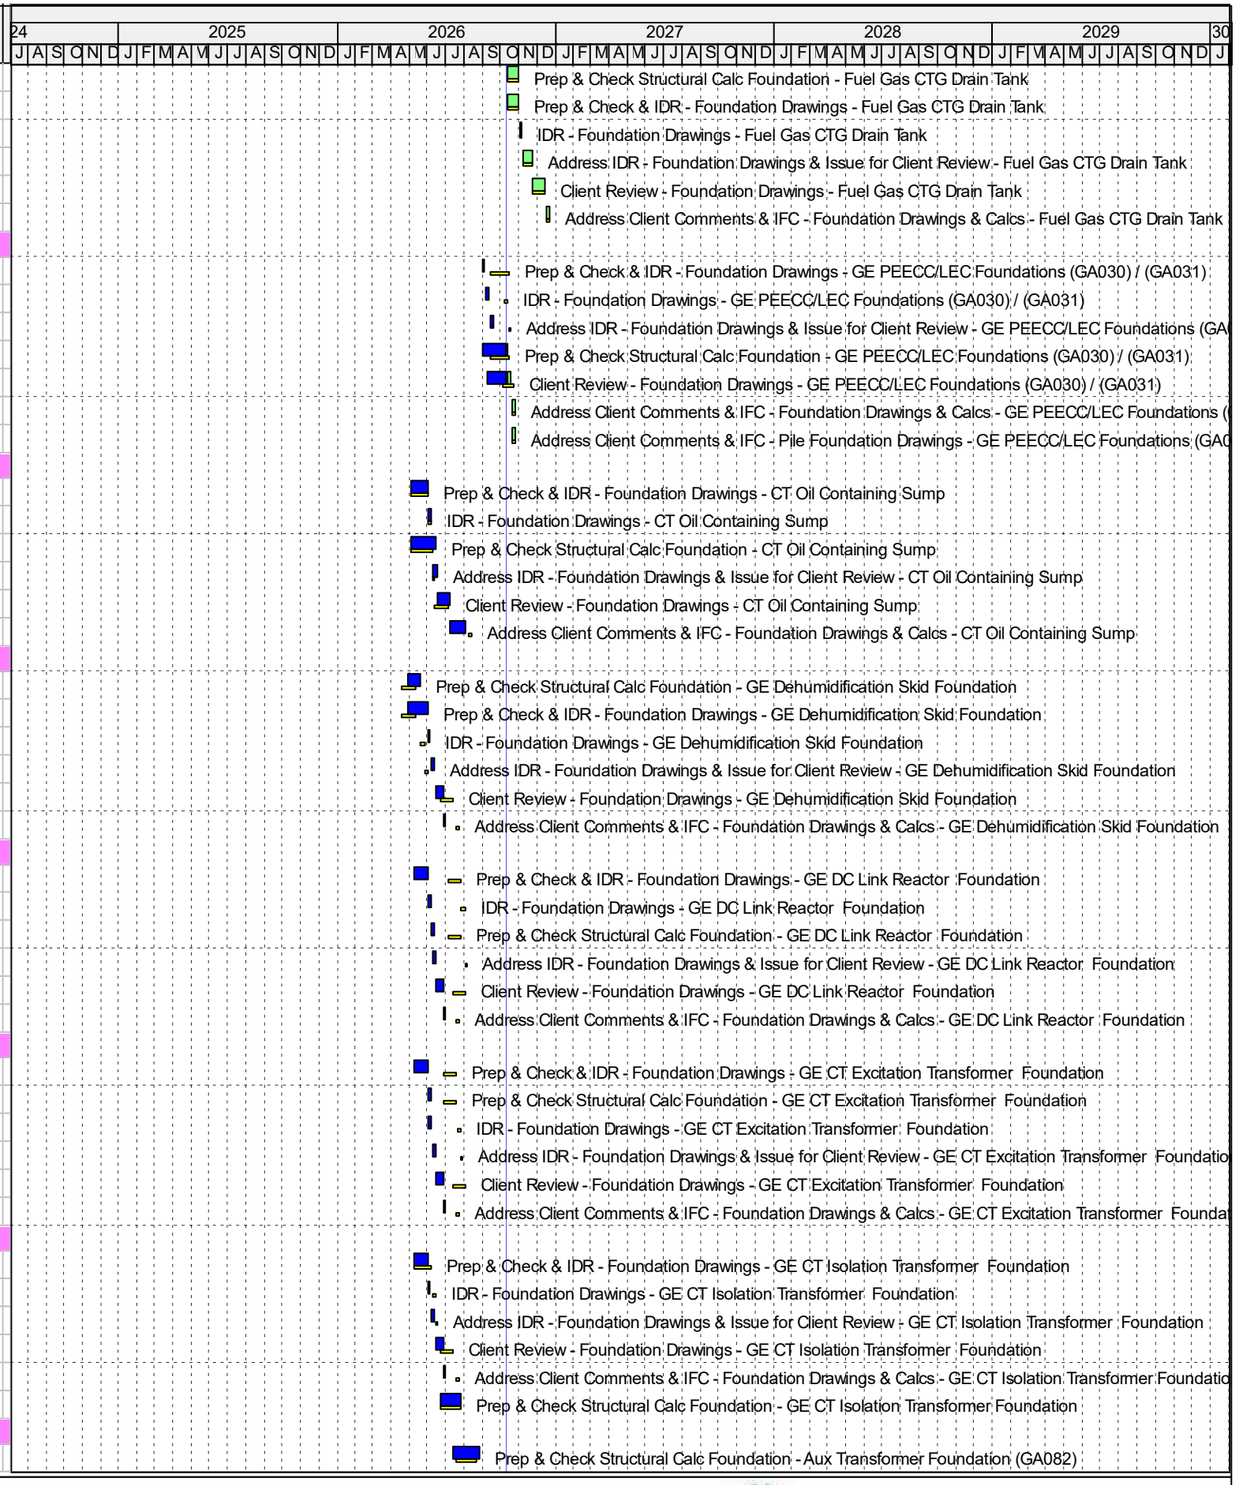
24
2025
2026
2027
2028
2029
30
J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC131185-0	Prep & Check & IDR - Foundation Drawings - Aux Transformer F	0	7/15/26 7:00 AM A	8/26/26 5:00 PM A	
AEC131185-1	IDR - Foundation Drawings - Aux Transformer Foundation (GA0	0	8/27/26 7:00 AM A	9/8/26 5:00 PM A	
AEC131185-1	Address IDR - Foundation Drawings & Issue for Client Review - /	0	9/8/26 7:00 AM A	9/11/26 5:00 PM A	
AEC131185-2	Client Review - Foundation Drawings - Aux Transformer Founda	0	9/11/26 7:00 AM A	10/2/26 5:00 PM A	
AEC131185-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	10/12/26 7:00 AM	10/16/26 5:00 PM	131
BH CNN-KPJV-MAST-LIVE,03,05,01,01,56 ENG - Structural - Calcs/Foundation Drawings - GE AC Reactor Foundation					
AEC130586-0	Prep & Check Structural Calc Foundation - GE AC Reactor Four	0	3/24/26 7:00 AM A	4/23/26 5:00 PM A	
AEC131186-0	Prep & Check & IDR - Foundation Drawings - GE AC Reactor Fo	0	3/24/26 7:00 AM A	4/23/26 5:00 PM A	
AEC131186-1	IDR - Foundation Drawings - GE AC Reactor Foundation	0	4/23/26 7:00 AM A	4/29/26 5:00 PM A	
AEC131186-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	4/30/26 7:00 AM A	5/1/26 5:00 PM A	
AEC131186-2	Client Review - Foundation Drawings - GE AC Reactor Foundatic	0	5/1/26 7:00 AM A	5/20/26 5:00 PM A	
AEC131186-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	5/21/26 7:00 AM A	5/28/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,57 ENG - Structural - Calcs/Foundation Drawings - GE APU Foundation					
AEC130587-0	Prep & Check Structural Calc Foundation - GE APU Foundation	0	3/20/26 7:00 AM A	4/23/26 5:00 PM A	
AEC131187-0	Prep & Check & IDR - Foundation Drawings - GE APU Foundatic	0	3/20/26 7:00 AM A	4/23/26 5:00 PM A	
AEC131187-1	IDR - Foundation Drawings - GE APU Foundation	0	4/23/26 7:00 AM A	4/30/26 5:00 PM A	
AEC131187-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	5/1/26 7:00 AM A	5/1/26 5:00 PM A	
AEC131187-2	Client Review - Foundation Drawings - GE APU Foundation	0	5/1/26 7:00 AM A	5/20/26 5:00 PM A	
AEC131187-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	5/21/26 7:00 AM A	5/26/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,58 ENG - Structural - Calcs/Foundation Drawings - GE Water Mist Fire Fighting Skid					
AEC130590-0	Prep & Check Structural Calc Foundation - GE Water Mist Fire F	0	3/17/26 7:00 AM A	4/23/26 5:00 PM A	
AEC131190-0	Prep & Check & IDR - Foundation Drawings - GE Water Mist Fir	0	3/17/26 7:00 AM A	4/23/26 5:00 PM A	
AEC131190-1	IDR - Foundation Drawings - GE Water Mist Fire Fighting Skid	0	4/23/26 7:00 AM A	4/30/26 5:00 PM A	
AEC131190-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	5/1/26 7:00 AM A	5/1/26 5:00 PM A	
AEC131190-2	Client Review - Foundation Drawings - GE Water Mist Fire Fighti	0	5/1/26 7:00 AM A	5/20/26 5:00 PM A	
AEC131190-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	5/21/26 7:00 AM A	5/26/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,59 ENG - Structural - Calcs/Foundation Drawings - GE Chromatograph Foundation					
AEC130591-0	Prep & Check Structural Calc Foundation - GE Chromatograph I	0	5/14/26 7:00 AM A	6/10/26 5:00 PM A	
AEC131191-0	Prep & Check & IDR - Foundation Drawings - GE Chromatograp	0	5/18/26 7:00 AM A	6/15/26 5:00 PM A	
AEC131191-1	IDR - Foundation Drawings - GE Chromatograph Foundation	0	6/16/26 7:00 AM A	6/22/26 5:00 PM A	
AEC131191-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	6/22/26 7:00 AM A	6/23/26 5:00 PM A	
AEC131191-2	Client Review - Foundation Drawings - GE Chromatograph Four	0	7/7/26 7:00 AM A	8/10/26 5:00 PM A	
AEC131191-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	8/11/26 7:00 AM A	9/30/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,60 ENG - Structural - Calcs/Foundation Drawings - Secondary Unit Substation Transformer Foundation					
AEC130592-0	Prep & Check Structural Calc Foundation - Secondary Unit Subs	0	7/13/26 7:00 AM A	9/8/26 5:00 PM A	
AEC131192-0	Prep & Check & IDR - Foundation Drawings - Secondary Unit Su	0	7/13/26 7:00 AM A	9/8/26 5:00 PM A	
AEC131192-1	IDR - Foundation Drawings - Secondary Unit Substation Transfo	0	9/23/26 7:00 AM A	9/30/26 5:00 PM A	
AEC131192-1	Address IDR - Foundation Drawings & Issue for Client Review - S	0	10/1/26 7:00 AM A	10/2/26 5:00 PM A	
AEC131192-2	Client Review - Foundation Drawings - Secondary Unit Substatic	10	10/2/26 7:00 AM A	10/23/26 5:00 PM	121
AEC131192-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	10/26/26 7:00 AM	10/30/26 5:00 PM	121
BH CNN-KPJV-MAST-LIVE,03,05,01,01,61 ENG - Structural - Calcs/Foundation Drawings - Admin HVAC Foundations					
AEC131193-0	Prep & Check & IDR - Foundation Drawings - Admin HVAC Four	0	8/17/26 7:00 AM A	9/2/26 5:00 PM A	
AEC131193-1	IDR - Foundation Drawings - Admin HVAC Foundations	0	9/3/26 7:00 AM A	9/10/26 5:00 PM A	
AEC130593-0	Prep & Check Structural Calc Foundation - Admin HVAC Founda	0	8/17/26 7:00 AM A	10/2/26 5:00 PM A	
AEC131193-1	Address IDR - Foundation Drawings & Issue for Client Review - /	5	9/11/26 7:00 AM A	10/16/26 5:00 PM	111
AEC131193-2	Client Review - Foundation Drawings - Admin HVAC Foundation	15	10/19/26 7:00 AM	11/6/26 5:00 PM	111
AEC131193-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	11/9/26 7:00 AM	11/16/26 5:00 PM	111
BH CNN-KPJV-MAST-LIVE,03,05,01,01,62 ENG - Structural - Calcs/Foundation Drawings - Liquid Fuel Enclosure HVAC Foundations					
AEC131194-0	Prep & Check & IDR - Foundation Drawings - Liquid Fuel Enclos	0	8/17/26 7:00 AM A	9/2/26 5:00 PM A	
AEC131194-1	IDR - Foundation Drawings - Liquid Fuel Enclosure HVAC Founc	0	9/3/26 7:00 AM A	9/10/26 5:00 PM A	
AEC130594-0	Prep & Check Structural Calc Foundation - Liquid Fuel Enclosur	0	8/17/26 7:00 AM A	10/2/26 5:00 PM A	



Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC131194-1	Address IDR - Foundation Drawings & Issue for Client Review - I	4	9/11/26 7:00 AM A	10/15/26 5:00 PM	112
AEC131194-2	Client Review - Foundation Drawings - Liquid Fuel Enclosure HV	15	10/16/26 7:00 AM	11/5/26 5:00 PM	112
AEC131194-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	11/18/26 7:00 AM	11/24/26 5:00 PM	105
BH CNN-KPJV-MAST-LIVE,03,05,01,01,63 ENG - Structural - Calcs/Foundation Drawings - Fuel Gas Compressor Enclosure HVAC Foundations					
AEC131195-0	Prep & Check & IDR - Foundation Drawings - Fuel Gas Compres	0	8/17/26 7:00 AM A	9/2/26 5:00 PM A	
AEC131195-1	IDR - Foundation Drawings - Fuel Gas Compressor Enclosure H	0	9/3/26 7:00 AM A	9/21/26 5:00 PM A	
AEC130595-0	Prep & Check Structural Calc Foundation - Fuel Gas Compressc	0	8/17/26 7:00 AM A	9/22/26 5:00 PM A	
AEC131195-1	Address IDR - Foundation Drawings & Issue for Client Review - I	5	9/23/26 7:00 AM A	10/16/26 5:00 PM	111
AEC131195-2	Client Review - Foundation Drawings - Fuel Gas Compressor En	15	10/19/26 7:00 AM	11/6/26 5:00 PM	111
AEC131195-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	11/18/26 7:00 AM	11/24/26 5:00 PM	105
BH CNN-KPJV-MAST-LIVE,03,05,01,01,08 ENG - Structural - Calcs/Foundation Drawings - Misc. Foundations					
AEC130511-0	Prep & Check Structural Calc Foundation - Misc. Foundations	0	6/1/26 7:00 AM A	8/28/26 5:00 PM A	
AEC131111-0	Prep & Check & IDR - Foundation Drawings - Misc. Foundations	0	6/8/26 7:00 AM A	8/28/26 5:00 PM A	
AEC131111-1	IDR - Foundation Drawings - Misc. Foundations	0	8/31/26 7:00 AM A	9/21/26 5:00 PM A	
AEC131111-1	Address IDR - Foundation Drawings & Issue for Client Review - I	1	9/22/26 7:00 AM A	10/12/26 5:00 PM	115
AEC131111-2	Client Review - Foundation Drawings - Misc. Foundations	15	10/13/26 7:00 AM	11/2/26 5:00 PM	115
AEC131111-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	11/3/26 7:00 AM	11/9/26 5:00 PM	115
BH CNN-KPJV-MAST-LIVE,03,05,01,01,10 ENG - Structural - Calcs/Foundation Drawings - Fuel Gas Compressor Enclosure					
AEC130513-0	Prep & Check Structural Calc Foundation - Fuel Gas Compressc	15	11/5/26 7:00 AM	11/27/26 5:00 PM	53
AEC131113-0	Prep & Check & IDR - Foundation Drawings - Fuel Gas Compres	15	11/30/26 7:00 AM	12/18/26 5:00 PM	53
AEC131113-1	IDR - Foundation Drawings - Fuel Gas Compressor Enclosure	5	12/21/26 7:00 AM	12/29/26 5:00 PM	53
AEC131113-1	Address IDR - Foundation Drawings & Issue for Client Review - I	10	12/30/26 7:00 AM	1/14/27 5:00 PM	53
AEC131113-2	Client Review - Foundation Drawings - Fuel Gas Compressor En	15	1/15/27 7:00 AM	2/5/27 5:00 PM	53
AEC131113-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	2/8/27 7:00 AM	2/12/27 5:00 PM	53
AEC131113-3	Address Client Comments & IFC - Pile Foundation Drawings - Fu	5	2/8/27 7:00 AM	2/12/27 5:00 PM	53
BH CNN-KPJV-MAST-LIVE,03,05,01,01,11 ENG - Structural - Calcs/Foundation Drawings - Administration/Warehouse Building					
AEC131114-0	Prep & Check & IDR - Foundation Drawings - Administration/Wa	1	9/1/26 7:00 AM A	10/12/26 5:00 PM	3
AEC131114-1	IDR - Foundation Drawings - Administration/Warehouse Building	5	10/13/26 7:00 AM	10/19/26 5:00 PM	3
AEC131114-1	Address IDR - Foundation Drawings & Issue for Client Review - A	5	10/20/26 7:00 AM	10/26/26 5:00 PM	3
AEC130514-0	Prep & Check Structural Calc Foundation - Administration/Warel	15	9/1/26 7:00 AM A	10/30/26 5:00 PM	3
AEC131114-2	Client Review - Foundation Drawings - Administration/Warehous	15	10/27/26 7:00 AM	11/17/26 5:00 PM	3
AEC131114-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	11/18/26 7:00 AM	11/24/26 5:00 PM	98
AEC131114-3	Address Client Comments & IFC - Pile Foundation Drawings - Ac	5	11/25/26 7:00 AM	12/2/26 5:00 PM	100
BH CNN-KPJV-MAST-LIVE,03,05,01,01,12 ENG - Structural - Calcs/Foundation Drawings - Liquid Fuel Pump Enclosure					
AEC130515-0	Prep & Check Structural Calc Foundation - Liquid Fuel Pump Er	5	9/11/26 7:00 AM A	10/16/26 5:00 PM	15
AEC131115-0	Prep & Check & IDR - Foundation Drawings - Liquid Fuel Pump	5	9/21/26 7:00 AM A	10/16/26 5:00 PM	15
AEC131115-1	IDR - Foundation Drawings - Liquid Fuel Pump Enclosure	5	10/19/26 7:00 AM	10/23/26 5:00 PM	15
AEC131115-1	Address IDR - Foundation Drawings & Issue for Client Review - I	10	10/26/26 7:00 AM	11/6/26 5:00 PM	15
AEC131115-2	Client Review - Foundation Drawings - Liquid Fuel Pump Enclos	15	11/9/26 7:00 AM	12/1/26 5:00 PM	15
AEC131115-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	12/2/26 7:00 AM	12/8/26 5:00 PM	96
AEC131115-3	Address Client Comments & IFC - Pile Foundation Drawings - Li	5	12/2/26 7:00 AM	12/8/26 5:00 PM	96
BH CNN-KPJV-MAST-LIVE,03,05,01,01,25 ENG - Structural - Calcs/Foundation Drawings - Stack Foundations (incl.Exhaust Duct)					
AEC131135-0	Prep & Check & IDR - Foundation Drawings - Stack Foundations	0	5/11/26 7:00 AM A	6/10/26 5:00 PM A	
AEC131135-1	IDR - Foundation Drawings - Stack Foundations (incl. Exhaust D	0	6/10/26 7:00 AM A	6/12/26 5:00 PM A	
AEC130535-0	Prep & Check Structural Calc Foundation - Stack Foundations (i	0	3/30/26 7:00 AM A	6/19/26 5:00 PM A	
AEC131135-1	Address IDR - Foundation Drawings & Issue for CR1 - Stack Fou	0	6/15/26 7:00 AM A	6/22/26 5:00 PM A	
AEC131135-2	Client Review - Foundation Drawings - Stack Foundations (incl. I	0	6/23/26 7:00 AM A	7/10/26 5:00 PM A	
AEC131135-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	7/15/26 7:00 AM A	8/7/26 5:00 PM A	
AEC131135-3	Address Client Comments & IFC - Pile Foundation Drawings - St	0	7/15/26 7:00 AM A	8/7/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,26 ENG - Structural - Calcs/Foundation Drawings - Accessory Module					
AEC131115-8	Prep & Check & IDR - Foundation Drawings - Accessory Module	0	4/13/26 7:00 AM A	5/1/26 5:00 PM A	




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC130515-1	Prep & Check Structural Calc Foundation - Accessory Module Fc	0	3/30/26 7:00 AM A	5/8/26 5:00 PM A	
AEC131115-1	Address IDR - Foundation Drawings & Issue for Client Review - A	0	5/15/26 7:00 AM A	5/15/26 5:00 PM A	
AEC131115-9	IDR - Foundation Drawings - Accessory Module Foundation	0	5/8/26 7:00 AM A	5/15/26 5:00 PM A	
AEC131115-1	Client Review - Foundation Drawings - Accessory Module Found	0	5/15/26 7:00 AM A	6/16/26 5:00 PM A	
AEC131115-1	Address Client Comments & IFC - Pile Foundation Drawings - Ac	0	6/16/26 7:00 AM A	6/29/26 5:00 PM A	
AEC131115-1	Address Client Comments & IFC - Foundation Drawings & Calcs	0	6/16/26 7:00 AM A	6/30/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,15 ENG - Structural - Calcs/Foundation Drawings - Plant Services Enclosure					
AEC131118-0	Prep & Check & IDR - Foundation Drawings - Plant Services Enc	1	9/8/26 7:00 AM A	10/12/26 5:00 PM	100
AEC130518-0	Prep & Check Structural Calc Foundation - Plant Services Enclo	15	8/20/26 7:00 AM A	10/30/26 5:00 PM	86
AEC131118-1	IDR - Foundation Drawings - Plant Services Enclosure	5	11/2/26 7:00 AM	11/6/26 5:00 PM	86
AEC131118-1	Address IDR - Foundation Drawings & Issue for Client Review - I	10	11/9/26 7:00 AM	11/23/26 5:00 PM	86
AEC131118-2	Client Review - Foundation Drawings - Plant Services Enclosure	15	11/24/26 7:00 AM	12/15/26 5:00 PM	86
AEC131118-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	12/16/26 7:00 AM	12/22/26 5:00 PM	86
BH CNN-KPJV-MAST-LIVE,03,05,01,01,16 ENG - Structural - Calcs/Foundation Drawings - PDC Enclosure					
AEC130519-0	Prep & Check Structural Calc Foundation - PDC Enclosure	0	3/23/26 7:00 AM A	4/21/26 5:00 PM A	
AEC131119-0	Prep & Check & IDR - Foundation Drawings - PDC Enclosure	0	4/13/26 7:00 AM A	5/1/26 5:00 PM A	
AEC131119-1	IDR - Foundation Drawings - PDC Enclosure	0	5/4/26 7:00 AM A	5/8/26 5:00 PM A	
AEC131119-1	Address IDR - Foundation Drawings & Issue for Client Review - I	0	6/5/26 7:00 AM A	7/15/26 5:00 PM A	
AEC131119-2	Client Review - Foundation Drawings - PDC Enclosure	0	7/15/26 7:00 AM A	7/29/26 5:00 PM A	
AEC131119-2	Address Client Comments & IFC - Foundation Drawings & Calcs	0	8/3/26 7:00 AM A	8/31/26 5:00 PM A	
AEC131119-3	Address Client Comments & IFC - Pile Foundation Drawings - P	0	8/3/26 7:00 AM A	8/31/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,17 ENG - Structural - Calcs/Foundation Drawings - Guard Shack					
AEC130520-0	Prep & Check Structural Calc Foundation - Guard Shack	0	6/1/26 7:00 AM A	7/6/26 5:00 PM A	
AEC131120-0	Prep & Check & IDR - Foundation Drawings - Guard Shack	0	6/1/26 7:00 AM A	7/14/26 5:00 PM A	
AEC131120-1	IDR - Foundation Drawings - Guard Shack	0	7/15/26 7:00 AM A	7/22/26 5:00 PM A	
AEC131120-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	7/22/26 7:00 AM A	7/23/26 5:00 PM A	
AEC131120-2	Client Review - Foundation Drawings - Guard Shack	0	7/23/26 7:00 AM A	9/17/26 5:00 PM A	
AEC131120-2	Received Vendor Information from Kokosing - Guard Shack	0		10/30/26 5:00 PM*	116
AEC131120-2	Address Client Comments & IFC - Foundation Drawings & Calcs	20	9/18/26 7:00 AM A	11/6/26 5:00 PM	116
BH CNN-KPJV-MAST-LIVE,03,05,01,01,18 ENG - Structural - Calcs/Foundation Drawings - Fire Pump House					
AEC131121-0	Prep & Check & IDR - Foundation Drawings - Fire Pump House	0	8/10/26 7:00 AM A	9/2/26 5:00 PM A	
AEC131121-1	IDR - Foundation Drawings - Fire Pump House	4	9/3/26 7:00 AM A	10/15/26 5:00 PM	102
AEC131121-1	Address IDR - Foundation Drawings & Issue for Client Review - I	10	10/16/26 7:00 AM	10/29/26 5:00 PM	102
AEC130521-0	Prep & Check Structural Calc Foundation - Fire Pump House	16	8/3/26 7:00 AM A	11/2/26 5:00 PM	102
AEC131121-2	Client Review - Foundation Drawings - Fire Pump House	15	10/30/26 7:00 AM	11/20/26 5:00 PM	102
AEC131121-2	Address Client Comments & IFC - Foundation Drawings & Calcs	5	11/23/26 7:00 AM	11/30/26 5:00 PM	102
BH CNN-KPJV-MAST-LIVE,03,05,01,01,23 ENG - Structural - Calcs/Foundation Drawings - All CTG's					
AEC131141-3	Evaluate - Revised GE Loads - Structural Drawings - Foundatior	0	4/13/26 7:00 AM A	4/17/26 5:00 PM A	
AEC131141-0	Model - Foundations - All CTG's	0	4/6/26 7:00 AM A	5/4/26 5:00 PM A	
AEC130541-0	Prep & Check Structural Static Calculation - Foundation - All CT(	0	3/16/26 7:00 AM A	5/8/26 5:00 PM A	
AEC131141-0	Prep & Check & IDR - Foundation Drawings - All CTG's	0	5/5/26 7:00 AM A	6/3/26 5:00 PM A	
AEC130541-1	Establish - PO w/Hopper for Structural Dynamic Analysis - Founc	0	5/26/26 7:00 AM A	6/9/26 5:00 PM A	
AEC131141-1	IDR - Structural Drawings - All CTG's	0	6/15/26 7:00 AM A	6/22/26 5:00 PM A	
AEC130541-0	Prep & Check & Issue for Client Review Structural Dynamic Anal	1	6/22/26 7:00 AM A	10/12/26 5:00 PM	0
AEC131141-1	Address IDR - Comments & Issue for Client Review Foundation	1	10/12/26 7:00 AM	10/12/26 5:00 PM	32
AEC130541-1	AESI Review of Dynamic Analysis - All CTG's	10	10/16/26 7:00 AM	10/29/26 5:00 PM	0
AEC130541-1	AESI Comments Incorporated & analysis issued for CR - All CTC	10	10/30/26 7:00 AM	11/13/26 5:00 PM	0
AEC131141-2	Client Review - Structural Drawings - Foundation - All CTG's	15	10/30/26 7:00 AM	11/20/26 5:00 PM	19
AEC130541-2	Client Review - Dynamic Analysis - All CTG's	14	11/16/26 7:00 AM	12/4/26 5:00 PM	0
AEC130541-2	Client Comments incorporated & Dynamic Analysis Issued Final	10	12/7/26 7:00 AM	12/18/26 5:00 PM	0

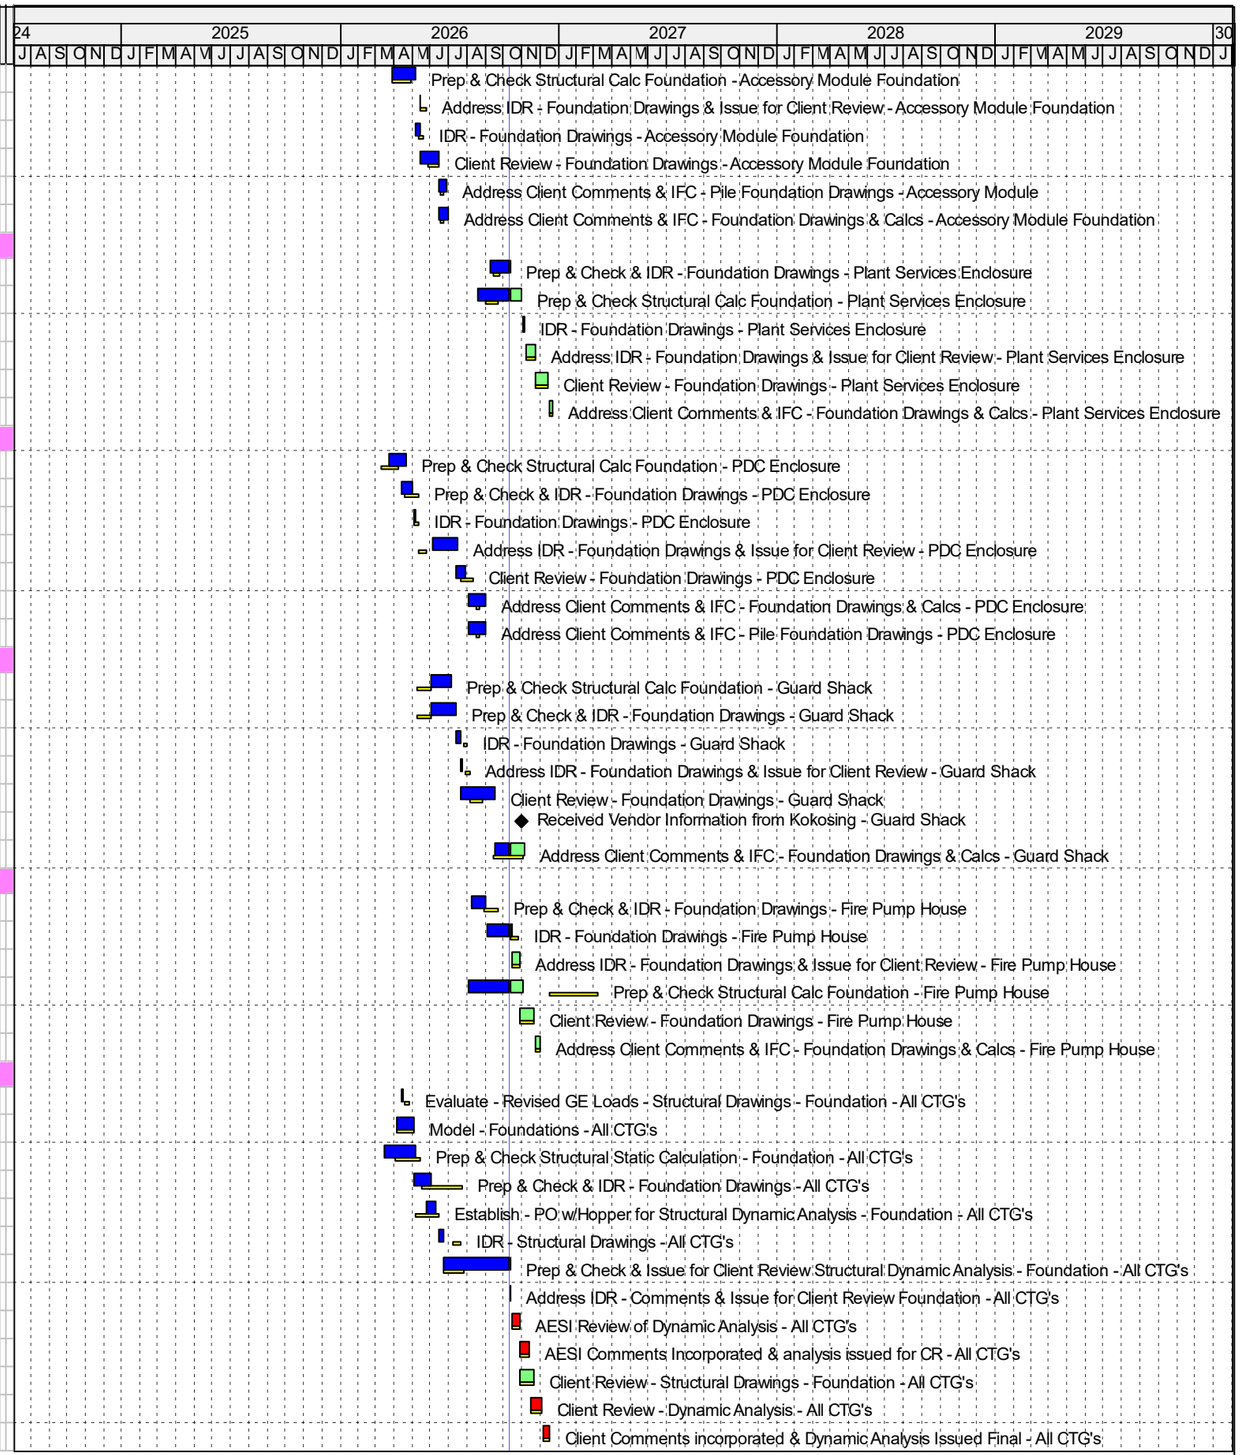

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC131141-2	Address Client Comments & IFC - Structural Drawings & Calcs -	5	12/21/26 7:00 AM	12/29/26 5:00 PM	34
AEC131141-4	Address Client Comments & IFC - Pile Foundation Drawings - Al	5	12/21/26 7:00 AM	12/29/26 5:00 PM	0
BH CNN-KPJV-MAST-LIVE,03,05,01,01,46 ENG - Structural - Calcs/Foundation Drawings - CT Wastewater Sumps					
AEC131122-0	Prep & Check & IDR - Foundation Drawings - CT Wastewater Su	0	4/20/26 7:00 AM A	6/3/26 5:00 PM A	
AEC130522-0	Prep & Check Structural Calculation - Foundation - CT Wastewa	0	4/9/26 7:00 AM A	6/12/26 5:00 PM A	
AEC131122-1	IDR - Structural Drawings - CT Wastewater Sump	0	6/4/26 7:00 AM A	6/15/26 5:00 PM A	
AEC131122-1	Address IDR - Comments & Issue for Client Review Foundation	0	6/16/26 7:00 AM A	6/18/26 5:00 PM A	
AEC131122-2	Client Review - Structural Drawings - Foundation - CT Wastewat	0	6/18/26 7:00 AM A	7/2/26 5:00 PM A	
AEC131122-2	Address Client Comments & IFC - Structural Drawings & Calcs -	0	7/6/26 7:00 AM A	7/30/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,47 ENG - Structural - Calcs/Foundation Drawings - Water Wash Skid					
AEC130524-0	Prep & Check Structural Calculation - Foundation - Water Wash	0	5/4/26 7:00 AM A	5/22/26 5:00 PM A	
AEC131124-0	Prep & Check & IDR - Foundation Drawings - Water Wash Skid	0	5/4/26 7:00 AM A	6/3/26 5:00 PM A	
AEC131124-1	IDR - Structural Drawings - Water Wash Skid	0	6/4/26 7:00 AM A	6/17/26 5:00 PM A	
AEC131124-1	Address IDR - Comments & Issue for Client Review Foundation	0	6/18/26 7:00 AM A	6/22/26 5:00 PM A	
AEC131124-2	Client Review - Structural Drawings - Foundation - Water Wash	0	6/22/26 7:00 AM A	6/29/26 5:00 PM A	
AEC131124-2	Address Client Comments & IFC - Structural Drawings & Calcs -	0	6/29/26 7:00 AM A	6/30/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,48 ENG - Structural - Calcs/Foundation Drawings - Wastewater Collection Sump					
AEC130526-0	Prep & Check Structural Calculation - Foundation - Wastewater	0	7/7/26 7:00 AM A	8/10/26 5:00 PM A	
AEC131126-0	Prep & Check & IDR - Foundation Drawings - Wastewater Collec	0	7/7/26 7:00 AM A	8/10/26 5:00 PM A	
AEC131126-1	IDR - Structural Drawings - Wastewater Collection Sump	0	8/11/26 7:00 AM A	8/24/26 5:00 PM A	
AEC131126-1	Address IDR - Comments & Issue for Client Review Foundation	0	8/25/26 7:00 AM A	8/27/26 5:00 PM A	
AEC131126-2	Client Review - Structural Drawings - Foundation - Wastewater C	0	8/28/26 7:00 AM A	9/11/26 5:00 PM A	
AEC131126-2	Address Client Comments & IFC - Structural Drawings & Calcs -	0	9/14/26 7:00 AM A	10/6/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,24 ENG - Structural - Calcs/Foundation Drawings - GSU Transformers					
AEC130523-0	Prep & Check Structural Calc Foundation - GSU (Generator Ste	0	7/22/26 7:00 AM A	8/26/26 5:00 PM A	
AEC131123-0	Prep & Check & IDR - Foundation Drawings - GSU (Generator S	0	8/17/26 7:00 AM A	8/26/26 5:00 PM A	
AEC131123-1	IDR - Foundation Drawings - GSU (Generator Step Up) Transfor	0	8/27/26 7:00 AM A	9/8/26 5:00 PM A	
AEC131123-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	9/9/26 7:00 AM A	9/11/26 5:00 PM A	
AEC131123-2	Client Review - Foundation Drawings - GSU (Generator Step Up	0	9/14/26 7:00 AM A	9/25/26 5:00 PM A	
AEC131123-2	Address Client Comments & IFC - Foundation Drawings - GSU (	5	10/12/26 7:00 AM	10/16/26 5:00 PM	131
AEC131123-3	Address Client Comments & IFC - Pile Foundation Drawings - G	5	10/12/26 7:00 AM	10/16/26 5:00 PM	2
BH CNN-KPJV-MAST-LIVE,03,05,01,01,39 ENG - Structural - Calcs/Foundation Drawings - CTG Stairs/Inlet Bleed Heat Supports					
AEC131165-0	Model - CTG Stairs/Inlet Bleed Heat Supports	0	5/18/26 7:00 AM A	6/8/26 5:00 PM A	
AEC131165-0	Prep & Check & IDR - Foundation Drawings - CTG Stairs/Inlet Bl	1	9/2/26 7:00 AM A	10/12/26 5:00 PM	51
AEC131165-1	IDR - Foundation Drawings - CTG Stairs/Inlet Bleed Heat Suppo	5	10/13/26 7:00 AM	10/19/26 5:00 PM	51
AEC131165-1	Address IDR - Foundation Drawings & Issue for Client Review - (	10	10/20/26 7:00 AM	11/2/26 5:00 PM	51
AEC131165-2	Client Review - Foundation Drawings - CTG Stairs/Inlet Bleed He	15	11/3/26 7:00 AM	11/24/26 5:00 PM	51
AEC131165-2	Address Client Comments & IFC - Foundation Drawings - CTG S	5	11/25/26 7:00 AM	12/2/26 5:00 PM	51
AEC131165-3	Address Client Comments & IFC - Pile Foundation Drawings - C	5	11/25/26 7:00 AM	12/2/26 5:00 PM	100
BH CNN-KPJV-MAST-LIVE,03,05,01,01,42 ENG - Structural - Calcs/Foundation Drawings - Ammonia Flow Control Unit					
AEC131189-0	Model - Ammonia Flow Control	0	4/30/26 7:00 AM A	6/11/26 5:00 PM A	
AEC131189-0	Prep & Check & IDR - Foundation Drawings - Ammonia Flow Co	0	5/12/26 7:00 AM A	7/28/26 5:00 PM A	
AEC131189-1	IDR - Foundation Drawings - Ammonia Flow Control	0	7/28/26 7:00 AM A	8/3/26 5:00 PM A	
AEC131189-1	Address IDR - Foundation Drawings & Issue for Client Review - A	0	8/4/26 7:00 AM A	8/14/26 5:00 PM A	
AEC131189-2	Client Review - Foundation Drawings - Foundation - Ammonia Fl	0	8/14/26 7:00 AM A	9/8/26 5:00 PM A	
AEC131189-2	Address Client Comments & IFC - Foundation Drawings - Ammo	2	9/9/26 7:00 AM A	10/13/26 5:00 PM	134
AEC131189-3	Address Client Comments & IFC - Pile Foundation Drawings - A	4	9/9/26 7:00 AM A	10/15/26 5:00 PM	15
BH CNN-KPJV-MAST-LIVE,03,05,01,01,30 ENG - Structural - Calcs/Foundation Drawings - GE Inlet Stair Tower					
AEC130512-0	Prep & Check Structural Calc Foundation - GE Inlet Stair Tower	0	6/22/26 7:00 AM A	7/2/26 5:00 PM A	
AEC131112-0	Prep & Check & IDR - Foundation Drawings - GE Inlet Stair Tow	0	6/22/26 7:00 AM A	7/7/26 5:00 PM A	
AEC131112-1	IDR - Foundation Drawings - GE Inlet Stair Tower	0	7/8/26 7:00 AM A	7/15/26 5:00 PM A	




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone


Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC131112-1	Address IDR - Foundation Drawings & Issue for Client Review - (	0	7/16/26 7:00 AM A	7/23/26 5:00 PM A	
AEC131112-2	Client Review - Foundation Drawings - GE Inlet Stair Tower	0	7/23/26 7:00 AM A	8/13/26 5:00 PM A	
AEC131112-2	Address Client Comments & IFC - Foundation Drawings - GE Inl	0	8/14/26 7:00 AM A	8/31/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,05,01,01,36 ENG - Structural - Calcs/Foundation Drawings - Administration Bldg. Aux. Transformer					
AEC130544-0	Prep & Check & IDR - Foundation Calc. - Aux Transformer - Adm	0	8/14/26 7:00 AM A	8/27/26 5:00 PM A	
AEC131144-0	Prep & Check & IDR - Foundation Drawings - Aux Transformer -	0	8/14/26 7:00 AM A	8/28/26 5:00 PM A	
AEC131144-1	IDR - Foundation Drawings - Aux Transformer - Admin Building A	0	8/31/26 7:00 AM A	9/8/26 5:00 PM A	
AEC131144-1	Address IDR - Foundation Drawings & Issue for Client Review - /	0	9/8/26 7:00 AM A	9/11/26 5:00 PM A	
AEC131144-2	Client Review - Foundation Drawings - Aux Transformer - Admin	0	9/11/26 7:00 AM A	9/28/26 5:00 PM A	
AEC131144-2	Address Client Comments & IFC - Foundation Drawings - Aux Tr	4	9/29/26 7:00 AM A	10/15/26 5:00 PM	132
BH CNN-KPJV-MAST-LIVE,03,05,01,01,37 ENG - Structural - Calcs/Foundation Drawings - Plant Services Auxiliary Transformer					
AEC131146-0	Prep & Check & IDR - Foundation Drawings - Aux Transformer -	0	8/10/26 7:00 AM A	8/21/26 5:00 PM A	
AEC131146-1	IDR - Foundation Drawings - Aux Transformer - Plant Services (C	0	8/24/26 7:00 AM A	9/2/26 5:00 PM A	
AEC130546-0	Prep & Check & IDR - Foundation Calc. - Aux Transformer - Plar	0	8/27/26 7:00 AM A	9/8/26 5:00 PM A	
AEC131146-1	Address IDR - Foundation Drawings & Issue for Client Review - /	0	9/3/26 7:00 AM A	9/10/26 5:00 PM A	
AEC131146-2	Client Review - Foundation Drawings - Aux Transformer - Plant S	0	9/11/26 7:00 AM A	9/28/26 5:00 PM A	
AEC131146-2	Address Client Comments & IFC - Foundation Drawings - Aux Tr	5	10/12/26 7:00 AM	10/16/26 5:00 PM	131
BH CNN-KPJV-MAST-LIVE,03,05,01,01,40 ENG - Structural - Calcs/Foundation Drawings - Pipe Support Sonotube					
AEC130551-0	Prep & Check & IDR - Foundation Calc. - Pipe Support Sonotub	10	10/12/26 7:00 AM	10/23/26 5:00 PM	86
AEC131151-0	Prep & Check & IDR - Foundation Drawings - Pipe Support Son	10	10/26/26 7:00 AM	11/6/26 5:00 PM	86
AEC131151-1	IDR - Foundation Drawings - Pipe Support Sonotube	5	11/9/26 7:00 AM	11/16/26 5:00 PM	86
AEC131151-1	Address IDR - Foundation Drawings & Issue for Client Review - I	5	11/17/26 7:00 AM	11/23/26 5:00 PM	86
AEC131151-2	Client Review - Foundation Drawings - Pipe Support Sonotube	15	11/24/26 7:00 AM	12/15/26 5:00 PM	86
AEC131151-2	Address Client Comments & IFC - Foundation Drawings - Pipe S	5	12/16/26 7:00 AM	12/22/26 5:00 PM	86
BH CNN-KPJV-MAST-LIVE,03,01 ENG - Mechanical					
BH CNN-KPJV-MAST-LIVE,03,01,03 ENG - Mechanical - Equipment/Line Sizing Calculations					
BH CNN-KPJV-MAST-LIVE,03,01,03,01 ENG - Mechanical - Equipment/Line Sizing Calculations - Fire Protection System					
AEC150563-90	Prep & Check & Issue Rev. A for Client Review - Mech. Calc - Fi	0	4/6/26 7:00 AM A	6/5/26 5:00 PM A	
AEC150563-92	Client Review - Mech. Calc - Fire Protection System	0	7/2/26 7:00 AM A	7/13/26 5:00 PM A	
AEC150563-99	Update & Issue For Rev. 0 - Mech. Calc - Fire Protection Systen	0	7/14/26 7:00 AM A	8/13/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,02 ENG - Mechanical - Equipment/Line Sizing Calculations - Insulation Thickness					
AEC150570-90	Prep & Check & Issue for Client Review - Mech. Calc- Insulation	0	4/1/26 7:00 AM A	4/6/26 5:00 PM A	
AEC150570-95	Client Review - Mech. Calc- Insulation Thickness	0	4/6/26 7:00 AM A	4/20/26 5:00 PM A	
AEC150570-99	Address Client Review Comments & Issue Rev. 0 - Mech. Calc-	0	4/20/26 7:00 AM A	4/27/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,03 ENG - Mechanical - Equipment/Line Sizing Calculations - Orifice Sizing (Fuel Oil Warming Pipe)					
AEC150571-90	Prep & Check & Issue Rev. A - Mech. Calc - Orifice Sizing (Fuel (	0	4/17/26 7:00 AM A	4/17/26 5:00 PM A	
AEC150571-99	Update & Issue For Rev. 0 - Mech. Calc - Orifice Sizing (Fuel Oil	0	4/17/26 7:00 AM A	4/17/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,23 ENG - Mechanical - Equipment/Line Sizing Calculations - Orifice Sizing (Demin Warming Pipe)					
AEC150572-90	Prep & Check Issue For Rev. A - Mech. Calc - Orifice Sizing (Der	0	4/17/26 7:00 AM A	4/17/26 5:00 PM A	
AEC150572-99	Update & Issue For Rev. 0 - Mech. Calc - Orifice Sizing (Demin \	0	4/17/26 7:00 AM A	4/17/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,04 ENG - Mechanical - Equipment/Line Sizing Calculations - Service Water Pump					
AEC150508-90	Prep & Check & Issue Rev. A - Mech. Calc - Service Water Pum	0	4/6/26 7:00 AM A	5/1/26 5:00 PM A	
AEC150508-99	Update & Issue For Rev. 0 - Mech. Calc - Service Water Pump	0	5/11/26 7:00 AM A	6/8/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,05 ENG - Mechanical - Equipment/Line Sizing Calculations - HVAC - A295 LF/WI Skid Enclosure					
AEC150510-90	Prep & Check & Issue for Client Review - Mech. Calc - HVAC A2	0	6/22/26 7:00 AM A	7/23/26 5:00 PM A	
AEC150510-95	Client Review - Mech. Calc- HVAC A295 LF/WI Skid Enclosure	0	7/23/26 7:00 AM A	8/13/26 5:00 PM A	
AEC150510-99	Address Client Review Comments & Issue Rev. 0 - Mech. Calc-	0	8/14/26 7:00 AM A	8/25/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,06 ENG - Mechanical - Equipment/Line Sizing Calculations - Fuel Unloading Pump					
AEC150503-90	Prep & Check & Issue Rev. A - Mech. Calc - Fuel Unloading Pun	0	4/20/26 7:00 AM A	5/4/26 5:00 PM A	
AEC150503-99	Update & Issue For Rev. 0 - Mech. Calc - Fuel Unloading Pump	0	5/4/26 7:00 AM A	5/8/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,07 ENG - Mechanical - Equipment/Line Sizing Calculations - Fuel Oil Line Sizing					

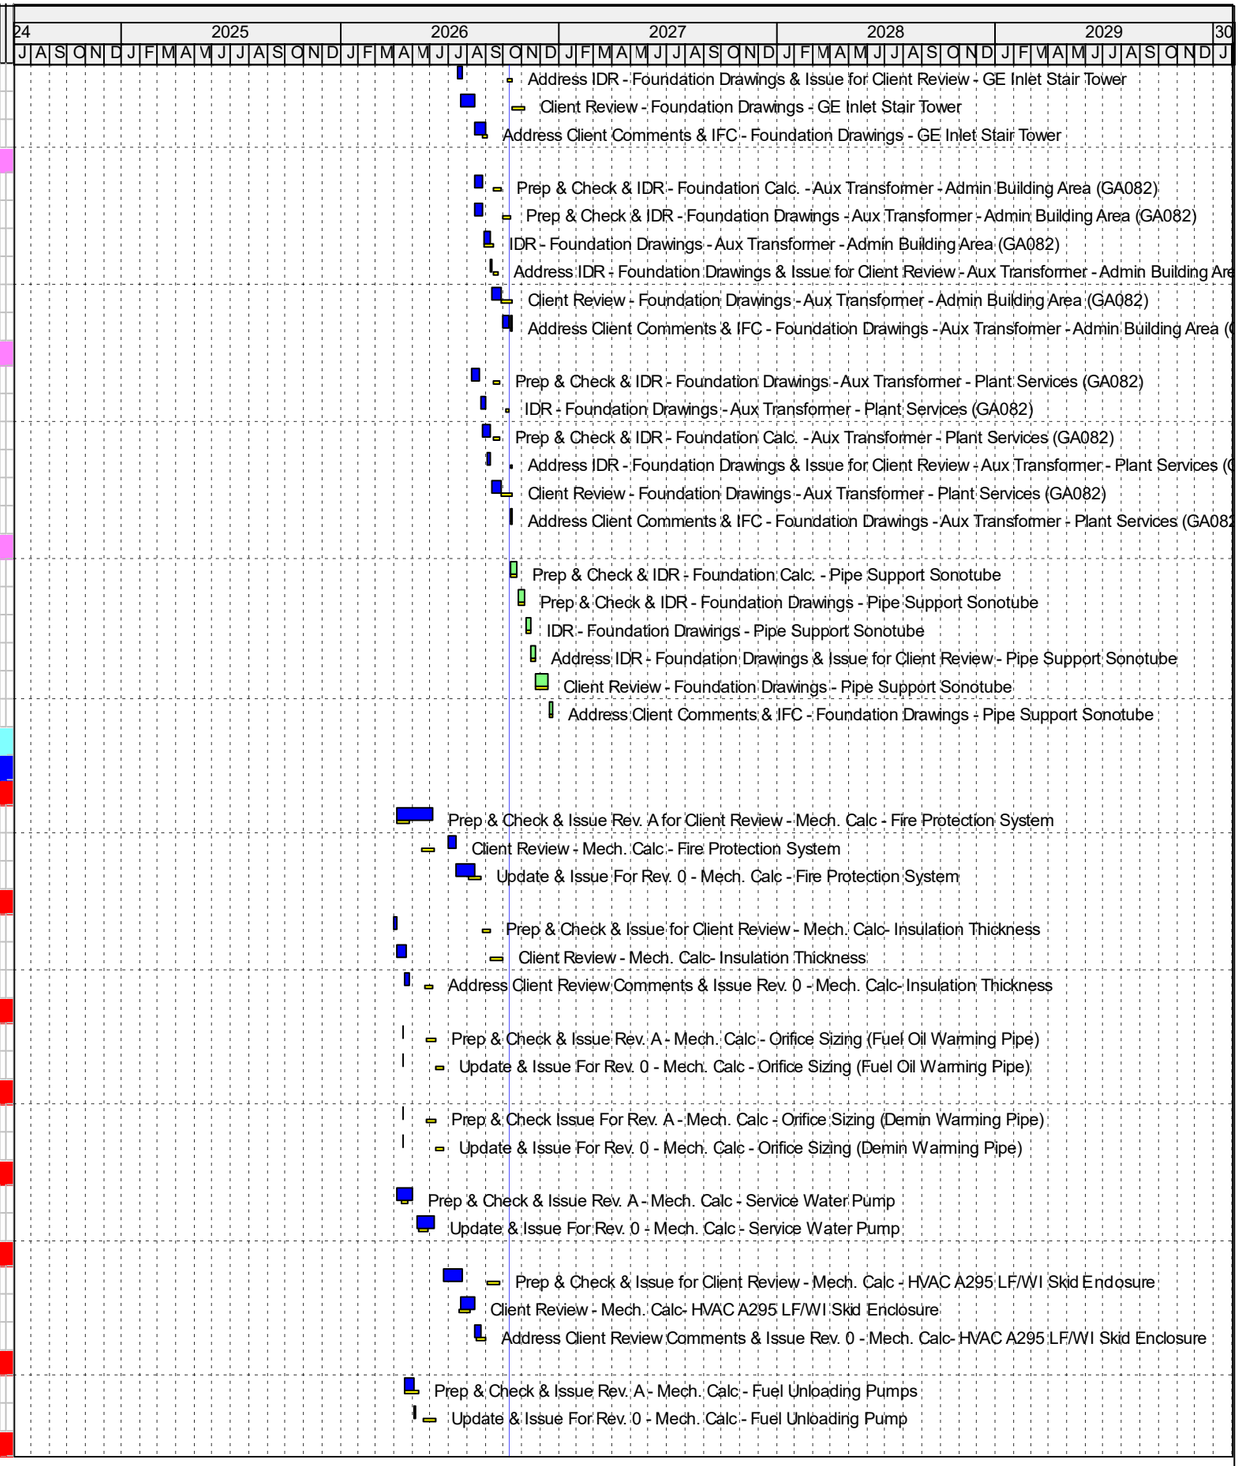
24
2025
2026
2027
2028
2029
30
J A S O N D J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC150562-90	Prep & Check & Issue Rev. A - Mech. Calc - Fuel Oil Line & War	0	4/20/26 7:00 AM A	5/1/26 5:00 PM A	
AEC150562-99	Update & Issue For Rev. 0 - Mech. Calc - Fuel Oil Line & Warmi	0	5/4/26 7:00 AM A	5/6/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,08 ENG - Mechanical - Equipment/Line Sizing Calculations - Fuel Gas System					
AEC150568-90	Prep & Check & Issue Rev. A - Mech. Calc - Fuel Gas System	0	5/4/26 7:00 AM A	5/18/26 5:00 PM A	
AEC150568-99	Update & Issue For Rev. 0 - Mech. Calc - Fuel Gas System	0	5/19/26 7:00 AM A	6/4/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,24 ENG - Mechanical - Equipment/Line Sizing Calculations - Fuel Gas Relief Valve Sizing					
AEC150588-90	Prep & Check & Issue Rev. A - Mech. Calc - Fuel Gas Relief Val	0	8/31/26 7:00 AM A	9/18/26 5:00 PM A	
AEC150588-99	Update & Issue For Rev. 0 - Mech. Calc - Fuel Gas Relief Valve	10	10/12/26 7:00 AM	10/23/26 5:00 PM	517
BH CNN-KPJV-MAST-LIVE,03,01,03,09 ENG - Mechanical - Equipment/Line Sizing Calculations - Compressed Air					
AEC150501-90	Prep & Check & Issue Rev. A for Client Review - Mech. Calc - Cc	0	4/6/26 7:00 AM A	4/29/26 5:00 PM A	
AEC150501-92	Client Review - Rev. A - Mech. Calc - Compressed Air	0	4/30/26 7:00 AM A	5/20/26 5:00 PM A	
AEC150501-99	Update & Issue For Rev. 0 - Mech. Calc - Compressed Air	0	5/21/26 7:00 AM A	6/5/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,10 ENG - Mechanical - Equipment/Line Sizing Calculations - Sanitary System					
AEC150569-90	Prep & Check & Issue Rev. A - Mech. Calc - Sanitary System	0	5/18/26 7:00 AM A	7/9/26 5:00 PM A	
AEC150569-99	Update & Issue For Rev. 0 - Mech. Calc - Sanitary System	0	7/27/26 7:00 AM A	8/4/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,11 ENG - Mechanical - Equipment/Line Sizing Calculations - Demin Water Line Sizing					
AEC150504-90	Prep & Check & Issue Rev. A - Mech. Calc - Demin Water Line S	0	4/20/26 7:00 AM A	5/8/26 5:00 PM A	
AEC150504-99	Update & Issue For Rev. 0 - Mech. Calc - Demin Water Line Siz	0	5/11/26 7:00 AM A	6/5/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,21 ENG - Mechanical - Equipment/Line Sizing Calculations - Demin Water Distribution Pump Sizing					
AEC150544-90	Prep & Check & Issue Rev. A - Mech. Calc - Demin Water Distrit	0	4/6/26 7:00 AM A	5/1/26 5:00 PM A	
AEC150544-99	Update & Issue For Rev. 0 - Mech. Calc - Demin Water Distribut	0	5/4/26 7:00 AM A	6/5/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,12 ENG - Mechanical - Equipment/Line Sizing Calculations - Compressed Gas (CO2/N2/H2)					
AEC150567-90	Prep & Check & Issue Rev. A - Mech. Calc - Compressed Gas (H	0	5/4/26 7:00 AM A	5/22/26 5:00 PM A	
AEC150567-99	Update & Issue For Rev. 0 - Mech. Calc - Compressed Gases (H	0	5/26/26 7:00 AM A	7/10/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,13 ENG - Mechanical - Equipment/Line Sizing Calculations - Closed Cooling Water System					
AEC150565-90	Prep & Check & Issue For Rev. A - Mech. Calc - Closed Cooling	0	5/11/26 7:00 AM A	5/22/26 5:00 PM A	
AEC150565-99	Update & Issue For Rev. 0 - Mech. Calc - Closed Cooling Water	0	5/26/26 7:00 AM A	6/1/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,14 ENG - Mechanical - Equipment/Line Sizing Calculations - Water Wash System					
AEC150566-90	Prep & Check & Issue Rev. A - Mech. Calc - Water Wash Syster	0	5/18/26 7:00 AM A	5/22/26 5:00 PM A	
AEC150566-99	Update & Issue For Rev. 0 - Mech. Calc - Water Wash System	0	5/26/26 7:00 AM A	6/30/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,15 ENG - Mechanical - Equipment/Line Sizing Calculations - Potable Water Line Sizing					
AEC150561-90	Prep & Check & Issue Rev. A - Mech. Calc - Potable Water Line	0	5/4/26 7:00 AM A	5/21/26 5:00 PM A	
AEC150561-99	Update & Issue For Rev. 0 - Mech. Calc - Potable Water Line Si	0	5/22/26 7:00 AM A	6/19/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,25 ENG - Mechanical - Equipment/Line Sizing Calculations - Potable Water Equipment (Hydropneumatic Tank					
AEC150589-90	Prep & Check & Issue Rev. A - Mech. Calc - Potable Water Equi	0	5/11/26 7:00 AM A	7/14/26 5:00 PM A	
AEC150589-99	Update & Issue For Rev. 0 - Mech. Calc - Potable Water Equipn	0	7/15/26 7:00 AM A	9/4/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,22 ENG - Mechanical - Equipment/Line Sizing Calculations - Ammonia Storage & Transfer Equipment					
AEC150542-90	Prep & Check & Issue Rev. A - Mech. Calc- Ammonia Storage &	0	4/20/26 7:00 AM A	5/18/26 5:00 PM A	
AEC150542-99	Update & Issue For Rev. 0 - Mech. Calc - Ammonia Storage & T	0	5/18/26 7:00 AM A	7/14/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,16 ENG - Mechanical - Equipment/Line Sizing Calculations - Wastewater & Submersible Pumps					
AEC150502-90	Prep & Check & Issue Rev. A - Mech. Calc- Wastewater & Subm	0	7/27/26 7:00 AM A	8/7/26 5:00 PM A	
AEC150502-99	Update & Issue For Rev. 0 - Mech. Calc - Wastewater & Subme	0	8/10/26 7:00 AM A	8/14/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,17 ENG - Mechanical - Equipment/Line Sizing Calculations - Mechanical - HVAC Admin Bldg.					
AEC150509-90	Prep & Check & Issue for Client Review - Mech. Calc - HVAC Ad	0	7/1/26 7:00 AM A	7/23/26 5:00 PM A	
AEC150509-95	Client Review - Mech. Calc- HVAC Admin Building	0	7/23/26 7:00 AM A	8/10/26 5:00 PM A	
AEC150509-99	Address Client Review Comments & Issue Rev. 0 - Mech. Calc-	0	8/14/26 7:00 AM A	9/11/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,18 ENG - Mechanical - Equipment/Line Sizing Calculations - HVAC Plant Service Enclosure					
AEC150511-90	Prep & Check & Issue for Client Review - Mech. Calc - HVAC Pla	0	7/6/26 7:00 AM A	7/23/26 5:00 PM A	
AEC150511-95	Client Review - Mech. Calc- HVAC Plant Services Enclosure	0	7/23/26 7:00 AM A	8/13/26 5:00 PM A	
AEC150511-10	Address Client Review Comments & Issue Rev. 0 - Mech. Calc-	0	8/13/26 7:00 AM A	9/1/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,19 ENG - Mechanical - Equipment/Line Sizing Calculations - HVAC Liquid Fuel Pump Enclosure					
AEC150513-90	Prep & Check & Issue for Client Review - Mech. Calc - HVAC Lic	0	5/26/26 7:00 AM A	7/23/26 5:00 PM A	

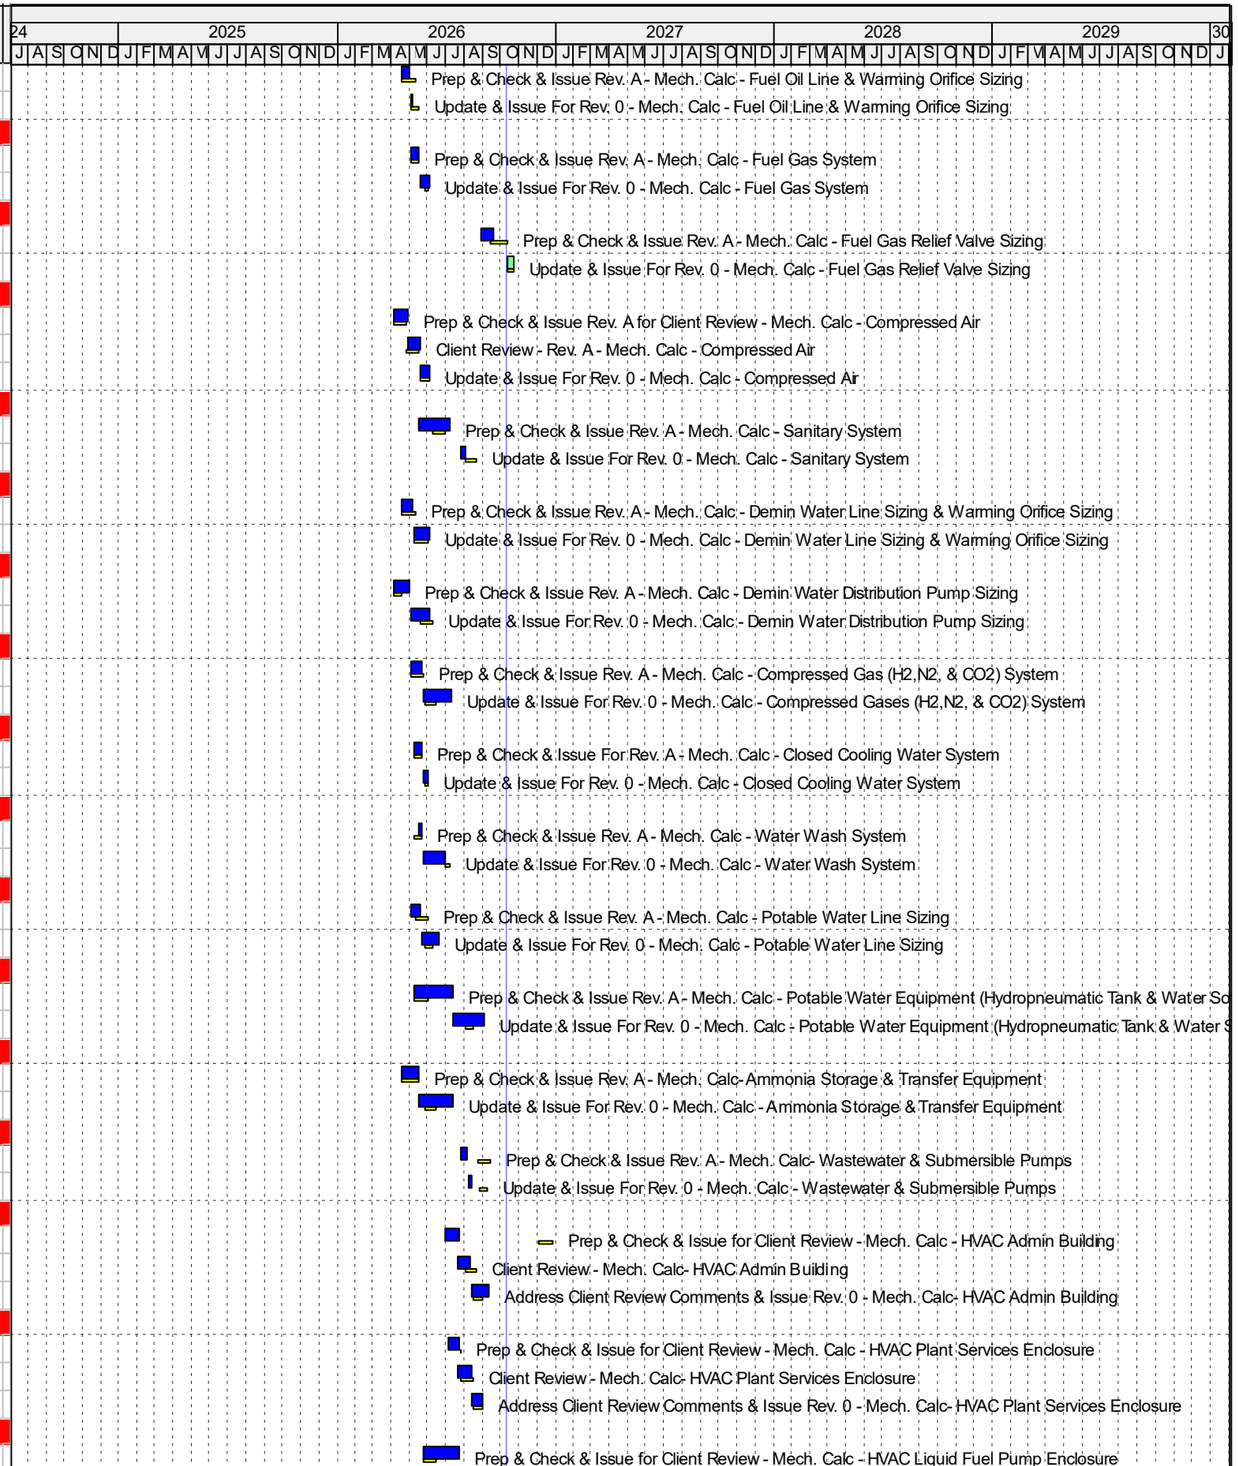


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC150513-95	Client Review - Mech. Calc- HVAC Liquid Fuel Pump Enclosure	0	7/23/26 7:00 AM A	8/13/26 5:00 PM A	
AEC150513-99	Address Client Review Comments & Issue Rev. 0 - Mech. Calc-	0	8/14/26 7:00 AM A	8/31/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,03,20 ENG - Mechanical - Equipment/Line Sizing Calculations - HVAC Fuel Gas Compressor Enclosure					
AEC150514-90	Prep & Check & Issue for Client Review - Mech. Calc - Fuel Gas	0	7/13/26 7:00 AM A	7/29/26 5:00 PM A	
AEC150514-95	Client Review - Mech. Calc- HVAC Fuel Gas Compressor Enclos	0	7/30/26 7:00 AM A	8/14/26 5:00 PM A	
AEC150514-99	Address Client Review Comments & Issue Rev. 0 - Mech. Calc-	0	8/17/26 7:00 AM A	9/2/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09 ENG - Mechanical - Specifications					
BH CNN-KPJV-MAST-LIVE,03,01,09,09 ENG - Mechanical - Specifications - Site Utility Specification					
AEC150800-05	Prep & Check & IDR - Spec. - Site Utilities Spec.	0	3/9/26 7:00 AM A	3/11/26 5:00 PM A	
AEC150800-20	IDR - Site Utilities Spec.	0	3/12/26 7:00 AM A	3/24/26 5:00 PM A	
AEC150800-25	Address Comments & Issue for Client Review - Mech Spec - Sit	0	3/25/26 7:00 AM A	3/31/26 5:00 PM A	
AEC150800-30	Client Review - Spec. - Site Utilities	0	4/1/26 7:00 AM A	4/20/26 5:00 PM A	
AEC150800-35	Address Client Comments & IFU - Site Utilities Spec.	0	4/21/26 7:00 AM A	4/28/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,02 ENG - Mechanical - Specifications - Air Compressors/Receivers/&Dryers					
AEC150801-05	Prep & Check & IDR - Spec. - Air Compressors/Receivers & Drye	0	4/13/26 7:00 AM A	5/1/26 5:00 PM A	
AEC150801-20	IDR - Spec. - Air Compressors/Receivers & Dryers	0	5/1/26 7:00 AM A	5/7/26 5:00 PM A	
AEC150801-25	Address Comments & Issue for Client Review - Mech Spec - Air	0	5/8/26 7:00 AM A	7/2/26 5:00 PM A	
AEC150801-30	Client Review - Spec. - Air Compressors/Receivers & Dryers	0	7/2/26 7:00 AM A	7/13/26 5:00 PM A	
AEC150801-35	Address Client Comments & Finalize Spec. - Air Compressors/R	0	7/14/26 7:00 AM A	7/17/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,15 ENG - Mechanical - Specifications - Fuel Gas Valves					
AEC150804-05	Prep & Check & IDR - Spec. - Fuel Gas Valves	0	4/1/26 7:00 AM A	4/10/26 5:00 PM A	
AEC150804-20	IDR - Spec. - Fuel Gas Valves	0	4/13/26 7:00 AM A	4/17/26 5:00 PM A	
AEC150804-25	Address Comments & Issue for Client Review - Mech Spec - Fu	0	4/17/26 7:00 AM A	5/22/26 5:00 PM A	
AEC150804-30	Client Review - Spec. - Fuel Gas Valves	0	5/22/26 7:00 AM A	6/8/26 5:00 PM A	
AEC150804-35	Address Client Comments & Finalize Spec. - Fuel Gas Valves	0	6/9/26 7:00 AM A	6/18/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,19 ENG - Mechanical - Specifications - Fuel Gas Knockout Drums					
AEC150818-05	Prep & Check & IDR - Spec. - Fuel Gas Knockout Drums	0	3/30/26 7:00 AM A	5/18/26 5:00 PM A	
AEC150818-10	IDR - Spec. - Fuel Gas Knockout Drums	0	5/19/26 7:00 AM A	5/29/26 5:00 PM A	
AEC150818-15	Address Comments & Issue for Client Review - Mech Spec - Fu	0	6/1/26 7:00 AM A	7/9/26 5:00 PM A	
AEC150818-20	Client Review - Spec. - Fuel Gas Knockout Drums	0	7/10/26 7:00 AM A	7/24/26 5:00 PM A	
AEC150818-25	Address Client Comments & Finalize Spec. - Fuel Gas Knockou	0	7/27/26 7:00 AM A	8/4/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,01 ENG - Mechanical - Specifications - Submersible Sump Pumps					
AEC150802-05	Prep & Check & IDR - Submersible Sump Pumps Spec.	0	5/4/26 7:00 AM A	5/20/26 5:00 PM A	
AEC150802-20	IDR - Submersible Sump Pumps Spec.	0	5/20/26 7:00 AM A	5/29/26 5:00 PM A	
AEC150802-25	Address Comments & Issue for Client Review - Submersible Su	0	6/1/26 7:00 AM A	7/10/26 5:00 PM A	
AEC150802-30	Client Review - Submersible Sump Pumps Spec.	0	7/10/26 7:00 AM A	7/24/26 5:00 PM A	
AEC150802-35	Address Client Comments & Finalize Spec. - Submersible Sump	0	7/27/26 7:00 AM A	8/20/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,23 ENG - Mechanical - Specifications - MO Diaphragm Sump Pumps					
AEC150822-05	Prep & Check & IDR - MO Diaphragm Sump Pumps Spec.	0	5/11/26 7:00 AM A	5/20/26 5:00 PM A	
AEC150822-10	IDR - MO Diaphragm Sump Pumps Spec.	0	5/20/26 7:00 AM A	6/19/26 5:00 PM A	
AEC150822-15	Address Comments & Issue for Client Review - MO Diaphragm S	0	7/6/26 7:00 AM A	7/9/26 5:00 PM A	
AEC150822-20	Client Review - Spec. - MO Diaphragm Sump Pumps	0	7/10/26 7:00 AM A	7/13/26 5:00 PM A	
AEC150822-25	Address Client Comments & Finalize Spec. - MO Diaphragm Su	0	7/14/26 7:00 AM A	8/20/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,03 ENG - Mechanical - Specifications - Fuel Oil Unloading Pumps					
AEC150803-05	Prep & Check & IDR - Fuel Oil Unloading Pumps Spec.	0	4/27/26 7:00 AM A	5/7/26 5:00 PM A	
AEC150803-10	IDR - Fuel Oil Unloading Pump Spec.	0	5/7/26 7:00 AM A	5/18/26 5:00 PM A	
AEC150803-15	Address Comments & Issue for Client Review - Fuel Oil Unloadi	0	5/18/26 7:00 AM A	6/11/26 5:00 PM A	
AEC150803-20	Client Review - Fuel Oil Unloading Pumps Spec.	0	6/12/26 7:00 AM A	6/30/26 5:00 PM A	
AEC150803-25	Address Client Comments & Finalize Spec. - Fuel Oil Unloading	0	6/30/26 7:00 AM A	7/2/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,08 ENG - Mechanical - Specifications - Service Water Pumps					
AEC150808-05	Prep & Check & IDR - Service Water Pumps Specs.	0	4/20/26 7:00 AM A	5/1/26 5:00 PM A	

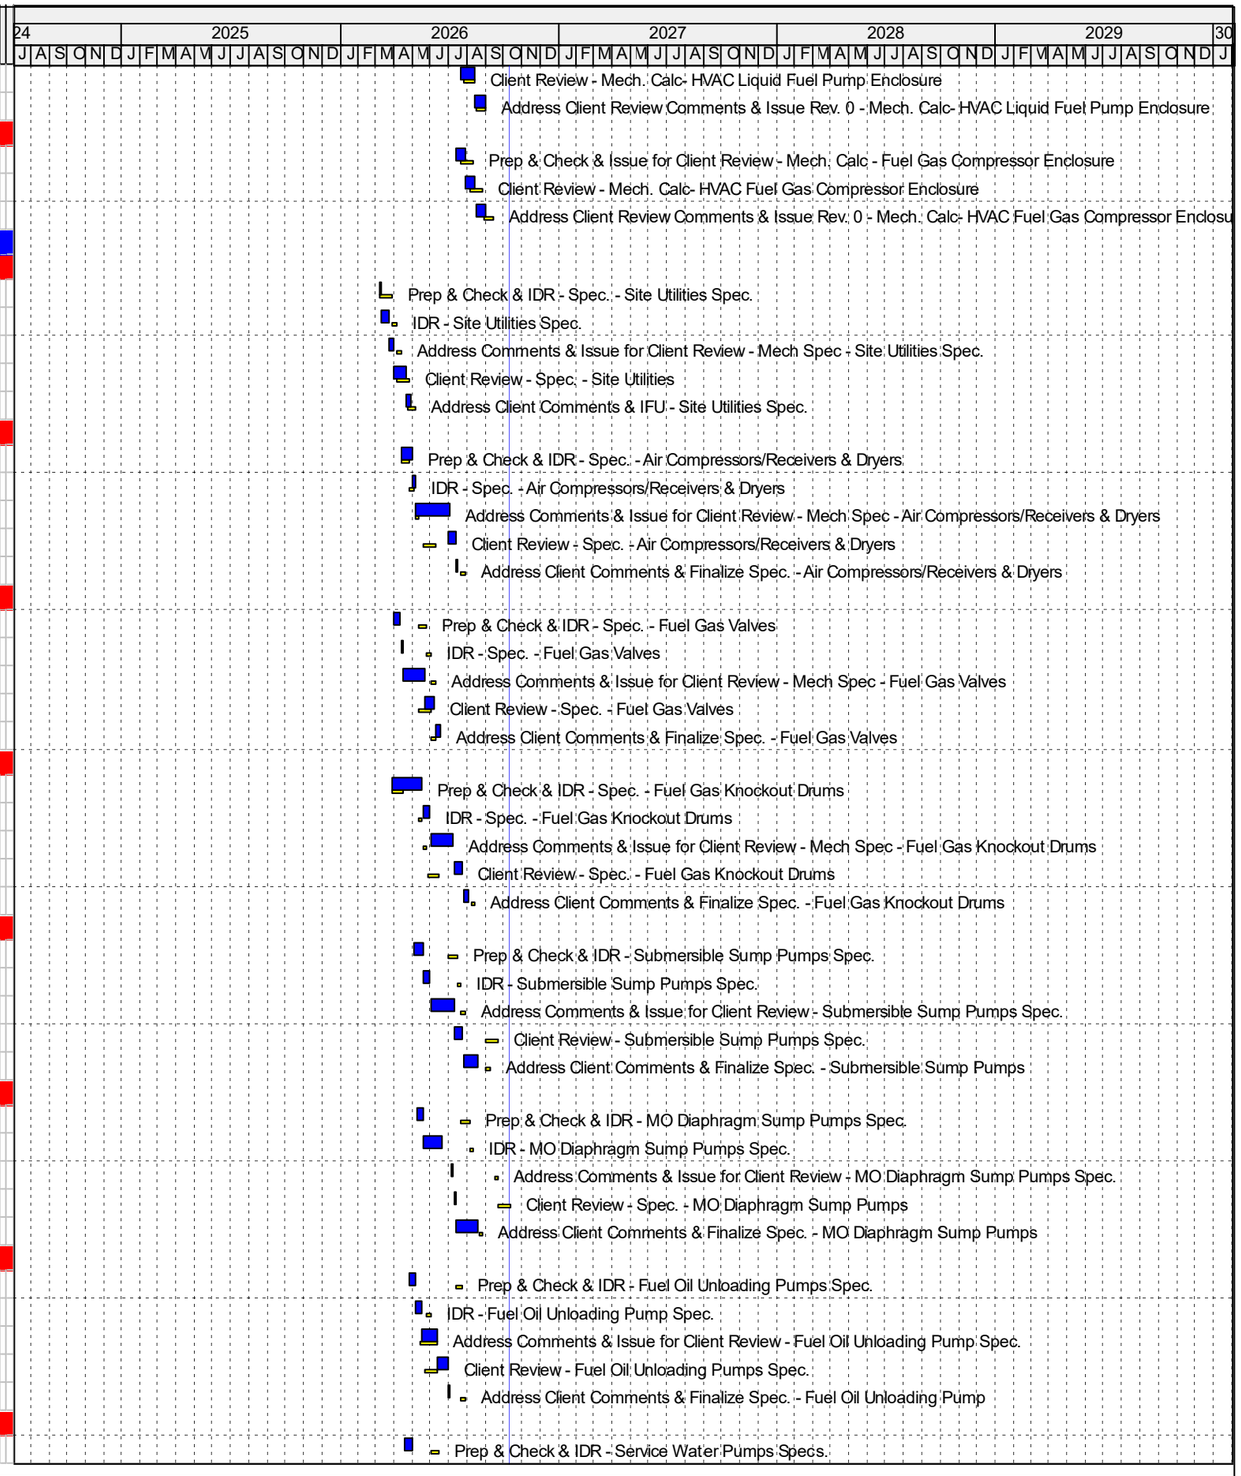


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC150808-20	IDR - Service Water Pumps Spec.	0	5/4/26 7:00 AM A	5/8/26 5:00 PM A	
AEC150808-25	Address Comments & Issue for Client Review - Service Water P	0	5/8/26 7:00 AM A	5/27/26 5:00 PM A	
AEC150808-30	Client Review - Spec. - Service Water Pumps	0	5/28/26 7:00 AM A	6/22/26 5:00 PM A	
AEC150808-35	Address Client Comments & Finalize Spec. - Service Water Pun	0	6/23/26 7:00 AM A	7/13/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,04 ENG - Mechanical - Specifications - Demineralized Water Distribution Pumps					
AEC150827-05	Prep & Check & IDR - Demineralized Water Distribution Pumps	0	4/27/26 7:00 AM A	5/13/26 5:00 PM A	
AEC150827-10	IDR - Demineralized Water Distribution Pumps	0	5/14/26 7:00 AM A	5/21/26 5:00 PM A	
AEC150827-15	Address Comments & Issue for Client Review - Demineralized W	0	5/22/26 7:00 AM A	5/27/26 5:00 PM A	
AEC150827-20	Client Review - Demineralized Water Distribution Pumps	0	5/28/26 7:00 AM A	6/22/26 5:00 PM A	
AEC150827-25	Address Client Comments & Finalize Spec. - Demineralized Wat	0	6/23/26 7:00 AM A	7/13/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,05 ENG - Mechanical - Specifications - Oil Water Separator					
AEC150805-05	Prep & Check & IDR - Oil Water Separator Spec.	0	4/23/26 7:00 AM A	5/7/26 5:00 PM A	
AEC150805-20	IDR - Spec. - Oil Water Separator Spec.	0	5/7/26 7:00 AM A	5/18/26 5:00 PM A	
AEC150805-25	Address Comments & Issue for Client Review - Oil Water Separ	0	5/18/26 7:00 AM A	7/2/26 5:00 PM A	
AEC150805-30	Client Review - Spec. - Oil Water Separator	0	7/2/26 7:00 AM A	7/13/26 5:00 PM A	
AEC150805-35	Address Client Comments & Finalize Spec. - Oil Water Separat	0	8/24/26 7:00 AM A	8/28/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,06 ENG - Mechanical - Specifications - Water Wash/False Start Tanks					
AEC150806-05	Prep & Check & IDR - Water Wash/False Start	0	3/16/26 7:00 AM A	3/19/26 5:00 PM A	
AEC150806-20	IDR - Water Wash/False Start	0	3/20/26 7:00 AM A	3/27/26 5:00 PM A	
AEC150806-25	Address Comments & Issue for Client Review - Water Wash/Fal	0	3/30/26 7:00 AM A	4/13/26 5:00 PM A	
AEC150806-30	Client Review - Water Wash/False Start Tanks	0	4/14/26 7:00 AM A	5/5/26 5:00 PM A	
AEC150806-35	Address Client Comments & Finalize Spec. - Water Wash/False	0	5/6/26 7:00 AM A	6/29/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,16 ENG - Mechanical - Specifications - A/G Shop Fabricated Tank (Fuel Gas Drain Tanks)					
AEC1508066-0	Prep & Check & IDR - A/G Shop Fabricated Tank (Fuel Gas Drai	0	4/1/26 7:00 AM A	4/14/26 5:00 PM A	
AEC1508066-2	IDR - A/G Shop Fabricated Tank (Fuel Gas Drain Tanks) Spec.	0	4/14/26 7:00 AM A	5/15/26 5:00 PM A	
AEC1508066-2	Address Comments & Issue for Client Review - A/G Shop Fabric	0	5/18/26 7:00 AM A	5/22/26 5:00 PM A	
AEC1508066-3	Client Review - A/G Shop Fabricated Tank (Fuel Gas Drain Tanks	0	5/26/26 7:00 AM A	6/15/26 5:00 PM A	
AEC1508066-3	Address Client Comments & Finalize Spec. - A/G Shop Fabricat	0	6/15/26 7:00 AM A	6/19/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,18 ENG - Mechanical - Specifications - Field Erected Tanks					
AEC150816-05	Prep & Check & IDR - Field Erected Tanks	0	3/9/26 7:00 AM A	4/6/26 5:00 PM A	
AEC150816-10	IDR - Field Erected Tanks	0	3/30/26 7:00 AM A	4/10/26 5:00 PM A	
AEC150816-15	Address Comments & Issue for Client Review - Field Erected Ta	0	4/13/26 7:00 AM A	4/28/26 5:00 PM A	
AEC150816-20	Client Review - Field Erected Tanks	0	4/28/26 7:00 AM A	5/19/26 5:00 PM A	
AEC150816-25	Address Client Comments & Finalize Spec. - Field Erected Tank	0	5/20/26 7:00 AM A	6/19/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,11 ENG - Mechanical - Specifications - Safety Showers & Eyewashes					
AEC150809-05	Prep & Check & IDR - Safety Showers & Eyewashes Spec.	0	6/15/26 7:00 AM A	7/31/26 5:00 PM A	
AEC150809-20	IDR - Safety Showers & Eyewashes Spec.	0	8/3/26 7:00 AM A	8/7/26 5:00 PM A	
AEC150809-25	Address Comments & Issue for Client Review - Safety Showers	0	8/17/26 7:00 AM A	9/3/26 5:00 PM A	
AEC150809-30	Client Review - Spec. - Safety Showers & Eyewashes	0	9/3/26 7:00 AM A	9/18/26 5:00 PM A	
AEC150809-35	Address Client Comments & Finalize Spec. - Safety Showers &	0	9/18/26 7:00 AM A	9/22/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,14 ENG - Mechanical - Specifications - Sanitary Lift Station					
AEC150812-05	Prep & Check & IDR - Sanitary Lift Station Spec.	0	7/1/26 7:00 AM A	7/10/26 5:00 PM A	
AEC150812-10	IDR - Sanitary Lift Station Spec.	0	7/13/26 7:00 AM A	7/17/26 5:00 PM A	
AEC150812-15	Address Comments & Issue for Client Review - Sanitary Lift Sta	0	7/20/26 7:00 AM A	8/4/26 5:00 PM A	
AEC150812-20	Client Review - Sanitary Lift Station Spec.	0	8/5/26 7:00 AM A	8/21/26 5:00 PM A	
AEC150812-25	Address Client Comments & Finalize Spec. - Sanitary Lift Statio	0	8/24/26 7:00 AM A	9/22/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,17 ENG - Mechanical - Specifications - Ammonia Storage & Transfer Equipment					
AEC150819-05	Prep & Check & IDR - Ammonia Storage & Transfer Equip. Spe	0	4/13/26 7:00 AM A	5/8/26 5:00 PM A	
AEC150819-10	IDR - Ammonia Storage & Transfer Equip. Spec.	0	5/13/26 7:00 AM A	5/20/26 5:00 PM A	
AEC150819-15	Address Comments & Issue for Client Review - Ammonia Storag	0	5/21/26 7:00 AM A	7/15/26 5:00 PM A	
AEC150819-20	Client Review - Ammonia Storage & Transfer Equip. Spec.	0	7/16/26 7:00 AM A	8/4/26 5:00 PM A	

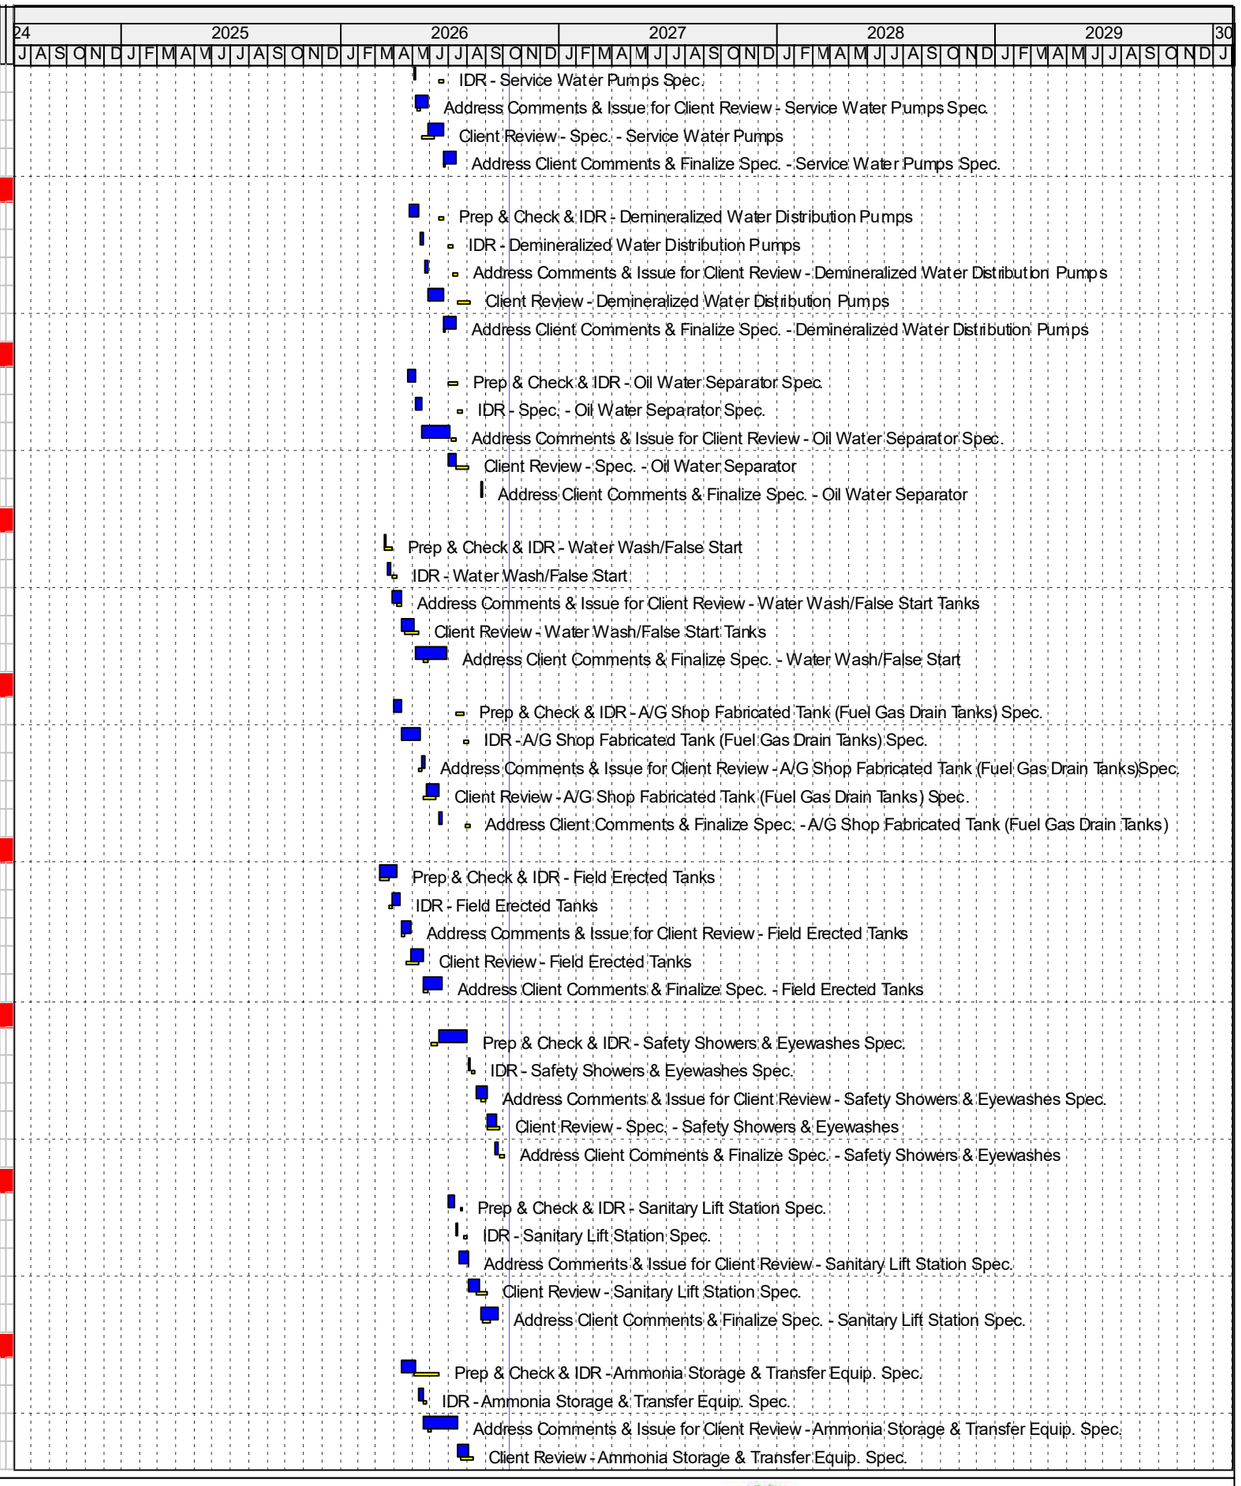

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC150819-25	Address Client Comments & Finalize Spec. - Ammonia Storage	0	8/5/26 7:00 AM A	8/20/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,10 ENG - Mechanical - Specifications - Chemical Pot Feeders					
AEC150844-05	Prep & Check & IDR - Chemical Pot Feeder BOM	0	7/27/26 7:00 AM A	8/31/26 5:00 PM A	
AEC150844-10	IDR - Chemical Pot Feeder BOM	0	9/1/26 7:00 AM A	9/2/26 5:00 PM A	
AEC150844-15	Address Comments & Issue for Client Review - Chemical Pot Fe	0	9/3/26 7:00 AM A	9/3/26 5:00 PM A	
AEC150844-20	Client Review - Chemical Pot Feeder BOM	0	9/4/26 7:00 AM A	9/17/26 5:00 PM A	
AEC150844-25	Address Client Comments & Finalize Spec. - Chemical Pot Feec	0	9/18/26 7:00 AM A	9/22/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,12 ENG - Mechanical - Specifications - Expansion Joint Data Sheets					
AEC150810-05	Prep & Check & IDR - Data Sheets - Expansion Joints	10	1/4/27 7:00 AM	1/15/27 5:00 PM	146
AEC150810-10	IDR - Mechanical Data Sheets - Expansion Joints	5	1/19/27 7:00 AM	1/25/27 5:00 PM	146
AEC150810-15	Address Comments & Issue for Client Review - Data Sheets - E:	7	1/26/27 7:00 AM	2/3/27 5:00 PM	146
AEC150810-20	Client Review - Data Sheets - Expansion Joints	15	2/4/27 7:00 AM	2/25/27 5:00 PM	146
AEC150810-25	Address Client Comments & IFC - Data Sheets - Expansion Joir	5	2/26/27 7:00 AM	3/4/27 5:00 PM	146
BH CNN-KPJV-MAST-LIVE,03,01,09,13 ENG - Mechanical - Specifications - Backflow Preventor Data Sheets					
AEC150811-05	Prep & Check & IDR - Mechanical Lists/Data Sheets - Backflow	0	7/20/26 7:00 AM A	7/31/26 5:00 PM A	
AEC150811-10	IDR - Mechanical Lists/Data Sheets - Backflow Preventor	0	8/3/26 7:00 AM A	8/7/26 5:00 PM A	
AEC150811-15	Address Comments & Issue for Client Review - Mechanical Lists	0	8/10/26 7:00 AM A	8/17/26 5:00 PM A	
AEC150811-20	Client Review - Mechanical Lists/Data Sheets - Backflow Preven	0	8/18/26 7:00 AM A	9/1/26 5:00 PM A	
AEC150811-25	Address Client Comments & IFC - Mechanical Lists/Data Sheets	0	9/2/26 7:00 AM A	9/15/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,21 ENG - Mechanical - Specifications - Orifice Plate Data Sheets					
AEC150820-05	Prep & Check & IDR - Data Sheets - Orifice Plate	0	7/6/26 7:00 AM A	7/14/26 5:00 PM A	
AEC150820-10	IDR - Mechanical Data Sheets - Orifice Plate	0	7/15/26 7:00 AM A	7/24/26 5:00 PM A	
AEC150820-15	Address Comments & Issue for Client Review - Data Sheets - O	0	7/27/26 7:00 AM A	9/29/26 5:00 PM A	
AEC150820-20	Client Review - Data Sheets - Orifice Plate	7	9/29/26 7:00 AM A	10/20/26 5:00 PM	191
AEC150820-25	Address Client Comments & IFC - Data Sheets - Orifice Plate	5	10/21/26 7:00 AM	10/27/26 5:00 PM	191
BH CNN-KPJV-MAST-LIVE,03,01,09,22 ENG - Mechanical - Specifications - Coalescing Filters					
AEC150825-05	Prep & Check & IDR - Data Sheets - Coalescing Filters	0	6/29/26 7:00 AM A	7/8/26 5:00 PM A	
AEC150825-10	IDR - Mechanical Data Sheets - Coalescing Filters	0	7/8/26 7:00 AM A	7/17/26 5:00 PM A	
AEC150825-15	Address Comments & Issue for Client Review - Data Sheets - C	0	7/20/26 7:00 AM A	8/4/26 5:00 PM A	
AEC150825-20	Client Review - Data Sheets - Coalescing Filters	0	8/5/26 7:00 AM A	8/13/26 5:00 PM A	
AEC150825-25	Address Client Comments & IFC - Data Sheets - Coalescing Filt	0	8/21/26 7:00 AM A	9/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,07 ENG - Mechanical - Specifications - Duplex Strainers					
AEC150826-05	Prep & Check & IDR - Data Sheets - Duplex Strainers	0	7/20/26 7:00 AM A	7/31/26 5:00 PM A	
AEC150826-10	IDR - Mechanical Data Sheets - Duplex Strainers	0	8/3/26 7:00 AM A	8/7/26 5:00 PM A	
AEC150826-15	Address Comments & Issue for Client Review - Data Sheets - D	0	8/10/26 7:00 AM A	8/14/26 5:00 PM A	
AEC150826-20	Client Review - Data Sheets - Duplex Strainers	0	8/17/26 7:00 AM A	9/8/26 5:00 PM A	
AEC150826-25	Address Client Comments & IFC - Data Sheets - Duplex Straine	0	9/9/26 7:00 AM A	9/18/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,24 ENG - Mechanical - Specifications - Potable Water Softener Tank					
AEC150847-05	Prep & Check & IDR - Potable Water Softener Tank Spec.	0	7/14/26 7:00 AM A	7/17/26 5:00 PM A	
AEC150847-10	IDR - Potable Water Softener Tank Spec.	0	7/20/26 7:00 AM A	7/22/26 5:00 PM A	
AEC150847-15	Address Comments & Issue for Client Review - Potable Water S	0	7/27/26 7:00 AM A	9/4/26 5:00 PM A	
AEC150847-20	Client Review - Spec. - Potable Water Softener Tank	0	9/7/26 7:00 AM A	9/23/26 5:00 PM A	
AEC150847-25	Address Client Comments & Finalize Spec. - Potable Water Sof	0	9/24/26 7:00 AM A	9/24/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,09,25 ENG - Mechanical - Specifications - Pulsation Dampener					
AEC150848-05	Prep & Check & IDR - Pulsation Dampener BOM	0	7/27/26 7:00 AM A	9/15/26 5:00 PM A	
AEC150848-10	IDR - Pulsation Dampener BOM	0	9/16/26 7:00 AM A	9/24/26 5:00 PM A	
AEC150848-15	Address Comments & Issue for Client Review - Pulsation Dampe	0	9/25/26 7:00 AM A	9/25/26 5:00 PM A	
AEC150848-20	Client Review - Pulsation Dampener BOM	6	9/28/26 7:00 AM A	10/19/26 5:00 PM	541
AEC150848-25	Address Client Comments & Finalize Spec. - Pulsation Dampen	5	10/20/26 7:00 AM	10/26/26 5:00 PM	541
BH CNN-KPJV-MAST-LIVE,03,01,09,26 ENG - Mechanical - Specifications - Injection Quill					
AEC150849-05	Prep & Check & IDR - Injection Quill BOM	0	9/8/26 7:00 AM A	9/14/26 5:00 PM A	



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC150849-10	IDR - Injection Quill BOM	0	9/15/26 7:00 AM A	9/24/26 5:00 PM A	
AEC150849-15	Address Comments & Issue for Client Review - Injection Quill BO	0	9/25/26 7:00 AM A	9/25/26 5:00 PM A	
AEC150849-20	Client Review - Injection Quill BOM	6	9/28/26 7:00 AM A	10/19/26 5:00 PM	541
AEC150849-25	Address Client Comments & Finalize Spec. - Injection Quill BOM	5	10/20/26 7:00 AM	10/26/26 5:00 PM	541
BH CNN-KPJV-MAST-LIVE,03,01,09,27 ENG - Mechanical - Specifications - Bleed Rings					
AEC150850-05	Prep & Check & IDR - Bleed Rings BOM	0	8/27/26 7:00 AM A	9/3/26 5:00 PM A	
AEC150850-10	IDR - Bleed Rings BOM	0	9/3/26 7:00 AM A	9/3/26 5:00 PM A	
AEC150850-15	Address Comments & Issue for Client Review - Bleed Rings BOM	0	9/3/26 7:00 AM A	9/3/26 5:00 PM A	
AEC150850-20	Client Review - Bleed Rings BOM	0	9/3/26 7:00 AM A	9/17/26 5:00 PM A	
AEC150850-25	Address Client Comments & Finalize Spec. - Bleed Rings BOM	0	9/18/26 7:00 AM A	9/22/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,02 ENG - Mechanical - Subcontractor Specifications					
BH CNN-KPJV-MAST-LIVE,03,01,02,01 ENG - Mechanical - Subcontractor Specifications - HVAC Supply & Installation					
AEC150901-05	Prep & Check & IDR - Supply/Installation Spec. - HVAC Supply &	0	8/7/26 7:00 AM A	8/21/26 5:00 PM A	
AEC150901-20	IDR - Supply/Installation Spec. - HVAC Supply & Installation	0	8/24/26 7:00 AM A	8/31/26 5:00 PM A	
AEC150901-25	Address Comments & Issue for Client Review - Mech Spec - HVAC	0	9/1/26 7:00 AM A	10/2/26 5:00 PM A	
AEC150901-30	Client Review - Supply/Installation - HVAC Supply & Installation	11	10/5/26 7:00 AM A	10/26/26 5:00 PM	105
AEC150901-35	Address Client Comments & Finalize Spec. - HVAC Supply & Ins	5	10/27/26 7:00 AM	11/2/26 5:00 PM	105
BH CNN-KPJV-MAST-LIVE,03,01,02,02 ENG - Mechanical - Subcontractor Specifications - Fire Protection/Detection					
AEC150902-05	Prep & Check & IDR - Supply/Installation Spec. - Fire Protection	0	6/22/26 7:00 AM A	8/21/26 5:00 PM A	
AEC150902-20	IDR - Supply/Installation Spec. - Fire Protection/Detection	0	8/24/26 7:00 AM A	9/8/26 5:00 PM A	
AEC150902-25	Address Comments & Issue for Client Review - Supply/Installatic	0	9/9/26 7:00 AM A	9/9/26 5:00 PM A	
AEC150902-30	Client Review - Supply/Installation Spec. - Fire Protection/Detect	0	9/9/26 7:00 AM A	10/5/26 5:00 PM A	
AEC150902-35	Address Client Comments & Finalize Supply/Installation Spec. -	6	10/6/26 7:00 AM A	10/19/26 5:00 PM	546
BH CNN-KPJV-MAST-LIVE,03,01,02,04 ENG - Mechanical - Subcontractor Specifications - Yard Fire Protection System (U/G)					
AEC150912-05	Prep & Check & IDR - Supply/Installation Spec. - Yard Fire Prote	0	7/13/26 7:00 AM A	7/24/26 5:00 PM A	
AEC150912-10	IDR - Supply/Installation Spec. - Yard Fire Protection System (U/	0	7/27/26 7:00 AM A	7/31/26 5:00 PM A	
AEC150912-15	Address Comments & Issue for Client Review - Supply/Installatic	0	8/3/26 7:00 AM A	8/20/26 5:00 PM A	
AEC150912-20	Client Review - Supply/Installation Spec. - Yard Fire Protection S	0	8/20/26 7:00 AM A	9/11/26 5:00 PM A	
AEC150912-25	Address Client Comments & Finalize Supply/Installation Spec. -	0	9/11/26 7:00 AM A	9/23/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,02,05 ENG - Mechanical - Subcontractor Specifications - Fire Pumps					
AEC150922-05	Prep & Check & IDR - Supply/Installation Spec. - Fire Pumps	0	7/20/26 7:00 AM A	7/24/26 5:00 PM A	
AEC150922-10	IDR - Supply/Installation Spec. - Fire Pumps	0	7/27/26 7:00 AM A	7/31/26 5:00 PM A	
AEC150922-15	Address Comments & Issue for Client Review - Supply/Installatic	0	8/3/26 7:00 AM A	8/20/26 5:00 PM A	
AEC150922-20	Client Review - Supply/Installation Spec. - Fire Pumps	0	8/20/26 7:00 AM A	9/11/26 5:00 PM A	
AEC150922-25	Address Client Comments & Finalize Supply/Installation Spec. -	0	9/11/26 7:00 AM A	9/21/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,02,03 ENG - Mechanical - Subcontractor Specifications - Piping Insulation					
AEC150903-05	Prep & Check & IDR - Piping Insulation Supply/Installation Spec	0	5/18/26 7:00 AM A	6/1/26 5:00 PM A	
AEC150903-20	IDR - Piping Insulation Supply/Installation Spec.	0	6/2/26 7:00 AM A	6/26/26 5:00 PM A	
AEC150903-25	Address Comments & Issue for Client Review - Piping Insulation	0	6/26/26 7:00 AM A	6/29/26 5:00 PM A	
AEC150903-30	Client Review - Spec. - Piping Insulation Supply/Installation	0	6/30/26 7:00 AM A	7/14/26 5:00 PM A	
AEC150903-35	Address Client Comments & Finalize Spec. - Piping Insulation S	0	7/15/26 7:00 AM A	7/17/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,01,01 ENG - Mechanical - Lists					
BH CNN-KPJV-MAST-LIVE,03,01,01,01 ENG - Mechanical - Lists - Equipment List					
AEC150701-05	Prep & Check & IDR - Prelim Equip List	5	9/22/26 7:00 AM A	10/16/26 5:00 PM	296
AEC150701-10	IDR - Prelim. Equip List	4	10/19/26 7:00 AM	10/22/26 5:00 PM	296
AEC150701-20	Address Comments & Issue for Client Review - Prelim. Equip Lis	5	10/23/26 7:00 AM	10/29/26 5:00 PM	296
AEC150701-25	Client Review - Preliminary - Equip List	15	10/30/26 7:00 AM	11/20/26 5:00 PM	296
AEC150701-30	Address Client Comments & Issue IFD - Equip List	5	11/23/26 7:00 AM	11/30/26 5:00 PM	296
AEC150701-35	Prep & Check & IFC - Final Equipment List	10	12/1/26 7:00 AM	12/14/26 5:00 PM	296
BH CNN-KPJV-MAST-LIVE,03,01,01,02 ENG - Mechanical - Lists - Piping Line List					
AEC150702-05	Prep & Check & IDR - Mechanical Lists - Line List	1	9/22/26 7:00 AM A	10/12/26 5:00 PM	52



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC150702-10	IDR - Mechanical Lists/Data Sheets - Line List	5	10/13/26 7:00 AM	10/19/26 5:00 PM	52
AEC150702-15	Address Comments & Issue for Client Review - Mechanical Lists	5	10/20/26 7:00 AM	10/26/26 5:00 PM	52
AEC150702-20	Client Review - Mechanical Lists/Data Sheets - Line List	15	10/27/26 7:00 AM	11/17/26 5:00 PM	416
AEC150702-25	Address Client Comments & IFC - Mechanical Lists/Data Sheets	5	11/18/26 7:00 AM	11/24/26 5:00 PM	416
BH CNN-KPJV-MAST-LIVE,03,01,01,03 ENG - Mechanical - Lists - Valve List					
AEC150703-05	Prep & Check & IDR - Mechanical Lists/Data Sheets - Valve List	1	9/22/26 7:00 AM A	10/12/26 5:00 PM	521
AEC150703-10	IDR - Mechanical Lists/Data Sheets - Valve List	5	10/13/26 7:00 AM	10/19/26 5:00 PM	521
AEC150703-15	Address Comments & Issue for Client Review - Mechanical Lists	5	10/20/26 7:00 AM	10/26/26 5:00 PM	521
AEC150703-20	Client Review - Mechanical Lists/Data Sheets - Valve List	15	10/27/26 7:00 AM	11/17/26 5:00 PM	521
AEC150703-25	Address Client Comments & IFC - Mechanical Lists/Data Sheets	5	11/18/26 7:00 AM	11/24/26 5:00 PM	521
BH CNN-KPJV-MAST-LIVE,03,01,01,04 ENG - Mechanical - Lists - Specialty List					
AEC150704-05	Prep & Check & IDR - Mechanical Lists/Data Sheets - Specialty	1	9/22/26 7:00 AM A	10/12/26 5:00 PM	521
AEC150704-10	IDR - Mechanical Lists/Data Sheets - Specialty List	5	10/13/26 7:00 AM	10/19/26 5:00 PM	521
AEC150704-15	Address Comments & Issue for Client Review - Mechanical Lists	5	10/20/26 7:00 AM	10/26/26 5:00 PM	521
AEC150704-20	Client Review - Mechanical Lists/Data Sheets - Specialty List	15	10/27/26 7:00 AM	11/17/26 5:00 PM	521
AEC150704-25	Address Client Comments & IFC - Mechanical Lists/Data Sheets	5	11/18/26 7:00 AM	11/24/26 5:00 PM	521
BH CNN-KPJV-MAST-LIVE,03,01,01,05 ENG - Mechanical - Lists - Terminal Point List					
AEC150705-05	Prep & Check & IDR - Mechanical Lists/Data Sheets - Terminal I	10	10/27/26 7:00 AM	11/9/26 5:00 PM	52
AEC150705-10	IDR - Mechanical Lists/Data Sheets - Terminal Point List	5	11/10/26 7:00 AM	11/17/26 5:00 PM	52
AEC150705-15	Address Comments & Issue for Client Review - Mechanical Lists	5	11/18/26 7:00 AM	11/24/26 5:00 PM	52
AEC150705-20	Client Review - Mechanical Lists/Data Sheets - Terminal Point Li	15	11/25/26 7:00 AM	12/16/26 5:00 PM	496
AEC150705-25	Address Client Comments & IFC - Mechanical Lists/Data Sheets	10	12/17/26 7:00 AM	1/5/27 5:00 PM	496
BH CNN-KPJV-MAST-LIVE,03,03 ENG - Piping					
BH CNN-KPJV-MAST-LIVE,03,03,17 ENG - Piping - Plant Water Balance					
AEC161144-35	Prep & Check & IDR - Plant Water Balance Dwg.	0	3/9/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161144-45	IDR - Plant Water Balance Dwg.	0	4/29/26 7:00 AM A	5/5/26 5:00 PM A	
AEC161144-55	Address IDR - Comments & Issue for Client Review - Plant Wate	0	5/6/26 7:00 AM A	5/28/26 5:00 PM A	
AEC161144-65	Client Review - Plant Water Balance Dwg.	0	5/29/26 7:00 AM A	6/19/26 5:00 PM A	
AEC161144-75	Address Client Comments & IFP - Equipment GA Dwg. - Plant V	0	8/7/26 7:00 AM A	9/21/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,03 ENG - Piping - Specifications					
BH CNN-KPJV-MAST-LIVE,03,03,03,04 ENG - Piping - Specifications - Piping Material Specification					
AEC160801-05	Prep & Check & IDR - Spec. - Pipe Material	0	5/11/26 7:00 AM A	6/12/26 5:00 PM A	
AEC160801-20	IDR - Spec. - Pipe Material	0	6/15/26 7:00 AM A	6/19/26 5:00 PM A	
AEC160801-25	Address Comments & Issue for Client Review - Mech Spec - Pip	0	6/22/26 7:00 AM A	6/30/26 5:00 PM A	
AEC160801-30	Client Review - Spec. - Pipe Material	0	7/1/26 7:00 AM A	7/14/26 5:00 PM A	
AEC160801-35	Address Client Comments & Finalize Spec. - Pipe Material	0	7/15/26 7:00 AM A	7/23/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,03,01 ENG - Piping - Specifications - Pipe Supports Supply & Fabrication Specification					
AEC160802-05	Prep & Check & IDR - Spec. - Pipe Supports Supply & Fabricatic	15	2/2/27 7:00 AM	2/23/27 5:00 PM	363
AEC160802-10	IDR - Spec. - Pipe Supports Supply & Fabrication	5	2/24/27 7:00 AM	3/2/27 5:00 PM	363
AEC160802-25	Address Comments & Issue for Client Review - Mech Spec - Pip	5	3/3/27 7:00 AM	3/9/27 5:00 PM	363
AEC160802-30	Client Review - Spec. - Pipe Supports Supply & Fabrication	15	3/10/27 7:00 AM	3/31/27 5:00 PM	363
AEC160802-35	Address Client Comments & Finalize Spec. - Pipe Supports Sup	5	4/1/27 7:00 AM	4/7/27 5:00 PM	433
BH CNN-KPJV-MAST-LIVE,03,03,03,03 ENG - Piping - Specifications - SB Cold Supports Cookbook					
AEC160803-05	Prepare/Check & IDR - SB Cold Supports Cookbook	15	2/9/27 7:00 AM	3/2/27 5:00 PM	428
AEC160803-20	IDR - Spec. - SB Cold Supports Cookbook	5	3/3/27 7:00 AM	3/9/27 5:00 PM	428
AEC160803-25	Address Comments & Issue for Client Review - Mech Spec - SB	5	3/10/27 7:00 AM	3/16/27 5:00 PM	428
AEC160803-30	Client Review - Spec. - SB Cold Supports Cookbook	15	3/17/27 7:00 AM	4/7/27 5:00 PM	428
AEC160803-35	Address Client Comments & Finalize Spec. - SB Cold Supports	5	4/8/27 7:00 AM	4/14/27 5:00 PM	428
BH CNN-KPJV-MAST-LIVE,03,03,04 ENG - Piping - Modeling & Drawings					
BH CNN-KPJV-MAST-LIVE,03,03,04,02 ENG - Piping - Modeling & Drawings - Plot Plan					
AEC161120-05	Prep & Check & IDR/CR - Plot Plan	0	3/9/26 7:00 AM A	3/12/26 5:00 PM A	




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC161120-10	IDR - Plot Plan	0	3/13/26 7:00 AM A	3/19/26 5:00 PM A	
AEC16112020	Client Review - Plot Plan	0	3/20/26 7:00 AM A	3/26/26 5:00 PM A	
AEC16112025	Address Client Comments & IFP - Equipment GA Dwg. - Plot Pla	0	3/27/26 7:00 AM A	4/13/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,03 ENG - Piping - Modeling & Drawings - Equipment General Arrangements					
BH CNN-KPJV-MAST-LIVE,03,03,04,03,01 ENG - Piping - Modeling & Drawings - Equipment GAs - Fuel Oil Pump Bldg.& Tank Area					
AEC161140-0	Prep & Check & IDR - Equipment GA Drawing - Fuel Oil Pump B	0	4/6/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161140-1	IDR - Equipment GA Dwg. - Fuel Oil Pump Building	0	4/20/26 7:00 AM A	4/30/26 5:00 PM A	
AEC161140-1	Address IDR - Comments & Issue for Client Review - Equipment	0	4/30/26 7:00 AM A	5/5/26 5:00 PM A	
AEC161140-2	Client Review - Equipment GA Dwg. - Fuel Oil Pump Building	0	5/5/26 7:00 AM A	5/26/26 5:00 PM A	
AEC161140-2	Address Client Comments & IFP - Equipment GA Dwg. - Fuel Oi	0	5/27/26 7:00 AM A	6/10/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,03,07 ENG - Piping - Modeling & Drawings - Equipment GAs - CTG Area					
AEC161135-0	Prep & Check & IDR - Equipment GA Drawings - CTG Area	0	4/6/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161135-1	IDR - Equipment GA CTG Area	0	4/20/26 7:00 AM A	4/30/26 5:00 PM A	
AEC161135-1	Address IDR - Comments & Issue for Client Review GA Drawing	0	4/30/26 7:00 AM A	5/5/26 5:00 PM A	
AEC161135-2	Client Review - Equipment GA Dwg. - CTG Area	0	5/5/26 7:00 AM A	5/26/26 5:00 PM A	
AEC161135-2	Address Client Comments & IFP - Equipment GA Dwg. - CTG Ar	0	5/27/26 7:00 AM A	6/10/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,03,02 ENG - Piping - Modeling & Drawings - Equipment GAs - Plant Services Area					
AEC161142-0	Prep & Check & IDR - Equipment GA Drawing - Plant Services A	0	4/1/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161142-1	IDR - Equipment GA Dwg. - Plant Services Area	0	4/20/26 7:00 AM A	4/30/26 5:00 PM A	
AEC161142-1	Address IDR - Comments & Issue for Client Review - Equipment	0	4/30/26 7:00 AM A	5/5/26 5:00 PM A	
AEC161142-2	Client Review - Equipment GA Dwg. - Plant Services Area	0	5/5/26 7:00 AM A	5/26/26 5:00 PM A	
AEC161142-2	Address Client Comments & IFP - Equipment GA Dwg. - Plant S	0	5/27/26 7:00 AM A	6/10/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,03,06 ENG - Piping - Modeling & Drawings - Equipment GAs - Admin / Maintenance Building					
AEC161149-0	Prep & Check & IDR - Equipment GA Drawing - Admin Building	0	4/1/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161149-1	IDR - Equipment GA Dwg. - Admin Building & Maintenance	0	4/17/26 7:00 AM A	4/30/26 5:00 PM A	
AEC161149-1	Address IDR - Comments & Issue for Client Review - Equipment	0	4/30/26 7:00 AM A	5/5/26 5:00 PM A	
AEC161149-2	Client Review - Equipment GA Dwg. - Admin Building & Mainten	0	5/5/26 7:00 AM A	5/26/26 5:00 PM A	
AEC161149-2	Address Client Comments & IFP - Equipment GA Dwg. - Admin	0	5/27/26 7:00 AM A	6/10/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,03,04 ENG - Piping - Modeling & Drawings - Equipment GAs - Fuel Gas Area					
AEC161146-0	Prep & Check & IDR - Equipment GA Drawing - Fuel Gas Area	0	4/6/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161146-1	IDR - Equipment GA Dwg. - Fuel Gas Area	0	4/20/26 7:00 AM A	4/30/26 5:00 PM A	
AEC161146-1	Address IDR - Comments & Issue for Client Review - Equipment	0	4/30/26 7:00 AM A	5/5/26 5:00 PM A	
AEC161146-2	Client Review - Equipment GA Dwg. - Fuel Gas Area	0	5/5/26 7:00 AM A	5/26/26 5:00 PM A	
AEC161146-2	Address Client Comments & IFP - Equipment GA Dwg. - Fuel G	0	5/27/26 7:00 AM A	6/10/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,03,03 ENG - Piping - Modeling & Drawings - Equipment GAs - Ammonia Storage and Transfer Area					
AEC161147-0	Prep & Check & IDR - Equipment GA Drawing - Ammonia Stora	0	4/1/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161147-1	IDR - Equipment GA Dwg. - Ammonia Storage & Transfer Area	0	4/20/26 7:00 AM A	4/30/26 5:00 PM A	
AEC161147-1	Address IDR - Comments & Issue for Client Review - Equipment	0	4/30/26 7:00 AM A	5/5/26 5:00 PM A	
AEC161147-2	Client Review - Equipment GA Dwg. - Ammonia Storage & Trans	0	5/5/26 7:00 AM A	5/26/26 5:00 PM A	
AEC161147-2	Address Client Comments & IFP - Equipment GA Dwg. - Ammor	0	5/27/26 7:00 AM A	6/10/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,03,05 ENG - Piping - Modeling & Drawings - Equipment GAs - Control Room and DCS Room					
AEC161148-0	Prep & Check & IDR - Equipment GA Drawing - Control Room &	0	6/29/26 7:00 AM A	8/5/26 5:00 PM A	
AEC161148-1	IDR - Equipment GA Dwg. - Control Room & DCS Room	0	8/6/26 7:00 AM A	8/17/26 5:00 PM A	
AEC161148-1	Address IDR - Comments & Issue for Client Review - Equipment	0	8/18/26 7:00 AM A	8/24/26 5:00 PM A	
AEC161148-2	Client Review - Equipment GA Dwg. - Control Room & DCS Roo	0	8/25/26 7:00 AM A	9/11/26 5:00 PM A	
AEC161148-2	Address Client Comments & IFP - Equipment GA Dwg. - Control	0	9/14/26 7:00 AM A	9/24/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,06 ENG - Piping - Modeling & Drawings - Underground Piping					
BH CNN-KPJV-MAST-LIVE,03,03,04,06,01 ENG - Piping - Modeling & Drawings - U/G Piping - General					
AEC161100-1	Model - U/G Pipe	0	6/12/26 7:00 AM A	8/18/26 5:00 PM A	
AEC161150-0	Prep & Check & IDR - Piping Drawings - U/G Piping	2	8/19/26 7:00 AM A	10/13/26 5:00 PM	20
AEC161150-1	IDR - Piping Drawings - U/G Piping	22	10/14/26 7:00 AM	11/13/26 5:00 PM	20

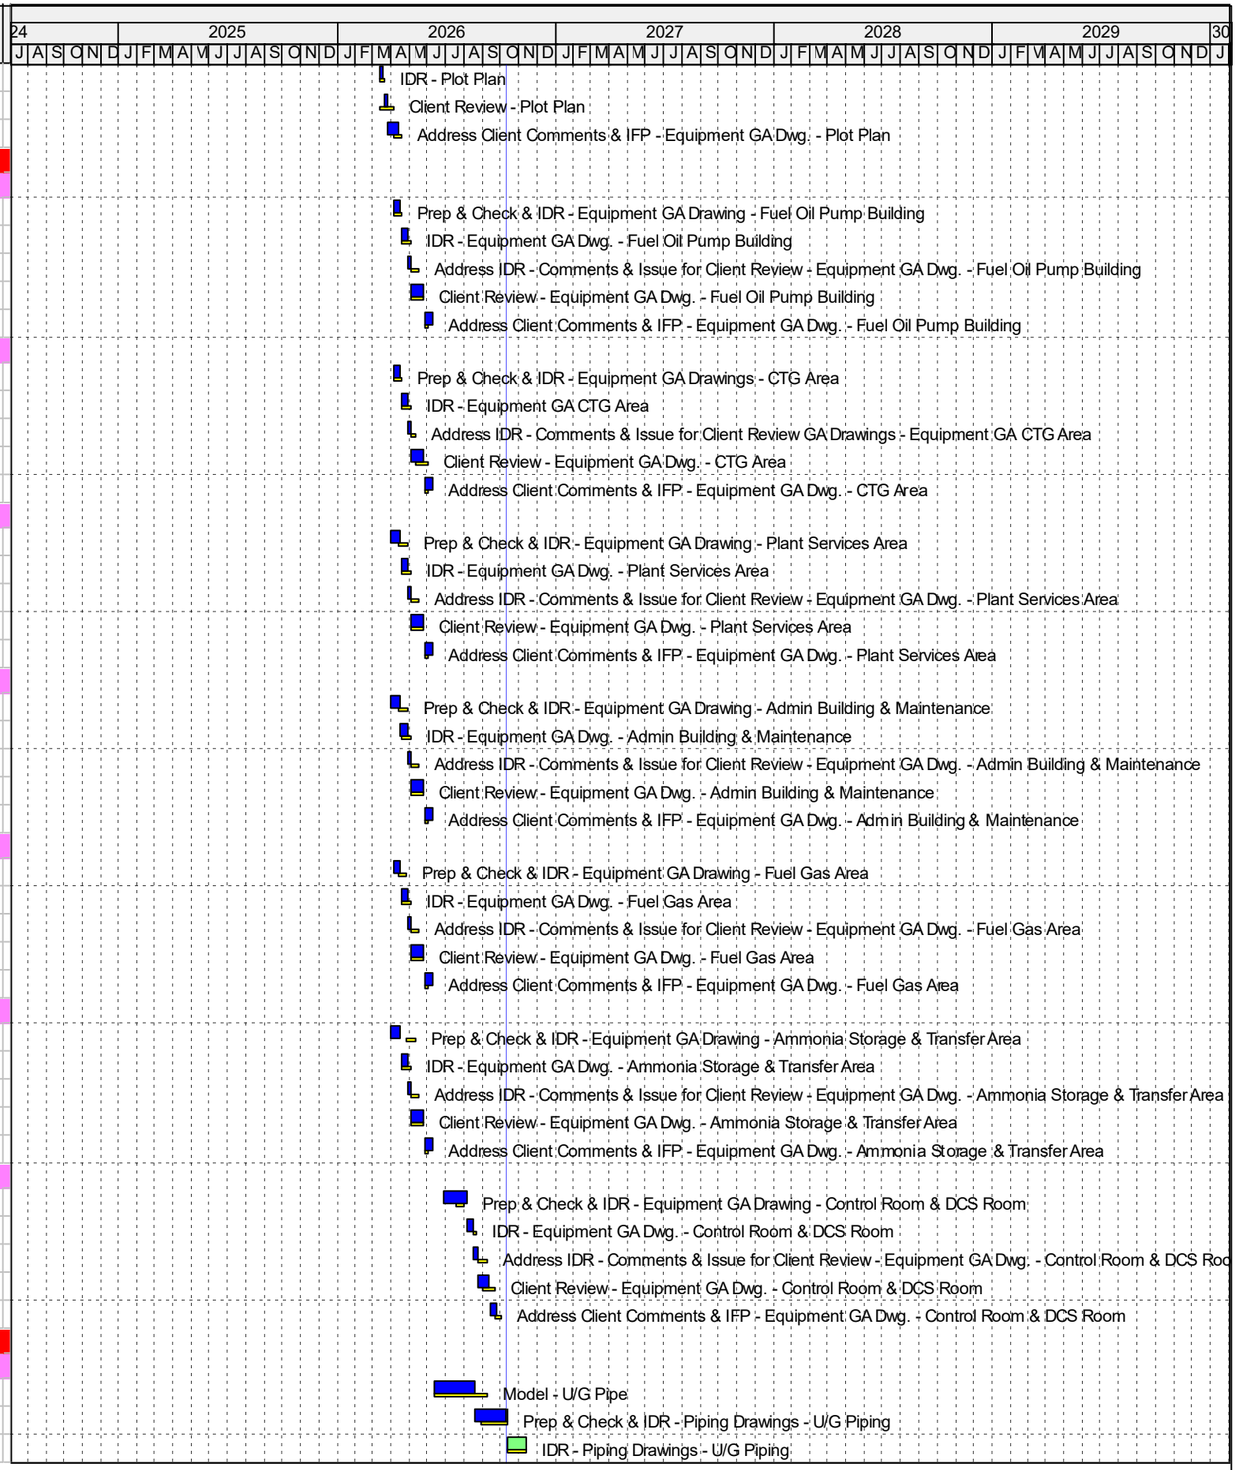

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC161150-1	Address Comments & Issue for Client Review - Piping Drawings	10	11/16/26 7:00 AM	11/30/26 5:00 PM	20
AEC161150-2	Client Review - Piping Drawings - U/G Piping	15	12/1/26 7:00 AM	12/21/26 5:00 PM	109
AEC161150-3	Finalize Dwg, & IFC - U/G Piping	10	12/22/26 7:00 AM	1/8/27 5:00 PM	109
BH CNN-KPJV-MAST-LIVE,03,03,04,06,03 ENG - Piping - Modeling & Drawings - U/G Piping - Fuel Gas Piping from the M&R Yard to FG Building					
AEC161100-1	Model - U/G Pipe - U/G Fuel Gas Piping from the M&R Yard to F	0	6/12/26 7:00 AM A	8/7/26 5:00 PM A	
AEC161150-0	Prep & Check & IDR - Piping Drawings - U/G Fuel Gas Piping frc	0	8/10/26 7:00 AM A	8/12/26 5:00 PM A	
AEC161150-1	IDR Piping Drawings - U/G Fuel Gas Piping from the M&R Yard	0	8/13/26 7:00 AM A	8/21/26 5:00 PM A	
AEC161150-2	Client Review Piping Drawings - U/G Fuel Gas Piping from the M	0	9/1/26 7:00 AM A	9/23/26 5:00 PM A	
AEC161150-2	Finalize Dwg, & Issue IFC - U/G Fuel Gas Piping from the M&R '	0	9/24/26 7:00 AM A	10/5/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,06,04 ENG - Piping - Modeling & Drawings - U/G Piping - BESS Fire Protection					
AEC151152-0	Pipe Model - BESS Fire Protection Piping	0	6/12/26 7:00 AM A	8/7/26 5:00 PM A	
AEC151152-0	Prep & Check & IDR - Piping Drawings - BESS Fire Protection P	0	8/10/26 7:00 AM A	8/17/26 5:00 PM A	
AEC151152-1	IDR Piping Drawings - BESS Fire Protection Piping	0	8/17/26 7:00 AM A	8/21/26 5:00 PM A	
AEC151152-1	Client Review Piping Drawings - BESS Fire Protection Piping	0	9/1/26 7:00 AM A	9/23/26 5:00 PM A	
AEC151152-2	Finalize Dwg, & Issue IFC - BESS Fire Protection Piping	0	9/24/26 7:00 AM A	10/8/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,06,02 ENG - Piping - Modeling & Drawings - U/G Piping - Embedded Exhaust Stack Foundation (CCW, CWW &					
AEC161175-0	Model - U/G CTG/Stack Foundation Embedded Piping (CCW, C	0	4/30/26 7:00 AM A	6/11/26 5:00 PM A	
AEC161175-1	Prep & Check & IDR - Piping Drawings - U/G CTG/Stack Founda	0	6/12/26 7:00 AM A	8/4/26 5:00 PM A	
AEC161175-2	IDR - Piping Drawings - U/G CTG/Stack Foundation Embedded	0	8/5/26 7:00 AM A	8/19/26 5:00 PM A	
AEC161175-2	Address Comments & Issue for Client Review - Piping Drawings	0	8/20/26 7:00 AM A	8/31/26 5:00 PM A	
AEC161175-3	Client Review - Piping Drawings - U/G CTG/Stack Foundation Er	0	9/1/26 7:00 AM A	9/23/26 5:00 PM A	
AEC161175-3	Finalize Dwg, & IFC - U/G CTG/Stack Foundation Embedded Pi	2	9/24/26 7:00 AM A	10/13/26 5:00 PM	56
BH CNN-KPJV-MAST-LIVE,03,03,04,04 ENG - Piping - Modeling & Drawings - P&IDs					
BH CNN-KPJV-MAST-LIVE,03,03,04,04,16 ENG - Piping - Modeling & Drawings - P&IDs - P&ID Index & Lead Sheets					
AEC161190-0	Prep & Check & IDR - Piping Drawings - P&ID - Drawing Index &	0	3/30/26 7:00 AM A	4/13/26 5:00 PM A	
AEC161190-1	IDR - Piping Drawings - P&ID - Drawing Index & Lead Sheets	0	4/14/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161190-1	Address Comments & Issue for Client Review - Piping Drawings	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161190-2	Client Review - Piping Drawings - P&ID - Drawing Index & Lead	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161190-2	Address Client Comments & Issue IFD - Piping Drawings - P&ID	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
AEC161190-3	Address Client Comments & IFC - Piping Drawings - P&ID - Drav	5	11/25/26 7:00 AM	12/2/26 5:00 PM	52
BH CNN-KPJV-MAST-LIVE,03,03,04,04,01 ENG - Piping - Modeling & Drawings - P&IDs - Fuel Gas					
AEC161101-0	Prep & Check & IDR - P&ID's - Fuel Gas	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161101-1	IDR - P&ID's - Fuel Gas	0	4/10/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161101-1	Address Comments & Issue for Client Review - P&ID's - Fuel Ga	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161101-2	Client Review - P&ID's - Fuel Gas	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161101-2	Address Client Comments & Issue IFD - P&ID's - Fuel Gas	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,02 ENG - Piping - Modeling & Drawings - P&IDs - Fuel Oil					
AEC161102-0	Prep & Check & IDR - P&ID's - Fuel Oil	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161102-1	IDR - P&ID's - Fuel Oil	0	4/13/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161102-1	Address Comments & Issue for Client Review - P&ID's - Fuel Oil	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161102-2	Client Review - P&ID's - Fuel Oil	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161102-2	Address Client Comments & Issue IFD - P&ID's - Fuel Oil	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,03 ENG - Piping - Modeling & Drawings - P&IDs - Demineralized Water					
AEC161103-0	Prep & Check & IDR - P&ID's - Demineralized Water	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161103-1	IDR - P&ID's - Demineralized Water	0	4/13/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161103-1	Address Comments & Issue for Client Review - P&ID's - Demine	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161103-2	Client Review - P&ID's - Demineralized Water	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161103-2	Address Client Comments & Issue IFD - P&ID's - Demineralized	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,04 ENG - Piping - Modeling & Drawings - P&IDs - Service Water					
AEC161104-0	Prep & Check & IDR - P&ID's - Service Water	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161104-1	IDR - P&ID's - Service Water	0	4/13/26 7:00 AM A	4/17/26 5:00 PM A	



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC161104-1	Address Comments & Issue for Client Review - P&ID's - Service	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161104-2	Client Review - P&ID's - Service Water	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161104-2	Address Client Comments & Issue IFD - P&ID's - Service Water	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,05 ENG - Piping - Modeling & Drawings - P&IDs - Closed Cooling Water					
AEC161105-0	Prep & Check & IDR - P&ID's - Closed Cooling Water	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161105-1	IDR - P&ID's - Closed Cooling Water	0	4/10/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161105-1	Address Comments & Issue for Client Review - P&ID's - Closed	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161105-2	Client Review - P&ID's - Closed Cooling Water	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161105-2	Address Client Comments & Issue IFD - P&ID's - Closed Cooling	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,06 ENG - Piping - Modeling & Drawings - P&IDs - Potable Water					
AEC161106-0	Prep & Check & IDR - P&ID's - Potable Water	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161106-1	IDR - P&ID's - Potable Water	0	4/6/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161106-1	Address Comments & Issue for Client Review - P&ID's - Potable	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161106-2	Client Review - P&ID's - Potable Water	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161106-2	Address Client Comments & Issue IFD - P&ID's - Potable Water	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,20 ENG - Piping - Modeling & Drawings - P&IDs - Sanitary System					
AEC161125-0	Prep & Check & IDR - P&ID's - Sanitary System	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161125-1	IDR - P&ID's - Sanitary System	0	4/13/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161125-1	Address Comments & Issue for Client Review - P&ID's - Sanitary	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161125-2	Client Review - P&ID's - Sanitary System	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161125-2	Address Client Comments & Issue IFD - P&ID's - Sanitary Syste	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,07 ENG - Piping - Modeling & Drawings - P&IDs - Compressed Air					
AEC161107-0	Prep & Check & IDR - P&ID's - Compressed Air	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161107-1	IDR - P&ID's - Compressed Air	0	4/10/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161107-1	Address Comments & Issue for Client Review - P&ID's - Compre	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161107-2	Client Review - P&ID's - Compressed Air	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161107-2	Address Client Comments & Issue IFD - P&ID's - Compressed A	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,08 ENG - Piping - Modeling & Drawings - P&IDs - Water Wash Drains					
AEC161108-0	Prep & Check & IDR - P&ID's - Water Wash	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161108-1	IDR - P&ID's - Water Wash	0	4/6/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161108-1	Address Comments & Issue for Client Review - P&ID's - Water \	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161108-2	Client Review - P&ID's - Water Wash Drains	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161108-2	Address Client Comments & Issue IFD - P&ID's - Water Wash D	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,18 ENG - Piping - Modeling & Drawings - P&IDs - Ammonia					
AEC161118-0	Prep & Check & IDR - P&ID's - Ammonia	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161118-1	IDR - P&ID's - Ammonia	0	4/10/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161118-1	Address Comments & Issue for Client Review - P&ID's - Ammon	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161118-2	Client Review - P&ID's - Ammonia	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161118-2	Address Client Comments & Issue IFD - P&ID's - Ammonia	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,09 ENG - Piping - Modeling & Drawings - P&IDs - Wastewater					
AEC161109-0	Prep & Check & IDR - P&ID's - Wastewater	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161109-1	IDR - P&ID's - Wastewater	0	4/10/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161109-1	Address Comments & Issue for Client Review - P&ID's - Wastev	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161109-2	Client Review - P&ID's - Wastewater	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161109-2	Address Client Comments & Issue IFD - P&ID's - Wastewater	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,10 ENG - Piping - Modeling & Drawings - P&IDs - Nitrogen					
AEC16111305	Prep & Check & IDR - P&ID's - Nitrogen	0	4/6/26 7:00 AM A	4/10/26 5:00 PM A	
AEC16111310	IDR - P&ID's - Nitrogen	0	4/10/26 7:00 AM A	4/17/26 5:00 PM A	
AEC16111315	Address Comments & Issue for Client Review - P&ID's - Nitroge	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC16111320	Client Review - P&ID's - Nitrogen	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC16111325	Address Client Comments & Issue IFD - P&ID's - Nitrogen	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
BH CNN-KPJV-MAST-LIVE,03,03,04,04,11 ENG - Piping - Modeling & Drawings - P&IDs - Carbon Dioxide					
AEC161111-0	Prep & Check & IDR - P&ID's - Carbon Dioxide	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161111-1	IDR - P&ID's - Carbon Dioxide	0	4/10/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161111-1	Address Comments & Issue for Client Review - P&ID's - Carbon	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161111-2	Client Review - P&ID's - Carbon Dioxide	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161111-2	Address Client Comments & Issue IFD - P&ID's - Carbon Dioxid	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,12 ENG - Piping - Modeling & Drawings - P&IDs - Hydrogen					
AEC161112-0	Prep & Check & IDR - P&ID's - Hydrogen	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161112-1	IDR - P&ID's - Hydrogen	0	4/10/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161112-1	Address Comments & Issue for Client Review - P&ID's - Hydroge	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161112-2	Client Review - P&ID's - Hydrogen	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161112-2	Address Client Comments & Issue IFD - P&ID's - Hydrogen	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,13 ENG - Piping - Modeling & Drawings - P&IDs - Water Mist System					
AEC161113-0	Prep & Check & IDR - P&ID's - Water Mist System	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161113-1	IDR - P&ID's - Water Mist System	0	4/10/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161113-1	Address Comments & Issue for Client Review - P&ID's - Water M	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161113-2	Client Review - P&ID's - Water Mist System	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161113-2	Address Client Comments & Issue IFD - P&ID's - Water Mist Sys	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,14 ENG - Piping - Modeling & Drawings - P&IDs - Fire Protection					
AEC161114-0	Prep & Check & IDR - P&ID's - Fire Protection	0	3/9/26 7:00 AM A	4/10/26 5:00 PM A	
AEC161114-1	IDR - P&ID's - Fire Protection	0	4/10/26 7:00 AM A	4/17/26 5:00 PM A	
AEC161114-1	Address Comments & Issue for Client Review - P&ID's - Fire Pro	0	4/20/26 7:00 AM A	4/28/26 5:00 PM A	
AEC161114-2	Client Review - P&ID's - Fire Protection	0	4/28/26 7:00 AM A	5/14/26 5:00 PM A	
AEC161114-2	Address Client Comments & Issue IFD - P&ID's - Fire Protection	0	5/15/26 7:00 AM A	6/3/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,15 ENG - Piping - Modeling & Drawings - P&IDs - Sanitary System & Potable Water Riser Diagrams					
AEC161115-0	Prep & Check & IDR - Sanitary System & Potable Water Riser D	0	5/18/26 7:00 AM A	7/24/26 5:00 PM A	
AEC161115-1	IDR - Sanitary System & Potable Water Riser Diagrams	0	7/27/26 7:00 AM A	7/31/26 5:00 PM A	
AEC161115-1	Address Comments & Issue for Client Review - Sanitary System	0	8/10/26 7:00 AM A	9/1/26 5:00 PM A	
AEC161115-2	Client Review - Sanitary System & Potable Water Riser Diagram	0	9/2/26 7:00 AM A	9/17/26 5:00 PM A	
AEC161115-2	Address Client Comments & Issue IFD - Sanitary System & Pota	0	9/18/26 7:00 AM A	9/22/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,03,04,04,19 ENG - Piping - Modeling & Drawings - P&IDs - OEM Update to P&IDs					
AEC161199-0	Address OEM P&IDs & IDR - P&ID's	20	11/12/26 7:00 AM	12/10/26 5:00 PM	160
AEC161199-1	IDR - OEM P&IDs	20	12/11/26 7:00 AM	1/13/27 5:00 PM	160
AEC161199-2	Address Client Comments & IFC - OEM P&IDs	20	1/14/27 7:00 AM	2/11/27 5:00 PM	160
BH CNN-KPJV-MAST-LIVE,03,03,04,05 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports					
BH CNN-KPJV-MAST-LIVE,03,03,04,05,01 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Fuel Gas					
AEC161101-3	Model - Piping - Fuel Gas	25	12/1/26 7:00 AM	1/8/27 5:00 PM	29
AEC161101-7	Model - Pipe Supports - Fuel Gas	20	12/22/26 7:00 AM	1/25/27 5:00 PM	29
AEC161101-4	Prep & Extract Isos. - Fuel Gas	20	1/11/27 7:00 AM	2/8/27 5:00 PM	35
AEC161101-4	Check Isos. - Fuel Gas	5	2/9/27 7:00 AM	2/16/27 5:00 PM	35
AEC161101-5	Address Comments & IDR - Fuel Gas	5	2/17/27 7:00 AM	2/23/27 5:00 PM	35
AEC161101-8	Prepare - Pipe Support Drawings - Fuel Gas	25	1/26/27 7:00 AM	3/2/27 5:00 PM	29
AEC161101-6	IDR - Fuel Gas	10	2/24/27 7:00 AM	3/9/27 5:00 PM	35
AEC161101-8	Check Pipe Support Drawings - Fuel Gas	5	3/3/27 7:00 AM	3/9/27 5:00 PM	29
AEC161101-6	Address Comments & Backcheck Isos. - Fuel Gas	5	3/10/27 7:00 AM	3/16/27 5:00 PM	35
AEC161101-9	Address Comments & Prepare IDR - Pipe Supports - Fuel Gas	5	3/10/27 7:00 AM	3/16/27 5:00 PM	29
AEC161101-9	IDR - Pipe Support Drawings - Fuel Gas	1	3/17/27 7:00 AM	3/17/27 5:00 PM	29
AEC161101-7	Issue Isos. - IFC - Fuel Gas	2	3/17/27 7:00 AM	3/18/27 5:00 PM	35
AEC161101-9	Address IDR - Comments & Backcheck Pipe Supports - Fuel Ga	5	3/18/27 7:00 AM	3/24/27 5:00 PM	29
AEC161101-9	Address Client Comments & IFC - Pipe Support Drwgs - Fuel Ga	2	3/25/27 7:00 AM	3/29/27 5:00 PM	29
BH CNN-KPJV-MAST-LIVE,03,03,04,05,02 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Fuel Oil					

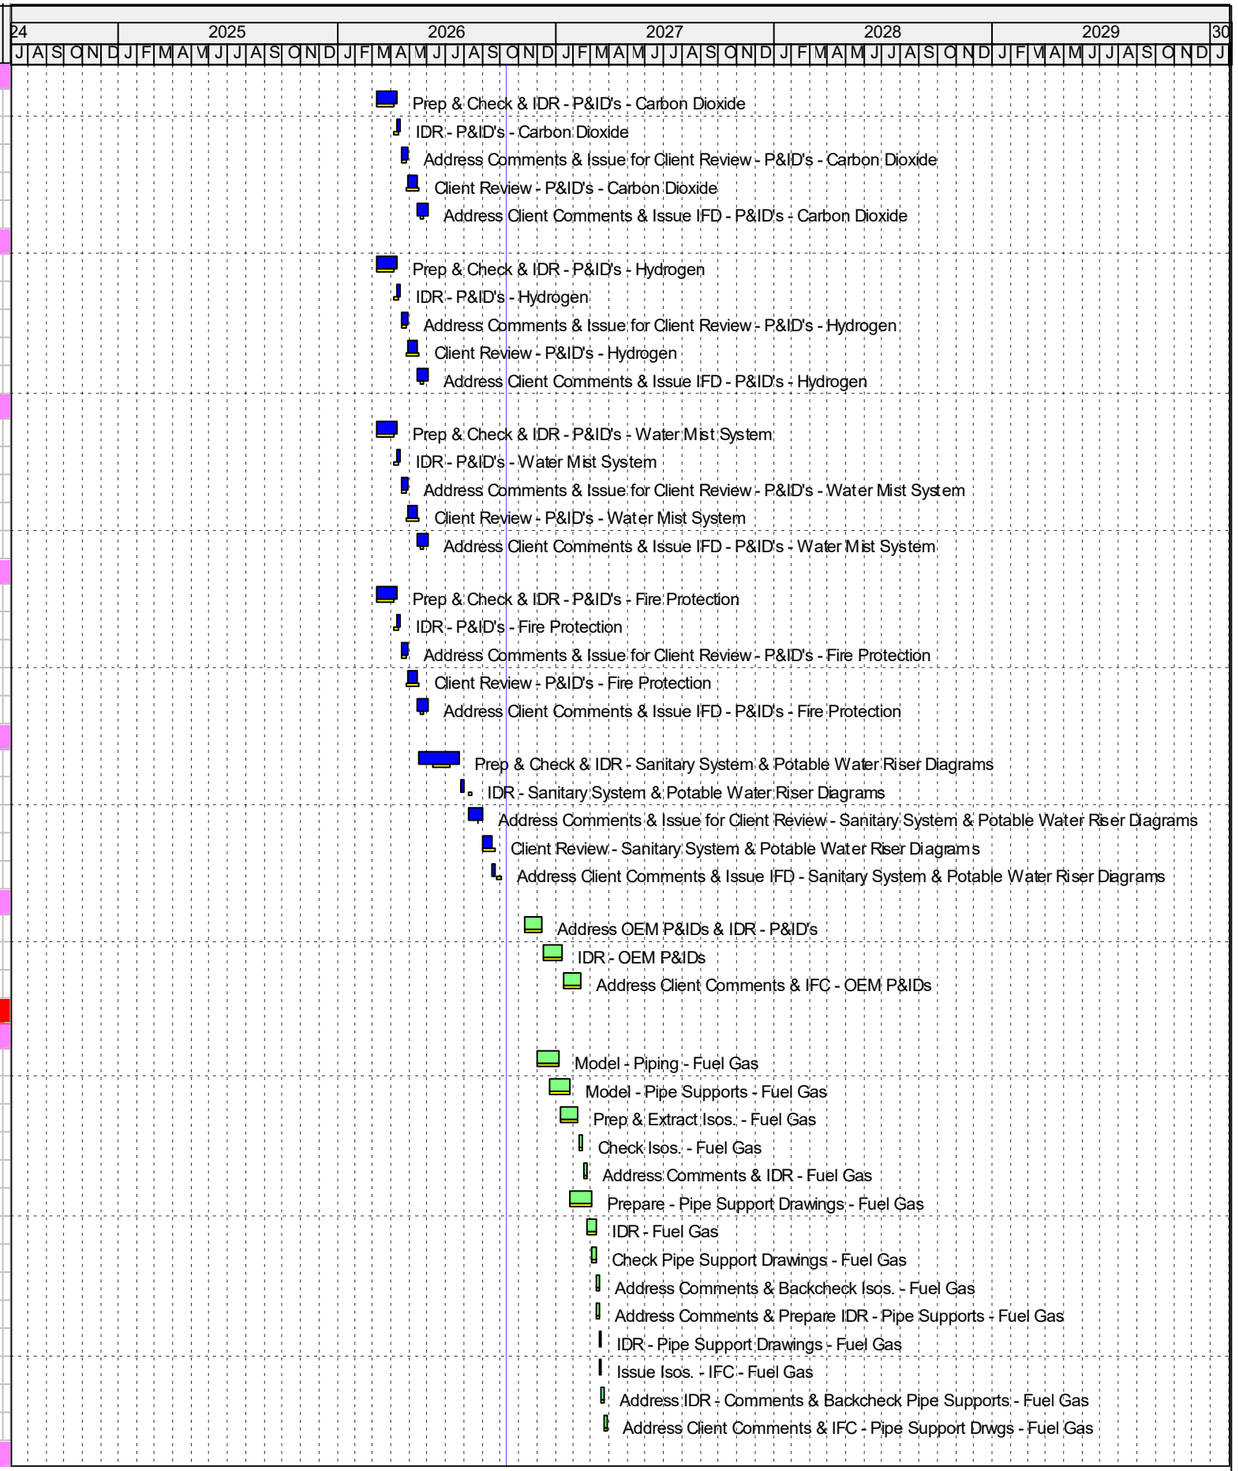

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC161102-3	Model - Piping - Fuel Oil	25	12/1/26 7:00 AM	1/8/27 5:00 PM	25
AEC161102-7	Model - Pipe Supports - Fuel Oil	20	12/22/26 7:00 AM	1/25/27 5:00 PM	44
AEC161102-4	Prep & Extract Isos. - Fuel Oil	20	1/11/27 7:00 AM	2/8/27 5:00 PM	35
AEC161102-4	Check Isos. - Fuel Oil	5	2/9/27 7:00 AM	2/16/27 5:00 PM	35
AEC161102-8	Prepare - Pipe Support Drawings - Fuel Oil	15	1/26/27 7:00 AM	2/16/27 5:00 PM	44
AEC161102-5	Address Comments & IDR - Fuel Oil	5	2/17/27 7:00 AM	2/23/27 5:00 PM	35
AEC161102-8	Check Pipe Support Drawings - Fuel Oil	5	2/17/27 7:00 AM	2/23/27 5:00 PM	44
AEC161102-9	Address Comments & Prepare IDR - Pipe Supports - Fuel Oil	5	2/24/27 7:00 AM	3/2/27 5:00 PM	44
AEC161102-9	IDR - Pipe Support Drawings - Fuel Oil	1	3/3/27 7:00 AM	3/3/27 5:00 PM	44
AEC161102-9	Address IDR - Comments & Backcheck Pipe Supports - Fuel Oil	1	3/4/27 7:00 AM	3/4/27 5:00 PM	44
AEC161102-9	Address Client Comments & IFC - Pipe Support Drwgs - Fuel Oil	1	3/5/27 7:00 AM	3/5/27 5:00 PM	44
AEC161102-6	IDR - Fuel Oil	10	2/24/27 7:00 AM	3/9/27 5:00 PM	35
AEC161102-6	Address Comments & Backcheck Isos. - Fuel Oil	5	3/10/27 7:00 AM	3/16/27 5:00 PM	35
AEC161102-7	Issue Isos. - IFC - Fuel Oil	2	3/17/27 7:00 AM	3/18/27 5:00 PM	35
BH CNN-KPJV-MAST-LIVE,03,03,04,05,03 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Demineralized Water					
AEC161103-3	Model - Piping - Demineralized Water	25	12/8/26 7:00 AM	1/15/27 5:00 PM	25
AEC161103-7	Model - Pipe Supports - Demineralized Water	20	1/4/27 7:00 AM	2/1/27 5:00 PM	25
AEC161103-4	Prep & Extract Isos. - Demineralized Water	20	2/2/27 7:00 AM	3/2/27 5:00 PM	25
AEC161103-8	Prepare - Pipe Support Drawings - Demineralized Water	20	2/8/27 7:00 AM	3/8/27 5:00 PM	30
AEC161103-4	Check Isos. - Demineralized Water	5	3/3/27 7:00 AM	3/9/27 5:00 PM	25
AEC161103-8	Check Pipe Support Drawings - Demineralized Water	5	3/9/27 7:00 AM	3/15/27 5:00 PM	30
AEC161103-5	Address Comments & IDR - Demineralized Water	5	3/10/27 7:00 AM	3/16/27 5:00 PM	25
AEC161103-9	Address Comments & Prepare IDR - Pipe Supports - Demineral	5	3/16/27 7:00 AM	3/22/27 5:00 PM	30
AEC161103-6	IDR - Demineralized Water	5	3/17/27 7:00 AM	3/23/27 5:00 PM	25
AEC161103-9	IDR - Pipe Support Drawings - Demineralized Water	1	3/23/27 7:00 AM	3/23/27 5:00 PM	30
AEC161103-9	Address IDR - Comments & Backcheck Pipe Supports - Demine	1	3/24/27 7:00 AM	3/24/27 5:00 PM	30
AEC161103-9	Address Client Comments & IFC - Pipe Support Drwgs - Demine	1	3/25/27 7:00 AM	3/25/27 5:00 PM	30
AEC161103-6	Address Comments & Backcheck Isos. - Demineralized Water	5	3/24/27 7:00 AM	3/31/27 5:00 PM	25
AEC161103-7	Issue Isos. - IFC - Demineralized Water	2	4/1/27 7:00 AM	4/2/27 5:00 PM	25
BH CNN-KPJV-MAST-LIVE,03,03,04,05,04 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Service Water					
AEC161104-3	Model - Piping - Service Water	25	12/8/26 7:00 AM	1/15/27 5:00 PM	30
AEC161104-7	Model - Pipe Supports - Service Water	20	1/4/27 7:00 AM	2/1/27 5:00 PM	30
AEC161104-4	Prep & Extract Isos. - Service Water	20	1/19/27 7:00 AM	2/16/27 5:00 PM	30
AEC161104-4	Check Isos. - Service Water	5	2/17/27 7:00 AM	2/23/27 5:00 PM	30
AEC161104-5	Address Comments & IDR - Service Water	5	2/24/27 7:00 AM	3/2/27 5:00 PM	30
AEC161104-8	Prepare - Pipe Support Drawings - Service Water	20	2/8/27 7:00 AM	3/8/27 5:00 PM	30
AEC161104-8	Check Pipe Support Drawings - Service Water	5	3/9/27 7:00 AM	3/15/27 5:00 PM	30
AEC161104-6	IDR - Service Water	10	3/3/27 7:00 AM	3/16/27 5:00 PM	30
AEC161104-9	Address Comments & Prepare IDR - Pipe Supports- Service Wa	5	3/16/27 7:00 AM	3/22/27 5:00 PM	30
AEC161104-6	Address Comments & Backcheck Isos. - Service Water	5	3/17/27 7:00 AM	3/23/27 5:00 PM	30
AEC161104-9	IDR - Pipe Support Drawings - Service Water	1	3/23/27 7:00 AM	3/23/27 5:00 PM	30
AEC161104-9	Address IDR - Comments & Backcheck Pipe Supports - Service	1	3/24/27 7:00 AM	3/24/27 5:00 PM	30
AEC161104-7	Issue Isos. - IFC - Service Water	2	3/24/27 7:00 AM	3/25/27 5:00 PM	30
AEC161104-9	Address Client Comments & IFC - Pipe Support Drwgs - Service	1	3/25/27 7:00 AM	3/25/27 5:00 PM	30
BH CNN-KPJV-MAST-LIVE,03,03,04,05,05 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Closed Cooling Water					
AEC161105-3	Model - Piping - Closed Cooling Water	22	10/7/26 7:00 AM A	11/10/26 5:00 PM	56
AEC161105-7	Model - Pipe Supports - Closed Cooling Water	20	11/27/26 7:00 AM	12/28/26 5:00 PM	56
AEC161105-8	Prepare - Pipe Support Drawings - Closed Cooling Water	20	12/29/26 7:00 AM	1/28/27 5:00 PM	56
AEC161105-8	Check Pipe Support Drawings - Closed Cooling Water	5	1/29/27 7:00 AM	2/4/27 5:00 PM	56
AEC161105-9	Address Comments & Prepare IDR - Pipe Supports - Closed Co	5	2/5/27 7:00 AM	2/11/27 5:00 PM	56



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC161105-9	IDR - Pipe Support Drawings - Closed Cooling Water	1	2/12/27 7:00 AM	2/12/27 5:00 PM	56
AEC161105-9	Address IDR - Comments & Backcheck Pipe Supports - Closed	1	2/16/27 7:00 AM	2/16/27 5:00 PM	56
AEC161105-9	Address Client Comments & IFC - Pipe Support Drwgs - Closed	1	2/17/27 7:00 AM	2/17/27 5:00 PM	56
AEC161105-4	Prep & Extract Isos. - Closed Cooling Water	15	2/23/27 7:00 AM	3/15/27 5:00 PM	16
AEC161105-4	Check Isos. - Closed Cooling Water	5	3/16/27 7:00 AM	3/22/27 5:00 PM	16
AEC161105-5	Address Comments & IDR - Closed Cooling Water	5	3/23/27 7:00 AM	3/30/27 5:00 PM	16
AEC161105-6	IDR - Closed Cooling Water	5	3/31/27 7:00 AM	4/6/27 5:00 PM	16
AEC161105-6	Address Comments & Backcheck Isos. - Closed Cooling Water	5	4/7/27 7:00 AM	4/13/27 5:00 PM	16
AEC161105-7	Issue Isos. - IFC - Closed Cooling Water	2	4/14/27 7:00 AM	4/15/27 5:00 PM	16
BH CNN-KPJV-MAST-LIVE,03,03,04,05,06 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Potable Water					
AEC161106-3	Model - Piping - Potable Water	25	12/15/26 7:00 AM	1/25/27 5:00 PM	20
AEC161106-4	Prep & Extract Isos. - Potable Water	20	2/2/27 7:00 AM	3/2/27 5:00 PM	20
AEC161106-4	Check Isos. - Potable Water	5	3/3/27 7:00 AM	3/9/27 5:00 PM	20
AEC161106-5	Address Comments & IDR - Potable Water	5	3/10/27 7:00 AM	3/16/27 5:00 PM	20
AEC161106-6	IDR - Potable Water	10	3/17/27 7:00 AM	3/31/27 5:00 PM	20
AEC161106-6	Address Comments & Backcheck Isos. - Potable Water	5	4/1/27 7:00 AM	4/7/27 5:00 PM	20
AEC161106-7	Issue Isos. - IFC - Potable Water	2	4/8/27 7:00 AM	4/9/27 5:00 PM	20
BH CNN-KPJV-MAST-LIVE,03,03,04,05,07 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Compressed Air					
AEC161107-3	Model - Piping - Compressed Air	1	9/4/26 7:00 AM A	10/12/26 5:00 PM	63
AEC161107-7	Model - Pipe Supports - Compressed Air	16	10/5/26 7:00 AM A	11/2/26 5:00 PM	92
AEC161107-4	Prep & Extract Isos. - Compressed Air	20	11/3/26 7:00 AM	12/2/26 5:00 PM	63
AEC161107-8	Prepare - Pipe Support Drawings - Compressed Air	20	11/3/26 7:00 AM	12/2/26 5:00 PM	92
AEC161107-4	Check Isos. - Compressed Air	5	12/3/26 7:00 AM	12/9/26 5:00 PM	63
AEC161107-8	Check Pipe Support Drawings - Compressed Air	5	12/3/26 7:00 AM	12/9/26 5:00 PM	92
AEC161107-5	Address Comments & IDR - Compressed Air	5	12/10/26 7:00 AM	12/16/26 5:00 PM	63
AEC161107-9	Address Comments & Prepare IDR - Pipe Supports- Compresse	5	12/10/26 7:00 AM	12/16/26 5:00 PM	92
AEC161107-9	IDR - Pipe Support Drawings - Compressed Air	1	12/17/26 7:00 AM	12/17/26 5:00 PM	92
AEC161107-9	Address IDR - Comments & Backcheck Pipe Supports - Compre	1	12/18/26 7:00 AM	12/18/26 5:00 PM	92
AEC161107-9	Address Client Comments & IFC - Pipe Support Drwgs - Compre	1	12/21/26 7:00 AM	12/21/26 5:00 PM	92
AEC161107-5	Perform - Pipe Stress Analysis - Compressed Air	15	12/17/26 7:00 AM	1/12/27 5:00 PM	63
AEC161107-6	IDR - Compressed Air	10	1/13/27 7:00 AM	1/27/27 5:00 PM	63
AEC161107-6	Address Comments & Backcheck Isos. - Compressed Air	5	1/28/27 7:00 AM	2/3/27 5:00 PM	63
AEC161107-7	Issue Isos. - IFC - Compressed Air	2	2/4/27 7:00 AM	2/5/27 5:00 PM	63
BH CNN-KPJV-MAST-LIVE,03,03,04,05,08 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Water Wash Drains					
AEC161108-7	Model - Pipe Supports - Water Wash Drains	10	10/15/26 7:00 AM	10/28/26 5:00 PM	81
AEC161108-3	Model - Piping - Water Wash Drains	14	9/24/26 7:00 AM A	10/29/26 5:00 PM	65
AEC161108-8	Prepare - Pipe Support Drawings - Water Wash Drains	20	10/29/26 7:00 AM	11/27/26 5:00 PM	81
AEC161108-8	Check Pipe Support Drawings - Water Wash Drains	5	11/30/26 7:00 AM	12/4/26 5:00 PM	81
AEC161108-9	Address Comments & Prepare IDR - Pipe Supports - Water Wa	5	12/7/26 7:00 AM	12/11/26 5:00 PM	81
AEC161108-9	IDR - Pipe Support Drawings - Water Wash Drains	10	12/14/26 7:00 AM	12/29/26 5:00 PM	81
AEC161108-9	Address IDR - Comments & Backcheck Pipe Supports - Water \	5	12/30/26 7:00 AM	1/7/27 5:00 PM	81
AEC161108-9	Address Client Comments & IFC - Pipe Support Drwgs - Water \	2	1/8/27 7:00 AM	1/11/27 5:00 PM	81
AEC161108-4	Prep & Extract Isos. - Water Wash Drains	20	2/23/27 7:00 AM	3/22/27 5:00 PM	6
AEC161108-4	Check Isos. - Water Wash Drains	5	3/23/27 7:00 AM	3/30/27 5:00 PM	6
AEC161108-5	Address Comments & IDR - Water Wash Drains	5	3/31/27 7:00 AM	4/6/27 5:00 PM	6
AEC161108-6	IDR - Water Wash Drains	10	4/7/27 7:00 AM	4/20/27 5:00 PM	6
AEC161108-6	Address Comments & Backcheck Isos. - Water Wash Drains	5	4/21/27 7:00 AM	4/27/27 5:00 PM	6
AEC161108-7	Issue Isos. - IFC - Water Wash Drains	2	4/28/27 7:00 AM	4/29/27 5:00 PM	6
BH CNN-KPJV-MAST-LIVE,03,03,04,05,17 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Ammonia					
AEC161118-4	Model - Pipe Supports - Ammonia Isometrics	10	1/8/27 7:00 AM	1/22/27 5:00 PM	125



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC161118-3	Model - Piping - Ammonia Isometrics	25	12/15/26 7:00 AM	1/25/27 5:00 PM	96
AEC161118-4	Prepare - Pipe Support Drawings - Ammonia Isometrics	20	1/25/27 7:00 AM	2/22/27 5:00 PM	125
AEC161118-5	Check Pipe Support Drawings - Ammonia Isometrics	5	2/23/27 7:00 AM	3/1/27 5:00 PM	125
AEC161118-6	Address Comments & Prepare IDR - Pipe Supports - Ammonia I	5	3/2/27 7:00 AM	3/8/27 5:00 PM	125
AEC161118-6	IDR - Pipe Support Drawings - Ammonia Isometrics	1	3/9/27 7:00 AM	3/9/27 5:00 PM	125
AEC161118-7	Address IDR - Comments & Backcheck Pipe Supports- Ammoni	1	3/10/27 7:00 AM	3/10/27 5:00 PM	125
AEC161118-7	Address Client Comments & IFC - Pipe Support Drawings - Amn	1	3/11/27 7:00 AM	3/11/27 5:00 PM	125
AEC161118-5	Prep & Extract Isos. - Ammonia Isometrics	20	2/16/27 7:00 AM	3/15/27 5:00 PM	96
AEC161118-8	Check Isos. - Ammonia Isometrics	5	3/16/27 7:00 AM	3/22/27 5:00 PM	96
AEC161118-8	Address Comments & IDR - Ammonia Isometrics	5	3/23/27 7:00 AM	3/30/27 5:00 PM	96
AEC161118-9	IDR - Ammonia Isometrics	10	3/31/27 7:00 AM	4/13/27 5:00 PM	96
AEC161118-9	Address Comments & Backcheck Isos. - Ammonia Isometrics	5	4/14/27 7:00 AM	4/20/27 5:00 PM	96
AEC161118-1	Issue Isos. - IFC - Ammonia Isometrics	2	4/21/27 7:00 AM	4/22/27 5:00 PM	96
BH CNN-KPJV-MAST-LIVE,03,03,04,05,09 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Wastewater					
AEC161109-3	Model - Piping - Wastewater	0	8/24/26 7:00 AM A	9/28/26 5:00 PM A	
AEC161109-7	Model - Pipe Supports - Wastewater	10	10/22/26 7:00 AM	11/4/26 5:00 PM	90
AEC161109-4	Prep & Extract Isos. - Wastewater	20	10/20/26 7:00 AM	11/17/26 5:00 PM	88
AEC161109-4	Check Isos. - Wastewater	5	11/18/26 7:00 AM	11/24/26 5:00 PM	88
AEC161109-5	Address Comments & IDR - Wastewater	5	11/25/26 7:00 AM	12/2/26 5:00 PM	88
AEC161109-8	Prepare - Pipe Support Drawings - Wastewater	20	11/5/26 7:00 AM	12/4/26 5:00 PM	90
AEC161109-8	Check Pipe Support Drawings - Wastewater	5	12/7/26 7:00 AM	12/11/26 5:00 PM	90
AEC161109-6	IDR - Wastewater	10	12/3/26 7:00 AM	12/16/26 5:00 PM	88
AEC161109-9	Address Comments & Prepare IDR - Pipe Supports - Wastewat	5	12/14/26 7:00 AM	12/18/26 5:00 PM	90
AEC161109-9	IDR - Pipe Support Drawings - Wastewater	1	12/21/26 7:00 AM	12/21/26 5:00 PM	90
AEC161109-9	Address IDR - Comments & Backcheck Pipe Supports- Wastew	1	12/22/26 7:00 AM	12/22/26 5:00 PM	90
AEC161109-6	Address Comments & Backcheck Isos. - Wastewater	5	12/17/26 7:00 AM	12/23/26 5:00 PM	88
AEC161109-9	Address Client Comments & IFC - Pipe Support Drwgs - Wastev	1	12/23/26 7:00 AM	12/23/26 5:00 PM	90
AEC161109-7	Issue Isos. - IFC - Wastewater	2	12/28/26 7:00 AM	12/29/26 5:00 PM	88
BH CNN-KPJV-MAST-LIVE,03,03,04,05,10 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Lube Oil					
AEC161110-3	Model - Piping - Lube Oil	25	12/8/26 7:00 AM	1/15/27 5:00 PM	20
AEC161110-4	Prep & Extract Isos - Lube Oil	20	2/23/27 7:00 AM	3/22/27 5:00 PM	36
AEC161110-4	Check Isos. - Lube Oil	5	3/23/27 7:00 AM	3/30/27 5:00 PM	36
AEC161110-5	Address Comments & IDR - Lube Oil	5	3/31/27 7:00 AM	4/6/27 5:00 PM	36
AEC161110-6	IDR - Lube Oil	10	4/7/27 7:00 AM	4/20/27 5:00 PM	36
AEC161110-6	Address Comments & Backcheck Isos. - Lube Oil	5	4/21/27 7:00 AM	4/27/27 5:00 PM	36
AEC161110-7	Issue Isos. - IFC - Lube Oil	2	4/28/27 7:00 AM	4/29/27 5:00 PM	36
BH CNN-KPJV-MAST-LIVE,03,03,04,05,11 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Carbon Dioxide					
AEC161111-3	Model - Piping - Carbon Dioxide	25	12/1/26 7:00 AM	1/8/27 5:00 PM	20
AEC161111-4	Prep & Extract Isos. - Carbon Dioxide	20	2/23/27 7:00 AM	3/22/27 5:00 PM	28
AEC161111-4	Check Isos. - Carbon Dioxide	5	3/23/27 7:00 AM	3/30/27 5:00 PM	28
AEC161111-5	Address Comments & IDR - Carbon Dioxide	5	3/31/27 7:00 AM	4/6/27 5:00 PM	28
AEC161111-6	IDR - Carbon Dioxide	10	4/7/27 7:00 AM	4/20/27 5:00 PM	28
AEC161111-6	Address Comments & Backcheck Isos. - Carbon Dioxide	5	4/21/27 7:00 AM	4/27/27 5:00 PM	28
AEC161111-7	Issue Isos. - IFC - Carbon Dioxide	2	4/28/27 7:00 AM	4/29/27 5:00 PM	36
BH CNN-KPJV-MAST-LIVE,03,03,04,05,12 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Hydrogen					
AEC161112-3	Model - Piping - Hydrogen	25	12/1/26 7:00 AM	1/8/27 5:00 PM	89
AEC161112-4	Prep & Extract Isos. - Hydrogen	15	2/23/27 7:00 AM	3/15/27 5:00 PM	83
AEC161112-4	Check Isos. - Hydrogen	5	3/16/27 7:00 AM	3/22/27 5:00 PM	83
AEC161112-5	Address Comments & IDR - Hydrogen	5	3/23/27 7:00 AM	3/30/27 5:00 PM	83
AEC161112-6	IDR - Hydrogen	10	3/31/27 7:00 AM	4/13/27 5:00 PM	83




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC161112-6	Address Comments & Backcheck Isos. - Hydrogen	5	4/14/27 7:00 AM	4/20/27 5:00 PM	83
AEC161112-7	Issue Isos. - IFC - Hydrogen	2	4/21/27 7:00 AM	4/22/27 5:00 PM	83
BH CNN-KPJV-MAST-LIVE,03,03,04,05,13 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Water Mist					
AEC161113-3	Model - Piping - Water Mist	25	1/26/27 7:00 AM	3/2/27 5:00 PM	37
AEC161113-1	Model - Pipe Supports - Water Mist	10	3/29/27 7:00 AM	4/9/27 5:00 PM	398
AEC161113-1	Prep & Extract Isos. - Water Mist	20	3/24/27 7:00 AM	4/21/27 5:00 PM	37
AEC161113-1	Check Isos. - Water Mist	5	4/22/27 7:00 AM	4/28/27 5:00 PM	37
AEC161113-1	Address Comments & IDR - Water Mist	5	4/29/27 7:00 AM	5/5/27 5:00 PM	37
AEC161113-1	Prepare - Pipe Support Drawings - Water Mist	20	4/12/27 7:00 AM	5/7/27 5:00 PM	398
AEC161113-1	Check Pipe Support Drawings - Water Mist	5	5/10/27 7:00 AM	5/14/27 5:00 PM	398
AEC161113-1	IDR - Water Mist	10	5/6/27 7:00 AM	5/19/27 5:00 PM	37
AEC161113-2	Address Comments & Prepare IDR - Pipe Supports - Water Mis	5	5/17/27 7:00 AM	5/21/27 5:00 PM	398
AEC161113-2	IDR - Pipe Support Drawings - Water Mist	1	5/24/27 7:00 AM	5/24/27 5:00 PM	398
AEC161113-2	Address IDR - Comments & Backcheck Pipe Supports- Water M	1	5/25/27 7:00 AM	5/25/27 5:00 PM	398
AEC161113-2	Address Comments & Backcheck Isos. - Water Mist	5	5/20/27 7:00 AM	5/26/27 5:00 PM	37
AEC161113-2	Address Client Comments & IFC - Pipe Support Drwgs - Water I	1	5/26/27 7:00 AM	5/26/27 5:00 PM	398
AEC161113-2	Issue Isos. - IFC - Water Mist	2	5/27/27 7:00 AM	5/28/27 5:00 PM	37
BH CNN-KPJV-MAST-LIVE,03,03,04,05,16 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Nitrogen					
AEC161113-8	Model - Piping - Nitrogen	70	1/4/27 7:00 AM	4/14/27 5:00 PM	85
AEC161113-9	Prep & Extract Isos. - Nitrogen	20	4/15/27 7:00 AM	5/12/27 5:00 PM	85
AEC161113-1	Check Isos. - Nitrogen	5	5/13/27 7:00 AM	5/19/27 5:00 PM	85
AEC161113-1	Address Comments & IDR - Nitrogen	5	5/20/27 7:00 AM	5/26/27 5:00 PM	85
AEC161113-1	IDR - Nitrogen	10	5/27/27 7:00 AM	6/10/27 5:00 PM	85
AEC161113-1	Address Comments & Backcheck Isos. - Nitrogen	5	6/11/27 7:00 AM	6/17/27 5:00 PM	85
AEC161113-1	Issue Isos. - IFC - Nitrogen	2	6/21/27 7:00 AM	6/22/27 5:00 PM	85
BH CNN-KPJV-MAST-LIVE,03,03,04,05,14 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Fire Protection					
AEC161165-0	Model - Piping - Fire Protection	25	12/1/26 7:00 AM	1/8/27 5:00 PM	72
AEC161165-1	Model - Pipe Supports - Fire Protection	10	2/4/27 7:00 AM	2/18/27 5:00 PM	74
AEC161165-1	Prep & Extract Isos. - Fire Protection	20	2/2/27 7:00 AM	3/2/27 5:00 PM	72
AEC161165-2	Check Isos. - Fire Protection	5	3/3/27 7:00 AM	3/9/27 5:00 PM	72
AEC161165-3	Address Comments & IDR - Fire Protection	5	3/10/27 7:00 AM	3/16/27 5:00 PM	72
AEC161165-2	Prepare - Pipe Support Drawings - Fire Protection	20	2/19/27 7:00 AM	3/18/27 5:00 PM	74
AEC161165-4	Check Pipe Support Drawings - Fire Protection	5	3/19/27 7:00 AM	3/25/27 5:00 PM	74
AEC161165-3	IDR - Fire Protection	10	3/17/27 7:00 AM	3/31/27 5:00 PM	72
AEC161165-4	Address Comments & Prepare IDR - Pipe Supports - Fire Protec	5	3/29/27 7:00 AM	4/2/27 5:00 PM	74
AEC161165-5	IDR - Pipe Support Drawings - Fire Protection	1	4/5/27 7:00 AM	4/5/27 5:00 PM	74
AEC161165-6	Address IDR - Comments & Backcheck Pipe Supports- Fire Prot	1	4/6/27 7:00 AM	4/6/27 5:00 PM	74
AEC161165-5	Address Comments & Backcheck Isos. - Fire Protection	5	4/1/27 7:00 AM	4/7/27 5:00 PM	72
AEC161165-6	Address Client Comments & IFC - Pipe Support Drwgs - Fire Prc	1	4/7/27 7:00 AM	4/7/27 5:00 PM	74
AEC161165-7	Issue Isos. - IFC - Fire Protection	2	4/8/27 7:00 AM	4/9/27 5:00 PM	72
BH CNN-KPJV-MAST-LIVE,03,03,04,05,15 ENG - Piping - Modeling & Drawings - Isometrics & Pipe Supports - Chemical Feed					
AEC161160-0	Model - Piping - Chemical Feed	25	12/15/26 7:00 AM	1/25/27 5:00 PM	30
AEC161160-1	Model - Pipe Supports - Chemical Feed	10	2/19/27 7:00 AM	3/4/27 5:00 PM	32
AEC161160-1	Prep & Extract Isos. - Chemical Feed	20	2/17/27 7:00 AM	3/16/27 5:00 PM	30
AEC161160-2	Check Isos. - Chemical Feed	5	3/17/27 7:00 AM	3/23/27 5:00 PM	30
AEC161160-3	Address Comments & IDR - Chemical Feed	5	3/24/27 7:00 AM	3/31/27 5:00 PM	30
AEC161160-2	Prepare - Pipe Support Drawings - Chemical Feed	20	3/5/27 7:00 AM	4/2/27 5:00 PM	32
AEC161160-4	Check Pipe Support Drawings - Chemical Feed	5	4/5/27 7:00 AM	4/9/27 5:00 PM	32
AEC161160-3	IDR - Chemical Feed	10	4/1/27 7:00 AM	4/14/27 5:00 PM	30
AEC161160-4	Address Comments & Prepare IDR - Pipe Supports - Chemical I	5	4/12/27 7:00 AM	4/16/27 5:00 PM	32

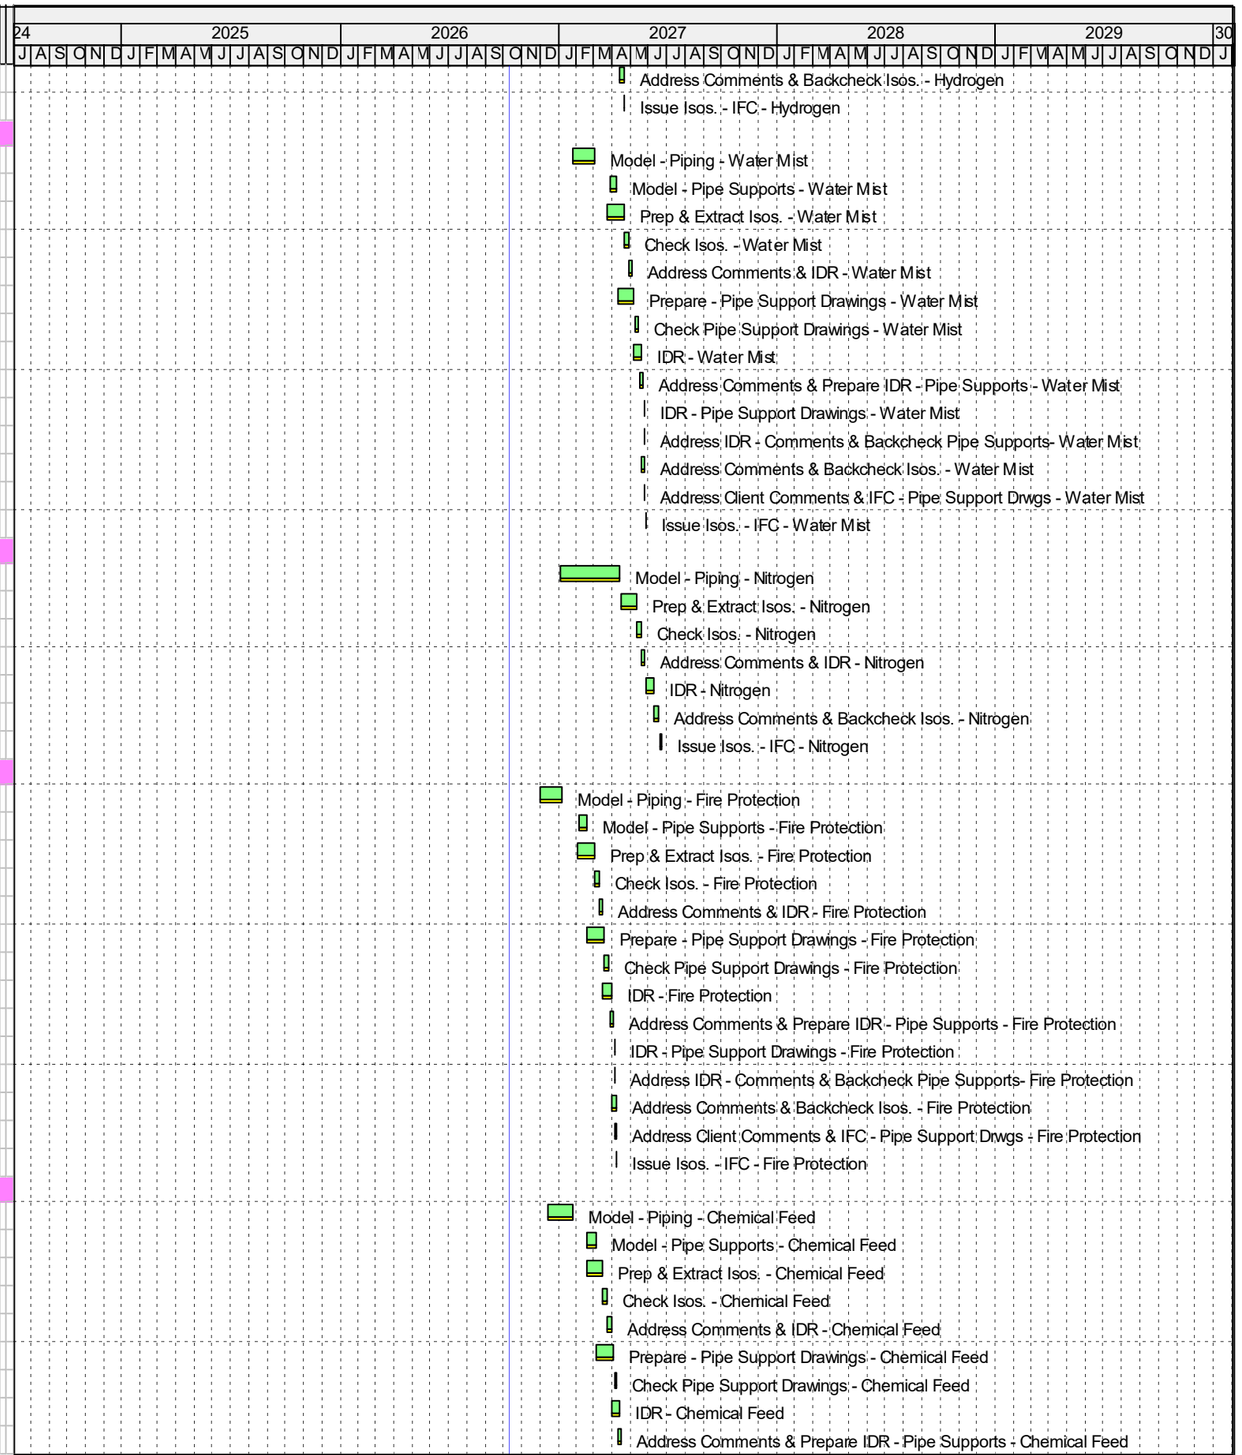

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC161160-5	IDR - Pipe Support Drawings - Chemical Feed	1	4/19/27 7:00 AM	4/19/27 5:00 PM	32
AEC161160-6	Address IDR - Comments & Backcheck Pipe Supports- Chemica	1	4/20/27 7:00 AM	4/20/27 5:00 PM	32
AEC161160-5	Address Comments & Backcheck Isos. - Chemical Feed	5	4/15/27 7:00 AM	4/21/27 5:00 PM	30
AEC161160-6	Address Client Comments & IFC - Pipe Support Drwgs - Chemic	1	4/21/27 7:00 AM	4/21/27 5:00 PM	32
AEC161160-7	Issue Isos. - IFC - Chemical Feed	2	4/22/27 7:00 AM	4/23/27 5:00 PM	30
BH CNN-KPJV-MAST-LIVE,03,02 ENG - Electrical					
AEC170001-20	Received - AMEREN Utility Data (short Circuit)	0		3/9/26 5:00 PM A	
AEC170001-25	Model - Power System Modeling	0	3/9/26 7:00 AM A	4/13/26 5:00 PM A	
AEC170001-15	Receive - Equipment GA Drawings	0	8/28/26 7:00 AM A	8/28/26 5:00 PM A	
AEC170001-10	Receive - Vendor Electrical Information	3	4/6/26 7:00 AM A	10/14/26 5:00 PM	454
AEC170001-05	Receive - Vendor Information - (GE)	25	10/12/26 7:00 AM	11/16/26 5:00 PM	392
BH CNN-KPJV-MAST-LIVE,03,02,08 ENG - Electrical - Specifications					
BH CNN-KPJV-MAST-LIVE,03,02,08,01 ENG - Electrical - Specifications - Relay & Metering Equipment					
AEC170805-05	Prep & Check & IDR - Spec. - Relay & Metering Equipment	7	8/18/26 7:00 AM A	10/20/26 5:00 PM	510
AEC170805-10	IDR - Procurement Spec. - Relay & Metering Equipment	5	10/21/26 7:00 AM	10/27/26 5:00 PM	510
AEC170805-15	Address Comments & Issue for Client Review - Spec. - Relay &	5	10/28/26 7:00 AM	11/3/26 5:00 PM	510
AEC170805-20	Client Review - Procurement Spec. - Relay & Metering Equipme	15	11/4/26 7:00 AM	11/25/26 5:00 PM	510
AEC170805-25	Address Client Comments & Finalize Spec. - Relay & Metering E	10	11/27/26 7:00 AM	12/10/26 5:00 PM	510
BH CNN-KPJV-MAST-LIVE,03,02,08,03 ENG - Electrical - Specifications - Isophase Bus Duct					
AEC170803-05	Prep & Check & IDR - Spec. - Isophase Bus Duct	0	3/2/26 7:00 AM A	4/7/26 5:00 PM A	
AEC170803-20	IDR - Procurement Spec. - Isophase Bus Duct	0	4/8/26 7:00 AM A	4/16/26 5:00 PM A	
AEC170803-25	Address Comments & Issue for Client Review - Mech Spec - Iso	0	4/17/26 7:00 AM A	4/17/26 5:00 PM A	
AEC170803-30	Client Review - Procurement Spec. - Isophase Bus Duct	0	4/20/26 7:00 AM A	5/4/26 5:00 PM A	
AEC170803-35	Address Client Comments & Finalize Spec. - Isophase Bus Duct	0	5/5/26 7:00 AM A	5/15/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,02,08,04 ENG - Electrical - Specifications - Motor Control Centers(Misc. Areas))					
AEC170804-05	Prep & Check & IDR - Spec. - Motor Control Centers (Admin Are	20	10/22/26 7:00 AM	11/19/26 5:00 PM	489
AEC170804-20	IDR - Procurement Spec. - Motor Control Centers (Admin Area)	5	11/20/26 7:00 AM	11/27/26 5:00 PM	489
AEC170804-25	Address Comments & Issue for Client Review - Spec. - Motor C	5	11/30/26 7:00 AM	12/4/26 5:00 PM	489
AEC170804-30	Client Review - Procurement Spec. - Motor Control Centers (Adr	15	12/7/26 7:00 AM	12/29/26 5:00 PM	489
AEC170804-35	Address Client Comments & Finalize Spec. - Motor Control Cent	10	12/30/26 7:00 AM	1/14/27 5:00 PM	489
BH CNN-KPJV-MAST-LIVE,03,02,08,09 ENG - Electrical - Specifications - 125VDC/120VAC Specifications					
AEC170809-05	Prep & Check & IDR - Spec. - 125VDC/120VAC	0	5/4/26 7:00 AM A	6/30/26 5:00 PM A	
AEC170809-20	IDR - Procurement Spec. - 125VDC/120VAC	0	7/1/26 7:00 AM A	7/9/26 5:00 PM A	
AEC170809-25	Address Comments & Issue for Client Review - Spec. - 125VDC	0	7/10/26 7:00 AM A	7/23/26 5:00 PM A	
AEC170809-30	Client Review - Procurement Spec. - 125VDC/120VAC	0	7/23/26 7:00 AM A	8/7/26 5:00 PM A	
AEC170809-35	Address Client Comments & Finalize Spec. - 125VDC/120VAC	0	8/10/26 7:00 AM A	8/24/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,02,08,10 ENG - Electrical - Specifications - Heat Trace Specification					
AEC170810-05	Prep & IDR - Spec. - Heat Trace	10	6/23/27 7:00 AM	7/7/27 5:00 PM	336
AEC170810-20	IDR - Procurement Spec. - Heat Trace	5	7/8/27 7:00 AM	7/14/27 5:00 PM	336
AEC170810-25	Address Comments & Issue for Client Review - Spec. - Heat Tra	5	7/15/27 7:00 AM	7/21/27 5:00 PM	336
AEC170810-30	Client Review - Procurement Spec. - Heat Trace	15	7/22/27 7:00 AM	8/11/27 5:00 PM	336
AEC170810-35	Address Client Comments & Finalize Spec. - Heat Trace	10	8/12/27 7:00 AM	8/25/27 5:00 PM	336
BH CNN-KPJV-MAST-LIVE,03,02,08,13 ENG - Electrical - Specifications - Cathodic Protection					
AEC170812-05	Prep & Check & IDR - Spec. - Cathodic Protection	10	11/16/26 7:00 AM	11/30/26 5:00 PM	483
AEC170812-10	IDR - Procurement Spec. - Cathodic Protection	5	12/1/26 7:00 AM	12/7/26 5:00 PM	483
AEC170812-15	Address Comments & Issue for Client Review - Spec. - Cathodic	5	12/8/26 7:00 AM	12/14/26 5:00 PM	483
AEC170812-20	Client Review - Procurement Spec. - Cathodic Protection	15	12/15/26 7:00 AM	1/8/27 5:00 PM	483
AEC170812-25	Address Client Comments & Finalize Spec. - Cathodic Protectio	10	1/11/27 7:00 AM	1/25/27 5:00 PM	483
BH CNN-KPJV-MAST-LIVE,03,02,01 ENG - Electrical - Calculations & Studies					
BH CNN-KPJV-MAST-LIVE,03,02,01,01 ENG - Electrical - Calculations & Studies - LF/SC Calculation					
AEC170501-05	Prepare & Issue for Client Review - Preliminary Electrical LF/SC	0	3/30/26 7:00 AM A	5/1/26 5:00 PM A	




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC170501-10	IDR - Preliminary Electrical LF/SC Calculations	0	5/4/26 7:00 AM A	5/6/26 5:00 PM A	
AEC170501-15	Address IDR Comments & Issue for CR - Preliminary Electrical L	0	5/6/26 7:00 AM A	5/13/26 5:00 PM A	
AEC170501-20	Client Review - Preliminary - Electrical LF/SC Calculations	0	5/13/26 7:00 AM A	5/26/26 5:00 PM A	
AEC170501-25	Address Client Review Comments & Issue Preliminary Electrical	5	5/27/26 7:00 AM A	10/16/26 5:00 PM	349
AEC170501-30	Prepare & Issue for Client Review - Final Electrical LF/SC Calcul	26	1/8/27 7:00 AM	2/16/27 5:00 PM	296
AEC170501-35	Client Review - Final Electrical LF/SC Calculations	15	2/17/27 7:00 AM	3/9/27 5:00 PM	296
AEC170501-40	Address Client Review Comments & Issue Final - Electrical LF/S	10	3/10/27 7:00 AM	3/23/27 5:00 PM	296
BH CNN-KPJV-MAST-LIVE,03,02,01,09 ENG - Electrical - Calculations & Studies - ENG - Electrical Interference Study					
AEC170507-05	Prepare & Issue for Client Review - Preliminary Electrical Interfer	15	4/1/27 7:00 AM	4/21/27 5:00 PM	303
AEC170507-10	Client Review - Preliminary - Electrical Interference Study	15	4/22/27 7:00 AM	5/12/27 5:00 PM	303
AEC170507-15	Address Client Review Comments & Issue Final - Electrical Inter	10	5/13/27 7:00 AM	5/26/27 5:00 PM	303
AEC170507-25	Client Review - Final Electrical Interference Study	15	5/27/27 7:00 AM	6/17/27 5:00 PM	303
AEC170507-30	Address Client Review Comments & Issue Final - Electrical Inter	10	6/21/27 7:00 AM	7/2/27 5:00 PM	303
BH CNN-KPJV-MAST-LIVE,03,02,01,10 ENG - Electrical - Calculations & Studies - Power System Stability Study					
AEC170508-05	Prepare & Issue for Client Review - Preliminary Power System S	15	3/29/27 7:00 AM	4/16/27 5:00 PM	296
AEC170508-10	Client Review - Preliminary - Power System Stability Study	15	4/19/27 7:00 AM	5/7/27 5:00 PM	296
AEC170508-20	Address Client Review Comments & Issue for Client Review - Fi	10	5/10/27 7:00 AM	5/21/27 5:00 PM	296
AEC170508-25	Client Review - Final Power System Stability Study	15	5/24/27 7:00 AM	6/14/27 5:00 PM	296
AEC170508-30	Address Client Review Comments & Issue Final - Power System	10	6/15/27 7:00 AM	6/29/27 5:00 PM	296
BH CNN-KPJV-MAST-LIVE,03,02,01,02 ENG - Electrical - Calculations & Studies - Isophase Bus Sizing Calculation					
AEC170502-05	Prepare - Preliminary Isophase Bus Sizing Calculation	0	3/9/26 7:00 AM A	4/1/26 5:00 PM A	
AEC170502-10	Issue for Client Review - Preliminary Electrical Isophase Bus Siz	0	4/1/26 7:00 AM A	4/7/26 5:00 PM A	
AEC170502-20	Client Review - Isophase Bus Sizing Calculation	0	4/7/26 7:00 AM A	5/8/26 5:00 PM A	
AEC170502-25	Address Client Review Comments & Issue Final - Isophase Bus	0	5/8/26 7:00 AM A	5/15/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,02,01,03 ENG - Electrical - Calculations & Studies - 125VDC/120VAC Load Calculation					
AEC170503-05	Prepare & IDR - 125VDC/120VAC Load Calculation	0	5/18/26 7:00 AM A	6/19/26 5:00 PM A	
AEC170503-10	IDR - 125VDC/120VAC Load Calculation	0	6/22/26 7:00 AM A	7/2/26 5:00 PM A	
AEC170503-15	Address IDR - Comments & Issue for Client Review - 125VDC/1	0	7/6/26 7:00 AM A	7/23/26 5:00 PM A	
AEC170503-20	Client Review - 125VDC/120VAC Load Calculation	0	7/23/26 7:00 AM A	8/7/26 5:00 PM A	
AEC170503-25	Address Client Review comments & Issue Final - 125VDC/120V	0	8/10/26 7:00 AM A	8/24/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,02,01,04 ENG - Electrical - Calculations & Studies - Lightning Protection Calculation					
AEC170504-05	Prepare - Preliminary Lightning Protection Calculation & Issue fc	0	8/3/26 7:00 AM A	10/1/26 5:00 PM A	
AEC170504-10	IDR - Preliminary Lightning Protection Calculation	0	10/1/26 7:00 AM A	10/7/26 5:00 PM A	
AEC170504-15	Address IDR - Comments & Issue for Client Review - Lightning F	13	10/8/26 7:00 AM A	10/28/26 5:00 PM	280
AEC170504-20	Client Review - Lightning Protection Calculation	15	10/29/26 7:00 AM	11/19/26 5:00 PM	280
AEC170504-25	Address Client Comments & IFC - Lightning Protection Calculati	5	11/20/26 7:00 AM	11/27/26 5:00 PM	280
BH CNN-KPJV-MAST-LIVE,03,02,01,05 ENG - Electrical - Calculations & Studies - Relay Setting & Coordination Study					
AEC170505-05	Prepare & Issue for Client Review - Preliminary Relay Setting & (	35	6/30/27 7:00 AM	8/18/27 5:00 PM	296
AEC170505-15	Client Review - Preliminary - Relay Setting & Coordination Study	15	8/19/27 7:00 AM	9/9/27 5:00 PM	311
AEC170505-20	Review & Revise - Study - Relay Setting & Coordination	5	9/10/27 7:00 AM	9/16/27 5:00 PM	311
AEC170505-25	Issue Final Relay Setting & Coordination Study	10	9/17/27 7:00 AM	9/30/27 5:00 PM	311
BH CNN-KPJV-MAST-LIVE,03,02,01,07 ENG - Electrical - Calculations & Studies - Grounding Calculation					
AEC170509-05	Prepare & Issue for Client Review - Grounding Calculation	0	4/16/26 7:00 AM A	6/25/26 5:00 PM A	
AEC170509-10	IDR - Grounding Calculation	0	6/24/26 7:00 AM A	7/8/26 5:00 PM A	
AEC170509-15	Address IDR - Comments & Issue for Client Review - Grounding	0	7/9/26 7:00 AM A	7/16/26 5:00 PM A	
AEC170509-20	Client Review - Grounding Calculation	0	7/17/26 7:00 AM A	7/24/26 5:00 PM A	
AEC170509-25	Address Client Comments & IFC - Grounding Calculation	0	7/27/26 7:00 AM A	8/20/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,02,01,08 ENG - Electrical - Calculations & Studies - Cable Take Off					
AEC171182-35	Take Off - Cable - MV	15	5/12/27 7:00 AM	6/2/27 5:00 PM	289
AEC171182-45	Take Off - Cable - LV	15	6/3/27 7:00 AM	6/24/27 5:00 PM	289
AEC171182-55	Take Off - Cable - Control	45	6/25/27 7:00 AM	8/27/27 5:00 PM	289

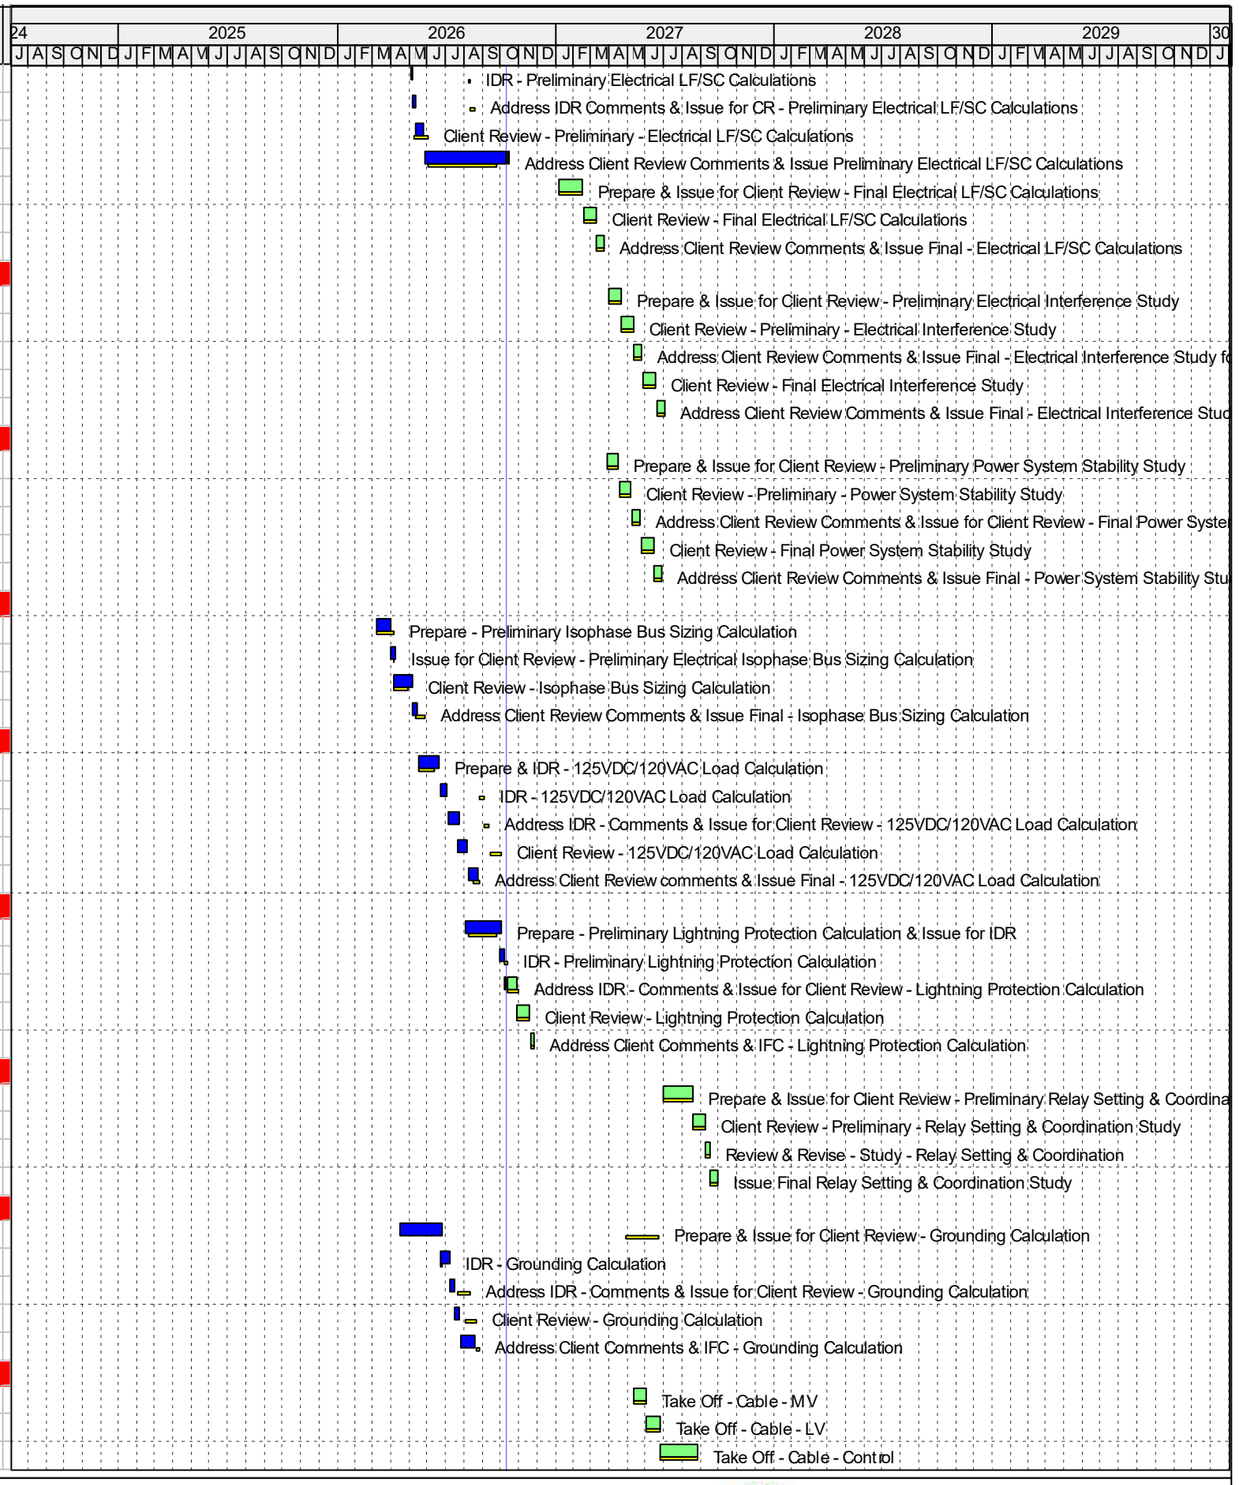

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC171182-65	Take Off - Cable - Instrumentation	45	8/30/27 7:00 AM	11/1/27 5:00 PM	289
BH CNN-KPJV-MAST-LIVE,03,02,01,06 ENG - Electrical - Calculations & Studies - ARC Flash Study					
AEC170506-05	Prepare & Issue for Client Review - Preliminary ARC Flash Study	40	7/15/27 7:00 AM	9/9/27 5:00 PM	296
AEC170506-15	Client Review - Preliminary - ARC Flash Study	15	9/10/27 7:00 AM	9/30/27 5:00 PM	296
AEC170506-20	Review & Revise - Study - ARC Flash	15	10/1/27 7:00 AM	10/21/27 5:00 PM	296
AEC170506-25	Issue Final ARC Flash Study	2	10/20/27 7:00 AM	10/21/27 5:00 PM	296
BH CNN-KPJV-MAST-LIVE,03,02,01,11 ENG - Electrical - Calculations & Studies - Lighting Calculations					
AEC170510-05	Prepare - Preliminary Lighting Calculation & IDR & CR	38	7/13/26 7:00 AM A	12/4/26 5:00 PM	54
AEC170510-10	IDR - Preliminary Lighting Calculation	5	12/7/26 7:00 AM	12/11/26 5:00 PM	509
AEC170510-20	Client Review - Lighting Calculation	15	12/7/26 7:00 AM	12/29/26 5:00 PM	54
AEC170510-25	Address Client Comments & IFC - Lighting Calculation	5	12/30/26 7:00 AM	1/7/27 5:00 PM	54
BH CNN-KPJV-MAST-LIVE,03,02,09 ENG - Electrical - Single Line & Three Line Diagrams					
BH CNN-KPJV-MAST-LIVE,03,02,09,01 ENG - Electrical - Single Line & Three Line Diagrams - 6900V SWGR, 480V SWGR - Single Lines					
AEC171101-05	Prepare - Preliminary Single Lines & IDR - 6900V SWGR, 480V	0	3/30/26 7:00 AM A	4/7/26 5:00 PM A	
AEC171101-10	IDR - Single Lines - 6900V SWGR, 480V SWGR	0	4/7/26 7:00 AM A	4/14/26 5:00 PM A	
AEC171101-15	Address IDR - Comments Single Lines & Issue for Client Review	0	4/15/26 7:00 AM A	4/17/26 5:00 PM A	
AEC171101-20	Client Review - Preliminary - Single Lines - 6900V SWGR, 480V	0	4/17/26 7:00 AM A	5/4/26 5:00 PM A	
AEC171101-25	Address Client Comments & Issue IFD - Single Lines - 6900V S	0	5/5/26 7:00 AM A	5/20/26 5:00 PM A	
AEC171101-30	Update with Vendor Information & Issue Final Single Lines - 690	5	3/24/27 7:00 AM	3/31/27 5:00 PM	438
BH CNN-KPJV-MAST-LIVE,03,02,09,02 ENG - Electrical - Single Line & Three Line Diagrams - Motor Control Centers - Single Lines					
AEC171102-05	Prepare - Preliminary Single Lines & Issue for Client Review - 48	0	4/6/26 7:00 AM A	5/15/26 5:00 PM A	
AEC171102-15	Client Review - Preliminary - Single Lines - 480V Motor Control C	0	5/15/26 7:00 AM A	6/15/26 5:00 PM A	
AEC171102-20	Address Client Comments & Issue IFD - Single Lines - 480V Mc	0	6/16/26 7:00 AM A	6/19/26 5:00 PM A	
AEC171102-25	Update with Vendor Information & Issue Final single Lines- 480V	15	11/17/26 7:00 AM	12/8/26 5:00 PM	392
BH CNN-KPJV-MAST-LIVE,03,02,09,03 ENG - Electrical - Single Line & Three Line Diagrams - Relaying Single Lines					
AEC171105-05	Prepare Preliminary Single Lines& Issue for IDR - Relaying Sing	0	5/1/26 7:00 AM A	5/22/26 5:00 PM A	
AEC171105-10	IDR Single Lines - Relaying Single Lines	0	5/26/26 7:00 AM A	6/9/26 5:00 PM A	
AEC171105-15	Address IDR comments Single Lines& Issue for CR - Relaying S	0	6/10/26 7:00 AM A	7/10/26 5:00 PM A	
AEC171105-20	Client Review Prelimin.Single Lines - Relaying Single Lines	0	7/10/26 7:00 AM A	7/31/26 5:00 PM A	
AEC171105-25	Incorporate Client Comments & Issue IFD. Single Lines - Relayi	0	8/3/26 7:00 AM A	8/20/26 5:00 PM A	
AEC171105-30	Update with Vendor Information & Issue Final Single Lines - Rel	5	10/12/26 7:00 AM	10/16/26 5:00 PM	427
BH CNN-KPJV-MAST-LIVE,03,02,09,05 ENG - Electrical - Single Line & Three Line Diagrams - DC Single Lines					
AEC171106-05	Prepare Preliminary Single Lines& Issue for IDR - DC Single Lin	0	5/1/26 7:00 AM A	6/3/26 5:00 PM A	
AEC171106-10	IDR Single Lines - DC Single Lines	0	6/4/26 7:00 AM A	6/18/26 5:00 PM A	
AEC171106-15	Address IDR comments Single Lines& Issue for CR - DC Single	0	6/19/26 7:00 AM A	7/21/26 5:00 PM A	
AEC171106-20	Client Review Prelimin.Single Lines - DC Single Lines	0	7/21/26 7:00 AM A	8/7/26 5:00 PM A	
AEC171106-25	Incorporate Client Comments & Issue IFD. Single Lines - DC Sir	0	8/11/26 7:00 AM A	8/17/26 5:00 PM A	
AEC171106-30	Update with Vendor Information & Issue Final Single Lines - DC	0	8/11/26 7:00 AM A	8/17/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,02,09,04 ENG - Electrical - Single Line & Three Line Diagrams - Three Lines					
AEC171104-05	Prepare - Preliminary & Issue Three Lines for Client Review	30	10/12/26 7:00 AM	11/23/26 5:00 PM	487
AEC171104-15	Client Review - Preliminary - Three Lines	15	11/24/26 7:00 AM	12/15/26 5:00 PM	487
AEC171104-20	Address Client Comments & Issue Preliminary - Three Lines	5	12/16/26 7:00 AM	12/22/26 5:00 PM	487
AEC171104-25	Update with Vendor Information & Issue Final - Three Lines	15	12/23/26 7:00 AM	1/19/27 5:00 PM	487
BH CNN-KPJV-MAST-LIVE,03,02,14 ENG - Electrical - Equipment Arrangement Drawings					
BH CNN-KPJV-MAST-LIVE,03,02,14,01 ENG - Electrical - Equipment Arrangement Drawings - Administration Area					
AEC171150-05	Model - EA's - Administration Area	0	4/24/26 7:00 AM A	5/8/26 5:00 PM A	
AEC171150-10	Prep & Issue Electrical EA's for IDR - Administration Area	0	5/7/26 7:00 AM A	5/22/26 5:00 PM A	
AEC171150-15	IDR - Electrical EA's - Administration Area	0	5/22/26 7:00 AM A	6/5/26 5:00 PM A	
AEC171150-20	Address IDR - Comments & Issue for Client Review Electrical EA	0	6/8/26 7:00 AM A	6/19/26 5:00 PM A	
AEC171150-25	Client Review - Electrical EA's - Administration Area	0	6/22/26 7:00 AM A	7/2/26 5:00 PM A	
AEC171150-30	Address Client Review Comments & Issue IFD Electrical EA's - A	0	7/13/26 7:00 AM A	7/14/26 5:00 PM A	




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
BH CNN-KPJV-MAST-LIVE,03,02,14,02 ENG - Electrical - Equipment Arrangement Drawings - Plant Service Area(Demin)					
AEC171160-05	Model - EA's - Plant Service Area (Demin)	0	5/15/26 7:00 AM A	6/26/26 5:00 PM A	
AEC171160-10	Prep & Issue Electrical EA's for IDR - Plant Service Area (Demin	0	7/2/26 7:00 AM A	7/2/26 5:00 PM A	
AEC171160-15	IDR - Electrical EA's - Plant Service Area (Demin)	0	7/6/26 7:00 AM A	7/10/26 5:00 PM A	
AEC171160-20	Address IDR - Comments & Issue for Client Review Electrical EA	0	7/10/26 7:00 AM A	7/23/26 5:00 PM A	
AEC171160-25	Client Review - Electrical EA's - Plant Service Area (Demin)	0	7/24/26 7:00 AM A	8/14/26 5:00 PM A	
AEC171160-30	Address Client Review Comments & Issue IFD Electrical EA's - F	0	9/21/26 7:00 AM A	9/29/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,02,14,03 ENG - Electrical - Equipment Arrangement Drawings - Fuel Oil Area					
AEC171127-05	Model - EA's - Fuel Oil Area	0	5/4/26 7:00 AM A	6/30/26 5:00 PM A	
AEC171127-10	Prep & Issue Electrical EA's for IDR - Fuel Oil Area	0	7/6/26 7:00 AM A	7/23/26 5:00 PM A	
AEC171127-15	IDR - Electrical EA's - Fuel Oil Area	0	7/24/26 7:00 AM A	8/4/26 5:00 PM A	
AEC171127-20	Address IDR - Comments & Issue for Client Review Electrical EA	0	8/5/26 7:00 AM A	8/14/26 5:00 PM A	
AEC171127-25	Client Review - Electrical EA's - Fuel Oil Area	0	8/14/26 7:00 AM A	9/10/26 5:00 PM A	
AEC171127-30	Address Client Review Comments & Issue IFD Electrical EA's - F	0	9/14/26 7:00 AM A	9/21/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,02,14,04 ENG - Electrical - Equipment Arrangement Drawings - Fuel Gas Area					
AEC171153-05	Model - EA's - Fuel Gas Area	0	7/6/26 7:00 AM A	7/9/26 5:00 PM A	
AEC171153-10	Prep & Issue Electrical EA's for IDR - Fuel Gas Area	0	7/10/26 7:00 AM A	7/23/26 5:00 PM A	
AEC171153-15	IDR - Electrical EA's - Fuel Gas Area	0	7/24/26 7:00 AM A	8/7/26 5:00 PM A	
AEC171153-20	Address IDR - Comments & Issue for Client Review Electrical EA	0	8/10/26 7:00 AM A	8/14/26 5:00 PM A	
AEC171153-25	Client Review - Electrical EA's - Fuel Gas Area	0	8/14/26 7:00 AM A	9/10/26 5:00 PM A	
AEC171153-30	Address Client Review Comments & Issue IFD Electrical EA's - F	0	9/14/26 7:00 AM A	9/21/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,02,14,05 ENG - Electrical - Equipment Arrangement Drawings - Equip. Layouts All CT Enclosures					
AEC171145-05	Prep & Check & IDR - Elec. Equip. Layouts - All CT Enclosers	0	8/31/26 7:00 AM A	10/6/26 5:00 PM A	
AEC171145-10	IDR - Electrical EA's - Elec. Equip. Layouts - All CT Enclosers	8	10/7/26 7:00 AM A	10/21/26 5:00 PM	509
AEC171145-15	Address IDR - Comments & Issue for Client Review Electrical EA	10	10/22/26 7:00 AM	11/4/26 5:00 PM	509
AEC171145-20	Client Review - Electrical EA's - Elec. Equip. Layouts - All CT Enc	15	11/5/26 7:00 AM	11/27/26 5:00 PM	509
AEC171145-25	Address Client Review Comments & Issue IFD Electrical EA's - E	10	11/30/26 7:00 AM	12/11/26 5:00 PM	509
BH CNN-KPJV-MAST-LIVE,03,02,10 ENG - Electrical - Electrical Load Lists					
AEC170701-05	Prepare & Issue for Client Review - Preliminary Electrical Load L	1	3/17/26 7:00 AM A	10/12/26 5:00 PM	431
AEC170701-15	Client Review - Preliminary - Electrical Load List	15	10/13/26 7:00 AM	11/2/26 5:00 PM	531
AEC170701-20	Address Client Comments & IFD - Electrical Load List	5	11/3/26 7:00 AM	11/9/26 5:00 PM	531
AEC170701-25	Issue Final Electrical Load List	0		3/23/27 5:00 PM	443
BH CNN-KPJV-MAST-LIVE,03,02,04 ENG - Electrical - U/G Ductbank, Raceway & Conduit Plans					
BH CNN-KPJV-MAST-LIVE,03,02,04,04 ENG - Electrical - U/G Ductbank Plans - CTG U4					
AEC171146-00	Model - U/G Raceway & Details - CTG Train 4	0	5/4/26 7:00 AM A	8/7/26 5:00 PM A	
AEC171146-05	Prep & IDR - U/G Duct Banks Plans & Details - CTG Train 4	0	8/10/26 7:00 AM A	9/9/26 5:00 PM A	
AEC171146-10	IDR - U/G Duct Bank Plans & Details - CTG Train 4	0	9/9/26 7:00 AM A	9/23/26 5:00 PM A	
AEC171146-15	Address Comments & Issue for Client Review - U/G Duct Banks	0	9/24/26 7:00 AM A	10/1/26 5:00 PM A	
AEC171146-20	Client Review - U/G Raceway Plans & Details - Duct Bank - CTG	4	10/1/26 7:00 AM A	10/15/26 5:00 PM	287
AEC171146-25	Address Client Comments & IFC - Duct Bank Plans & Details - C	10	10/16/26 7:00 AM	10/29/26 5:00 PM	287
BH CNN-KPJV-MAST-LIVE,03,02,04,09 ENG - Electrical - U/G Embedded Conduit - CTG U4					
AEC171146-00	Model - UG Embedded Conduit Plans & Details - CTG 4	0	5/4/26 7:00 AM A	7/17/26 5:00 PM A	
AEC171146-05	Prep & Issue for IDR - UG Embedded Conduit Plans & Details -	0	7/20/26 7:00 AM A	7/31/26 5:00 PM A	
AEC171146-10	IDR - UG Embedded Conduit Plans & Details - CTG 4	0	8/3/26 7:00 AM A	8/10/26 5:00 PM A	
AEC171146-15	Address Comments & Issue for CR - U/G Embedded Conduit - (	0	8/11/26 7:00 AM A	8/26/26 5:00 PM A	
AEC171146-20	Client Review - U/G Raceway Plans & Details Embedded Condu	0	8/27/26 7:00 AM A	9/11/26 5:00 PM A	
AEC171146-25	Address Client Comments & Issue IFC - U/G Raceway Plans & I	0	9/9/26 7:00 AM A	9/25/26 7:00 AM A	
BH CNN-KPJV-MAST-LIVE,03,02,04,03 ENG - Electrical - U/G Ductbank Plans - CTG U3					
AEC171136-00	Model - U/G Raceway & Conduit Plans & Details - CTG Train 3	0	7/22/26 7:00 AM A	9/14/26 5:00 PM A	
AEC171136-05	Prep & IDR - U/G Raceway & Conduit Plans & Details - CTG Trai	2	9/15/26 7:00 AM A	10/13/26 5:00 PM	6
AEC171136-10	IDR - U/G Raceway & Conduit Plans & Details - CTG Train 3	5	10/14/26 7:00 AM	10/20/26 5:00 PM	6

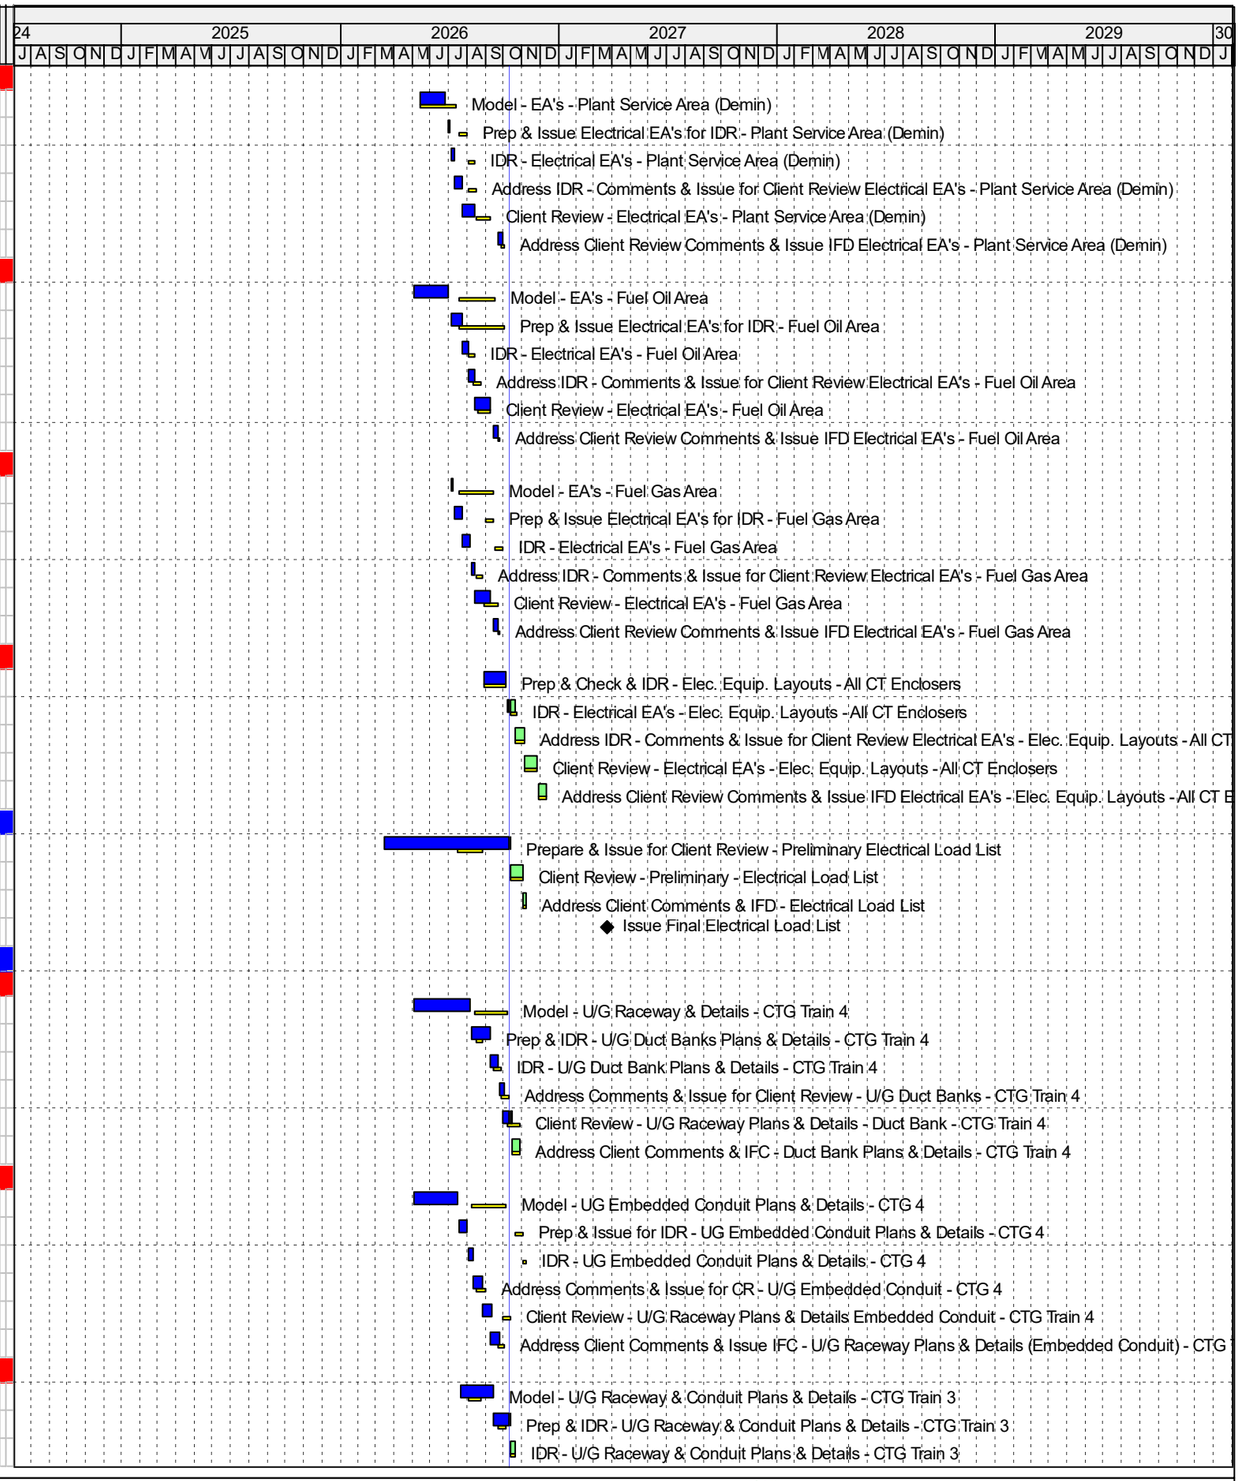


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC171136-15	Address Comments & Issue for Client Review - U/G Duct Banks	10	10/21/26 7:00 AM	11/3/26 5:00 PM	263
AEC171136-20	Client Review - U/G Raceway Plans & Details - Duct Bank - CTG	15	11/4/26 7:00 AM	11/25/26 5:00 PM	263
AEC171136-35	Address Client Comments & IFC - Duct Bank Plans & Details - C	10	11/27/26 7:00 AM	12/10/26 5:00 PM	263
BH CNN-KPJV-MAST-LIVE,03,02,04,10 ENG - Electrical - U/G Embedded Conduit - CTG U3					
AEC171136-00	Model - UG Embedded Conduit Plans & Details - CTG 3	0	7/22/26 7:00 AM A	8/28/26 5:00 PM A	
AEC171136-05	Prep & Issue for IDR - UG Embedded Conduit Plans & Details -	0	8/28/26 7:00 AM A	8/28/26 5:00 PM A	
AEC171136-10	IDR - UG Embedded Conduit Plans & Details - CTG 3	0	8/31/26 7:00 AM A	9/4/26 5:00 PM A	
AEC171136-25	Address Comments & Issue for Client Review - U/G Embedded	2	9/8/26 7:00 AM A	10/13/26 5:00 PM	241
AEC171136-30	Client Review - U/G Raceway Plans & Details (Embedded Condı	15	10/14/26 7:00 AM	11/3/26 5:00 PM	241
AEC171136-40	Address Client Comments & Issue IFC - U/G Raceway Plans & I	10	11/4/26 7:00 AM	11/18/26 5:00 PM	241
BH CNN-KPJV-MAST-LIVE,03,02,04,02 ENG - Electrical - U/G Ductbank Plans - CTG U2					
AEC171126-00	Model - U/G Raceway & Conduit Plans & Details - CTG Train 2	15	11/19/26 7:00 AM	12/10/26 5:00 PM	6
AEC171126-05	Prep & IDR - U/G Raceway & Conduit Plans & Details Duct Bank	15	12/11/26 7:00 AM	1/6/27 5:00 PM	20
AEC171126-10	IDR - U/G Raceway Plans & Detail Duct Bank - CTG Train 2	10	1/7/27 7:00 AM	1/21/27 5:00 PM	136
AEC171126-15	Address Comments & Issue for Client Review - U/G Duct Banks	5	2/5/27 7:00 AM	2/11/27 5:00 PM	170
AEC171126-20	Client Review - U/G Raceway Plans & Details - Duct Bank - CTG	15	2/12/27 7:00 AM	3/5/27 5:00 PM	170
AEC171126-35	Address Client Comments & IFC - Duct Bank Plans & Details - C	10	3/8/27 7:00 AM	3/19/27 5:00 PM	170
BH CNN-KPJV-MAST-LIVE,03,02,04,11 ENG - Electrical - U/G Embedded Conduit - CTG U2					
AEC171126-00	Model - UG Raceway Plans & Details (Embedded Conduit) - CT	15	11/19/26 7:00 AM	12/10/26 5:00 PM	136
AEC171126-05	Prep & Issue for IDR - UG Raceway Plans & Details (Embedded	15	12/11/26 7:00 AM	1/6/27 5:00 PM	136
AEC171126-10	IDR - U/G Raceway Plans & Details (Embedded Conduit) - CTG	10	1/7/27 7:00 AM	1/21/27 5:00 PM	136
AEC171126-15	Address Comments & Issue for CR - U/G Embedded Conduit - (	10	1/22/27 7:00 AM	2/4/27 5:00 PM	136
AEC171126-20	Client Review - UG Raceway Plans & Details (Embedded Condu	15	2/5/27 7:00 AM	2/26/27 5:00 PM	136
AEC171126-25	Address Client Comments & Issue IFC - U/G Raceway Plans & I	10	3/1/27 7:00 AM	3/12/27 5:00 PM	136
BH CNN-KPJV-MAST-LIVE,03,02,04,01 ENG - Electrical - U/G Ductbank Plans - CTG U1					
AEC171116-00	Model - U/G Raceway & Conduit Plans & Details - CTG Train 1	15	12/11/26 7:00 AM	1/6/27 5:00 PM	6
AEC171116-05	Prep & IDR - U/G Raceway & Conduit Plans & Details - CTG Trai	10	1/7/27 7:00 AM	1/21/27 5:00 PM	145
AEC171116-10	IDR - U/G Raceway & Conduit Plans & Details - CTG Train 1	5	1/22/27 7:00 AM	1/28/27 5:00 PM	145
AEC171116-15	Address Comments & Issue for Client Review - U/G Duct Banks	10	2/12/27 7:00 AM	2/26/27 5:00 PM	135
AEC171116-25	Client Review - U/G Raceway Plans & Details - Duct Bank - CTG	15	3/1/27 7:00 AM	3/19/27 5:00 PM	135
AEC171116-35	Address Client Comments & IFC - Duct Bank Plans & Details - C	10	3/22/27 7:00 AM	4/5/27 5:00 PM	135
BH CNN-KPJV-MAST-LIVE,03,02,04,12 ENG - Electrical - U/G Embedded Conduit - CTG U1					
AEC171116-00	Model - U/G Embedded Conduit - CTG Train 1	15	12/11/26 7:00 AM	1/6/27 5:00 PM	6
AEC171116-05	Prep & Issue for IDR- U/G Embedded Conduit - CTG 1	10	1/7/27 7:00 AM	1/21/27 5:00 PM	6
AEC171116-10	IDR - U/G Embedded Conduit - CTG Train 1	5	1/22/27 7:00 AM	1/28/27 5:00 PM	6
AEC171116-20	Address Comments & Issue for Client Review - U/G Embedded	10	1/29/27 7:00 AM	2/11/27 5:00 PM	6
AEC171116-30	Client Review - U/G Raceway Plans & Details (Embedded Condı	15	2/12/27 7:00 AM	3/5/27 5:00 PM	33
AEC171116-40	Address Client Comments & Issue IFC - U/G Raceway Plans & I	6	3/8/27 7:00 AM	3/15/27 5:00 PM	33
BH CNN-KPJV-MAST-LIVE,03,02,04,05 ENG - Electrical - U/G Raceway & Conduit Plans - Admin/Warehouse					
AEC171156-00	Model - U/G Raceway & Conduit Plans & Details - Admin/Wareh	20	10/21/26 7:00 AM	11/18/26 5:00 PM	6
AEC171156-05	Prep & IDR - U/G Raceway & Conduit Plans & Details - Admin/W	15	11/19/26 7:00 AM	12/10/26 5:00 PM	58
AEC171156-10	IDR - U/G Raceway & Conduit Plans & Details - Admin/Wareho	10	12/11/26 7:00 AM	12/28/26 5:00 PM	58
AEC171156-20	Client Review - U/G Raceway & Conduit Plans & Details - Admin	15	12/29/26 7:00 AM	1/21/27 5:00 PM	58
AEC171156-25	Address Client Comments & IFC - U/G Raceway & Conduit Plan	10	1/22/27 7:00 AM	2/4/27 5:00 PM	58
BH CNN-KPJV-MAST-LIVE,03,02,04,06 ENG - Electrical - U/G Raceway & Conduit Plans - Demin/Service Water Area					
AEC171176-00	Model - U/G Raceway & Conduit Plans & Details - Demin/Servic	15	11/24/26 7:00 AM	12/15/26 5:00 PM	142
AEC171176-05	Prep & IDR - U/G Raceway & Conduit Plans & Details - Demin/S	10	12/16/26 7:00 AM	1/4/27 5:00 PM	142
AEC171176-10	IDR - U/G Raceway & Conduit Plans & Details - Demin/Service V	10	1/5/27 7:00 AM	1/19/27 5:00 PM	166
AEC171176-20	Client Review - U/G Raceway & Conduit Plans & Details - Demin	15	1/5/27 7:00 AM	1/26/27 5:00 PM	142
AEC171176-25	Address Client Comments & IFC - U/G Raceway & Conduit Plan	10	1/27/27 7:00 AM	2/9/27 5:00 PM	142
BH CNN-KPJV-MAST-LIVE,03,02,04,07 ENG - Electrical - U/G Raceway & Conduit Plans - Fuel Gas & Compressor Area					

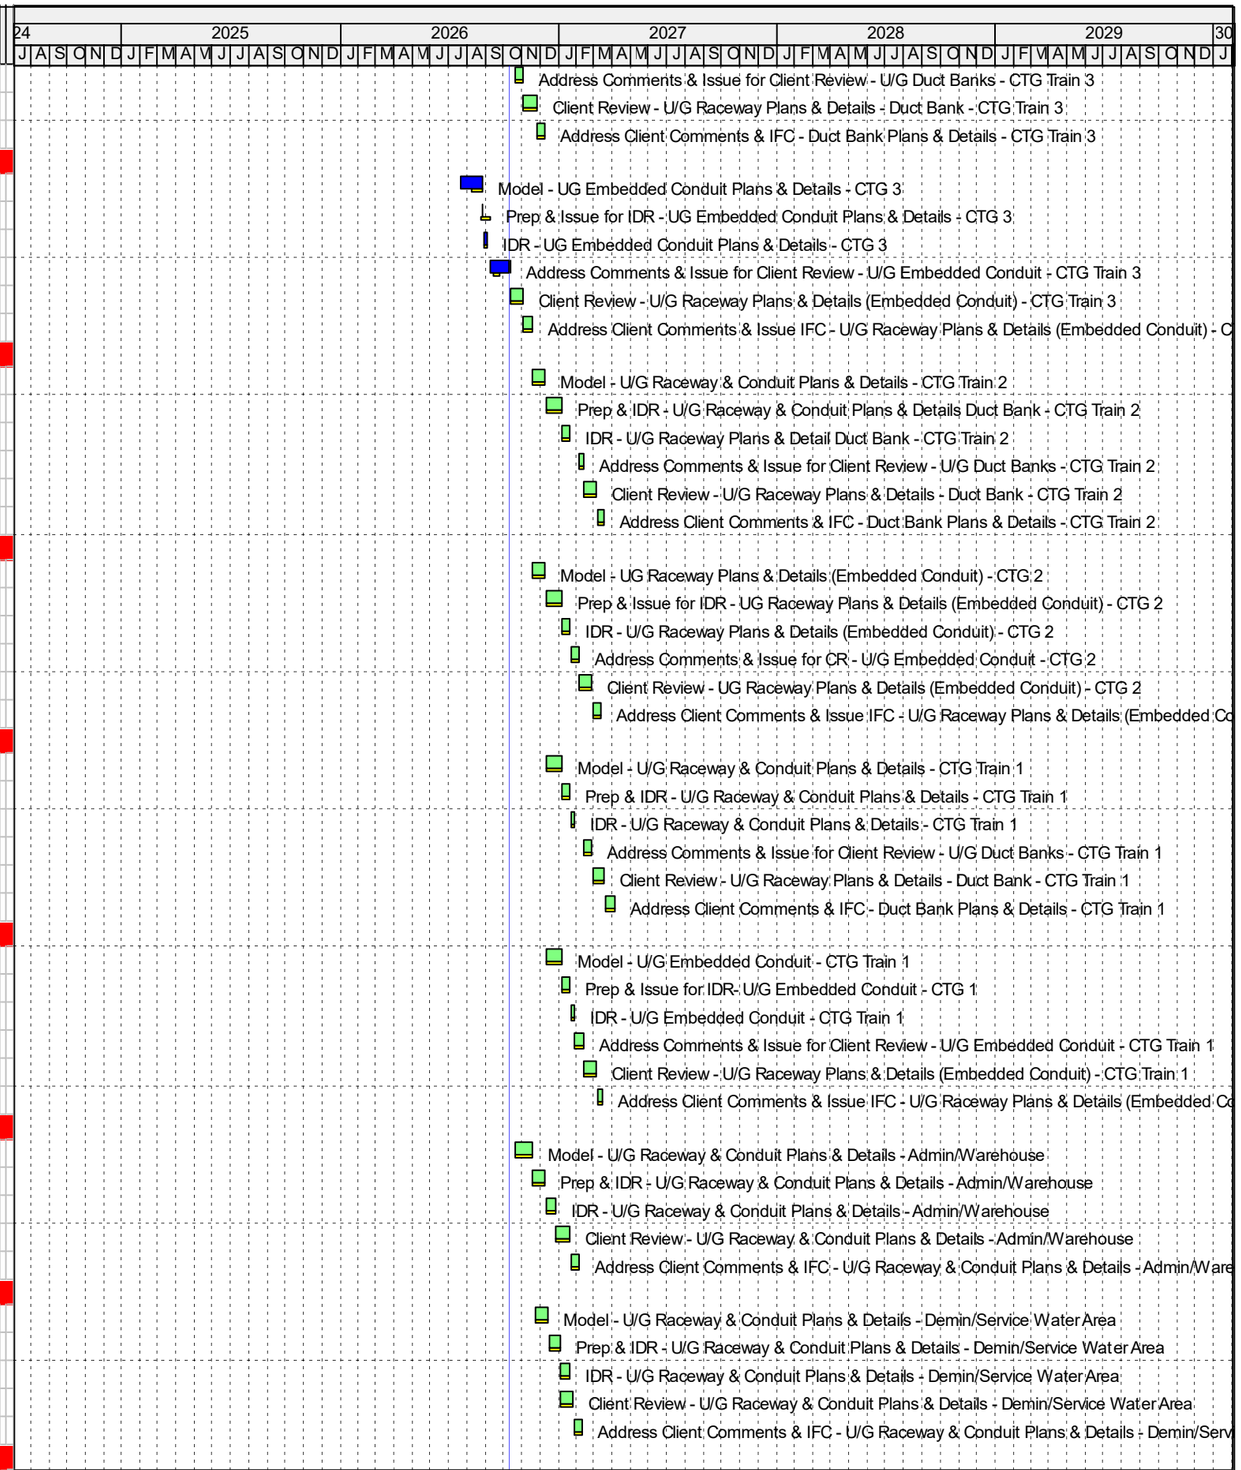

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC171166-00	Model - U/G Raceway & Conduit Plans & Details - Fuel Gas Area	20	1/15/27 7:00 AM	2/12/27 5:00 PM	59
AEC171166-05	Prep & IDR - U/G Raceway & Conduit Plans & Details - Fuel Gas	15	2/16/27 7:00 AM	3/8/27 5:00 PM	59
AEC171166-10	IDR - U/G Raceway & Conduit Plans & Details - Fuel Gas Area	10	3/9/27 7:00 AM	3/22/27 5:00 PM	107
AEC171166-20	Client Review - U/G Raceway & Conduit Plans & Details - Fuel G	15	3/9/27 7:00 AM	3/30/27 5:00 PM	59
AEC171166-25	Address Client Comments & IFC - U/G Raceway & Conduit Plan	10	3/31/27 7:00 AM	4/13/27 5:00 PM	59
BH CNN-KPJV-MAST-LIVE,03,02,04,08 ENG - Electrical - U/G Raceway & Conduit Plans - Fuel Oil Area					
AEC171186-00	Model - U/G Raceway & Conduit Plans & Details - Fuel Oil Area	20	11/9/26 7:00 AM	12/8/26 5:00 PM	166
AEC171186-12	Return Comments on Field Erected Fisher Tank Drawings - Fuel	10	12/9/26 7:00 AM	12/22/26 5:00 PM	171
AEC171186-05	Prep & IDR - U/G Raceway & Conduit Plans & Details - Fuel Oil A	15	12/9/26 7:00 AM	1/4/27 5:00 PM	166
AEC171186-10	IDR - U/G Raceway & Conduit Plans & Details - Fuel Oil Area	10	1/5/27 7:00 AM	1/19/27 5:00 PM	487
AEC171186-20	Client Review - U/G Raceway & Conduit Plans & Details - Fuel C	15	1/5/27 7:00 AM	1/26/27 5:00 PM	166
AEC171186-25	Address Client Comments & IFC - U/G Raceway & Conduit Plan	10	1/27/27 7:00 AM	2/9/27 5:00 PM	166
BH CNN-KPJV-MAST-LIVE,03,02,02 ENG - Electrical - A/G Raceway & Conduit Plans					
BH CNN-KPJV-MAST-LIVE,03,02,02,01 ENG - Electrical - A/G Raceway & Conduit Plans - CTG U1					
AEC171111-00	Model - A/G Raceway & Conduit Plans & Details - CTG Train 1	20	10/13/26 7:00 AM	11/9/26 5:00 PM	1
AEC171111-05	Prep & IDR - A/G Raceway & Conduit Plans & Details - CTG Trai	15	11/10/26 7:00 AM	12/2/26 5:00 PM	1
AEC171111-10	IDR - A/G Raceway & Conduit Plans & Details - CTG Train 1	10	12/3/26 7:00 AM	12/16/26 5:00 PM	1
AEC171111-15	Address Comments & Issue for Client Review - A/G Raceway &	10	12/17/26 7:00 AM	1/5/27 5:00 PM	186
AEC171111-20	Client Review - A/G Raceway & Conduit Plans & Details - CTG T	15	1/6/27 7:00 AM	1/27/27 5:00 PM	186
AEC171111-25	Address Client Comments & IFC - A/G Raceway & Conduit Plan	5	1/28/27 7:00 AM	2/3/27 5:00 PM	186
BH CNN-KPJV-MAST-LIVE,03,02,02,02 ENG - Electrical - A/G Raceway & Conduit Plans - CTG U2					
AEC171122-00	Model - A/G Raceway & Conduit Plans & Details - CTG Train 2	15	11/25/26 7:00 AM	12/16/26 5:00 PM	1
AEC171122-05	Prep & IDR - A/G Raceway & Conduit Plans & Details - CTG Trai	10	12/17/26 7:00 AM	1/5/27 5:00 PM	196
AEC171122-10	IDR - A/G Raceway & Conduit Plans & Details - CTG Train 2	5	1/6/27 7:00 AM	1/12/27 5:00 PM	196
AEC171122-15	Address Comments & Issue for Client Review - A/G Raceway &	5	1/13/27 7:00 AM	1/20/27 5:00 PM	196
AEC171122-20	Client Review - A/G Raceway & Conduit Plans & Details - CTG T	15	1/21/27 7:00 AM	2/10/27 5:00 PM	196
AEC171122-25	Address Client Comments & IFC - A/G Raceway & Conduit Plan	5	2/11/27 7:00 AM	2/18/27 5:00 PM	196
BH CNN-KPJV-MAST-LIVE,03,02,02,03 ENG - Electrical - A/G Raceway & Conduit Plans - CTG U3					
AEC171132-00	Model - A/G Raceway & Conduit Plans & Details - CTG Train 3	10	12/17/26 7:00 AM	1/5/27 5:00 PM	1
AEC171132-05	Prep & IDR - A/G Raceway & Conduit Plans & Details - CTG Trai	10	1/6/27 7:00 AM	1/20/27 5:00 PM	183
AEC171132-10	IDR - A/G Raceway & Conduit Plans & Details - CTG Train 3	5	1/21/27 7:00 AM	1/27/27 5:00 PM	183
AEC171132-15	Address Comments & Issue for Client Review - A/G Raceway &	5	2/19/27 7:00 AM	2/25/27 5:00 PM	168
AEC171132-20	Client Review - A/G Raceway & Conduit Plans & Details - CTG T	15	2/26/27 7:00 AM	3/18/27 5:00 PM	168
AEC171132-25	Address Client Comments & IFC - A/G Raceway & Conduit Plan	5	3/19/27 7:00 AM	3/25/27 5:00 PM	168
BH CNN-KPJV-MAST-LIVE,03,02,02,04 ENG - Electrical - A/G Raceway & Conduit Plans - CTG U4					
AEC171142-00	Model - A/G Raceway & Conduit Plans & Details - CTG Train 4	10	1/6/27 7:00 AM	1/20/27 5:00 PM	1
AEC171142-05	Prep & IDR - A/G Raceway & Conduit Plans & Details - CTG Trai	10	1/21/27 7:00 AM	2/3/27 5:00 PM	168
AEC171142-10	IDR - A/G Raceway & Conduit Plans & Details - CTG Train 4	5	2/4/27 7:00 AM	2/10/27 5:00 PM	168
AEC171142-15	Address Comments & Issue for Client Review - A/G Raceway &	5	2/11/27 7:00 AM	2/18/27 5:00 PM	168
AEC171142-20	Client Review - A/G Raceway & Conduit Plans & Details - CTG T	15	2/19/27 7:00 AM	3/11/27 5:00 PM	168
AEC171142-25	Address Client Comments & IFC - A/G Raceway & Conduit Plan	5	3/12/27 7:00 AM	3/18/27 5:00 PM	168
BH CNN-KPJV-MAST-LIVE,03,02,02,05 ENG - Electrical - A/G Raceway & Conduit Plans - Admin/Warehouse					
AEC171152-00	Model - A/G Raceway & Conduit Plans & Details - Admin/Wareh	20	3/22/27 7:00 AM	4/19/27 5:00 PM	58
AEC171152-05	Prep & IDR - A/G Raceway & Conduit Plans & Details - Admin/W	15	4/20/27 7:00 AM	5/10/27 5:00 PM	58
AEC171152-10	IDR - A/G Raceway & Conduit Plans & Details - Admin/Warehou	5	5/11/27 7:00 AM	5/17/27 5:00 PM	58
AEC171152-15	Address Comments & Issue for Client Review - A/G Raceway &	10	5/18/27 7:00 AM	6/1/27 5:00 PM	58
AEC171152-20	Client Review - A/G Raceway & Conduit Plans & Details - Admin	15	6/2/27 7:00 AM	6/23/27 5:00 PM	101
AEC171152-25	Address Client Comments & IFC - A/G Raceway & Conduit Plan	10	6/24/27 7:00 AM	7/8/27 5:00 PM	101
BH CNN-KPJV-MAST-LIVE,03,02,02,06 ENG - Electrical - A/G Raceway & Conduit Plans - Demin/Service Water Area					
AEC171172-00	Model - A/G Raceway & Conduit Plans & Details - Demin/Servic	20	2/16/27 7:00 AM	3/15/27 5:00 PM	166
AEC171172-05	Prep & IDR - A/G Raceway & Conduit Plans & Details - Demin/S	15	3/16/27 7:00 AM	4/6/27 5:00 PM	166



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC171172-10	IDR - A/G Raceway & Conduit Plans & Details - Demin/Service W	10	4/7/27 7:00 AM	4/20/27 5:00 PM	166
AEC171172-15	Address Comments & Issue for Client Review - A/G Raceway &	10	4/21/27 7:00 AM	5/4/27 5:00 PM	166
AEC171172-20	Client Review - A/G Raceway & Conduit Plans & Details - Demin	15	5/5/27 7:00 AM	5/25/27 5:00 PM	166
AEC171172-25	Address Client Comments & IFC - A/G Raceway & Conduit Plan	10	5/26/27 7:00 AM	6/9/27 5:00 PM	166
BH CNN-KPJV-MAST-LIVE,03,02,02,07 ENG - Electrical - A/G Raceway & Conduit Plans - Fuel Gas Area					
AEC171162-00	Model - A/G Raceway & Conduit Plans & Details - Fuel Gas Area	20	4/14/27 7:00 AM	5/11/27 5:00 PM	92
AEC171162-05	Prep & IDR - A/G Raceway & Conduit Plans & Details - Fuel Gas	15	5/12/27 7:00 AM	6/2/27 5:00 PM	92
AEC171162-10	IDR - A/G Raceway & Conduit Plans & Details - Fuel Gas Area	10	6/3/27 7:00 AM	6/16/27 5:00 PM	92
AEC171162-15	Address Comments & Issue for Client Review - A/G Raceway &	10	6/17/27 7:00 AM	7/1/27 5:00 PM	92
AEC171162-20	Client Review - A/G Raceway & Conduit Plans & Details - Fuel G	15	7/2/27 7:00 AM	7/23/27 5:00 PM	92
AEC171162-25	Address Client Comments & IFC - A/G Raceway & Conduit Plan	10	7/26/27 7:00 AM	8/6/27 5:00 PM	92
BH CNN-KPJV-MAST-LIVE,03,02,02,08 ENG - Electrical - A/G Raceway & Conduit Plans - Fuel Oil Area					
AEC171182-00	Model - A/G Raceway & Conduit Plans & Details - Fuel Oil Area	19	2/18/27 7:00 AM	3/16/27 5:00 PM	188
AEC171182-05	Prep & IDR - A/G Raceway & Conduit Plans & Details - Fuel Oil A	10	3/17/27 7:00 AM	3/31/27 5:00 PM	188
AEC171182-10	IDR - A/G Raceway & Conduit Plans & Details - Fuel Oil Area	10	4/1/27 7:00 AM	4/14/27 5:00 PM	188
AEC171182-15	Address IDR - Comments & Issue for Client Review - A/G Racew	10	4/15/27 7:00 AM	4/28/27 5:00 PM	188
AEC171182-20	Client Review - A/G Raceway & Conduit Plans & Details - Fuel C	15	4/29/27 7:00 AM	5/19/27 5:00 PM	188
AEC171182-25	Address Client Comments & IFC - A/G Raceway & Conduit Plan	10	5/20/27 7:00 AM	6/3/27 5:00 PM	188
BH CNN-KPJV-MAST-LIVE,03,02,03 ENG - Electrical - Lighting Plans					
BH CNN-KPJV-MAST-LIVE,03,02,03,01 ENG - Electrical - Lighting Plans - CTG U1					
AEC171112-05	Prep & IDR - Lighting Plans - CTG Train 1	20	10/13/26 7:00 AM	11/9/26 5:00 PM	31
AEC171112-10	IDR - Lighting Plans - CTG Train 1	10	11/10/26 7:00 AM	11/24/26 5:00 PM	31
AEC171112-15	Address IDR - Comments & Issue for Client Review - Lighting Pl	10	11/25/26 7:00 AM	12/9/26 5:00 PM	31
AEC171112-20	Client Review - Lighting Plans - CTG Train 1	15	12/10/26 7:00 AM	1/5/27 5:00 PM	184
AEC171112-25	Address Client Comments & IFC - Lighting Plans - CTG Train 1	10	4/5/27 7:00 AM	4/16/27 5:00 PM	124
BH CNN-KPJV-MAST-LIVE,03,02,03,02 ENG - Electrical - Lighting Plans - CTG U2					
AEC171124-05	Prep & IDR - Lighting Plans - CTG Train 2	10	1/7/27 7:00 AM	1/21/27 5:00 PM	20
AEC171124-10	IDR - Lighting Plans - CTG Train 2	5	1/22/27 7:00 AM	1/28/27 5:00 PM	20
AEC171124-15	Address IDR - Comments & Issue for Client Review - Lighting Pl	5	2/26/27 7:00 AM	3/4/27 5:00 PM	1
AEC171124-20	Client Review - Lighting Plans - CTG Train 2	15	3/5/27 7:00 AM	3/25/27 5:00 PM	1
AEC171124-25	Address Client Comments & IFC - Lighting Plans - CTG Train 2	5	3/29/27 7:00 AM	4/2/27 5:00 PM	1
BH CNN-KPJV-MAST-LIVE,03,02,03,03 ENG - Electrical - Lighting Plans - CTG U3					
AEC171134-05	Prep & IDR - Lighting Plans - CTG Train 3	10	1/6/27 7:00 AM	1/20/27 5:00 PM	16
AEC171134-10	IDR - Lighting Plans - CTG Train 3	5	1/21/27 7:00 AM	1/27/27 5:00 PM	16
AEC171134-15	Address IDR - Comments & Issue for Client Review - Lighting Pl	5	2/19/27 7:00 AM	2/25/27 5:00 PM	1
AEC171134-20	Client Review - Lighting Plans - CTG Train 3	15	2/26/27 7:00 AM	3/18/27 5:00 PM	6
AEC171134-25	Address Client Comments & IFC - Lighting Plans - CTG Train 3	5	3/29/27 7:00 AM	4/2/27 5:00 PM	1
BH CNN-KPJV-MAST-LIVE,03,02,03,04 ENG - Electrical - Lighting Plans - CTG U4					
AEC171144-05	Prep & IDR - Lighting Plans - CTG Train 4	10	1/21/27 7:00 AM	2/3/27 5:00 PM	1
AEC171144-10	IDR - Lighting Plans - CTG Train 4	5	2/4/27 7:00 AM	2/10/27 5:00 PM	1
AEC171144-15	Address IDR - Comments & Issue for Client Review - Lighting Pl	5	2/11/27 7:00 AM	2/18/27 5:00 PM	1
AEC171144-20	Client Review - Lighting Plans - CTG Train 4	15	2/19/27 7:00 AM	3/11/27 5:00 PM	11
AEC171144-25	Address Client Comments & IFC - Lighting Plans - CTG Train 4	5	3/29/27 7:00 AM	4/2/27 5:00 PM	1
BH CNN-KPJV-MAST-LIVE,03,02,03,05 ENG - Electrical - Lighting Plans - Admin/Warehouse					
AEC171154-05	Prep & IDR - Lighting Plans - Admin/Warehouse	20	6/7/27 7:00 AM	7/6/27 5:00 PM	58
AEC171154-10	IDR - Lighting Plans - Admin/Warehouse	10	7/7/27 7:00 AM	7/20/27 5:00 PM	58
AEC171154-15	Address Comments & Issue for Client Review - Lighting Plans -	10	7/21/27 7:00 AM	8/3/27 5:00 PM	58
AEC171154-20	Client Review - Lighting Plans - Admin/Warehouse	15	8/4/27 7:00 AM	8/24/27 5:00 PM	58
AEC171154-25	Address Client Comments & IFC - Lighting Plans - Admin/Warel	10	8/25/27 7:00 AM	9/8/27 5:00 PM	58
BH CNN-KPJV-MAST-LIVE,03,02,03,06 ENG - Electrical - Lighting Plans - Demin/Service Water Area					
AEC171174-05	Prep & IDR - Lighting Plans - Demin/Service Water Area	15	4/21/27 7:00 AM	5/11/27 5:00 PM	369



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC171174-10	IDR - Lighting Plans - Demin/Service Water Area	5	5/12/27 7:00 AM	5/18/27 5:00 PM	369
AEC171174-15	Address Comments & Issue for Client Review - Lighting Plans -	10	5/19/27 7:00 AM	6/2/27 5:00 PM	369
AEC171174-20	Client Review - Lighting Plans - Demin/Service Water Area	15	6/3/27 7:00 AM	6/24/27 5:00 PM	369
AEC171174-25	Address Client Comments & IFC - Lighting Plans - Demin/Servic	10	8/25/27 7:00 AM	9/8/27 5:00 PM	327
BH CNN-KPJV-MAST-LIVE,03,02,03,07 ENG - Electrical - Lighting Plans - Fuel Gas Area					
AEC171164-05	Prep & IDR - Lighting Plans - Fuel Gas Area	15	6/21/27 7:00 AM	7/12/27 5:00 PM	323
AEC171164-10	IDR - Lighting Plans - Fuel Gas Area	10	7/13/27 7:00 AM	7/26/27 5:00 PM	323
AEC171164-15	Address Comments & Issue for Client Review - Lighting Plans -	10	7/27/27 7:00 AM	8/9/27 5:00 PM	323
AEC171164-20	Client Review - Lighting Plans - Fuel Gas Area	15	8/10/27 7:00 AM	8/30/27 5:00 PM	323
AEC171164-25	Address Client Comments & IFC - Lighting Plans - Fuel Gas Are	10	8/31/27 7:00 AM	9/14/27 5:00 PM	323
BH CNN-KPJV-MAST-LIVE,03,02,03,08 ENG - Electrical - Lighting Plans - Fuel Oil Area					
AEC171184-05	Prep & IDR - Lighting Plans - Fuel Oil Area	15	5/20/27 7:00 AM	6/10/27 5:00 PM	343
AEC171184-10	IDR - Lighting Plans - Fuel Oil Area	10	6/11/27 7:00 AM	6/25/27 5:00 PM	343
AEC171184-15	Address IDR - Comments & Issue for Client Review - Lighting Pl	10	6/28/27 7:00 AM	7/12/27 5:00 PM	343
AEC171184-20	Client Review - Lighting Plans - Fuel Oil Area	15	7/13/27 7:00 AM	8/2/27 5:00 PM	343
AEC171184-25	Address Client Comments & IFC - Lighting Plans - Fuel Oil Area	10	8/3/27 7:00 AM	8/16/27 5:00 PM	343
BH CNN-KPJV-MAST-LIVE,03,02,06 ENG - Electrical - Grounding Plans					
BH CNN-KPJV-MAST-LIVE,03,02,06,04 ENG - Electrical - Grounding Plans - CTG U4					
AEC171148-05	Prep & IDR - Electrical Drawings - Grounding Plans - CTG Train 4	0	6/24/26 7:00 AM A	8/7/26 5:00 PM A	
AEC171148-10	IDR - Electrical Drawings - Grounding Plans - CTG Train 4	0	8/10/26 7:00 AM A	8/14/26 5:00 PM A	
AEC171148-15	Address IDR - Comments & Issue for Client Review - Grounding	0	8/17/26 7:00 AM A	8/28/26 5:00 PM A	
AEC171148-20	Client Review - Grounding Plans - CTG Train 4	0	8/31/26 7:00 AM A	9/17/26 5:00 PM A	
AEC171148-25	Address Client Comments & IFC - Grounding Plans - CTG Train	5	9/18/26 7:00 AM A	10/16/26 5:00 PM	243
BH CNN-KPJV-MAST-LIVE,03,02,06,03 ENG - Electrical - Grounding Plans - CTG U3					
AEC171138-05	Prep & IDR - Electrical Drawings - Grounding Plans - CTG Train 3	0	8/10/26 7:00 AM A	8/25/26 5:00 PM A	
AEC171138-10	IDR - Electrical Drawings - Grounding Plans - CTG Train 3	0	8/25/26 7:00 AM A	8/31/26 5:00 PM A	
AEC171138-15	Address IDR - Comments & Issue for Client Review - Grounding	0	9/1/26 7:00 AM A	9/9/26 5:00 PM A	
AEC171138-20	Client Review - Grounding Plans - CTG Train 3	0	9/9/26 7:00 AM A	9/23/26 5:00 PM A	
AEC171138-25	Address Client Comments & IFC - Grounding Plans - CTG Train	5	12/30/26 7:00 AM	1/7/27 5:00 PM	195
BH CNN-KPJV-MAST-LIVE,03,02,06,02 ENG - Electrical - Grounding Plans - CTG U2					
AEC171128-05	Prep & IDR - Electrical Drawings - Grounding Plans - CTG Train 2	6	8/24/26 7:00 AM A	10/19/26 5:00 PM	212
AEC171128-10	IDR - Electrical Drawings - Grounding Plans - CTG Train 2	5	10/20/26 7:00 AM	10/26/26 5:00 PM	222
AEC171128-15	Address IDR - Comments & Issue for Client Review - Grounding	5	10/27/26 7:00 AM	11/2/26 5:00 PM	222
AEC171128-20	Client Review - Grounding Plans - CTG Train 2	15	11/3/26 7:00 AM	11/24/26 5:00 PM	222
AEC171128-25	Address Client Comments & IFC - Grounding Plans - CTG Train	5	1/8/27 7:00 AM	1/14/27 5:00 PM	195
BH CNN-KPJV-MAST-LIVE,03,02,06,01 ENG - Electrical - Grounding Plans - CTG U1					
AEC171118-05	Prep & IDR - Electrical Drawings - Grounding Plans - CTG Train 1	10	10/20/26 7:00 AM	11/2/26 5:00 PM	212
AEC171118-10	IDR - Electrical Drawings - Grounding Plans - CTG Train 1	5	11/3/26 7:00 AM	11/9/26 5:00 PM	212
AEC171118-15	Address IDR - Comments & Issue for Client Review - Grounding	5	11/10/26 7:00 AM	11/17/26 5:00 PM	212
AEC171118-20	Client Review - Grounding Plans - CTG Train 1	15	11/18/26 7:00 AM	12/9/26 5:00 PM	212
AEC171118-25	Address Client Comments & IFC - Grounding Plans - CTG Train	5	1/8/27 7:00 AM	1/14/27 5:00 PM	195
BH CNN-KPJV-MAST-LIVE,03,02,06,05 ENG - Electrical - Grounding Plans - Admin/Warehouse					
AEC171158-05	Prep & IDR - Grounding Plans - Admin/Warehouse	10	10/5/26 7:00 AM A	10/23/26 5:00 PM	215
AEC171158-10	IDR - Grounding Plans - Admin/Warehouse	10	10/26/26 7:00 AM	11/6/26 5:00 PM	215
AEC171158-15	Address Comments & Issue for Client Review - Grounding Plans	10	11/9/26 7:00 AM	11/23/26 5:00 PM	215
AEC171158-20	Client Review - Grounding Plans - Admin/Warehouse	15	11/24/26 7:00 AM	12/15/26 5:00 PM	215
AEC171158-25	Address Client Comments & IFC - Grounding Plans - Admin/Wa	10	12/16/26 7:00 AM	1/4/27 5:00 PM	215
BH CNN-KPJV-MAST-LIVE,03,02,06,06 ENG - Electrical - Grounding Plans - Plant Services/Service Water Area					
AEC171178-05	Prep & IDR - Grounding Plans - Plant Services / Service Water A	29	12/23/26 7:00 AM	2/8/27 5:00 PM	402
AEC171178-10	IDR - Grounding Plans - Plant Services / Service Water Area	10	2/9/27 7:00 AM	2/23/27 5:00 PM	402
AEC171178-15	Address Comments & Issue for Client Review - Grounding Plans	11	2/24/27 7:00 AM	3/10/27 5:00 PM	402




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC171178-20	Client Review - Grounding Plans - Plant Services / Service Wate	15	3/11/27 7:00 AM	4/1/27 5:00 PM	427
AEC171178-25	Address Client Comments & IFC - Grounding Plans - Plant Serv	10	4/2/27 7:00 AM	4/15/27 5:00 PM	427
BH CNN-KPJV-MAST-LIVE,03,02,06,09 ENG - Electrical - Grounding Plans - Demineriliz er Tanks					
AEC171179-05	Prep & Issue for IDR - Grounding Plans - Demineriliz er Tanks	4	9/4/26 7:00 AM A	10/15/26 5:00 PM	173
AEC171179-10	IDR - Grounding Plans - Demineriliz er Tanks	10	10/16/26 7:00 AM	10/29/26 5:00 PM	173
AEC171179-15	Address Client Comments & Issue CR - Grounding Plans - Dem	10	10/30/26 7:00 AM	11/13/26 5:00 PM	173
AEC171179-20	Client Review - Grounding Plans - Demineriliz er Tanks	15	11/16/26 7:00 AM	12/7/26 5:00 PM	173
AEC171179-25	Address Comments & Issue IFC - Grounding Plans - Demineriliz	10	12/8/26 7:00 AM	12/21/26 5:00 PM	173
BH CNN-KPJV-MAST-LIVE,03,02,06,07 ENG - Electrical - Grounding Plans - Fuel Gas Area					
AEC171168-05	Prep & IDR - Grounding Plans - Fuel Gas Area	15	1/15/27 7:00 AM	2/5/27 5:00 PM	429
AEC171168-10	IDR - Grounding Plans - Fuel Gas Area	10	2/8/27 7:00 AM	2/22/27 5:00 PM	429
AEC171168-15	Address Comments & Issue for Client Review - Grounding Plans	10	2/23/27 7:00 AM	3/8/27 5:00 PM	429
AEC171168-20	Client Review - Grounding Plans - Fuel Gas Area	15	3/9/27 7:00 AM	3/30/27 5:00 PM	429
AEC171168-25	Address Client Comments & IFC - Grounding Plans - Fuel Gas A	10	3/31/27 7:00 AM	4/13/27 5:00 PM	429
BH CNN-KPJV-MAST-LIVE,03,02,06,08 ENG - Electrical - Grounding Plans - Fuel Oil Area					
AEC171188-05	Prep & IDR - Grounding Plans Fuel Oil Area	0	6/1/26 7:00 AM A	6/12/26 5:00 PM A	
AEC171188-10	IDR - Grounding Plans Fuel Oil Area	0	6/18/26 7:00 AM A	7/2/26 5:00 PM A	
AEC171188-15	Address Comments & Issue for Client Review - Grounding Plans	0	7/8/26 7:00 AM A	7/22/26 5:00 PM A	
AEC171188-20	Client Review - Grounding Plans - Fuel Oil Area	0	7/22/26 7:00 AM A	7/30/26 5:00 PM A	
AEC171188-25	Address Client Comments & IFC - Grounding Plans - Fuel Oil An	0	7/31/26 7:00 AM A	9/1/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,02,05 ENG - Electrical - Cable List - Power Cable					
AEC171113-05	Prepare - Initial Power Cable List Set-up	0	3/23/26 7:00 AM A	5/18/26 5:00 PM A	
AEC171113-10	Input Information - Power Cable List	0	5/19/26 7:00 AM A	8/10/26 5:00 PM A	
AEC171113-15	Prep & IDR - Power Cable List	0	8/11/26 7:00 AM A	8/28/26 5:00 PM A	
AEC171113-20	IDR - Power Cable List	0	8/28/26 7:00 AM A	9/22/26 5:00 PM A	
AEC171113-25	Address IDR - Comments & Issue for Client Review - Final Powe	3	9/23/26 7:00 AM A	10/14/26 5:00 PM	524
AEC171113-35	Client Review - Power Cable List	15	10/15/26 7:00 AM	11/4/26 5:00 PM	524
AEC171113-40	Address Client Comments & IFC - Power Cable List	10	11/5/26 7:00 AM	11/19/26 5:00 PM	524
BH CNN-KPJV-MAST-LIVE,03,02,13 ENG - Electrical - Raceway List (CCL)					
AEC171114-05	Prep Raceway List for IDR - Raceway List(CCL)	110	3/2/27 7:00 AM	8/6/27 5:00 PM	304
AEC171114-10	IDR - Raceway List (CCL)	10	8/9/27 7:00 AM	8/20/27 5:00 PM	304
AEC171114-15	Address IDR - Comments & Issue for Client Review - Raceway L	5	8/23/27 7:00 AM	8/27/27 5:00 PM	304
AEC171114-20	Client Review - Raceway List (CCL)	15	8/30/27 7:00 AM	9/20/27 5:00 PM	304
AEC171114-25	Address Client Review Comments & Issue Final - Raceway List	15	9/21/27 7:00 AM	10/11/27 5:00 PM	304
BH CNN-KPJV-MAST-LIVE,03,02,15 ENG - Electrical - Cable List - Control Cable					
AEC171113-05A	Prep & Issue for IDR - Control Cable List	5	10/19/26 7:00 AM	10/23/26 5:00 PM	497
AEC171113-10A	IDR - Control Cable List	5	10/26/26 7:00 AM	10/30/26 5:00 PM	497
AEC171113-15A	Address IDR Comments & Issue CR - Final Control Cable List	15	11/2/26 7:00 AM	11/23/26 5:00 PM	497
AEC171113-20A	Client Review - Control Cable List	15	11/24/26 7:00 AM	12/15/26 5:00 PM	497
AEC171113-25A	Incorporate Client Comments & Issue IFC - Control Cable List	10	12/16/26 7:00 AM	1/4/27 5:00 PM	497
BH CNN-KPJV-MAST-LIVE,03,02,07 ENG - Electrical - Schematics & Wiring Diagrams					
BH CNN-KPJV-MAST-LIVE,03,02,07,04 ENG - Electrical - Schematics - Medium Voltage System					
AEC171155-05	Prepare - Schematic Diagrams - Medium Voltage System	30	11/2/26 7:00 AM	12/15/26 5:00 PM	26
AEC171155-15	Address Vendor Information & Issue for Client Review - Schema	20	12/16/26 7:00 AM	1/19/27 5:00 PM	26
AEC171155-20	Client Review - Schematic Diagrams - Medium Voltage System	15	1/20/27 7:00 AM	2/9/27 5:00 PM	458
AEC171155-25	Address Client Comments & IFC - Schematics - Medium Voltage	14	2/10/27 7:00 AM	3/2/27 5:00 PM	458
BH CNN-KPJV-MAST-LIVE,03,02,07,20 ENG - Electrical - Wiring Diagrams - Medium Voltage System					
AEC171159-00	Receive MV submittals - Wiring Diagrams - Medium Voltage Sys	0		11/16/26 5:00 PM	442
AEC171159-05	Prepare - Wiring Diagrams - Medium Voltage Systems	25	11/17/26 7:00 AM	12/22/26 5:00 PM	442
AEC171159-10	Address information & IDR - Wiring Diagrams - Medium Voltage	25	12/23/26 7:00 AM	2/2/27 5:00 PM	442
AEC171159-15	IDR - Wiring Diagrams - Medium Voltage Systems	5	2/3/27 7:00 AM	2/9/27 5:00 PM	442

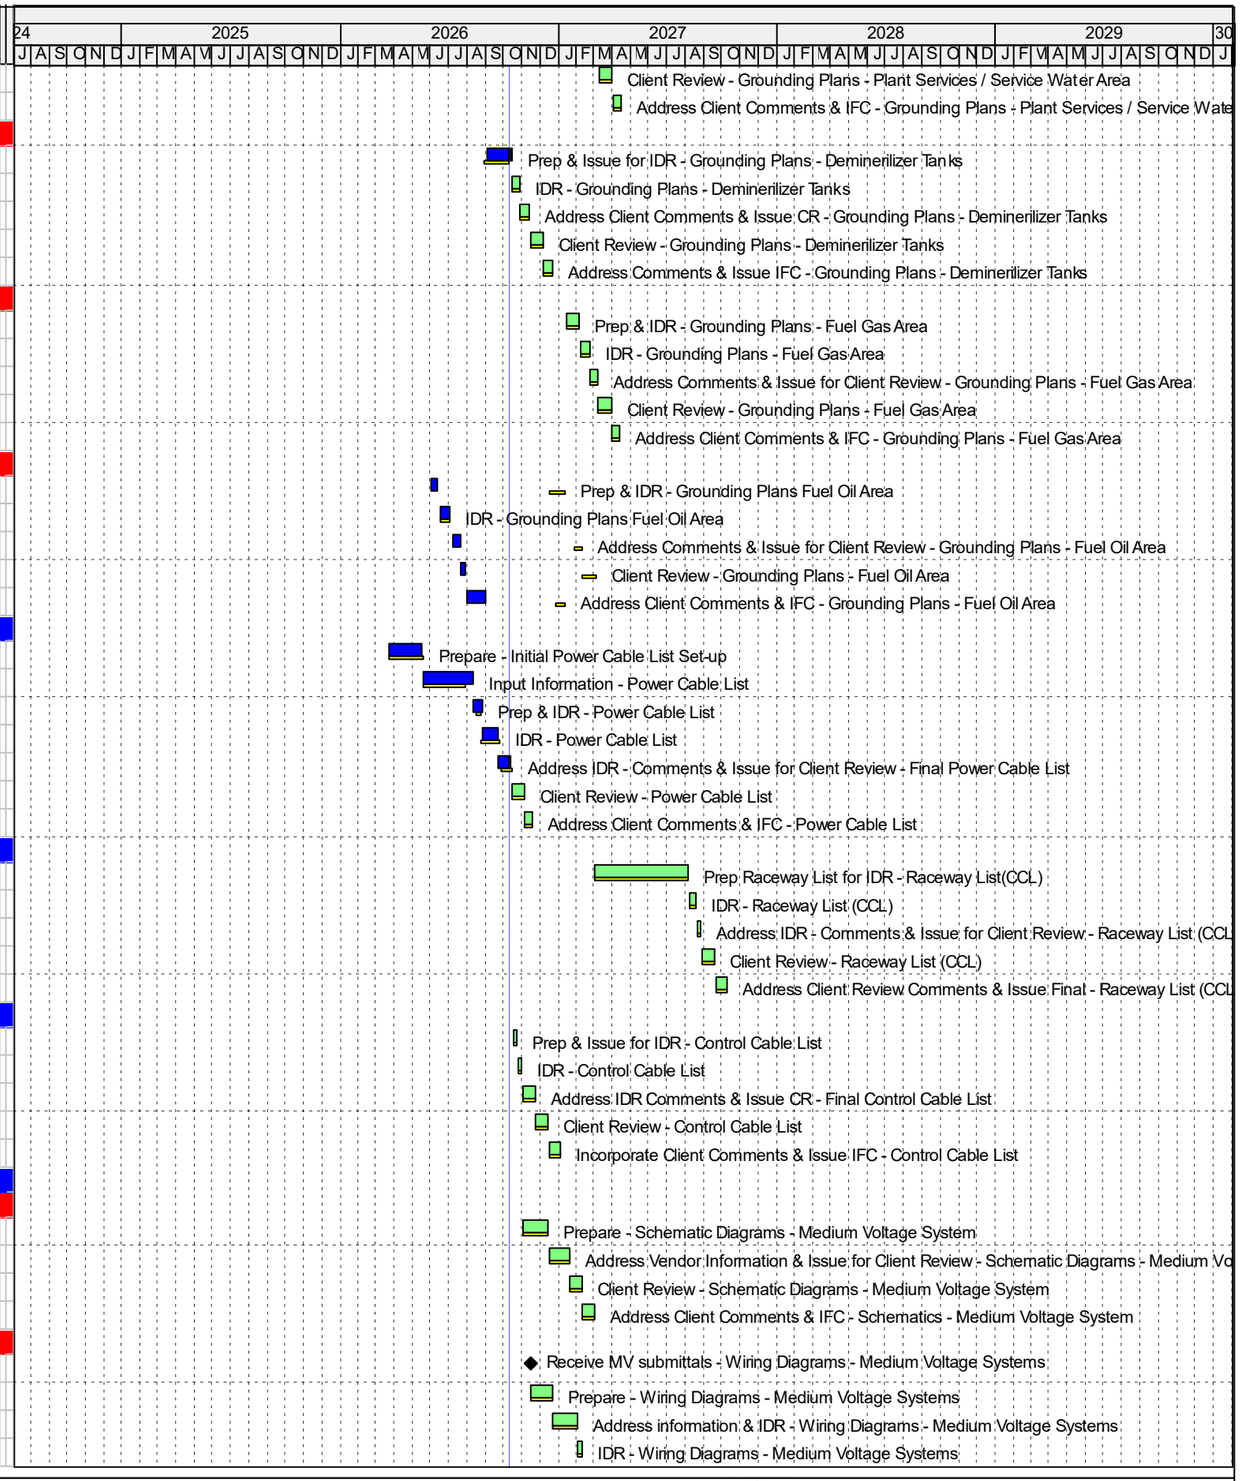


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC171159-20	Address IDR - Comments & Issue for Client Review - Wirings - M	5	2/10/27 7:00 AM	2/17/27 5:00 PM	442
AEC171159-25	Client Review - Wiring Diagrams - Medium Voltage Systems	15	2/18/27 7:00 AM	3/10/27 5:00 PM	442
AEC171159-30	Address Client Comments & Update w/Final Vendor Info & IFC -	10	3/11/27 7:00 AM	3/24/27 5:00 PM	442
BH CNN-KPJV-MAST-LIVE,03,02,07,16 ENG - Electrical - Schematics - Low Voltage System					
AEC171157-00	Receive ABB Vendor Information - Schematic Diagrams - Low V	15	10/12/26 7:00 AM	10/30/26 5:00 PM	26
AEC171157-05	Prepare - Schematic Diagrams & IDR - Low Voltage System	30	11/2/26 7:00 AM	12/15/26 5:00 PM	189
AEC171157-10	IDR - Low Voltage System	5	12/16/26 7:00 AM	12/22/26 5:00 PM	189
AEC171157-15	Adress IDR - Comments & Issue for Client Review - Low Voltage	10	12/23/26 7:00 AM	1/11/27 5:00 PM	189
AEC171157-20	Client Review - Schematic Diagrams - Low Voltage System	15	1/12/27 7:00 AM	2/2/27 5:00 PM	392
AEC171157-25	Address Client Comments & IFC - Schematics - Low Voltage Sy	10	2/3/27 7:00 AM	2/17/27 5:00 PM	392
BH CNN-KPJV-MAST-LIVE,03,02,07,21 ENG - Electrical - Wiring Diagrams - Low Voltage System					
AEC171163-00	Received - Vendor Submittals - Wiring Diagrams - Low Voltage	0		10/15/26 5:00 PM	453
AEC171163-05	Prepare - Wiring Diagrams - Low Voltage Systems	40	10/16/26 7:00 AM	12/14/26 5:00 PM	453
AEC171163-10	Address information & IDR - Wiring Diagrams - Low Voltage Sys	10	12/15/26 7:00 AM	12/30/26 5:00 PM	453
AEC171163-15	IDR - Wiring Diagrams - Low Voltage Systems	10	1/4/27 7:00 AM	1/15/27 5:00 PM	453
AEC171163-20	Address IDR - Comments & Issue for Client Review - Wirings - L	10	1/19/27 7:00 AM	2/1/27 5:00 PM	453
AEC171163-25	Client Review - Wiring Diagrams - Low Voltage Systems	15	2/2/27 7:00 AM	2/23/27 5:00 PM	453
AEC171163-30	Address Client Comments & Update w/Final Vendor Info & IFC -	10	2/24/27 7:00 AM	3/9/27 5:00 PM	453
BH CNN-KPJV-MAST-LIVE,03,02,07,17 ENG - Electrical - Wiring Diagrams - DC & UPS System					
AEC171161-00	Received - Vendor Information - Wiring Diagrams - DC & UPS S	0		3/31/27 5:00 PM	363
AEC171161-05	Prepare - Wiring Diagrams - DC & UPS System	30	4/1/27 7:00 AM	5/12/27 5:00 PM	363
AEC171161-15	Address information & Issue for Client Review - Wiring Diagrams	20	5/13/27 7:00 AM	6/10/27 5:00 PM	363
AEC171161-20	Client Review - Wiring Diagrams - DC & UPS System	15	6/11/27 7:00 AM	7/2/27 5:00 PM	363
AEC171161-25	Address Client Comments & Update w/Final Vendor Info & IFC -	10	7/6/27 7:00 AM	7/19/27 5:00 PM	363
BH CNN-KPJV-MAST-LIVE,03,02,07,18 ENG - Electrical - Wiring Diagrams - CTG Unit 1					
AEC171165-00	Receive - Vendor Information - Wiring & Wiring Diagrams - CTG	1	10/12/26 7:00 AM	10/12/26 5:00 PM	90
AEC171165-05	Prepare - Wiring Diagrams & IDR - CTG Train 1	38	10/13/26 7:00 AM	12/7/26 5:00 PM	391
AEC171165-10	IDR - Wiring Diagrams - CTG Train 1	5	12/8/26 7:00 AM	12/14/26 5:00 PM	391
AEC171165-15	Address IDR - Comments & Issue for Client Review - Wiring Diag	5	12/15/26 7:00 AM	12/21/26 5:00 PM	391
AEC171165-20	Client Review - Wiring Diagrams - CTG Train 1	15	12/22/26 7:00 AM	1/15/27 5:00 PM	483
AEC171165-25	Address Client Comments & Update w/Final Vendor Info & IFC -	5	1/19/27 7:00 AM	1/25/27 5:00 PM	483
BH CNN-KPJV-MAST-LIVE,03,02,07,26 ENG - Electrical - Wiring Diagrams - CTG Unit 2					
AEC171167-35	Prepare - Wiring Diagrams - CTG Train 2	20	1/20/27 7:00 AM	2/17/27 5:00 PM	26
AEC171167-45	Receive Vendor Information - Wiring Diagrams - CTG Train 2	8	3/18/27 7:00 AM	3/30/27 5:00 PM	394
AEC171167-55	Incorporate Info & Issue for Client Review - Wiring Diagrams - C	20	3/31/27 7:00 AM	4/27/27 5:00 PM	394
AEC171167-65	Client Review - Wiring Diagrams - CTG Train 2	15	4/28/27 7:00 AM	5/18/27 5:00 PM	394
AEC171167-75	Address Client Comments & Update w/Final Vendor Info & IFC -	10	5/19/27 7:00 AM	6/2/27 5:00 PM	394
BH CNN-KPJV-MAST-LIVE,03,02,07,15 ENG - Electrical - Wiring Diagrams - CTG Unit 3					
AEC171170-35	Prepare - Wiring Diagrams - CTG Train 3	20	2/10/27 7:00 AM	3/10/27 5:00 PM	26
AEC171170-45	IDR - Wiring Diagrams - CTG Train 3	5	3/11/27 7:00 AM	3/17/27 5:00 PM	394
AEC171170-55	Incorporate Information & Issue for Client Review - Wiring Diagr	5	3/18/27 7:00 AM	3/24/27 5:00 PM	397
AEC171170-65	Client Review - Wiring Diagrams - CTG Train 3	15	3/25/27 7:00 AM	4/15/27 5:00 PM	407
AEC171170-75	Address Client Comments & Update w/Final Vendor Info & IFC -	10	4/16/27 7:00 AM	4/29/27 5:00 PM	407
BH CNN-KPJV-MAST-LIVE,03,02,07,19 ENG - Electrical - Wiring Diagrams - CTG Unit 4					
AEC171175-05	Prepare - Wiring Diagrams - CTG Train 4	20	1/20/27 7:00 AM	2/17/27 5:00 PM	404
AEC171175-10	IDR - Wiring Diagrams - CTG Train 4	5	2/18/27 7:00 AM	2/24/27 5:00 PM	404
AEC171175-15	Incorporate Information & Issue for Client Review - Wiring Diagr	5	2/25/27 7:00 AM	3/3/27 5:00 PM	407
AEC171175-20	Client Review - Wiring Diagrams - CTG Train 4	15	3/4/27 7:00 AM	3/24/27 5:00 PM	412
AEC171175-25	Address Client Comments & Update w/Final Vendor Info & IFC -	10	3/25/27 7:00 AM	4/8/27 5:00 PM	412
BH CNN-KPJV-MAST-LIVE,03,02,07,25 ENG - Electrical - Wiring Diagrams - Misc. CTG Systems					
AEC171177-05	Prepare - Wiring Diagrams - Misc. CTG Systems	20	12/15/26 7:00 AM	1/15/27 5:00 PM	483

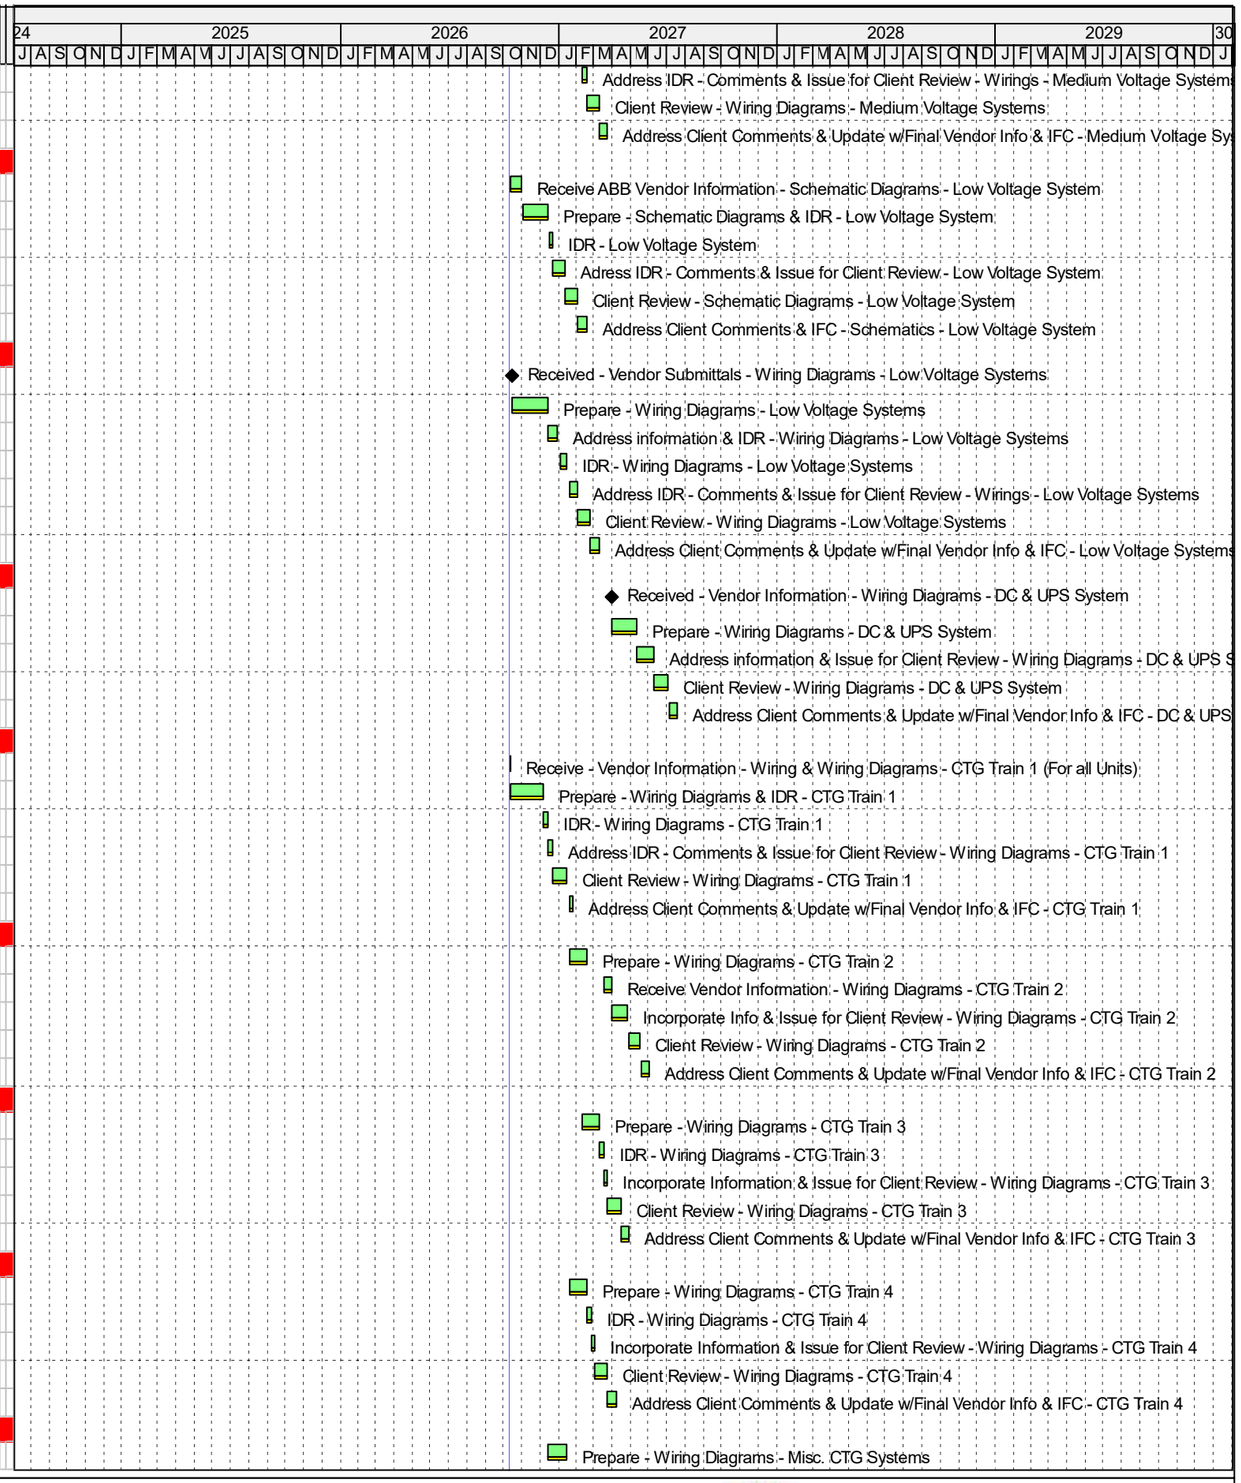

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC171177-10	IDR - Wiring Diagrams - Misc. CTG Systems	5	1/19/27 7:00 AM	1/25/27 5:00 PM	483
AEC171177-00	Received - Vendor Information - Misc. CTG Systems	0		3/10/27 5:00 PM	402
AEC171177-15	Address information & Issue for Client Review - Wiring Diagrams	25	3/11/27 7:00 AM	4/15/27 5:00 PM	402
AEC171177-20	Client Review - Wiring Diagrams - Misc. CTG Systems	15	4/16/27 7:00 AM	5/6/27 5:00 PM	402
AEC171177-25	Address Client Comments & Update w/Final Vendor Info & IFC -	10	5/7/27 7:00 AM	5/20/27 5:00 PM	402
BH CNN-KPJV-MAST-LIVE,03,02,07,01 ENG - Electrical - Wiring Diagrams - Fuel Gas					
AEC171115-07	Prepare - Wiring Diagrams - Fuel Gas	30	2/25/27 7:00 AM	4/8/27 5:00 PM	377
AEC171115-10	Receive - Vendor Information - Wiring Diagrams - Fuel Gas	10	4/9/27 7:00 AM	4/22/27 5:00 PM	377
AEC171115-15	Address information & Issue for Client Review - Wiring Diagrams	20	4/23/27 7:00 AM	5/20/27 5:00 PM	377
AEC171115-20	Client Review - Wiring Diagrams - Fuel Gas	15	5/21/27 7:00 AM	6/11/27 5:00 PM	377
AEC171115-25	Address Client Comments & Update w/Final Vendor Info & IFC -	10	6/14/27 7:00 AM	6/28/27 5:00 PM	377
BH CNN-KPJV-MAST-LIVE,03,02,07,06 ENG - Electrical - Wiring Diagrams - Demineralized Water					
AEC171117-07	Prepare - Wiring Diagrams - Demin Water	10	12/15/26 7:00 AM	12/30/26 5:00 PM	391
AEC171117-12	Receive - Vendor Information - Wiring Diagrams - Demin Water	10	1/4/27 7:00 AM	1/15/27 5:00 PM	391
AEC171117-17	Address information & Issue for Client Review - Wiring Diagrams	12	1/19/27 7:00 AM	2/3/27 5:00 PM	391
AEC171117-22	Client Review - Wiring Diagrams - Demin Water	15	2/4/27 7:00 AM	2/25/27 5:00 PM	451
AEC171117-27	Address Client Comments & Update w/Final Vendor Info & IFC -	10	2/26/27 7:00 AM	3/11/27 5:00 PM	451
BH CNN-KPJV-MAST-LIVE,03,02,07,09 ENG - Electrical - Wiring Diagrams - Fuel Oil					
AEC171107-05	Prepare - Wiring Diagrams - Fuel Oil	15	2/4/27 7:00 AM	2/25/27 5:00 PM	406
AEC171107-12	Receive - Vendor Information - Wiring Diagrams - Fuel Oil	10	2/26/27 7:00 AM	3/11/27 5:00 PM	406
AEC171107-17	Address information & Issue for Client Review - Wiring Diagrams	20	3/12/27 7:00 AM	4/9/27 5:00 PM	406
AEC171107-22	Client Review - Wiring Diagrams - Fuel Oil	15	4/12/27 7:00 AM	4/30/27 5:00 PM	406
AEC171107-27	Address Client Comments & Update w/Final Vendor Info & IFC -	10	5/3/27 7:00 AM	5/14/27 5:00 PM	406
BH CNN-KPJV-MAST-LIVE,03,02,07,07 ENG - Electrical - Wiring Diagrams - Closed Cooling Water					
AEC171127-07	Prepare - Wiring Diagrams - Closed Cooling Water	15	2/25/27 7:00 AM	3/17/27 5:00 PM	392
AEC171127-12	Receive - Vendor Information - Wiring Diagrams - Closed Coolin	10	3/18/27 7:00 AM	4/1/27 5:00 PM	392
AEC171127-17	Address information & Issue for Client Review - Wiring Diagrams	20	4/2/27 7:00 AM	4/29/27 5:00 PM	392
AEC171127-22	Client Review - Wiring Diagrams - Closed Cooling Water	15	4/30/27 7:00 AM	5/20/27 5:00 PM	392
AEC171127-27	Address Client Comments & Update w/Final Vendor Info & IFC -	10	5/21/27 7:00 AM	6/4/27 5:00 PM	392
BH CNN-KPJV-MAST-LIVE,03,02,07,10 ENG - Electrical - Wiring Diagrams - Service Water					
AEC171119-07	Prepare - Wiring Diagrams - Service Water	20	2/4/27 7:00 AM	3/4/27 5:00 PM	401
AEC171119-12	Receive - Vendor Information - Wiring Diagrams - Service Wate	10	3/5/27 7:00 AM	3/18/27 5:00 PM	401
AEC171119-17	Address information & Issue for Client Review - Wiring Diagrams	20	3/19/27 7:00 AM	4/16/27 5:00 PM	401
AEC171119-22	Client Review - Wiring Diagrams - Service Water	15	4/19/27 7:00 AM	5/7/27 5:00 PM	401
AEC171119-27	Address Client Comments & Update w/Final Vendor Info & IFC -	10	5/10/27 7:00 AM	5/21/27 5:00 PM	401
BH CNN-KPJV-MAST-LIVE,03,02,07,08 ENG - Electrical - Wiring Diagrams - Compressed Air					
AEC171131-07	Prepare - Wiring Diagrams - Compressed Air	18	2/25/27 7:00 AM	3/22/27 5:00 PM	159
AEC171131-12	Receive - Vendor Information - Wiring Diagrams - Compressed A	10	3/23/27 7:00 AM	4/6/27 5:00 PM	389
AEC171131-17	Address information & Issue for Client Review - Wiring Diagrams	20	4/7/27 7:00 AM	5/4/27 5:00 PM	389
AEC171131-22	Client Review - Wiring Diagrams - Compressed Air	15	5/5/27 7:00 AM	5/25/27 5:00 PM	389
AEC171131-27	Address Client Comments & Update w/Final Vendor Info & IFC -	10	5/26/27 7:00 AM	6/9/27 5:00 PM	389
BH CNN-KPJV-MAST-LIVE,03,02,07,11 ENG - Electrical - Wiring Diagrams - Potable Water					
AEC171133-07	Prepare - Wiring Diagrams - Potable Water	30	3/31/27 7:00 AM	5/11/27 5:00 PM	354
AEC171133-12	Receive - Vendor Information - Wiring Diagrams - Potable Wate	10	5/12/27 7:00 AM	5/25/27 5:00 PM	354
AEC171133-17	Address information & Issue for Client Review - Wiring Diagrams	20	5/26/27 7:00 AM	6/24/27 5:00 PM	354
AEC171133-22	Client Review - Wiring Diagrams - Potable Water	15	6/25/27 7:00 AM	7/16/27 5:00 PM	354
AEC171133-27	Address Client Comments & Update w/Final Vendor Info & IFC -	10	7/19/27 7:00 AM	7/30/27 5:00 PM	354
BH CNN-KPJV-MAST-LIVE,03,02,07,12 ENG - Electrical - Wiring Diagrams - Water Wash					
AEC171137-07	Prepare - Wiring Diagrams - Water Wash	30	2/25/27 7:00 AM	4/8/27 5:00 PM	159
AEC171137-12	Receive - Vendor Information - Wiring Diagrams - Water Wash	10	4/9/27 7:00 AM	4/22/27 5:00 PM	159
AEC171137-17	Address information & Issue for Client Review - Wiring Diagrams	20	4/23/27 7:00 AM	5/20/27 5:00 PM	159




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC171137-22	Client Review - Wiring Diagrams - Water Wash	15	5/21/27 7:00 AM	6/11/27 5:00 PM	159
AEC171137-27	Address Client Comments & Update w/Final Vendor Info & IFC -	10	6/14/27 7:00 AM	6/28/27 5:00 PM	159
BH CNN-KPJV-MAST-LIVE,03,02,07,22 ENG - Electrical - Wiring Diagrams - HVAC Systems					
AEC171180-05	Prepare - Wiring Diagrams - HVAC Systems	30	4/9/27 7:00 AM	5/20/27 5:00 PM	347
AEC171180-10	Receive - Vendor Information - Wiring Diagrams - HVAC System	10	5/21/27 7:00 AM	6/4/27 5:00 PM	347
AEC171180-15	Address information & Issue for Client Review - Wiring Diagrams	20	6/7/27 7:00 AM	7/6/27 5:00 PM	347
AEC171180-20	Client Review - Wiring Diagrams - HVAC Systems	15	7/7/27 7:00 AM	7/27/27 5:00 PM	347
AEC171180-25	Address Client Comments & Update w/Final Vendor Info & IFC -	10	7/28/27 7:00 AM	8/10/27 5:00 PM	347
BH CNN-KPJV-MAST-LIVE,03,02,07,23 ENG - Electrical - Wiring Diagrams - Misc. Low Voltage Systems					
AEC171185-05	Prepare - Wiring Diagrams - Misc. Low Voltage Systems	30	4/9/27 7:00 AM	5/20/27 5:00 PM	347
AEC171185-10	Receive - Vendor Information - Wiring Diagrams - Misc. Low Vol	10	5/21/27 7:00 AM	6/4/27 5:00 PM	347
AEC171185-15	Address information & Issue for Client Review - Wiring Diagrams	20	6/7/27 7:00 AM	7/6/27 5:00 PM	347
AEC171185-20	Client Review - Wiring Diagrams - Misc. Low Voltage Systems	15	7/7/27 7:00 AM	7/27/27 5:00 PM	347
AEC171185-25	Address Client Comments & Update w/Final Vendor Info & IFC -	10	7/28/27 7:00 AM	8/10/27 5:00 PM	347
BH CNN-KPJV-MAST-LIVE,03,02,07,13 ENG - Electrical - Wiring Diagrams - Waste Water					
AEC171139-07	Prepare - Wiring Diagrams - Waste Water	35	11/19/26 7:00 AM	1/13/27 5:00 PM	206
AEC171139-12	Receive - Vendor Information - Wiring Diagrams - Waste Water	10	1/14/27 7:00 AM	1/28/27 5:00 PM	206
AEC171139-17	Address information & Issue for Client Review - Wiring Diagrams	20	1/29/27 7:00 AM	2/26/27 5:00 PM	206
AEC171139-22	Client Review - Wiring Diagrams - Waste Water	15	3/1/27 7:00 AM	3/19/27 5:00 PM	206
AEC171139-27	Address Client Comments & Update w/Final Vendor Info & IFC -	10	3/22/27 7:00 AM	4/5/27 5:00 PM	206
BH CNN-KPJV-MAST-LIVE,03,02,07,14 ENG - Electrical - Wiring Diagrams - Compressed Gas (CO2,H2, & N2)					
AEC171141-07	Prepare - Wiring Diagrams - Compressed Gases (H2,N2, & CO2	30	2/4/27 7:00 AM	3/18/27 5:00 PM	391
AEC171141-12	Receive - Vendor Information - Wiring Diagrams - Compressed (	10	3/19/27 7:00 AM	4/2/27 5:00 PM	391
AEC171141-17	Address information & Issue for Client Review - Wiring Diagrams	20	4/5/27 7:00 AM	4/30/27 5:00 PM	391
AEC171141-22	Client Review - Wiring Diagrams - Compressed Gases (H2,N2, &	15	5/3/27 7:00 AM	5/21/27 5:00 PM	391
AEC171141-27	Address Client Comments & Update w/Final Vendor Info & IFC -	10	5/24/27 7:00 AM	6/7/27 5:00 PM	391
BH CNN-KPJV-MAST-LIVE,03,02,07,05 ENG - Electrical - Wiring Diagrams - Fire Protection					
AEC171145-07	Prepare - Wiring Diagrams - Fire Protection	30	2/12/27 7:00 AM	3/29/27 5:00 PM	26
AEC171145-12	Receive - Vendor Information - Wiring Diagrams - Fire Protection	10	3/30/27 7:00 AM	4/12/27 5:00 PM	26
AEC171145-17	Address information & Issue for Client Review - Wiring Diagrams	20	4/13/27 7:00 AM	5/10/27 5:00 PM	26
AEC171145-22	Client Review - Wiring Diagrams - Fire Protection	15	5/11/27 7:00 AM	6/1/27 5:00 PM	26
AEC171145-27	Address Client Comments & Update w/Final Vendor Info & IFC -	10	6/2/27 7:00 AM	6/15/27 5:00 PM	26
BH CNN-KPJV-MAST-LIVE,03,02,07,02 ENG - Electrical - Wiring Diagrams - Sanitary System					
AEC171147-07	Prepare - Wiring Diagrams - Sanitary System	30	3/15/27 7:00 AM	4/26/27 5:00 PM	365
AEC171147-12	Receive - Vendor Information - Wiring Diagrams - Sanitary Syste	10	4/27/27 7:00 AM	5/10/27 5:00 PM	365
AEC171147-17	Address information & Issue for Client Review - Wiring Diagrams	20	5/11/27 7:00 AM	6/8/27 5:00 PM	365
AEC171147-22	Client Review - Wiring Diagrams - Sanitary System	15	6/9/27 7:00 AM	6/30/27 5:00 PM	365
AEC171147-27	Address Client Comments & Update w/Final Vendor Info & IFC -	10	7/1/27 7:00 AM	7/15/27 5:00 PM	365
BH CNN-KPJV-MAST-LIVE,03,02,07,24 ENG - Electrical - Wiring Diagrams - DCS Power Supplies					
AEC171190-05	Prepare - Wiring Diagrams - DCS Power Supplies	28	2/25/27 7:00 AM	4/6/27 5:00 PM	379
AEC171190-10	Receive - Vendor Information - Wiring Diagrams - DCS Power Su	10	4/7/27 7:00 AM	4/20/27 5:00 PM	379
AEC171190-15	Address information & Issue for Client Review - Wiring Diagrams	20	4/21/27 7:00 AM	5/18/27 5:00 PM	379
AEC171190-20	Client Review - Wiring Diagrams - DCS Power Supplies	15	5/19/27 7:00 AM	6/9/27 5:00 PM	379
AEC171190-25	Address Client Comments & Update w/Final Vendor Info & IFC -	10	6/10/27 7:00 AM	6/24/27 5:00 PM	379
BH CNN-KPJV-MAST-LIVE,03,02,11 ENG - Electrical - Hazardous Area Drawings					
AEC171120-05	Prepare & IDR - Hazardous Area Drawings	35	11/17/26 7:00 AM	1/11/27 5:00 PM	432
AEC171120-10	IDR - Hazardous Area Drawings	10	1/12/27 7:00 AM	1/26/27 5:00 PM	432
AEC171120-15	Address IDR - Comments & Issue for Client Review - Hazardous	10	1/27/27 7:00 AM	2/9/27 5:00 PM	432
AEC171120-20	Client Review - Hazardous Area Drawings	15	2/10/27 7:00 AM	3/3/27 5:00 PM	432
AEC171120-25	Address Client Comments & Issue Final - Hazardous Area Drawi	25	3/4/27 7:00 AM	4/8/27 5:00 PM	432
BH CNN-KPJV-MAST-LIVE,03,02,12 ENG - Electrical - Panel Schedules					

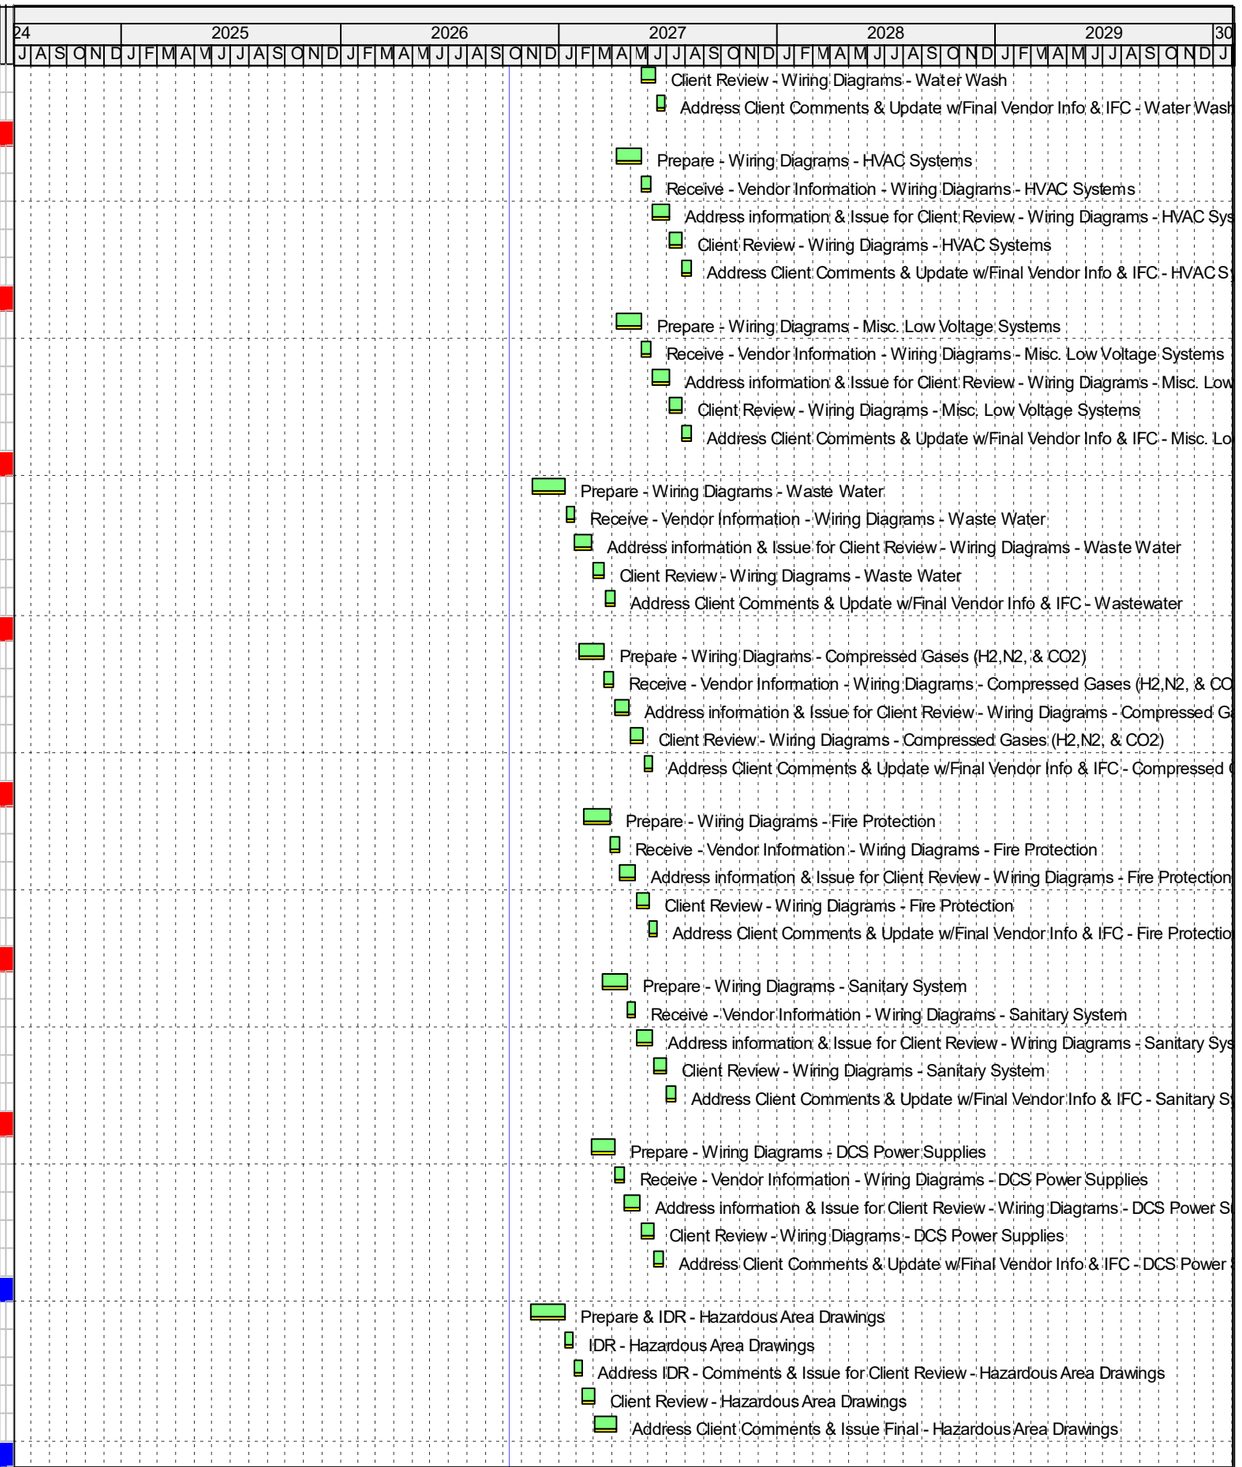


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
BH CNN-KPJV-MAST-LIVE,03,02,12,01 ENG - Electrical - Panel Schedules - CTG 1 Area					
AEC171121-05	Prepare & IDR - Panel Schedule - CTG Train 1 Area	0	6/1/26 7:00 AM A	6/15/26 5:00 PM A	
AEC171121-10	IDR - Panel Schedule - CTG Train 1 Area	0	6/15/26 7:00 AM A	6/26/26 5:00 PM A	
AEC171121-15	Address IDR - Comments & Issue for Client Review - Panel Sch	0	6/29/26 7:00 AM A	7/21/26 5:00 PM A	
AEC171121-20	Client Review - Panel Schedule - CTG Train 1 Area	0	7/21/26 7:00 AM A	8/7/26 5:00 PM A	
AEC171121-25	Address Client Comments & Issue Final - Panel Schedule - CTG	0	8/10/26 7:00 AM A	8/14/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,02,12,02 ENG - Electrical - Panel Schedules - CTG 2 Area					
AEC171131-05	Prepare & IDR - Panel Schedule - CTG Train 2 Area	0	7/30/26 7:00 AM A	8/13/26 5:00 PM A	
AEC171131-15	Address IDR - Comments & Issue for Client Review - Panel Sch	0	8/10/26 7:00 AM A	8/13/26 5:00 PM A	
AEC171131-20	Client Review - Panel Schedule - CTG Train 2 Area	0	8/14/26 7:00 AM A	8/25/26 5:00 PM A	
AEC171131-10	IDR - Panel Schedule - CTG Train 2 Area	0	8/14/26 7:00 AM A	8/31/26 5:00 PM A	
AEC171131-25	Address Client Comments & Issue Final - Panel Schedule - CTG	12	8/26/26 7:00 AM A	10/27/26 5:00 PM	540
BH CNN-KPJV-MAST-LIVE,03,02,12,03 ENG - Electrical - Panel Schedules - CTG 3 Area					
AEC171141-05	Prepare & IDR - Panel Schedule - CTG Train 3 Area	0	7/30/26 7:00 AM A	8/13/26 5:00 PM A	
AEC171141-15	Address IDR - Comments & Issue for Client Review - Panel Sch	0	8/10/26 7:00 AM A	8/13/26 5:00 PM A	
AEC171141-10	IDR - Panel Schedule - CTG Train 3 Area	0	8/14/26 7:00 AM A	8/25/26 5:00 PM A	
AEC171141-20	Client Review - Panel Schedule - CTG Train 3 Area	0	8/14/26 7:00 AM A	8/25/26 5:00 PM A	
AEC171141-25	Address Client Comments & Issue Final - Panel Schedule - CTG	1	10/6/26 7:00 AM A	10/20/26 5:00 PM	545
BH CNN-KPJV-MAST-LIVE,03,02,12,04 ENG - Electrical - Panel Schedules - CTG 4 Area					
AEC171151-05	Prepare & IDR - Panel Schedule - CTG Train 4 Area	0	7/30/26 7:00 AM A	8/13/26 5:00 PM A	
AEC171151-15	Address IDR - Comments & Issue for Client Review - Panel Sch	0	8/10/26 7:00 AM A	8/13/26 5:00 PM A	
AEC171151-20	Client Review - Panel Schedule - CTG Train 4 Area	0	8/14/26 7:00 AM A	8/24/26 5:00 PM A	
AEC171151-10	IDR - Panel Schedule - CTG Train 4 Area	0	8/14/26 7:00 AM A	8/25/26 5:00 PM A	
AEC171151-25	Address Client Comments & Issue Final - Panel Schedule - CTG	6	10/6/26 7:00 AM A	10/19/26 5:00 PM	545
BH CNN-KPJV-MAST-LIVE,03,02,12,05 ENG - Electrical - Panel Schedules - Admin Area					
AEC171173-05	Prepare & IDR - Panel Schedule - Admin Area	0	8/24/26 7:00 AM A	9/4/26 5:00 PM A	
AEC171173-10	IDR - Panel Schedule - Admin Area	0	9/8/26 7:00 AM A	9/18/26 5:00 PM A	
AEC171173-15	Address IDR - Comments & Issue for Client Review - Panel Sch	0	9/21/26 7:00 AM A	10/6/26 5:00 PM A	
AEC171173-20	Client Review - Panel Schedule - Admin Area	13	10/7/26 7:00 AM A	10/28/26 5:00 PM	529
AEC171173-25	Address Client Comments & Issue Final - Panel Schedule - Adm	10	10/29/26 7:00 AM	11/12/26 5:00 PM	529
BH CNN-KPJV-MAST-LIVE,03,02,12,06 ENG - Electrical - Panel Schedules - Plant Services Area					
AEC171183-05	Prepare & IDR - Panel Schedule - Plant Services Area	0	9/9/26 7:00 AM A	9/24/26 5:00 PM A	
AEC171183-10	IDR - Panel Schedule - Plant Services Area	0	9/24/26 7:00 AM A	10/1/26 5:00 PM A	
AEC171183-15	Address IDR - Comments & Issue for Client Review - Panel Sch	5	10/2/26 7:00 AM A	10/16/26 5:00 PM	522
AEC171183-20	Client Review - Panel Schedule - Plant Services Area	15	10/19/26 7:00 AM	11/6/26 5:00 PM	522
AEC171183-25	Address Client Comments & Issue Final - Panel Schedule - Plar	10	11/9/26 7:00 AM	11/23/26 5:00 PM	522
BH CNN-KPJV-MAST-LIVE,03,02,12,07 ENG - Electrical - Panel Schedules - Fuel Oil Area					
AEC171187-05	Prepare & IDR - Panel Schedule - Fuel Oil Area	0	9/9/26 7:00 AM A	9/24/26 5:00 PM A	
AEC171187-10	IDR - Panel Schedule - Fuel Oil Area	0	9/24/26 7:00 AM A	10/1/26 5:00 PM A	
AEC171187-15	Address IDR - Comments & Issue for Client Review - Panel Sch	4	10/2/26 7:00 AM A	10/15/26 5:00 PM	523
AEC171187-20	Client Review - Panel Schedule - Fuel Oil Area	15	10/16/26 7:00 AM	11/5/26 5:00 PM	523
AEC171187-25	Address Client Comments & Issue Final - Panel Schedule - Fue	10	11/6/26 7:00 AM	11/20/26 5:00 PM	523
BH CNN-KPJV-MAST-LIVE,03,02,12,08 ENG - Electrical - Panel Schedules - Fuel Gas Area					
AEC171189-05	Prepare & IDR - Panel Schedule - Fuel Gas Area	0	9/9/26 7:00 AM A	9/24/26 5:00 PM A	
AEC171189-10	IDR - Panel Schedule - Fuel Gas Area	0	9/24/26 7:00 AM A	10/1/26 5:00 PM A	
AEC171189-15	Address IDR - Comments & Issue for Client Review - Panel Sch	5	10/2/26 7:00 AM A	10/16/26 5:00 PM	522
AEC171189-20	Client Review - Panel Schedule - Fuel Gas Area	15	10/26/26 7:00 AM	11/16/26 5:00 PM	517
AEC171189-25	Address Client Comments & Issue Final - Panel Schedule - Fue	10	11/17/26 7:00 AM	12/1/26 5:00 PM	517
BH CNN-KPJV-MAST-LIVE,03,06 ENG - Instrumentation & Control					
BH CNN-KPJV-MAST-LIVE,03,06,01 ENG - Instrumentation & Control - Instrument Data Sheets					
BH CNN-KPJV-MAST-LIVE,03,06,01,01 ENG - Instrumentation & Control - Instrument Data Sheets - Pressure Transmitters					

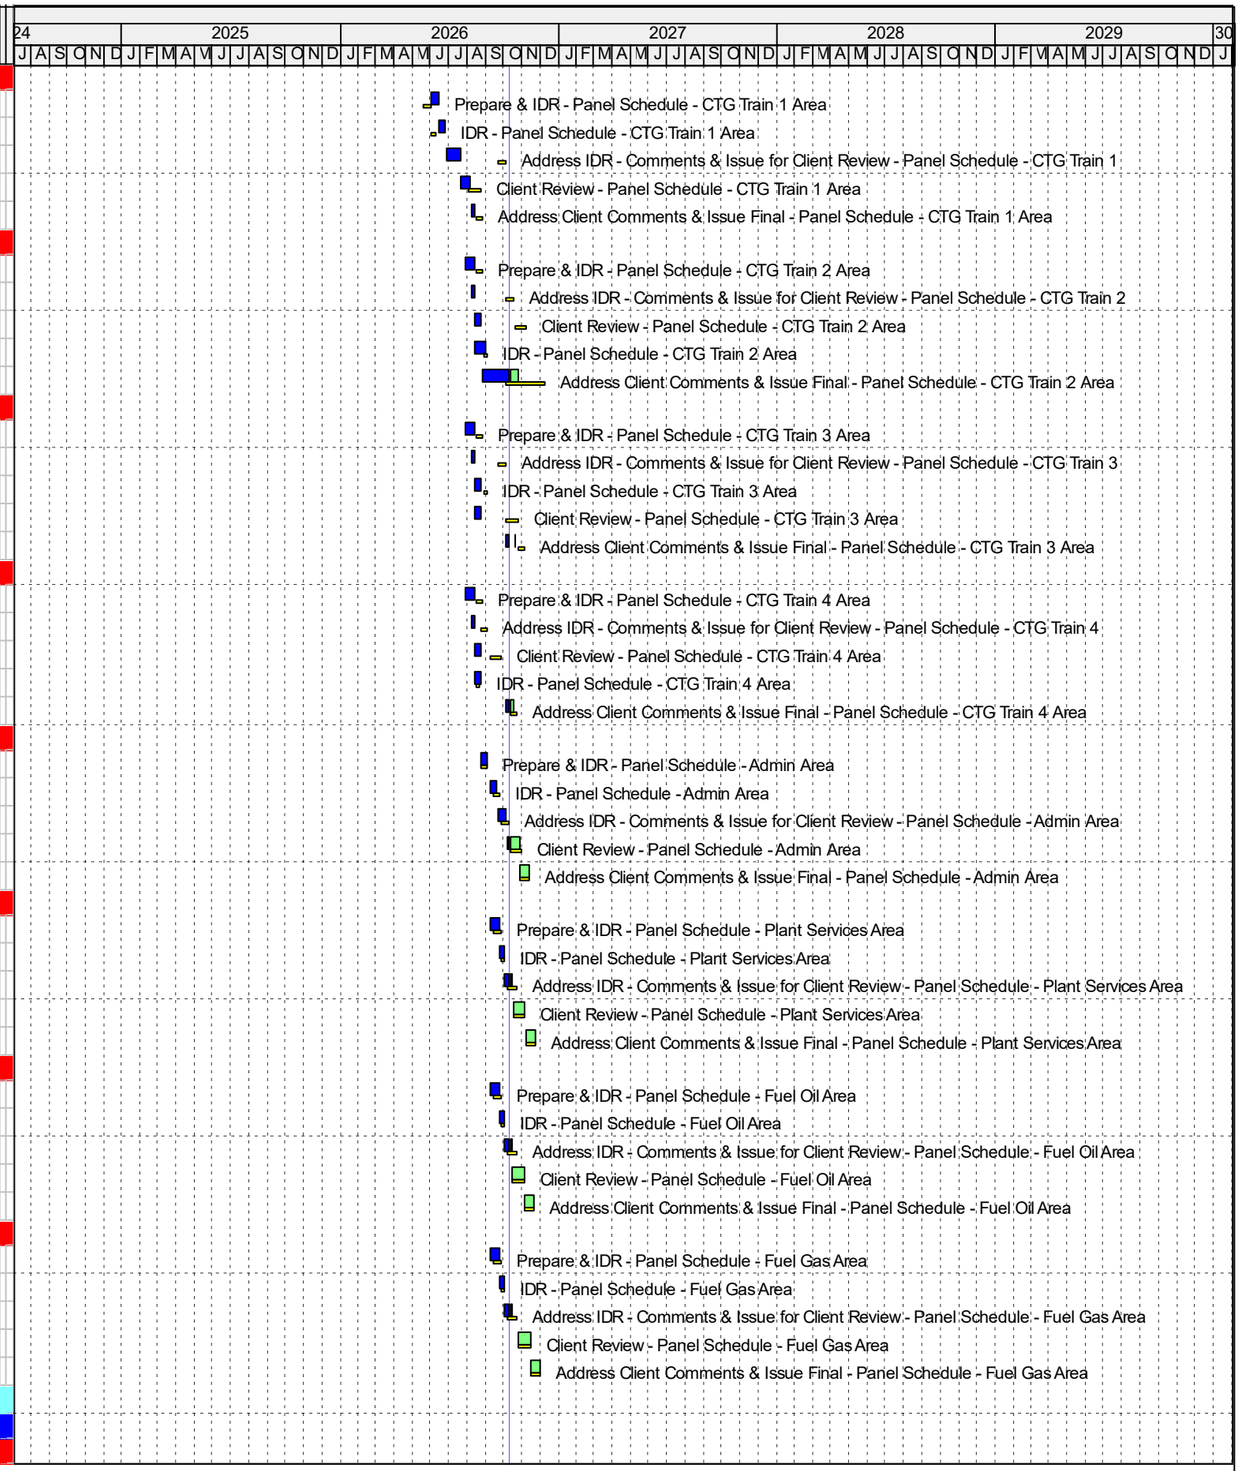

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC190802-05	Prep Instrument Data Sheets & IDR - Pressure Transmitters	20	12/3/26 7:00 AM	1/5/27 5:00 PM	419
AEC190802-20	IDR - Instrument Data Sheets - Pressure Transmitters	5	1/6/27 7:00 AM	1/12/27 5:00 PM	419
AEC190802-25	Address Comments & Issue for Client Review - Instrument Data	5	1/13/27 7:00 AM	1/20/27 5:00 PM	419
AEC190802-30	Client Review - Instrument Data Sheets - Pressure Transmitters	15	1/21/27 7:00 AM	2/10/27 5:00 PM	419
AEC190802-35	Address Client Comments & Finalize Instrument Data Sheets - I	10	2/11/27 7:00 AM	2/25/27 5:00 PM	419
BH CNN-KPJV-MAST-LIVE,03,06,01,13 ENG - Instrumentation & Control - Instrument Data Sheets - Temperature Indicators					
AEC190814-05	Prep Instrument Data Sheets & IDR - Temperature Indicators	10	3/2/27 7:00 AM	3/15/27 5:00 PM	419
AEC190814-10	IDR - Instrument Data Sheets - Temperature Indicators	5	3/16/27 7:00 AM	3/22/27 5:00 PM	419
AEC190814-15	Address Comments & Issue for Client Review - Instrument Data	5	3/23/27 7:00 AM	3/30/27 5:00 PM	419
AEC190814-20	Client Review - Instrument Data Sheets - Temperature Indicators	15	3/31/27 7:00 AM	4/20/27 5:00 PM	419
AEC190814-25	Address Client Comments & Finalize Instrument Data Sheets - T	5	4/21/27 7:00 AM	4/27/27 5:00 PM	419
BH CNN-KPJV-MAST-LIVE,03,06,01,02 ENG - Instrumentation & Control - Instrument Data Sheets - Level Transmitters					
AEC190803-10	Prep Instrument Data Sheets & IDR - Level Transmitters	5	12/17/26 7:00 AM	12/23/26 5:00 PM	446
AEC190803-15	IDR - Instrument Data Sheets - Level Transmitters	5	12/28/26 7:00 AM	1/5/27 5:00 PM	446
AEC190803-20	Address Comments & Issue for Client Review - Instrument Data	5	1/6/27 7:00 AM	1/12/27 5:00 PM	446
AEC190803-25	Client Review - Instrument Data Sheets - Level Transmitters	15	1/13/27 7:00 AM	2/3/27 5:00 PM	471
AEC190803-30	Address Client Comments & Finalize Instrument Data Sheets - I	5	2/4/27 7:00 AM	2/10/27 5:00 PM	471
BH CNN-KPJV-MAST-LIVE,03,06,01,03 ENG - Instrumentation & Control - Instrument Data Sheets - Pressure Indicators					
AEC190804-10	Prep Instrument Data Sheets & IDR - Pressure Indicators	10	1/13/27 7:00 AM	1/27/27 5:00 PM	446
AEC190804-15	IDR - Instrument Data Sheets - Pressure Indicators	5	1/28/27 7:00 AM	2/3/27 5:00 PM	446
AEC190804-20	Address Comments & Issue for Client Review - Instrument Data	5	2/4/27 7:00 AM	2/10/27 5:00 PM	446
AEC190804-25	Client Review - Instrument Data Sheets - Pressure Indicators	15	2/11/27 7:00 AM	3/4/27 5:00 PM	446
AEC190804-30	Address Client Comments & Finalize Instrument Data Sheets - I	10	3/5/27 7:00 AM	3/18/27 5:00 PM	446
BH CNN-KPJV-MAST-LIVE,03,06,01,04 ENG - Instrumentation & Control - Instrument Data Sheets - Flowmeters					
AEC190805-10	Prep Instrument Data Sheets & IDR - Flowmeters	20	12/14/26 7:00 AM	1/14/27 5:00 PM	419
AEC190805-15	IDR - Instrument Data Sheets - Flowmeters	5	1/15/27 7:00 AM	1/22/27 5:00 PM	419
AEC190805-20	Address Comments & Issue for Client Review - Instrument Data	10	1/25/27 7:00 AM	2/5/27 5:00 PM	419
AEC190805-25	Client Review - Instrument Data Sheets - Flowmeters	15	2/8/27 7:00 AM	3/1/27 5:00 PM	419
AEC190805-30	Address Client Comments & Finalize Instrument Data Sheets - I	10	3/2/27 7:00 AM	3/15/27 5:00 PM	419
BH CNN-KPJV-MAST-LIVE,03,06,01,05 ENG - Instrumentation & Control - Instrument Data Sheets - Weather Station					
AEC190806-10	Prep Instrument Data Sheets & IDR - Weather Station	10	11/25/26 7:00 AM	12/9/26 5:00 PM	481
AEC190806-15	IDR - Instrument Data Sheets - Weather Station	5	12/10/26 7:00 AM	12/16/26 5:00 PM	481
AEC190806-20	Address Comments & Issue for Client Review - Instrument Data	5	12/17/26 7:00 AM	12/23/26 5:00 PM	481
AEC190806-25	Client Review - Instrument Data Sheets - Weather Station	15	12/28/26 7:00 AM	1/20/27 5:00 PM	481
AEC190806-30	Address Client Comments & Finalize Instrument Data Sheets - \	5	1/21/27 7:00 AM	1/27/27 5:00 PM	481
BH CNN-KPJV-MAST-LIVE,03,06,01,06 ENG - Instrumentation & Control - Instrument Data Sheets - Gas Detectors					
AEC190807-10	Prep Instrument Data Sheets & IDR - Gas Detectors	10	11/25/26 7:00 AM	12/9/26 5:00 PM	476
AEC190807-15	IDR - Instrument Data Sheets - Gas Detectors	5	12/10/26 7:00 AM	12/16/26 5:00 PM	476
AEC190807-20	Address Comments & Issue for Client Review - Instrument Data	5	12/17/26 7:00 AM	12/23/26 5:00 PM	476
AEC190807-25	Client Review - Instrument Data Sheets - Gas Detectors	15	12/28/26 7:00 AM	1/20/27 5:00 PM	476
AEC190807-30	Address Client Comments & Finalize Instrument Data Sheets - (	10	1/21/27 7:00 AM	2/3/27 5:00 PM	476
BH CNN-KPJV-MAST-LIVE,03,06,01,07 ENG - Instrumentation & Control - Instrument Data Sheets - Pressure Switches					
AEC190808-10	Prep Instrument Data Sheets & IDR - Pressure Switches	5	3/9/27 7:00 AM	3/15/27 5:00 PM	419
AEC190808-15	IDR - Instrument Data Sheets - Pressure Switches	5	3/16/27 7:00 AM	3/22/27 5:00 PM	419
AEC190808-20	Address Comments & Issue for Client Review - Instrument Data	5	3/23/27 7:00 AM	3/30/27 5:00 PM	419
AEC190808-25	Client Review - Instrument Data Sheets - Pressure Switches	15	3/31/27 7:00 AM	4/20/27 5:00 PM	419
AEC190808-30	Address Client Comments & Finalize Instrument Data Sheets - I	5	4/21/27 7:00 AM	4/27/27 5:00 PM	419
BH CNN-KPJV-MAST-LIVE,03,06,01,08 ENG - Instrumentation & Control - Instrument Data Sheets - Temperature Elements					
AEC190809-10	Prep Instrument Data Sheets & IDR - Temperature Elements	5	3/2/27 7:00 AM	3/8/27 5:00 PM	424
AEC190809-15	IDR - Instrument Data Sheets - Temperature Elements	5	3/9/27 7:00 AM	3/15/27 5:00 PM	424
AEC190809-20	Address Comments & Issue for Client Review - Instrument Data	5	3/16/27 7:00 AM	3/22/27 5:00 PM	424



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC190809-25	Client Review - Instrument Data Sheets - Temperature Elements	15	3/23/27 7:00 AM	4/13/27 5:00 PM	424
AEC190809-30	Address Client Comments & Finalize Instrument Data Sheets - T	5	4/14/27 7:00 AM	4/20/27 5:00 PM	424
BH CNN-KPJV-MAST-LIVE,03,06,01,09 ENG - Instrumentation & Control - Instrument Data Sheets - On/Off Valves					
AEC190810-10	Prep Instrument Data Sheets & IDR - On/Off Valves	5	1/13/27 7:00 AM	1/20/27 5:00 PM	462
AEC190810-15	IDR - Instrument Data Sheets - On/Off Valves	3	1/21/27 7:00 AM	1/25/27 5:00 PM	462
AEC190810-20	Address Comments & Issue for Client Review - Instrument Data	2	1/26/27 7:00 AM	1/27/27 5:00 PM	462
AEC190810-25	Client Review - Instrument Data Sheets - On/Off Valves	15	1/28/27 7:00 AM	2/18/27 5:00 PM	462
AEC190810-30	Address Client Comments & Finalize Instrument Data Sheets - (	4	2/19/27 7:00 AM	2/24/27 5:00 PM	462
BH CNN-KPJV-MAST-LIVE,03,06,01,10 ENG - Instrumentation & Control - Instrument Data Sheets - Conductivity Analyzers					
AEC190811-10	Prep Instrument Data Sheets & IDR - Conductivity Analyzers	10	3/5/27 7:00 AM	3/18/27 5:00 PM	416
AEC190811-15	IDR - Instrument Data Sheets - Conductivity Analyzers	5	3/19/27 7:00 AM	3/25/27 5:00 PM	416
AEC190811-20	Address Comments & Issue for Client Review - Instrument Data	5	3/29/27 7:00 AM	4/2/27 5:00 PM	416
AEC190811-25	Client Review - Instrument Data Sheets - Conductivity Analyzers	15	4/5/27 7:00 AM	4/23/27 5:00 PM	416
AEC190811-30	Address Client Comments & Finalize Instrument Data Sheets - (	5	4/26/27 7:00 AM	4/30/27 5:00 PM	416
BH CNN-KPJV-MAST-LIVE,03,06,01,11 ENG - Instrumentation & Control - Instrument Data Sheets - Pressure Reducing Valves					
AEC190812-10	Prep Instrument Data Sheets & IDR - Pressure Reducing Valves	5	1/13/27 7:00 AM	1/20/27 5:00 PM	456
AEC190812-15	IDR - Instrument Data Sheets - Pressure Reducing Valves	5	1/21/27 7:00 AM	1/27/27 5:00 PM	456
AEC190812-20	Address Comments & Issue for Client Review - Instrument Data	5	1/28/27 7:00 AM	2/3/27 5:00 PM	456
AEC190812-25	Client Review - Instrument Data Sheets - Pressure Reducing Va	15	2/4/27 7:00 AM	2/25/27 5:00 PM	456
AEC190812-30	Address Client Comments & Finalize Instrument Data Sheets - I	5	2/26/27 7:00 AM	3/4/27 5:00 PM	456
BH CNN-KPJV-MAST-LIVE,03,06,01,12 ENG - Instrumentation & Control - Instrument Data Sheets - Fuel Gas Emergency Shutoff Valves					
AEC190813-10	Prep Instrument Data Sheets & IDR - Fuel Gas Emergency Shu	10	12/28/26 7:00 AM	1/12/27 5:00 PM	456
AEC190813-15	IDR - Instrument Data Sheets - Fuel Gas Emergency Shutoff Va	5	1/13/27 7:00 AM	1/20/27 5:00 PM	456
AEC190813-20	Address Comments & Issue for Client Review - Instrument Data	5	1/21/27 7:00 AM	1/27/27 5:00 PM	456
AEC190813-25	Client Review - Instrument Data Sheets - Fuel Gas Emergency S	15	1/28/27 7:00 AM	2/18/27 5:00 PM	456
AEC190813-30	Address Client Comments & Finalize Instrument Data Sheets - I	10	2/19/27 7:00 AM	3/4/27 5:00 PM	456
BH CNN-KPJV-MAST-LIVE,03,06,02 ENG - Instrumentation & Control - Control Valves					
AEC190801-05	Prep & Check & IDR Data Sheets - Control Valves	20	12/3/26 7:00 AM	1/5/27 5:00 PM	431
AEC190801-15	IDR - Data Sheets - Control Valves	5	1/6/27 7:00 AM	1/12/27 5:00 PM	431
AEC190801-25	Address Comments & Issue for Client Review - Mech Spec - Co	5	1/13/27 7:00 AM	1/20/27 5:00 PM	431
AEC190801-30	Client Review - Data Sheets - Control Valves	15	1/21/27 7:00 AM	2/10/27 5:00 PM	461
AEC190801-35	Address Client Comments & Finalize Instrument Data Sheets - (	10	2/11/27 7:00 AM	2/25/27 5:00 PM	461
BH CNN-KPJV-MAST-LIVE,03,06,03 ENG - Instrumentation & Control - BOP I/O List (for DCS Hardware Definition)					
AEC190701-05	Prep Prelim. I/O List (for DCS Hardware Definition) & Issue for ID	0	4/27/26 7:00 AM A	5/8/26 5:00 PM A	
AEC190701-10	IDR - Prelim. I/O List (for DCS Hardware Definition)	0	7/1/26 7:00 AM A	7/6/26 5:00 PM A	
AEC190701-15	Address Comments & Issue for Client Review - Prelim. I/O List (f	0	7/6/26 7:00 AM A	7/10/26 5:00 PM A	
AEC190701-20	Client Review - Preliminary - I/O List (for DCS Hardware Definitio	0	7/13/26 7:00 AM A	7/30/26 5:00 PM A	
AEC190701-25	Address Client Comments & Prep Final I/O List (for DCS Hardwa	5	12/9/26 7:00 AM	12/15/26 5:00 PM	442
AEC190701-30	IDR - Final I/O List (for DCS Hardware Definition)	5	12/16/26 7:00 AM	12/22/26 5:00 PM	467
AEC190701-35	Address IDR - Comments & Issue for Client Review Final I/O Lis	5	12/23/26 7:00 AM	1/4/27 5:00 PM	467
AEC190701-40	Client Review - Final I/O List (for DCS Hardware Definition)	15	1/5/27 7:00 AM	1/26/27 5:00 PM	467
AEC190701-45	Address Client Comments & Issue Final - I/O List (for DCS Hard	15	1/27/27 7:00 AM	2/17/27 5:00 PM	467
BH CNN-KPJV-MAST-LIVE,03,06,04 ENG - Instrumentation & Control - Instrument List					
AEC190702-05	Prep Initial Instrument List & Issue for IDR	0	7/7/26 7:00 AM A	8/18/26 5:00 PM A	
AEC190702-10	IDR - Instrument Lists	0	8/18/26 7:00 AM A	8/24/26 5:00 PM A	
AEC190702-15	Address Comments & Issue for Client Review - Instrument List	0	8/31/26 7:00 AM A	9/3/26 5:00 PM A	
AEC190702-20	Client Review - Instrument List	0	9/3/26 7:00 AM A	9/18/26 5:00 PM A	
AEC190702-25	Address Client Comments & Finalize Instrument List	10	10/12/26 7:00 AM	10/23/26 5:00 PM	542
BH CNN-KPJV-MAST-LIVE,03,06,06 ENG - Instrumentation & Control - Control System Description					
BH CNN-KPJV-MAST-LIVE,03,06,06,01 ENG - Instrumentation & Control - Control System Description - Demineralized Water					
AEC191102-05	Prep Control Narrative/Logic Diagrams/HMI Graphics & IDR - De	20	10/12/26 7:00 AM	11/6/26 5:00 PM	412



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC191102-10	IDR - Control Narrative/Logic Diagrams/HMI Graphics - Demin W	5	11/9/26 7:00 AM	11/16/26 5:00 PM	432
AEC191102-15	Address Comments & Issue for Client Review - Control Narrative	10	11/17/26 7:00 AM	12/1/26 5:00 PM	432
AEC191102-20	Client Review - Control Narrative/Logic Diagrams/HMI Graphics -	15	12/2/26 7:00 AM	12/22/26 5:00 PM	432
AEC191102-25	Address Client Comments & Issue Control Narrative/Logic Diagr	10	12/23/26 7:00 AM	1/11/27 5:00 PM	432
BH CNN-KPJV-MAST-LIVE,03,06,06,03 ENG - Instrumentation & Control - Control System Description - Service Water/Potable Water					
AEC191101-05	Prep Control Narrative/Logic Diagrams/HMI Graphics & IDR - Se	20	10/12/26 7:00 AM	11/6/26 5:00 PM	432
AEC191101-10	IDR - Control Narrative/Logic Diagrams/HMI Graphics - Service W	5	11/9/26 7:00 AM	11/16/26 5:00 PM	432
AEC191101-15	Address Comments & Issue for Client Review - Control Narrative	10	11/17/26 7:00 AM	12/1/26 5:00 PM	432
AEC191101-20	Client Review - Control Narrative/Logic Diagrams/HMI Graphics -	15	12/2/26 7:00 AM	12/22/26 5:00 PM	432
AEC191101-25	Address Client Comments & Issue Control Narrative/Logic Diagr	10	12/23/26 7:00 AM	1/11/27 5:00 PM	432
BH CNN-KPJV-MAST-LIVE,03,06,06,02 ENG - Instrumentation & Control - Control System Description - Waste Water					
AEC191106-05	Prep Control Narrative/Logic Diagrams/HMI Graphics & IDR - Wa	20	11/25/26 7:00 AM	12/23/26 5:00 PM	401
AEC191106-10	IDR - Control Narrative/Logic Diagrams/HMI Graphics - Waste W	5	12/28/26 7:00 AM	1/5/27 5:00 PM	401
AEC191106-15	Address Comments & Issue for Client Review - Control Narrative	10	1/6/27 7:00 AM	1/20/27 5:00 PM	401
AEC191106-20	Client Review - Control Narrative/Logic Diagrams/HMI Graphics -	15	1/21/27 7:00 AM	2/10/27 5:00 PM	401
AEC191106-25	Address Client Comments & Issue Control Narrative/Logic Diagr	10	2/11/27 7:00 AM	2/25/27 5:00 PM	401
BH CNN-KPJV-MAST-LIVE,03,06,06,04 ENG - Instrumentation & Control - Control System Description - Fuel Oil					
AEC191104-05	Prep Control Narrative/Logic Diagrams/HMI Graphics & IDR - Fu	20	10/12/26 7:00 AM	11/6/26 5:00 PM	432
AEC191104-10	IDR - Control Narrative/Logic Diagrams/HMI Graphics - Fuel Oil s	5	11/9/26 7:00 AM	11/16/26 5:00 PM	432
AEC191104-15	Address Comments & Issue for Client Review - Control Narrative	10	11/17/26 7:00 AM	12/1/26 5:00 PM	432
AEC191104-20	Client Review - Control Narrative/Logic Diagrams/HMI Graphics -	15	12/2/26 7:00 AM	12/22/26 5:00 PM	432
AEC191104-25	Address Client Comments & Issue Control Narrative/Logic Diagr	10	12/23/26 7:00 AM	1/11/27 5:00 PM	432
BH CNN-KPJV-MAST-LIVE,03,06,06,05 ENG - Instrumentation & Control - Control System Description - BOP Electrical System					
AEC191107-05	Prep Control Narrative/Logic Diagrams/HMI Graphics & IDR - BC	20	12/9/26 7:00 AM	1/11/27 5:00 PM	392
AEC191107-10	IDR - Control Narrative/Logic Diagrams/HMI Graphics - BOP Ele	5	1/12/27 7:00 AM	1/19/27 5:00 PM	392
AEC191107-15	Address Comments & Issue for Client Review - Control Narrative	10	1/20/27 7:00 AM	2/2/27 5:00 PM	392
AEC191107-20	Client Review - Control Narrative/Logic Diagrams/HMI Graphics -	15	2/3/27 7:00 AM	2/24/27 5:00 PM	392
AEC191107-25	Address Client Comments & Issue Control Narrative/Logic Diagr	10	2/25/27 7:00 AM	3/10/27 5:00 PM	392
BH CNN-KPJV-MAST-LIVE,03,06,06,06 ENG - Instrumentation & Control - Control System Description - Compressed Air System					
AEC191105-05	Prep Control Narrative/Logic Diagrams/HMI Graphics & IDR - Co	20	10/13/26 7:00 AM	11/9/26 5:00 PM	431
AEC191105-10	IDR - Control Narrative/Logic Diagrams/HMI Graphics - Compres	5	11/10/26 7:00 AM	11/17/26 5:00 PM	431
AEC191105-15	Address Comments & Issue for Client Review - Control Narrative	10	11/18/26 7:00 AM	12/2/26 5:00 PM	431
AEC191105-20	Client Review - Control Narrative/Logic Diagrams/HMI Graphics -	15	12/3/26 7:00 AM	12/23/26 5:00 PM	431
AEC191105-25	Address Client Comments & Issue Control Narrative/Logic Diagr	10	12/28/26 7:00 AM	1/12/27 5:00 PM	431
BH CNN-KPJV-MAST-LIVE,03,06,06,07 ENG - Instrumentation & Control - Control System Description - Fuel Gas					
AEC191103-05	Prep Control Narrative/Logic Diagrams/HMI Graphics & IDR - Fu	20	10/29/26 7:00 AM	11/27/26 5:00 PM	419
AEC191103-10	IDR - Control Narrative/Logic Diagrams/HMI Graphics - Fuel Gas	5	11/30/26 7:00 AM	12/4/26 5:00 PM	419
AEC191103-15	Address Comments & Issue for Client Review - Control Narrative	10	12/7/26 7:00 AM	12/18/26 5:00 PM	419
AEC191103-20	Client Review - Control Narrative/Logic Diagrams/HMI Graphics -	15	12/21/26 7:00 AM	1/14/27 5:00 PM	419
AEC191103-25	Address Client Comments & Issue Control Narrative/Logic Diagr	10	1/15/27 7:00 AM	1/29/27 5:00 PM	419
BH CNN-KPJV-MAST-LIVE,03,06,06,08 ENG - Instrumentation & Control - Control System Description - Plant Interfaces					
AEC191108-05	Prep Control Narrative/Logic Diagrams/HMI Graphics & IDR - Pla	20	11/9/26 7:00 AM	12/8/26 5:00 PM	412
AEC191108-10	IDR - Control Narrative/Logic Diagrams/HMI Graphics - Plant Inte	5	12/9/26 7:00 AM	12/15/26 5:00 PM	412
AEC191108-15	Address Comments & Issue for Client Review - Control Narrative	10	12/16/26 7:00 AM	1/4/27 5:00 PM	412
AEC191108-20	Client Review - Control Narrative/Logic Diagrams/HMI Graphics -	15	1/5/27 7:00 AM	1/26/27 5:00 PM	412
AEC191108-25	Address Client Comments & Issue Control Narrative/Logic Diagr	10	1/27/27 7:00 AM	2/9/27 5:00 PM	412
BH CNN-KPJV-MAST-LIVE,03,06,09 ENG - Instrumentation & Control - I/O Datalink					
AEC191109-35	Receive - I/O Datalink Vendor Information	10	12/16/26 7:00 AM	1/4/27 5:00 PM	442
AEC191109-05	Prep & Check & IDR - I/O Datalink	20	1/21/27 7:00 AM	2/18/27 5:00 PM	431
AEC191109-10	Complete IDR - I/O Datalink	5	2/19/27 7:00 AM	2/25/27 5:00 PM	431
AEC191109-15	Address Comments & Issue for Client Review - I & C - I/O Datali	5	2/26/27 7:00 AM	3/4/27 5:00 PM	431



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC191109-20	Client Review - I&C Drawings - I/O Datalink	15	3/5/27 7:00 AM	3/25/27 5:00 PM	431
AEC191109-25	Address Client Comments & Issue - AFC - I/O Datalink	10	3/29/27 7:00 AM	4/9/27 5:00 PM	431
BH CNN-KPJV-MAST-LIVE,03,06,05 ENG - Instrumentation & Control - Network Drawings					
AEC191113-05	Prep Network Drawings for IDR - Network Drawings	20	3/11/27 7:00 AM	4/8/27 5:00 PM	392
AEC191113-10	IDR - Network Drawings	5	4/9/27 7:00 AM	4/15/27 5:00 PM	392
AEC191113-15	Address Comments & Issue for Client Review - Network Drawing	10	4/16/27 7:00 AM	4/29/27 5:00 PM	392
AEC191113-20	Client Review - Network Drawings	15	4/30/27 7:00 AM	5/20/27 5:00 PM	392
AEC191113-25	Address Client Comments & Issue Final - Network Drawings	10	5/21/27 7:00 AM	6/4/27 5:00 PM	392
BH CNN-KPJV-MAST-LIVE,03,06,07 ENG - Instrumentation & Control - Instrument Location Drawings					
AEC191114-05	Prep Network Drawings for IDR - Instrument Location Drawings	20	6/11/27 7:00 AM	7/12/27 5:00 PM	328
AEC191114-10	IDR - Instrument Location Drawings	5	7/13/27 7:00 AM	7/19/27 5:00 PM	328
AEC191114-15	Address Comments & Issue for Client Review - Instrument Loca	10	7/20/27 7:00 AM	8/2/27 5:00 PM	328
AEC191114-20	Client Review - Instrument Location Drawings	15	8/3/27 7:00 AM	8/23/27 5:00 PM	328
AEC191114-25	Address Client Comments & Issue Final - Instrument Location D	10	8/24/27 7:00 AM	9/7/27 5:00 PM	328
BH CNN-KPJV-MAST-LIVE,03,07 ENG - Architectural					
BH CNN-KPJV-MAST-LIVE,03,07,07 ENG - Architectural Specifications					
BH CNN-KPJV-MAST-LIVE,03,07,07,05 ENG - Architectural Specifications - Buildings					
BH CNN-KPJV-MAST-LIVE,03,07,07,05,08 ENG - Architectural Specifications - Buildings - PEMB Specification					
AEC180803-0	Prep & Check & IDR (Internal Design Review) - Architectural Spe	0	3/9/26 7:00 AM A	4/15/26 5:00 PM A	
AEC180803-1	IDR - Architectural Specs. - PEMB Buildings	0	4/15/26 7:00 AM A	4/21/26 5:00 PM A	
AEC180803-1	Address IDR - Comments & Issue for Client Review Architectural	0	4/22/26 7:00 AM A	4/27/26 5:00 PM A	
AEC180803-2	Client Review - Architectural Specs. - PEMB Buildings	0	4/27/26 7:00 AM A	5/12/26 5:00 PM A	
AEC180803-2	Address Client Comments & IFC - Architectural Spec. - PEMB B	0	5/13/26 7:00 AM A	5/29/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,07,07,05,01 ENG - Architectural Specifications - Buildings - Life Safety Code Analysis Specification					
AEC180802-0	Prep & Check & IDR - Architectural Specs. - Life Safety Code Ar	0	2/23/26 7:00 AM A	3/16/26 5:00 PM A	
AEC180802-1	IDR - Architectural Specs. - Life Safety Code Analysis Spec.	0	3/17/26 7:00 AM A	3/31/26 5:00 PM A	
AEC180802-1	Address IDR - Comments & Issue for Client Review Architectural	0	4/1/26 7:00 AM A	4/9/26 5:00 PM A	
AEC180802-2	Client Review - Architectural Specs. - Life Safety Code Analysis	0	4/9/26 7:00 AM A	4/20/26 5:00 PM A	
AEC180802-2	Address Client Comments & IFC - Architectural Spec. - Life Safe	0	4/21/26 7:00 AM A	4/27/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,07,01 ENG - Architectural - Drawings					
BH CNN-KPJV-MAST-LIVE,03,07,01,01 ENG - Architectural - Drawings - Fuel Oil Pump Enclosure					
AEC181102-05	Prep & Check & IDR - Architectural Plan/Elev/Sections/Details - I	0	4/20/26 7:00 AM A	4/30/26 5:00 PM A	
AEC181102-10	IDR - Architectural Plan/Elev/Sections/Details - Fuel Oil Pump Er	0	5/1/26 7:00 AM A	5/8/26 5:00 PM A	
AEC181102-15	Address Comments & Issue for Client Review - Architectural Plar	0	5/8/26 7:00 AM A	5/18/26 5:00 PM A	
AEC181102-20	Client Review - Architectural Plan/Elev/Sections/Details - Fuel Oil	0	5/19/26 7:00 AM A	7/2/26 5:00 PM A	
AEC181102-25	Address Client Comments & IFU - Architectural Plan/Elev/Sectio	0	7/2/26 7:00 AM A	7/23/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,07,01,02 ENG - Architectural - Drawings - Plant Services Enclosure					
AEC181103-05	Prep & Check & IDR - Architectural Plan/Elev/Sections/Details - I	0	3/30/26 7:00 AM A	4/15/26 5:00 PM A	
AEC181103-10	IDR - Architectural Specs. - Plant Services Enclosure	0	4/15/26 7:00 AM A	4/21/26 5:00 PM A	
AEC181103-15	Address IDR - Comments & Issue for Client Review Architectural	0	4/21/26 7:00 AM A	4/24/26 5:00 PM A	
AEC181103-20	Client Review - Architectural Specs. - Plant Services Enclosure	0	4/24/26 7:00 AM A	5/12/26 5:00 PM A	
AEC181103-25	Address Client Comments & IFU - Architectural Plan/Elev/Sectio	0	5/13/26 7:00 AM A	7/2/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,03,07,01,03 ENG - Architectural - Drawings - Fuel Gas Compressor Enclosure					
AEC181104-05	Prep & Check & IDR - Architectural Plan/Elev/Sections/Details - I	0	6/4/26 7:00 AM A	6/15/26 5:00 PM A	
AEC181104-10	IDR - Architectural Plan/Elev/Sections/Details - Fuel Gas Compre	0	6/15/26 7:00 AM A	6/19/26 5:00 PM A	
AEC181104-15	Address Comments & Issue for Client Review - Architectural Plar	0	6/22/26 7:00 AM A	9/11/26 5:00 PM A	
AEC181104-20	Client Review - Architectural Plan/Elev/Sections/Details - Fuel Ga	5	9/11/26 7:00 AM A	10/16/26 5:00 PM	2
AEC181104-25	Address Client Comments & Issue IFD - (Permit) Architectural Pl	5	10/19/26 7:00 AM	10/23/26 5:00 PM	2
AEC181104-35	Address Client Comments & IFC - Architectural Plan/Elev/Sectio	5	10/26/26 7:00 AM	10/30/26 5:00 PM	2
AEC181104-45	Address Client Comments & Issue IFC Architectural Plan/Elev/S	5	10/26/26 7:00 AM	10/30/26 5:00 PM	121
BH CNN-KPJV-MAST-LIVE,03,07,01,04 ENG - Architectural - Drawings - Admin/Warehouse					




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
AEC181101-05	Prep & Check & IDR - Architectural Plan/Elev/Sections/Details - /	0	3/9/26 7:00 AM A	3/27/26 5:00 PM A	
AEC181101-10	IDR - Architectural Plan/Elev/Sections/Details - Admin/Warehous	0	3/30/26 7:00 AM A	4/21/26 5:00 PM A	
AEC181101-15	Address Comments & Issue for Client Review - Architectural Plar	0	4/22/26 7:00 AM A	4/27/26 5:00 PM A	
AEC181101-20	Client Review - Architectural Plan/Elev/Sections/Details - Admin/	0	4/27/26 7:00 AM A	6/1/26 5:00 PM A	
AEC181101-25	Address Client Comments & Issue IFD - (Permit) Architectural Pl	0	6/5/26 7:00 AM A	7/23/26 5:00 PM A	
AEC181101-35	Address Client Comments & IFC - Architectural Plan/Elev/Sectio	1	9/10/26 7:00 AM A	10/12/26 5:00 PM	3
BH CNN-KPJV-MAST-LIVE,20 PROCUREMENT					
BH CNN-KPJV-MAST-LIVE,20,00 PRO - Milestones					
KPA.PRO.MI.100	Start Procurement	0	4/30/26 7:00 AM A		
BH CNN-KPJV-MAST-LIVE,20,01 PRO - OFE (Owner-Furnished Equipment)					
BH CNN-KPJV-MAST-LIVE,20,01,GE PRO - OFE / GE Provided					
BH CNN-KPJV-MAST-LIVE,20,01,GE,01 PRO - OFE / GE Provided - Generator					
BH CNN-KPJV-MAST-LIVE,20,01,GE,01,01 PRO - OFE / GE Provided - Generator - Train 1					
GE MLI B7G0	Received - Gen Pkg - Foundation Embedments (GE MLI B7G0	0		6/1/27 7:00 AM*	65
GE MLI B7G1	Received - Gen Pkg - Foundation Hardware Arrangement (GE M	0		6/1/27 7:00 AM*	65
GE MLI W1CI	Received - Gen Pkg - Gen Control Hardware (GE MLI W1CH) -	0		6/2/27 5:00 PM*	63
GE MLI B7J0-	Received - Gen Pkg - Spares List (GE MLI B7J0) - Train 1	0		7/29/27 5:00 PM*	23
GE MLI 1207/	Received - Gen Pkg - Batteries & Accessories (GE MLI 1207A) -	0		8/2/27 7:00 AM*	22
GE MLI A059-	Received - Gen Pkg - PEECC (Package Electrical & Electronic C	0		8/2/27 7:00 AM*	22
GE MLI A111-	Received - Gen Pkg - Generator Terminal Enclosure (GE MLI A1	0		8/2/27 7:00 AM*	22
GE MLI A140I	Received - Gen Pkg - AC Reactor (GE MLI A140B) - GA027 - Tr	0		8/2/27 7:00 AM*	22
GE MLI A141-	Received - Gen Pkg - CT Isolation Transformer (GE MLI A141) -	0		8/2/27 7:00 AM*	22
GE MLI A150-	Received - Gen Pkg - CT Excitation Transformer (GE MLI A150)	0		8/2/27 7:00 AM*	22
GE MLI A192-	Received - Gen Pkg - LEC (Load Commutative Inverter & Excita	0		8/2/27 7:00 AM*	64
GE MLI AGHM	Received - Gen Pkg - Generator Health Monitor Enclosure (GE I	0		8/2/27 7:00 AM*	22
GE MLI B4J1-	Received - Gen Pkg - Fitup Piping (Fld Instld) (GE MLI B4J1) - T	0		8/2/27 7:00 AM*	22
GE MLI B6HC	Received - Gen Pkg - Shaft Voltage Monitor Assy (GE MLI B6H	0		8/2/27 7:00 AM*	22
GE MLI B8H0	Received - Gen Pkg - Rotor Removalinsertion (GE MLI B8H0) -	0		8/2/27 7:00 AM*	22
GE MLI B8H7	Received - Gen Pkg - Rolling Support For Generator Rotor Rem	0		8/2/27 7:00 AM*	22
GE MLI B9F1-	Received - Gen Pkg - Turning Gear (GE MLI B9F1) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI B9JJ-	Received - Gen Pkg - Piping Hardware (GE MLI B9JJ) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI B9X0	Received - Gen Pkg - GT Enclosure Interface (GE MLI B9X0) -	0		8/2/27 7:00 AM*	22
GE MLI CABA	Received - Gen Pkg - Generator Cab Assembly (GE MLI CABA)	0		8/2/27 7:00 AM*	22
GE MLI D2B1	Received - Gen Pkg - Junction Box Install (GE MLI D2B1) - Trair	0		8/2/27 7:00 AM*	22
GE MLI D4CS	Received - Gen Pkg - Collector Fans (GE MLI D4CS) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI G125	Received - Gen Pkg - Gen PP Lube Oil Flush Field Hardware (G	0		8/2/27 7:00 AM*	22
GE MLI G125	Received - Gen Pkg - Gen PP Lube Oil Flush Field Piping (GE M	0		8/2/27 7:00 AM*	22
GE MLI G125	Received - Gen Pkg - Gen PP Lube Oil Flush Field Tubing (GE I	0		8/2/27 7:00 AM*	22
GE MLI G125	Received - Gen Pkg - Gen PP Lube Oil Flush Field Valves (GE M	0		8/2/27 7:00 AM*	22
GE MLI G252	Received - Gen Pkg - Consumables, Gen PP Lube Oil Flush Fie	0		8/2/27 7:00 AM*	22
GE MLI G2K0	Received - Gen Pkg - H2 Gas Manifold (Hdwr) (GE MLI G2K0) -	0		8/2/27 7:00 AM*	22
GE MLI G2M(	Received - Gen Pkg - Hydrogen Gas Dryer (GE MLI G2M0) - GA	0		8/2/27 7:00 AM*	22
GE MLI G2N0	Received - Gen Pkg - Carbon Dioxide Bottle Manifold (GE MLI (	0		8/2/27 7:00 AM*	22
GE MLI G3E0	Received - Gen Pkg - Hygrogen Flow Totalizer (GE MLI G3E0) -	0		8/2/27 7:00 AM*	22
GE MLI G4JS	Received - Gen Pkg - Field Installed Piping (GE MLI G4JS) - Tra	0		8/2/27 7:00 AM*	22
GE MLI G4RV	Received - Gen Pkg - Pressure Relief Valves (GE MLI G4RV) - T	0		8/2/27 7:00 AM*	22
GE MLI H45-T	Received - Gen Pkg - GT Generator (GE MLI H45) - Train 1	0		8/31/27 5:00 PM*	0
BH CNN-KPJV-MAST-LIVE,20,01,GE,01,02 PRO - OFE / GE Provided - Generator - Train 2					
GE MLI B7G0	Received - Gen Pkg - Foundation Embedments (GE MLI B7G0	0		6/30/27 5:00 PM*	64
GE MLI B7G1	Received - Gen Pkg - Foundation Hardware Arrangement (GE M	0		6/30/27 5:00 PM*	64

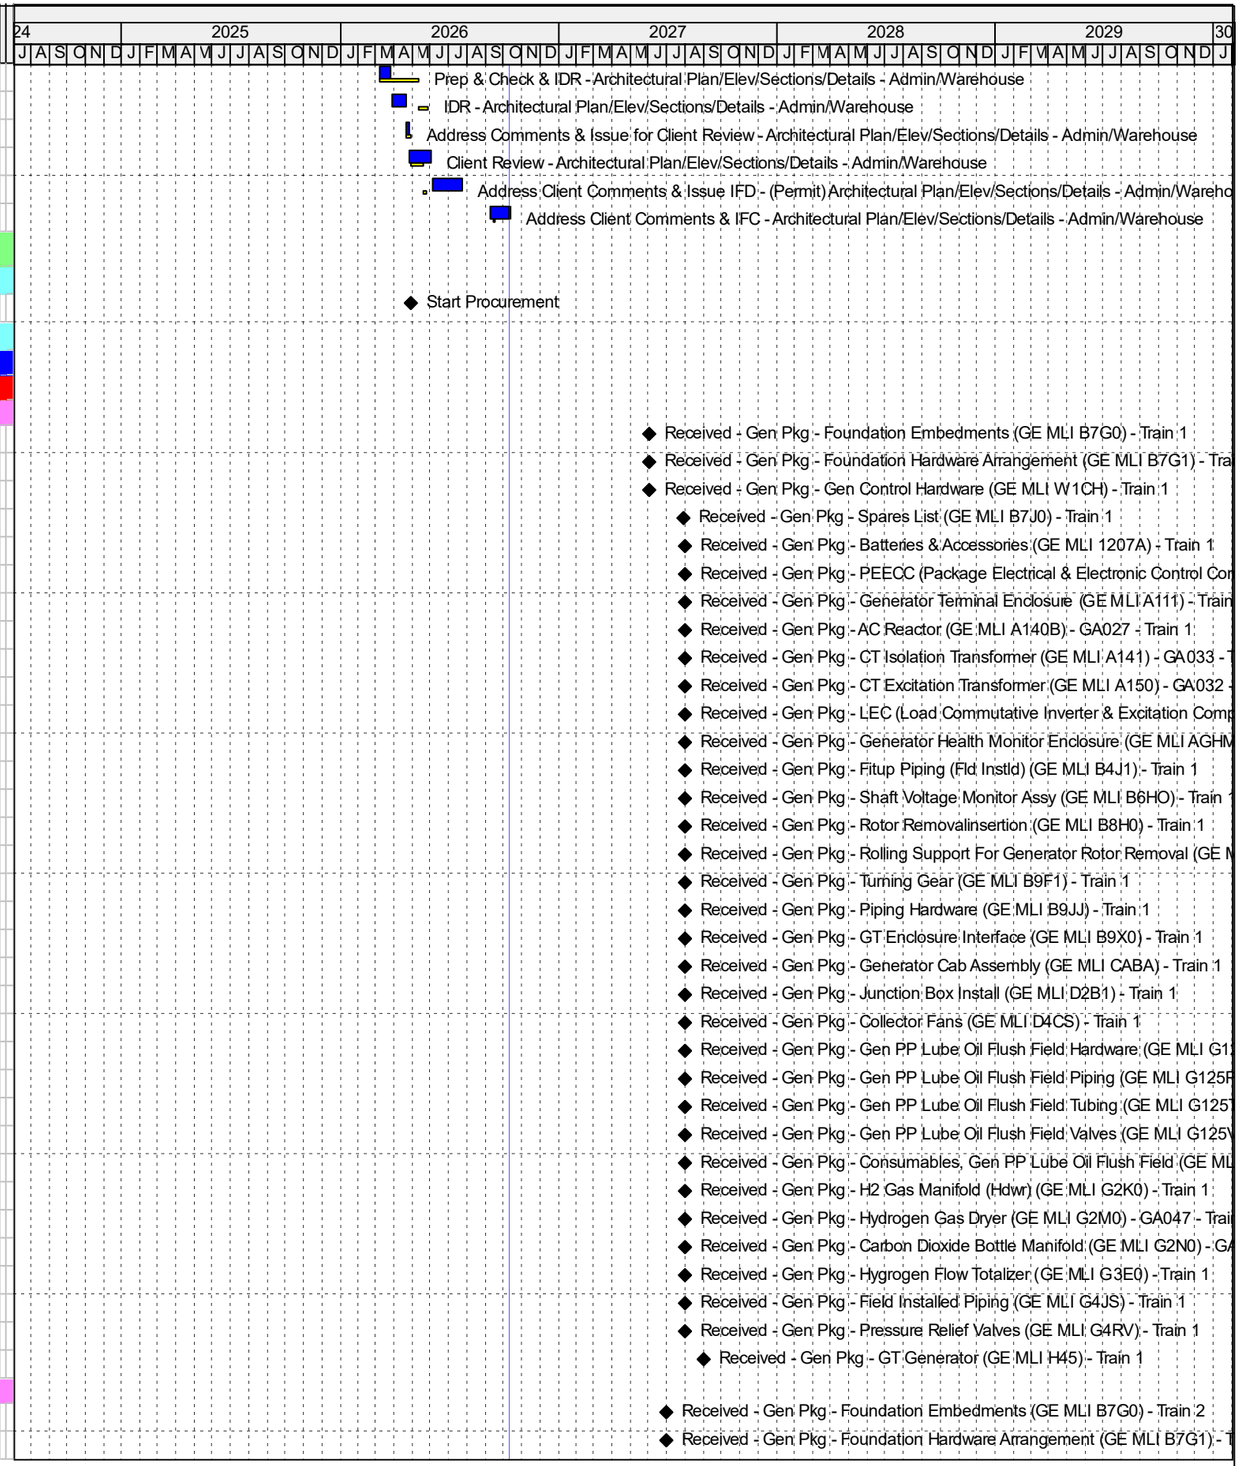

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI W1CI	Received - Gen Pkg - Gen Control Hardware (GE MLI W1CH) -	0		7/2/27 5:00 PM*	62
GE MLI B7J0-	Received - Gen Pkg - Spares List (GE MLI B7J0) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI B9F1·	Received - Gen Pkg - Turning Gear (GE MLI B9F1) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI B9JJ-	Received - Gen Pkg - Piping Hardware (GE MLI B9JJ) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI B9X0	Received - Gen Pkg - GT Enclosure Interface (GE MLI B9X0) -	0		8/31/27 5:00 PM*	21
GE MLI CABA	Received - Gen Pkg - Generator Cab Assembly (GE MLI CABA)	0		8/31/27 5:00 PM*	21
GE MLI D2B1	Received - Gen Pkg - Junction Box Install (GE MLI D2B1) - Trair	0		8/31/27 5:00 PM*	21
GE MLI D4CS	Received - Gen Pkg - Collector Fans (GE MLI D4CS) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI G252	Received - Gen Pkg - Consumables, Gen PP Lube Oil Flush Fie	0		8/31/27 5:00 PM*	21
GE MLI G2K0	Received - Gen Pkg - H2 Gas Manifold (Hdwr) (GE MLI G2K0) -	0		8/31/27 5:00 PM*	21
GE MLI G3E0	Received - Gen Pkg - Hygrogen Flow Totalizer (GE MLI G3E0) -	0		8/31/27 5:00 PM*	21
GE MLI G4JS	Received - Gen Pkg - Field Installed Piping (GE MLI G4JS) - Tra	0		8/31/27 5:00 PM*	21
GE MLI G4RV	Received - Gen Pkg - Pressure Relief Valves (GE MLI G4RV) - T	0		8/31/27 5:00 PM*	21
GE MLI 1207/	Received - Gen Pkg - Batteries & Accessories (GE MLI 1207A) -	0		9/1/27 5:00 PM*	20
GE MLI A059-	Received - Gen Pkg - PEECC (Package Electrical & Electronic C	0		9/1/27 5:00 PM*	20
GE MLI A111-	Received - Gen Pkg - Generator Terminal Enclosure (GE MLI A1	0		9/1/27 5:00 PM*	20
GE MLI A140I	Received - Gen Pkg - AC Reactor (GE MLI A140B) - GA027 - Tr	0		9/1/27 5:00 PM*	20
GE MLI A141-	Received - Gen Pkg - CT Isolation Transformer (GE MLI A141) -	0		9/1/27 5:00 PM*	20
GE MLI A150-	Received - Gen Pkg - CT Excitation Transformer (GE MLI A150)	0		9/1/27 5:00 PM*	20
GE MLI A192-	Received - Gen Pkg - LEC (Load Commutative Inverter & Excita	0		9/1/27 5:00 PM*	20
GE MLI AGHM	Received - Gen Pkg - Generator Health Monitor Enclosure (GE I	0		9/1/27 5:00 PM*	20
GE MLI B4J1-	Received - Gen Pkg - Fitup Piping (Fld Instld) (GE MLI B4J1) - T	0		9/1/27 5:00 PM*	20
GE MLI B6HC	Received - Gen Pkg - Shaft Voltage Monitor Assy (GE MLI B6H	0		9/1/27 5:00 PM*	20
GE MLI G2M(	Received - Gen Pkg - Hydrogen Gas Dryer (GE MLI G2M0) - GA	0		9/1/27 5:00 PM*	20
GE MLI G2N0	Received - Gen Pkg - Carbon Dioxide Bottle Manifold (GE MLI (	0		9/1/27 5:00 PM*	20
GE MLI H45-T	Received - Gen Pkg - GT Generator (GE MLI H45) - Train 2	0		9/30/27 5:00 PM*	0
BH CNN-KPJV-MAST-LIVE,20,01,GE,01,03 PRO - OFE / GE Provided - Generator - Train 3					
GE MLI B7G0	Received - Gen Pkg - Foundation Embedments (GE MLI B7G0)	0		8/2/27 7:00 AM*	64
GE MLI B7G1	Received - Gen Pkg - Foundation Hardware Arrangement (GE M	0		8/2/27 7:00 AM*	64
GE MLI W1CI	Received - Gen Pkg - Gen Control Hardware (GE MLI W1CH) -	0		8/2/27 5:00 PM*	63
GE MLI 1207/	Received - Gen Pkg - Batteries & Accessories (GE MLI 1207A) -	0		10/1/27 5:00 PM*	20
GE MLI A059-	Received - Gen Pkg - PEECC (Package Electrical & Electronic C	0		10/1/27 5:00 PM*	20
GE MLI A111-	Received - Gen Pkg - Generator Terminal Enclosure (GE MLI A1	0		10/1/27 5:00 PM*	20
GE MLI A140I	Received - Gen Pkg - AC Reactor (GE MLI A140B) - GA027 - Tr	0		10/1/27 5:00 PM*	20
GE MLI A141-	Received - Gen Pkg - CT Isolation Transformer (GE MLI A141) -	0		10/1/27 5:00 PM*	20
GE MLI A150-	Received - Gen Pkg - CT Excitation Transformer (GE MLI A150)	0		10/1/27 5:00 PM*	20
GE MLI A192-	Received - Gen Pkg - LEC (Load Commutative Inverter & Excita	0		10/1/27 5:00 PM*	20
GE MLI AGHM	Received - Gen Pkg - Generator Health Monitor Enclosure (GE I	0		10/1/27 5:00 PM*	20
GE MLI B4J1-	Received - Gen Pkg - Fitup Piping (Fld Instld) (GE MLI B4J1) - T	0		10/1/27 5:00 PM*	20
GE MLI B6HC	Received - Gen Pkg - Shaft Voltage Monitor Assy (GE MLI B6H	0		10/1/27 5:00 PM*	20
GE MLI B7J0-	Received - Gen Pkg - Spares List (GE MLI B7J0) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI B9F1·	Received - Gen Pkg - Turning Gear (GE MLI B9F1) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI B9JJ-	Received - Gen Pkg - Piping Hardware (GE MLI B9JJ) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI B9X0	Received - Gen Pkg - GT Enclosure Interface (GE MLI B9X0) -	0		10/1/27 5:00 PM*	20
GE MLI CABA	Received - Gen Pkg - Generator Cab Assembly (GE MLI CABA)	0		10/1/27 5:00 PM*	20
GE MLI D2B1	Received - Gen Pkg - Junction Box Install (GE MLI D2B1) - Trair	0		10/1/27 5:00 PM*	20
GE MLI D4CS	Received - Gen Pkg - Collector Fans (GE MLI D4CS) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI G125	Received - Gen Pkg - Gen PP Lube Oil Flush Field Hardware (G	0		10/1/27 5:00 PM*	20
GE MLI G125	Received - Gen Pkg - Gen PP Lube Oil Flush Field Piping (GE M	0		10/1/27 5:00 PM*	20
GE MLI G125	Received - Gen Pkg - Gen PP Lube Oil Flush Field Tubing (GE I	0		10/1/27 5:00 PM*	20



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI G125	Received - Gen Pkg - Gen PP Lube Oil Flush Field Valves (GE M	0		10/1/27 5:00 PM*	20
GE MLI G252	Received - Gen Pkg - Consumables, Gen PP Lube Oil Flush Fie	0		10/1/27 5:00 PM*	20
GE MLI G2K0	Received - Gen Pkg - H2 Gas Manifold (Hdwr) (GE MLI G2K0) -	0		10/1/27 5:00 PM*	20
GE MLI G2M(	Received - Gen Pkg - Hydrogen Gas Dryer (GE MLI G2M0) - GA	0		10/1/27 5:00 PM*	20
GE MLI G2N0	Received - Gen Pkg - Carbon Dioxide Bottle Manifold (GE MLI (	0		10/1/27 5:00 PM*	20
GE MLI G3E0	Received - Gen Pkg - Hygrogen Flow Totalizer (GE MLI G3E0) -	0		10/1/27 5:00 PM*	20
GE MLI G4JS	Received - Gen Pkg - Field Installed Piping (GE MLI G4JS) - Tra	0		10/1/27 5:00 PM*	20
GE MLI G4RV	Received - Gen Pkg - Pressure Relief Valves (GE MLI G4RV) - T	0		10/1/27 5:00 PM*	20
GE MLI H45-T	Received - Gen Pkg - GT Generator (GE MLI H45) - Train 3	0		11/1/27 7:00 AM*	0
BH CNN-KPJV-MAST-LIVE,20,01,GE,01,04 PRO - OFE / GE Provided - Generator - Train 4					
GE MLI B7G0	Received - Gen Pkg - Foundation Embedments (GE MLI B7G0)	0		8/31/27 5:00 PM*	63
GE MLI B7G1	Received - Gen Pkg - Foundation Hardware Arrangement (GE M	0		8/31/27 5:00 PM*	63
GE MLI W1CI	Received - Gen Pkg - Gen Control Hardware (GE MLI W1CH) -	0		9/1/27 5:00 PM*	62
GE MLI B7J0-	Received - Gen Pkg - Spares List (GE MLI B7J0) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI B9F1·	Received - Gen Pkg - Turning Gear (GE MLI B9F1) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI B9JJ-	Received - Gen Pkg - Piping Hardware (GE MLI B9JJ) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI B9X0	Received - Gen Pkg - GT Enclosure Interface (GE MLI B9X0) -	0		11/1/27 7:00 AM*	21
GE MLI CABA	Received - Gen Pkg - Generator Cab Assembly (GE MLI CABA)	0		11/1/27 7:00 AM*	21
GE MLI D2B1	Received - Gen Pkg - Junction Box Install (GE MLI D2B1) - Trair	0		11/1/27 7:00 AM*	21
GE MLI D4CS	Received - Gen Pkg - Collector Fans (GE MLI D4CS) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI G125	Received - Gen Pkg - Gen PP Lube Oil Flush Field Hardware (G	0		11/1/27 7:00 AM*	21
GE MLI G252	Received - Gen Pkg - Consumables, Gen PP Lube Oil Flush Fie	0		11/1/27 7:00 AM*	21
GE MLI G2K0	Received - Gen Pkg - H2 Gas Manifold (Hdwr) (GE MLI G2K0) -	0		11/1/27 7:00 AM*	21
GE MLI G3E0	Received - Gen Pkg - Hygrogen Flow Totalizer (GE MLI G3E0) -	0		11/1/27 7:00 AM*	21
GE MLI G4JS	Received - Gen Pkg - Field Installed Piping (GE MLI G4JS) - Tra	0		11/1/27 7:00 AM*	21
GE MLI G4RV	Received - Gen Pkg - Pressure Relief Valves (GE MLI G4RV) - T	0		11/1/27 7:00 AM*	21
GE MLI 1207	Received - Gen Pkg - Batteries & Accessories (GE MLI 1207A) -	0		11/1/27 5:00 PM*	20
GE MLI A059-	Received - Gen Pkg - PEECC (Package Electrical & Electronic C	0		11/1/27 5:00 PM*	20
GE MLI A111-	Received - Gen Pkg - Generator Terminal Enclosure (GE MLI A1	0		11/1/27 5:00 PM*	20
GE MLI A140I	Received - Gen Pkg - AC Reactor (GE MLI A140B) - GA027 - Tr	0		11/1/27 5:00 PM*	20
GE MLI A141-	Received - Gen Pkg - CT Isolation Transformer (GE MLI A141) -	0		11/1/27 5:00 PM*	20
GE MLI A150-	Received - Gen Pkg - CT Excitation Transformer (GE MLI A150)	0		11/1/27 5:00 PM*	20
GE MLI A192-	Received - Gen Pkg - LEC (Load Commutative Inverter & Excita	0		11/1/27 5:00 PM*	20
GE MLI AGHM	Received - Gen Pkg - Generator Health Monitor Enclosure (GE I	0		11/1/27 5:00 PM*	20
GE MLI B4J1-	Received - Gen Pkg - Fitup Piping (Fld Instld) (GE MLI B4J1) - T	0		11/1/27 5:00 PM*	20
GE MLI B6HC	Received - Gen Pkg - Shaft Voltage Monitor Assy (GE MLI B6H	0		11/1/27 5:00 PM*	20
GE MLI G2M(	Received - Gen Pkg - Hydrogen Gas Dryer (GE MLI G2M0) - GA	0		11/1/27 5:00 PM*	20
GE MLI G2N0	Received - Gen Pkg - Carbon Dioxide Bottle Manifold (GE MLI (	0		11/1/27 5:00 PM*	20
GE MLI H45-T	Received - Gen Pkg - GT Generator (GE MLI H45) - Train 4	0		11/30/27 5:00 PM*	0
BH CNN-KPJV-MAST-LIVE,20,01,GE,02 PRO - OFE / GE Provided - Gas Turbine					
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,01 PRO - OFE / GE Provided - Gas Turbine - Train 1					
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,01,01 PRO - OFE / GE Provided - Gas Turbine - Train 1 - Equip					
GE MLI A13(	Received - GT Pkg - APU (Air Processing Unit) (GE MLI A130) -	0		7/12/27 5:00 PM*	36
GE MLI 063	Received - GT Pkg - Fuel Gas Coriolis Flow Meter (GE MLI 063	0		8/2/27 7:00 AM*	22
GE MLI 099	Received - GT Pkg - Liquid Fuel Module (Pump) (GE MLI 0992)	0		8/2/27 7:00 AM*	22
GE MLI 161	Received - GT Pkg - Load Compartment Enclosure Assembly (G	0		8/2/27 7:00 AM*	22
GE MLI 163	Received - GT Pkg - Enclosure, Gas Turbine (GE MLI 1634) - Tr	0		8/2/27 7:00 AM*	22
GE MLI 164	Received - GT Pkg - Overhead Travel Crane (GE MLI 1648) - Tra	0		8/2/27 7:00 AM*	22
GE MLI A04(	Received - GT Pkg - Inlet Filter House (GE MLI A040) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI A07	Received - GT Pkg - CWM (Cooling Water Modules Unit) (GE M	0		8/2/27 7:00 AM*	22




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI A132	Received - GT Pkg - Cooling Fan Module (GE MLI A132) - Train	0		8/2/27 7:00 AM*	22
GE MLI A160	Received - GT Pkg - Oil & Gas Accessory Module (GE MLI A160	0		8/2/27 7:00 AM*	22
GE MLI A295	Received - GT Pkg - LF Emulsion Control Skid (GE MLI A295) -	0		8/2/27 7:00 AM*	22
GE MLI A40F	Received - GT Pkg - Inlet Filter House Evaporative Cooler ME (G	0		8/2/27 7:00 AM*	22
GE MLI G015	Received - GT Pkg - Fuel Gas Absolute Separator Skid (GE MLI	0		8/2/27 7:00 AM*	22
GE MLI G023	Received - GT Pkg - Fuel Gas Chromatograph (GE MLI G023) -	0		8/2/27 7:00 AM*	22
GE MLI N32A	Received - GT Pkg - PEECC Fire Protection (GE MLI N32A) - Tra	0		8/2/27 7:00 AM*	22
GE MLI 7F.04	Received - GT Pkg - Gas Turbine (GE MLI 7F.04) - Train 1	0		8/31/27 5:00 PM*	0
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,01,02 PRO - OFE / GE Provided - Gas Turbine - Train 1 - Piping					
GE MLI 924A	Received - GT Pkg - PPG ARR IBH Air Extraction Flexhoses (GE	0		6/2/27 5:00 PM*	63
GE MLI 924B	Received - GT Pkg - PPG ARR Air Extraction OBB Flexhose (GE	0		6/2/27 5:00 PM*	63
GE MLI 924B	Received - GT Pkg - PPG ARR, Air Extraction OBB-Hardware (G	0		6/2/27 5:00 PM*	63
GE MLI 924B	Received - GT Pkg - PPG ARR, Air Extraction OBB-Insulation (G	0		6/14/27 7:00 AM*	56
GE MLI 0909	Received - GT Pkg - PPG ARR Cooling & Sealing Air Flexhose (	0		7/2/27 5:00 PM*	41
GE MLI 0905	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Hardware	0		8/2/27 7:00 AM*	22
GE MLI 0905	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Piping (GI	0		8/2/27 7:00 AM*	22
GE MLI 0905	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Support (	0		8/2/27 7:00 AM*	22
GE MLI 0906	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Load Pipi	0		8/2/27 7:00 AM*	22
GE MLI 0906	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Load Sup	0		8/2/27 7:00 AM*	22
GE MLI 0907	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Hardware	0		8/2/27 7:00 AM*	22
GE MLI 0907	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Piping (GI	0		8/2/27 7:00 AM*	22
GE MLI 0907	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain 2 BRG (G	0		8/2/27 7:00 AM*	22
GE MLI 0909	Received - GT Pkg - PPG ARR Cooling & Sealing Air Hardware (	0		8/2/27 7:00 AM*	22
GE MLI 0909	Received - GT Pkg - PPG ARR Cooling & Sealing - Piping Insula	0		8/2/27 7:00 AM*	22
GE MLI 0909	Received - GT Pkg - PPG ARR Cooling & Sealing Air Piping (GE	0		8/2/27 7:00 AM*	22
GE MLI 0909	Received - GT Pkg - PPG ARR Cooling & Sealing Air Supports (	0		8/2/27 7:00 AM*	22
GE MLI 0920	Received - GT Pkg - PPG ARR False Start Drain Hardware (GE I	0		8/2/27 7:00 AM*	22
GE MLI 0920	Received - GT Pkg - PPG ARR False Start Drain Piping (GE MLI	0		8/2/27 7:00 AM*	22
GE MLI 0920	Received - GT Pkg - PPG ARR, False Start Drain Supports (GE I	0		8/2/27 7:00 AM*	22
GE MLI 0920	Received - GT Pkg - PPG ARR False Start Drain Tubing (GE ML	0		8/2/27 7:00 AM*	22
GE MLI 0953	Received - GT Pkg - PPG, Comprwash Hardware (GE MLI 0953	0		8/2/27 7:00 AM*	22
GE MLI 0953	Received - GT Pkg - PPG, Comprwash Piping (GE MLI 0953PG	0		8/2/27 7:00 AM*	22
GE MLI 0962	Received - GT Pkg - PPG ARR Fuel Gas Turb Sysflexhose (GE I	0		8/2/27 7:00 AM*	22
GE MLI 0962	Received - GT Pkg - PPG ARR Fuel Gas Turb Syshardware (GE	0		8/2/27 7:00 AM*	22
GE MLI 0962	Received - GT Pkg - PPG ARR Fuel Gas Turb Syspiping (GE ML	0		8/2/27 7:00 AM*	22
GE MLI 0964	Received - GT Pkg - PPG ARR Fire Prot GT Compt Hardware (G	0		8/2/27 7:00 AM*	22
GE MLI 0964	Received - GT Pkg - PPG ARR Fire Prot GT Compt Supports (GI	0		8/2/27 7:00 AM*	22
GE MLI 0964	Received - GT Pkg - PPG ARR Fire Prot GT Compt Tubing (GE I	0		8/2/27 7:00 AM*	22
GE MLI 0972	Received - GT Pkg - PPG ARR Cooling Air EXH FR Flexhose (GI	0		8/2/27 7:00 AM*	22
GE MLI 0972	Received - GT Pkg - PPG ARR Cooling Air EXH FR Hardware (G	0		8/2/27 7:00 AM*	22
GE MLI 0972	Received - GT Pkg - PPG ARR Cooling Air EXH FR Piping (GE M	0		8/2/27 7:00 AM*	22
GE MLI 0976	Received - GT Pkg - PPG Exhaust Plenum Drain Hardware (GE	0		8/2/27 7:00 AM*	22
GE MLI 0976	Received - GT Pkg - PPG Exhaust Plenum Drain Piping (GE ML	0		8/2/27 7:00 AM*	22
GE MLI 0979	Received - GT Pkg - PPG ARR Inlet Plenum Drain (GE MLI 097	0		8/2/27 7:00 AM*	22
GE MLI 0979	Received - GT Pkg - PPG ARR Inlet Plenum Drain Piping (GE M	0		8/2/27 7:00 AM*	22
GE MLI 0995	Received - GT Pkg - PPG ARR Fire Protection EXH Compt Hard	0		8/2/27 7:00 AM*	22
GE MLI 0995	Received - GT Pkg - PPG ARR Fire Protection EXH Compt Supp	0		8/2/27 7:00 AM*	22
GE MLI 0995	Received - GT Pkg - PPG ARR Fire Protection EXH Compt Tubir	0		8/2/27 7:00 AM*	22
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Hardware (GE M	0		8/2/27 7:00 AM*	22
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Piping (GE MLI	0		8/2/27 7:00 AM*	22

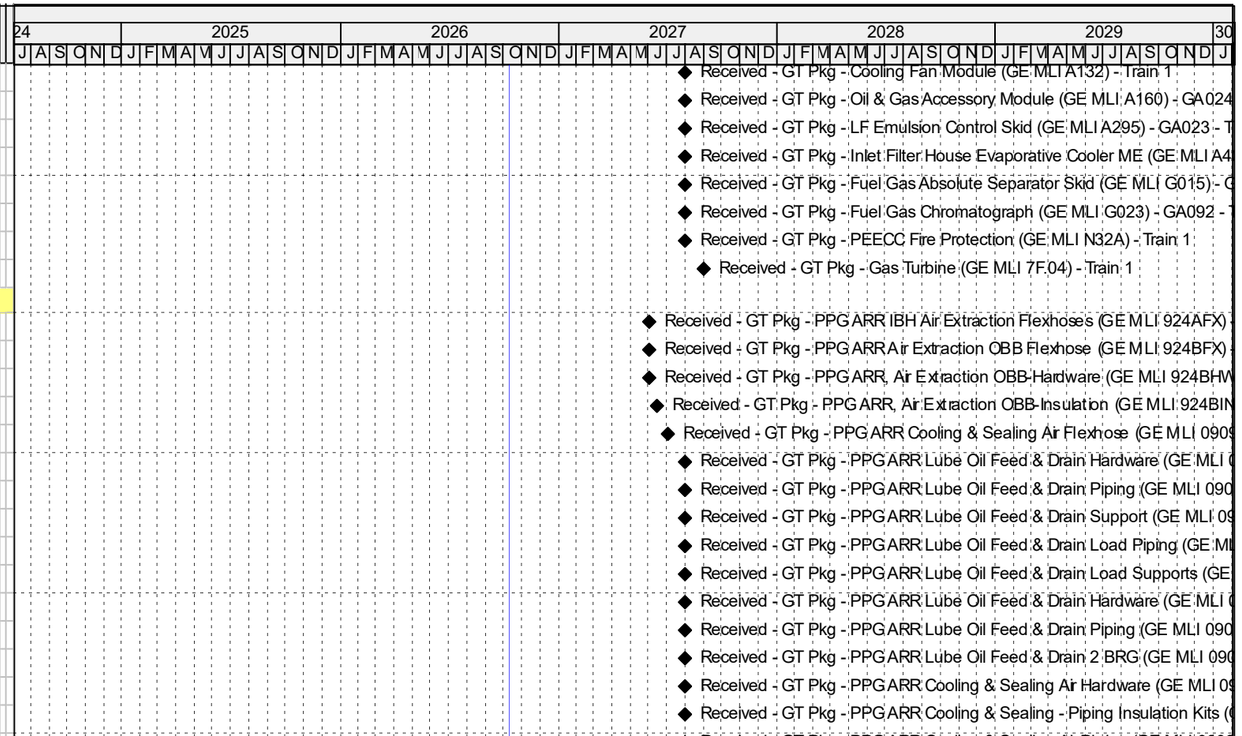


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Supports (GE M	0		8/2/27 7:00 AM*	22
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Tubing (GE MLI	0		8/2/27 7:00 AM*	22
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Tubing (GE MLI	0		8/2/27 7:00 AM*	22
GE MLI 9019	Received - GT Pkg - PPG ARR Impingement Cooling Hardware	0		8/2/27 7:00 AM*	22
GE MLI 9019	Received - GT Pkg - PP ARR Impgmnt Clg Casing Manifold (GE	0		8/2/27 7:00 AM*	22
GE MLI 9019	Received - GT Pkg - PP ARR Impgmnt Clg Bendable Duct (GE I	0		8/2/27 7:00 AM*	22
GE MLI 9019	Received - GT Pkg - PPG ARR Impingement Cooling Piping (GE	0		8/2/27 7:00 AM*	22
GE MLI 9024	Received - GT Pkg - Hardwares, Piping Inlet Dehumidification (G	0		8/2/27 7:00 AM*	22
GE MLI 9024	Received - GT Pkg - Piping, Inlet Dehumidification Piping (GE M	0		8/2/27 7:00 AM*	22
GE MLI 9024	Received - GT Pkg - Piping, Inlet Dehumidification Support (GE	0		8/2/27 7:00 AM*	22
GE MLI 924A	Received - GT Pkg - PPG ARR IBH Air Extraction Hardware (GE	0		8/2/27 7:00 AM*	22
GE MLI 924A	Received - GT Pkg - PPG ARR IBH Air Extraction Insulation (GE	0		8/2/27 7:00 AM*	22
GE MLI 924A	Received - GT Pkg - PPG ARR IBH Air Extraction Piping (GE ML	0		8/2/27 7:00 AM*	22
GE MLI 924B	Received - GT Pkg - PPG ARR Air Extraction OBB Piping (GE M	0		8/2/27 7:00 AM*	22
GE MLI 924B	Received - GT Pkg - PPG ARR Air Extraction OBB Supports (GE	0		8/2/27 7:00 AM*	22
GE MLI 924D	Received - GT Pkg - PPG ARR, Air Extraction Flexhose (GE MLI	0		8/2/27 7:00 AM*	22
GE MLI 924D	Received - GT Pkg - PPG ARR, Air Extraction Hardware (GE ML	0		8/2/27 7:00 AM*	22
GE MLI 924D	Received - GT Pkg - PPG ARR, Air Extraction Piping (GE MLI 92	0		8/2/27 7:00 AM*	22
GE MLI 924D	Received - GT Pkg - PPG ARR, Air Extraction Supports (GE MLI	0		8/2/27 7:00 AM*	22
GE MLI 924D	Received - GT Pkg - PPG ARR, Air Extraction Tubing (GE MLI 9	0		8/2/27 7:00 AM*	22
GE MLI 969A	Received - GT Pkg - INTC PPG Lube Oil Hardware (GE MLI 969	0		8/2/27 7:00 AM*	22
GE MLI 969A	Received - GT Pkg - INTC PPG Lube Oil Piping (GE MLI 969AP	0		8/2/27 7:00 AM*	22
GE MLI 969G	Received - GT Pkg - Piping ARR Gas Skid Flexhose (GE MLI 96	0		8/2/27 7:00 AM*	22
GE MLI 969G	Received - GT Pkg - Piping ARR Gas Skid Hardware (GE MLI 96	0		8/2/27 7:00 AM*	22
GE MLI 969G	Received - GT Pkg - Piping Insulation, Cooled Cooling Air (GE M	0		8/2/27 7:00 AM*	22
GE MLI 969G	Received - GT Pkg - Piping ARR Gas Skid Piping (GE MLI 969G	0		8/2/27 7:00 AM*	22
GE MLI 969M	Received - GT Pkg - PPG ARR INTC PPG Ctrl Oil Hardware (GE	0		8/2/27 7:00 AM*	22
GE MLI 969M	Received - GT Pkg - PPG ARR INTC PPG Ctrl Oil Piping (GE MLI	0		8/2/27 7:00 AM*	22
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Hardware (G	0		8/2/27 7:00 AM*	22
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Piping (GE I	0		8/2/27 7:00 AM*	22
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Tubing (GE	0		8/2/27 7:00 AM*	22
GE MLI A184	Received - GT Pkg - INTC PPG Inlet Heating Hardware (GE MLI	0		8/2/27 7:00 AM*	22
GE MLI A184	Received - GT Pkg - INTC PPG Inlet Heating Piping (GE MLI A1	0		8/2/27 7:00 AM*	22
GE MLI A184	Received - GT Pkg - INTC PPG Inlet Heating Support (GE MLI A	0		8/2/27 7:00 AM*	22
GE MLI A341	Received - GT Pkg - PPG ARR Duct Inlet Bleed Heating Hardwa	0		8/2/27 7:00 AM*	22
GE MLI A341	Received - GT Pkg - PPG ARR Duct Inlet Bleed Heating Piping (	0		8/2/27 7:00 AM*	22
GE MLI A341	Received - GT Pkg - PPG ARR Duct Inlet Bleed Heating Suppor	0		8/2/27 7:00 AM*	22
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,01,03 PRO - OFE / GE Provided - Gas Turbine - Train 1 - Valves					
GE MLI 0572	Received - GT Pkg - Fuel Gas Emergency Stop Valve (GE MLI (	0		8/2/27 7:00 AM*	22
GE MLI 0920	Received - GT Pkg - PPG ARR False Start Drain Valve (GE MLI	0		8/2/27 7:00 AM*	22
GE MLI 0953	Received - GT Pkg - Valve Kit Part (GE MLI 0953VV) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI 1022	Received - GT Pkg - Compressor Bleed Valve (GE MLI 1022) - T	0		8/2/27 7:00 AM*	22
GE MLI 1026	Received - GT Pkg - Valves, Regulator False Start Drain (GE ML	0		8/2/27 7:00 AM*	22
GE MLI 1087	Received - GT Pkg - Valves (GE MLI 1087VV) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI 510C	Received - GT Pkg - Drains Module Valves (GE MLI 510C) - Trai	0		8/2/27 7:00 AM*	22
GE MLI 924B	Received - GT Pkg - PPG ARR, Air Extraction Valves (GE MLI 92	0		8/2/27 7:00 AM*	22
GE MLI 924D	Received - GT Pkg - PPG ARR, Air Extraction Valves (GE MLI 92	0		8/2/27 7:00 AM*	22
GE MLI 969A	Received - GT Pkg - Valve, INTC Lube Oil (GE MLI 969AVV) - Tr	0		8/2/27 7:00 AM*	22
GE MLI A037	Received - GT Pkg - Inlet Bleed Heat Valve (GE MLI A037) - Tra	0		8/2/27 7:00 AM*	22
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Valves (GE I	0		8/2/27 7:00 AM*	22

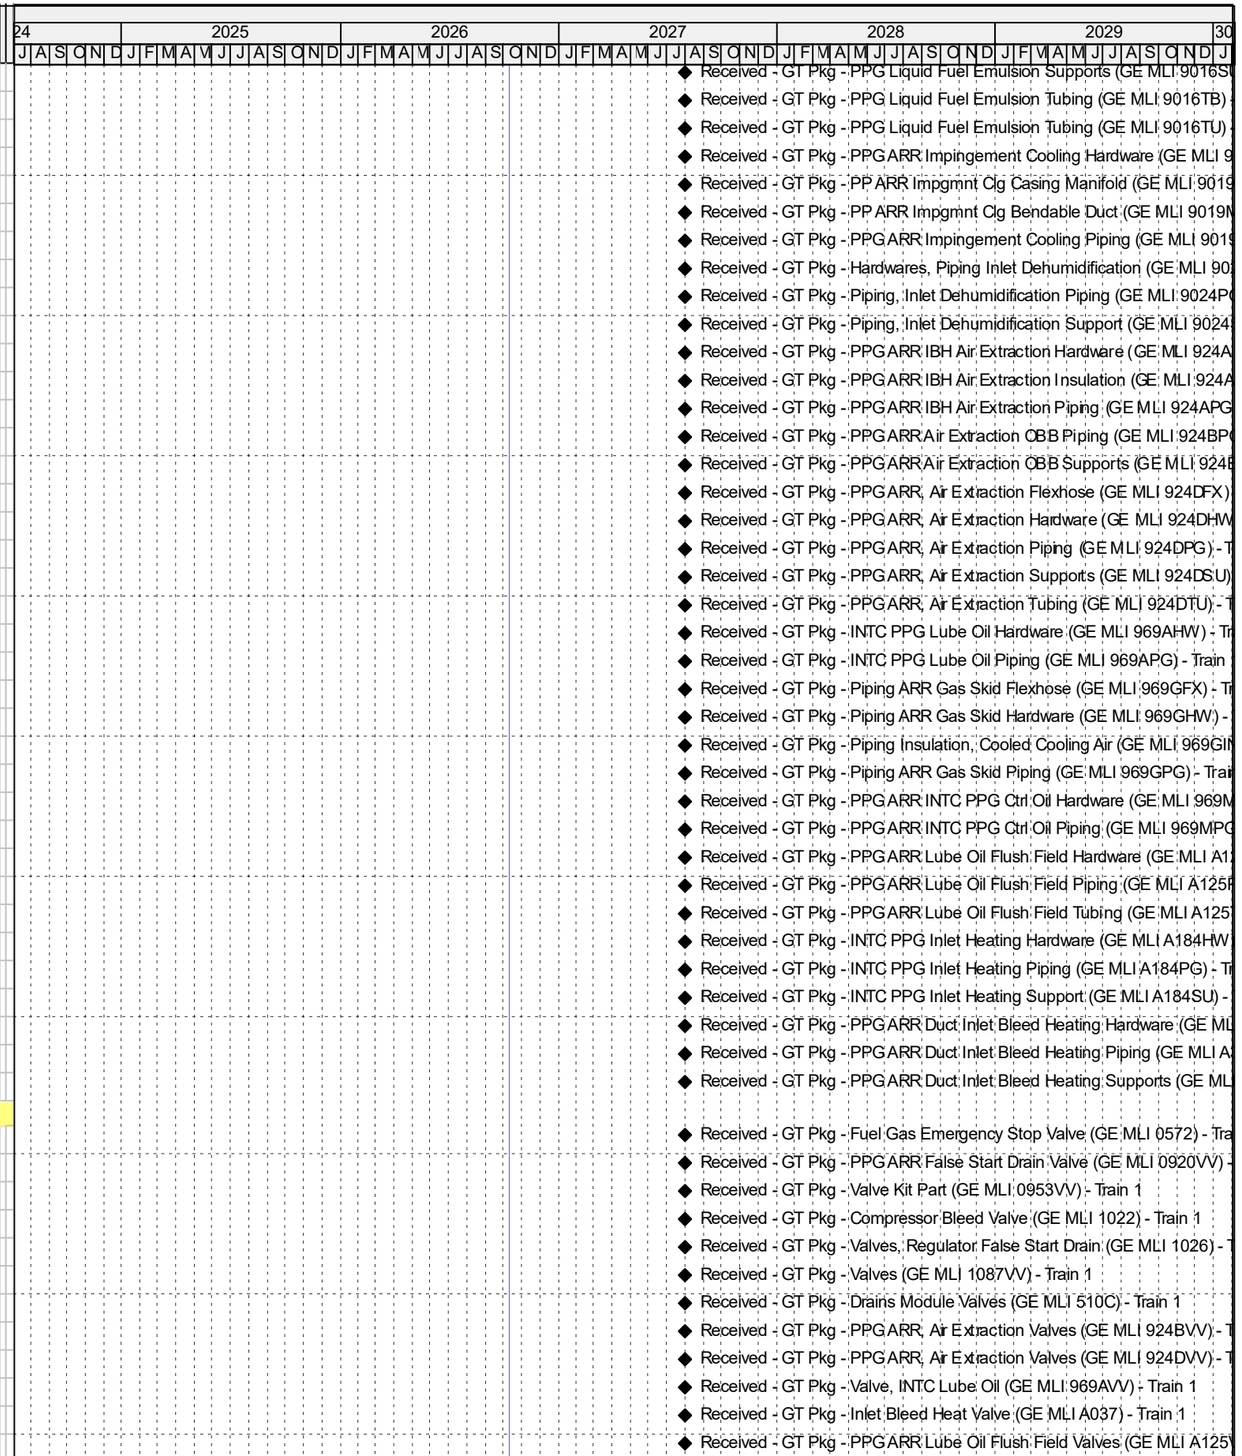


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI A278	Received - GT Pkg - Valves CTM CTRL Stop (GE MLI A278) - Tr	0		8/2/27 7:00 AM*	22
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,01,04 PRO - OFE / GE Provided - Gas Turbine - Train 1 - Misc					
GE MLI 1603	Received - GT Pkg - Foundation Bolting Arrangement (GE MLI	0		6/1/27 7:00 AM*	65
GE MLI 1604	Received - GT Pkg - Bolting & Doweling ARR (GE MLI 1604) - Tr	0		6/1/27 7:00 AM*	65
GE MLI 1121	Received - GT Pkg - Flame Detector (GE MLI 1121) - Train 1	0		6/2/27 5:00 PM*	63
GE MLI 1261	Received - GT Pkg - Combustion Dynamics Monitoring (GE MLI	0		6/2/27 5:00 PM*	63
GE MLI 595A	Received - GT Pkg - Emuls Fuel Solenoid Assy (GE MLI 595A) -	0		6/2/27 5:00 PM*	63
GE MLI A273	Received - GT Pkg - Watermist Fire Protection Skid (GE MLI A2	0		6/2/27 5:00 PM*	63
GE MLI 1647	Received - GT Pkg - Damper Door (GE MLI 1647) - Train 1	0		7/12/27 5:00 PM*	36
GE MLI 0401	Received - GT Pkg - Wire List Field Wiring (GE MLI 0401) - Trai	0		8/2/27 7:00 AM*	22
GE MLI 0585	Received - GT Pkg - Panel, Gas Detector (GE MLI 0585) - Train	0		8/2/27 7:00 AM*	22
GE MLI 0623	Received - GT Pkg - Exhaust Thermocouple (GE MLI 0623) - Tr	0		8/2/27 7:00 AM*	22
GE MLI 0706	Received - GT Pkg - Diffuser Assy, Exhaust (GE MLI 0706) - Tra	0		8/2/27 7:00 AM*	22
GE MLI 0726	Received - GT Pkg - Dynamics Monitor Combustion (GE MLI 07	0		8/2/27 7:00 AM*	22
GE MLI 0953	Received - GT Pkg - Support Fab Kit Part (GE MLI 0953SU) - Tr	0		8/2/27 7:00 AM*	22
GE MLI 0953	Received - GT Pkg - Tubing Kit Part (GE MLI 0953TU) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI 0962	Received - GT Pkg - Support Kit (GE MLI 0962SU) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI 0987	Received - GT Pkg - Tubing ARR, Performance Monitoring (GE I	0		8/2/27 7:00 AM*	22
GE MLI 1049	Received - GT Pkg - Inlet Dehumidification (GE MLI 1049) - GA(	0		8/2/27 7:00 AM*	22
GE MLI 1087	Received - GT Pkg - Hardware (GE MLI 1087HW) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI 1155	Received - GT Pkg - Junction Box AR (GE MLI 1155) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI 1213	Received - GT Pkg - Transformer, PWR Stepup, LGN (GE MLI 1	0		8/2/27 7:00 AM*	22
GE MLI 1309	Received - GT Pkg - Load Coupling Hardware Kit (GE MLI 1309	0		8/2/27 7:00 AM*	22
GE MLI 1311	Received - GT Pkg - Load Coupling Guard Assembly (GE MLI 1	0		8/2/27 7:00 AM*	22
GE MLI 1319	Received - GT Pkg - Rigid Load Coupling Machining (GE MLI 13	0		8/2/27 7:00 AM*	22
GE MLI 1323	Received - GT Pkg - Load Coupling Tooling Kit (GE MLI 1323) -	0		8/2/27 7:00 AM*	22
GE MLI 1612	Received - GT Pkg - Inlet Plenum Assembly (GE MLI 1612) - Tra	0		8/2/27 7:00 AM*	22
GE MLI 1627	Received - GT Pkg - Acoustic Barrier Wall (GE MLI 1627) - Train	0		8/2/27 7:00 AM*	22
GE MLI 1635	Received - GT Pkg - Duct Assy, External CLG & SLG Air (GE ML	0		8/2/27 7:00 AM*	22
GE MLI 1643	Received - GT Pkg - Ventilation Fans For Enclosures (GE MLI 16	0		8/2/27 7:00 AM*	22
GE MLI 1645	Received - GT Pkg - Floorunit Grating ARR (GE MLI 1645) - Trai	0		8/2/27 7:00 AM*	22
GE MLI 1652	Received - GT Pkg - Ladder T/C Access (GE MLI 1652) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI 557A	Received - GT Pkg - Turbine Transmitter Arrangement (GE MLI 5	0		8/2/27 7:00 AM*	22
GE MLI 557T	Received - GT Pkg - Transducer Arrangement (GE MLI 557T) - T	0		8/2/27 7:00 AM*	22
GE MLI 9010	Received - GT Pkg - 9010 Hardware (GE MLI 9010HW) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI 9010	Received - GT Pkg - 9010 Suppport (GE MLI 9010SU) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Misc (GE MLI 90	0		8/2/27 7:00 AM*	22
GE MLI 969A	Received - GT Pkg - Supports, INTC Lube Oil (GE MLI 969ASU	0		8/2/27 7:00 AM*	22
GE MLI 969M	Received - GT Pkg - Supports 969M (GE MLI 969MSU) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI A035	Received - GT Pkg - Water Injection Module (Pumping Skid) (GE	0		8/2/27 7:00 AM*	22
GE MLI A041	Received - GT Pkg - Inlet Duct Assembly (GE MLI A041) - Train	0		8/2/27 7:00 AM*	22
GE MLI A042	Received - GT Pkg - Exhaust Diffuser General ARR (GE MLI A04	0		8/2/27 7:00 AM*	22
GE MLI A070	Received - GT Pkg - Filter Elementair Inlet (GE MLI A070) - Trai	0		8/2/27 7:00 AM*	22
GE MLI A122	Received - GT Pkg - Humidity Sensory (GE MLI A122) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Misc (GE MI	0		8/2/27 7:00 AM*	22
GE MLI A151	Received - GT Pkg - External Insulation (GE MLI A151) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI A179	Received - GT Pkg - Strainer Field Temporary (GE MLI A179) - T	0		8/2/27 7:00 AM*	22
GE MLI A209	Received - GT Pkg - Universal On Site Monitoring (GE MLI A209	0		8/2/27 7:00 AM*	22
GE MLI A252	Received - GT Pkg - Consumables LO Flush (GE MLI A252) - Tr	0		8/2/27 7:00 AM*	22
GE MLI A258	Received - GT Pkg - Station, Vibration Analysis (GE MLI A258) -	0		8/2/27 7:00 AM*	22

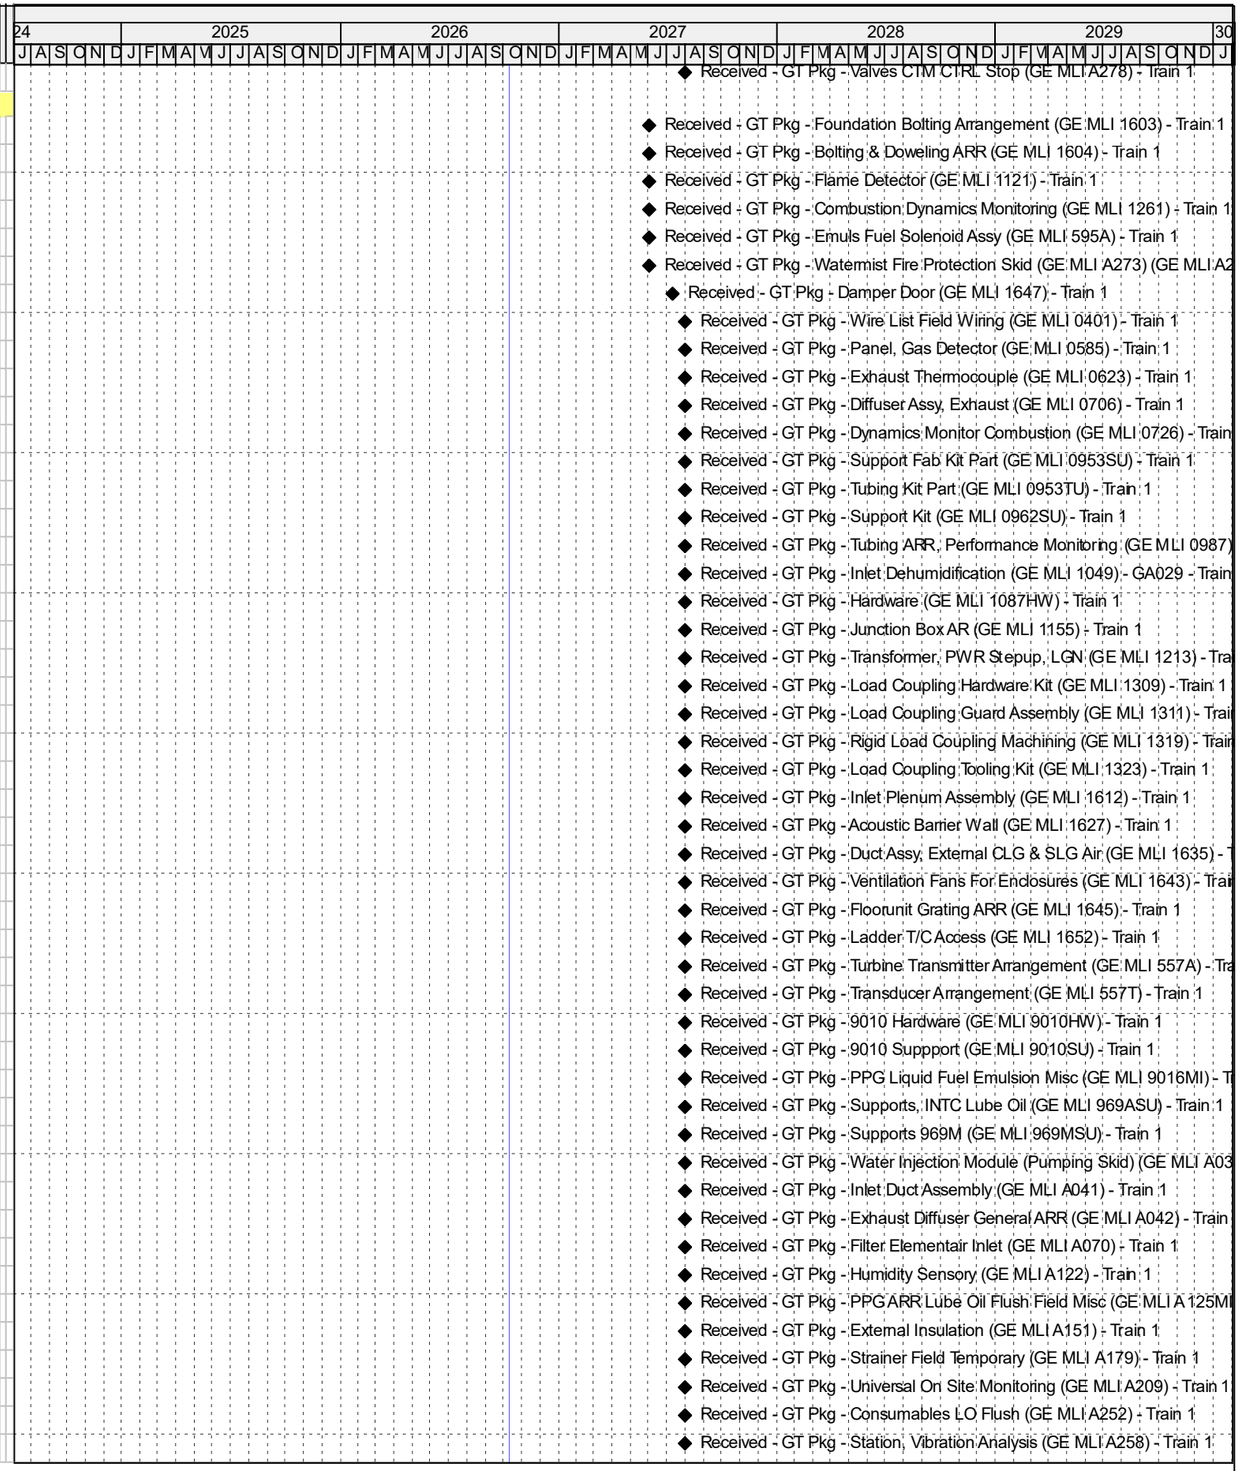


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI A31	Received - GT Pkg - TCP Aux Panel For Gas Chromatograph (G	0		8/2/27 7:00 AM*	22
GE MLI A33	Received - GT Pkg - Major Inspection : Tool Kit For GT Casing D	0		8/2/27 7:00 AM*	22
GE MLI A33	Received - GT Pkg - Basic Tool Kit & Cart (GE MLI A33H) - Train	0		8/2/27 7:00 AM*	22
GE MLI A33	Received - GT Pkg - Hydraulic Torque Wrench For GT Casing Di	0		8/2/27 7:00 AM*	22
GE MLI A33	Received - GT Pkg - Hydraulic Tensioner (GE MLI A33J) - Train	0		8/2/27 7:00 AM*	22
GE MLI A33	Received - GT Pkg - Lifting Beam GT Rotor Plus Guides (GE MI	0		8/2/27 7:00 AM*	22
GE MLI A40	Received - GT Pkg - Inlet System Caulk (GE MLI A40T) - Train 1	0		8/2/27 7:00 AM*	22
GE MLI A98	Received - GT Pkg - Inlet Support Structure (GE MLI A980) - Tra	0		8/2/27 7:00 AM*	22
GE MLI A99	Received - GT Pkg - KKS Hardware Tags For Unit-1 (GE MLI A9	0		8/2/27 7:00 AM*	22
GE MLI MSS	Received - GT Pkg - Gt Summary Sheet Container (GE MLI MS	0		8/2/27 7:00 AM*	22
GE MLI N32	Received - GT Pkg - LCI Compartment Fire Protection (GE MLI	0		8/2/27 7:00 AM*	22
GE MLI QCF	Received - GT Pkg - Touchup Paint (GE MLI QCF0) - Train 1	0		8/2/27 7:00 AM*	22
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,02 PRO - OFE / GE Provided - Gas Turbine - Train 2					
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,02,01 PRO - OFE / GE Provided - Gas Turbine - Train 2 - Equip					
GE MLI G02	Received - GT Pkg - Fuel Gas Chromatograph (GE MLI G023) -	0		8/2/27 7:00 AM*	43
GE MLI A13	Received - GT Pkg - APU (Air Processing Unit) (GE MLI A130) -	0		8/11/27 5:00 PM*	35
GE MLI 063	Received - GT Pkg - Fuel Gas Coriolis Flow Meter (GE MLI 063	0		8/31/27 5:00 PM*	21
GE MLI 099	Received - GT Pkg - Liquid Fuel Module (Pump) (GE MLI 0992)	0		8/31/27 5:00 PM*	21
GE MLI 161	Received - GT Pkg - Load Compartment Enclosure Assembly (G	0		8/31/27 5:00 PM*	21
GE MLI 163	Received - GT Pkg - Enclosure, Gas Turbine (GE MLI 1634) - Tr	0		8/31/27 5:00 PM*	21
GE MLI 164	Received - GT Pkg - Overhead Travel Crane (GE MLI 1648) - Tra	0		8/31/27 5:00 PM*	21
GE MLI A13	Received - GT Pkg - Cooling Fan Module (GE MLI A132) - Train	0		8/31/27 5:00 PM*	21
GE MLI A16	Received - GT Pkg - Oil & Gas Accessory Module (GE MLI A16	0		8/31/27 5:00 PM*	21
GE MLI A29	Received - GT Pkg - LF Emulsion Control Skid (GE MLI A295) -	0		8/31/27 5:00 PM*	21
GE MLI A40	Received - GT Pkg - Inlet Filter House Evaporative Cooler ME (G	0		8/31/27 5:00 PM*	21
GE MLI G01	Received - GT Pkg - Fuel Gas Absolute Separator Skid (GE MLI	0		8/31/27 5:00 PM*	21
GE MLI N32	Received - GT Pkg - PEECC Fire Protection (GE MLI N32A) - Tra	0		8/31/27 5:00 PM*	21
GE MLI A04	Received - GT Pkg - Inlet Filter House (GE MLI A040) - Train 2	0		9/1/27 5:00 PM*	20
GE MLI A07	Received - GT Pkg - CWM (Cooling Water Modules Unit) (GE M	0		9/1/27 5:00 PM*	20
GE MLI 7F.0	Received - GT Pkg - Gas Turbine (GE MLI 7F.04) - Train 2	0		9/30/27 5:00 PM*	0
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,02,02 PRO - OFE / GE Provided - Gas Turbine - Train 2 - Piping					
GE MLI 924	Received - GT Pkg - PPG ARR, Air Extraction OBB-Insulation (G	0		6/14/27 7:00 AM*	77
GE MLI 924	Received - GT Pkg - PPG ARR IBH Air Extraction Flexhoses (GE	0		7/2/27 5:00 PM*	62
GE MLI 924	Received - GT Pkg - PPG ARR Air Extraction OBB Flexhose (GE	0		7/2/27 5:00 PM*	62
GE MLI 924	Received - GT Pkg - PPG ARR, Air Extraction OBB-Hardware (G	0		7/2/27 5:00 PM*	62
GE MLI A12	Received - GT Pkg - PPG ARR Lube Oil Flush Field Hardware (G	0		8/2/27 7:00 AM*	43
GE MLI A12	Received - GT Pkg - PPG ARR Lube Oil Flush Field Piping (GE I	0		8/2/27 7:00 AM*	43
GE MLI A12	Received - GT Pkg - PPG ARR Lube Oil Flush Field Tubing (GE	0		8/2/27 7:00 AM*	43
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Hardware	0		8/31/27 5:00 PM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Piping (GI	0		8/31/27 5:00 PM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Support (	0		8/31/27 5:00 PM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Load Pipi	0		8/31/27 5:00 PM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Load Sup	0		8/31/27 5:00 PM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Hardware	0		8/31/27 5:00 PM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Piping (GI	0		8/31/27 5:00 PM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain 2 BRG (G	0		8/31/27 5:00 PM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Cooling & Sealing Air Flexhose (	0		8/31/27 5:00 PM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Cooling & Sealing Air Hardware (	0		8/31/27 5:00 PM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Cooling & Sealing - Piping Insula	0		8/31/27 5:00 PM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Cooling & Sealing Air Piping (GE	0		8/31/27 5:00 PM*	21

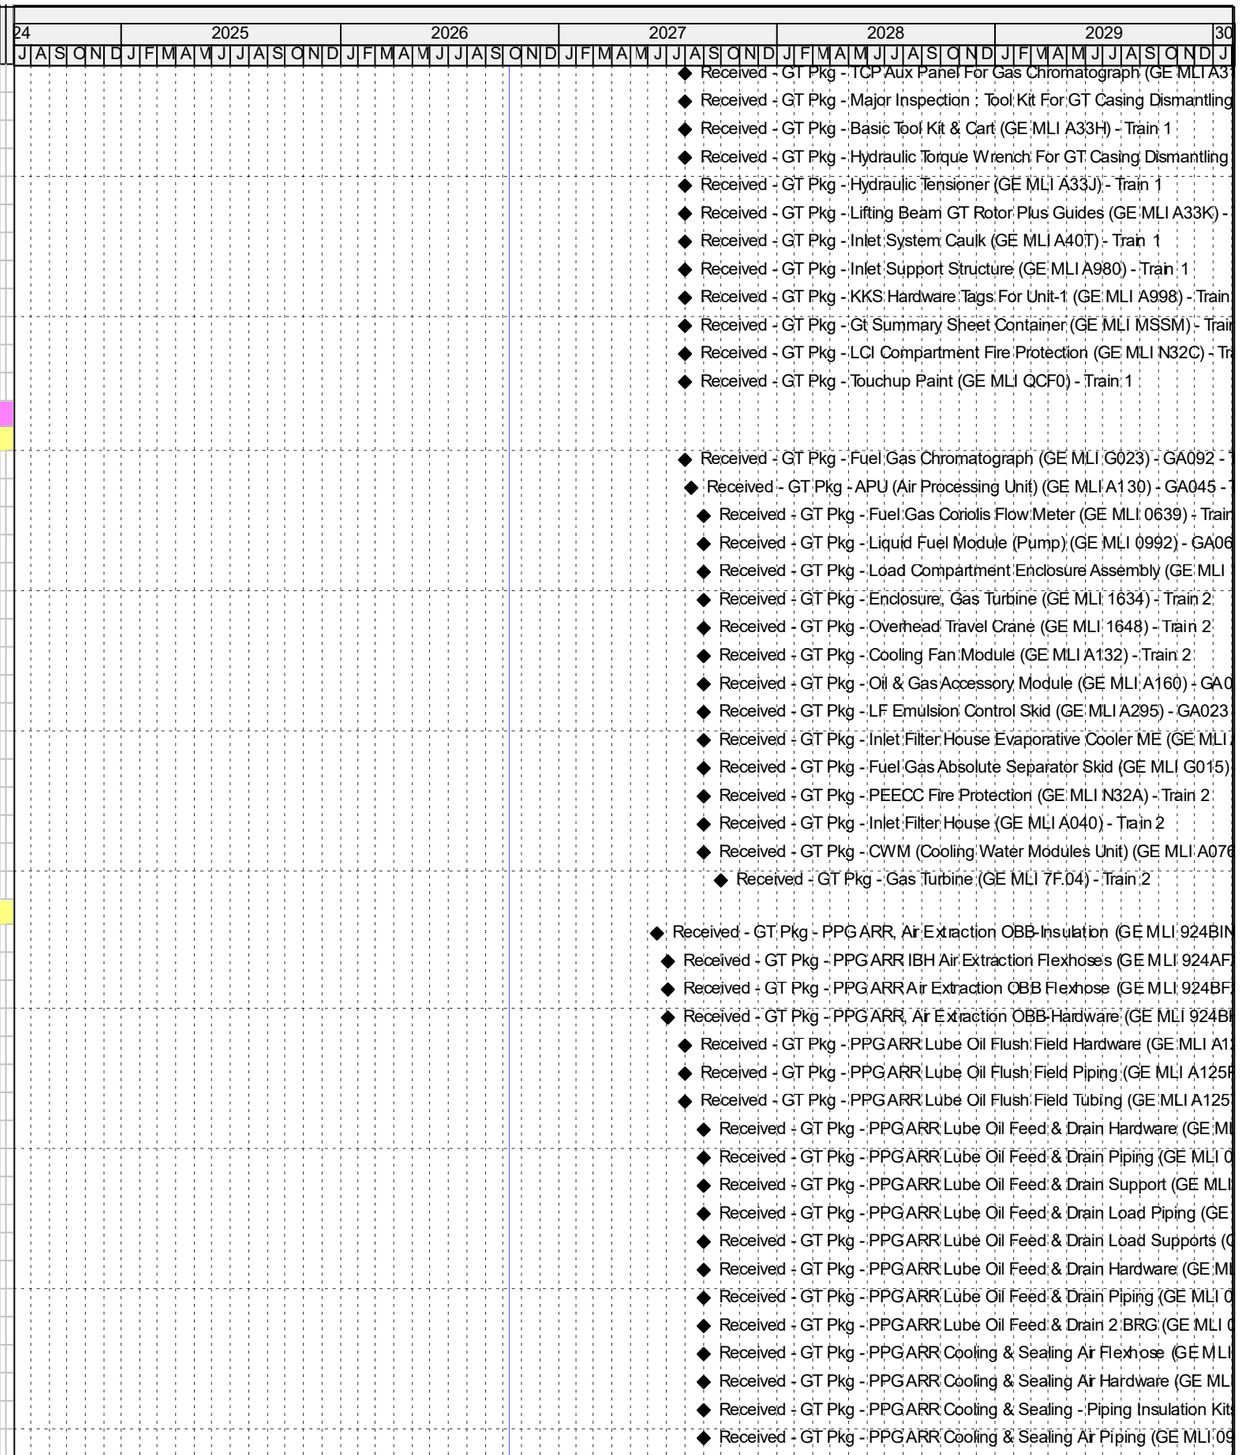

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI 0909	Received - GT Pkg - PPG ARR Cooling & Sealing Air Supports ((	0		8/31/27 5:00 PM*	21
GE MLI 0920	Received - GT Pkg - PPG ARR False Start Drain Hardware (GE I	0		8/31/27 5:00 PM*	21
GE MLI 0920	Received - GT Pkg - PPG ARR False Start Drain Piping (GE MLI	0		8/31/27 5:00 PM*	21
GE MLI 0920	Received - GT Pkg - PPG ARR, False Start Drain Supports (GE I	0		8/31/27 5:00 PM*	21
GE MLI 0920	Received - GT Pkg - PPG ARR False Start Drain Tubing (GE ML	0		8/31/27 5:00 PM*	21
GE MLI 0953	Received - GT Pkg - PPG, Comprwash Hardware (GE MLI 0953	0		8/31/27 5:00 PM*	21
GE MLI 0953	Received - GT Pkg - PPG, Comprwash Piping (GE MLI 0953PG	0		8/31/27 5:00 PM*	21
GE MLI 0962	Received - GT Pkg - PPG ARR Fuel Gas Turb Sysflexhose (GE I	0		8/31/27 5:00 PM*	21
GE MLI 0962	Received - GT Pkg - PPG ARR Fuel Gas Turb Syshardware (GE	0		8/31/27 5:00 PM*	21
GE MLI 0962	Received - GT Pkg - PPG ARR Fuel Gas Turb Syspiping (GE ML	0		8/31/27 5:00 PM*	21
GE MLI 0964	Received - GT Pkg - PPG ARR Fire Prot GT Compt Hardware (G	0		8/31/27 5:00 PM*	21
GE MLI 0964	Received - GT Pkg - PPG ARR Fire Prot GT Compt Supports (GI	0		8/31/27 5:00 PM*	21
GE MLI 0964	Received - GT Pkg - PPG ARR Fire Prot GT Compt Tubing (GE I	0		8/31/27 5:00 PM*	21
GE MLI 0972	Received - GT Pkg - PPG ARR Cooling Air EXH FR Flexhose (GI	0		8/31/27 5:00 PM*	21
GE MLI 0972	Received - GT Pkg - PPG ARR Cooling Air EXH FR Hardware (G	0		8/31/27 5:00 PM*	21
GE MLI 0972	Received - GT Pkg - PPG ARR Cooling Air EXH FR Piping (GE M	0		8/31/27 5:00 PM*	21
GE MLI 0976	Received - GT Pkg - PPG Exhaust Plenum Drain Hardware (GE	0		8/31/27 5:00 PM*	21
GE MLI 0976	Received - GT Pkg - PPG Exhaust Plenum Drain Piping (GE ML	0		8/31/27 5:00 PM*	21
GE MLI 0979	Received - GT Pkg - PPG ARR Inlet Plenum Drain (GE MLI 097	0		8/31/27 5:00 PM*	21
GE MLI 0979	Received - GT Pkg - PPG ARR Inlet Plenum Drain Piping (GE M	0		8/31/27 5:00 PM*	21
GE MLI 0995	Received - GT Pkg - PPG ARR Fire Protection EXH Compt Hard	0		8/31/27 5:00 PM*	21
GE MLI 0995	Received - GT Pkg - PPG ARR Fire Protection EXH Compt Supp	0		8/31/27 5:00 PM*	21
GE MLI 0995	Received - GT Pkg - PPG ARR Fire Protection EXH Compt Tubi	0		8/31/27 5:00 PM*	21
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Hardware (GE M	0		8/31/27 5:00 PM*	21
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Piping (GE MLI	0		8/31/27 5:00 PM*	21
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Supports (GE M	0		8/31/27 5:00 PM*	21
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Tubing (GE MLI	0		8/31/27 5:00 PM*	21
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Tubing (GE MLI	0		8/31/27 5:00 PM*	21
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Tubing (GE MLI	0		8/31/27 5:00 PM*	21
GE MLI 9019	Received - GT Pkg - PPG ARR Impingement Cooling Hardware	0		8/31/27 5:00 PM*	21
GE MLI 9019	Received - GT Pkg - PP ARR Impgmnt Clg Casing Manifold (GE	0		8/31/27 5:00 PM*	21
GE MLI 9019	Received - GT Pkg - PP ARR Impgmnt Clg Bendable Duct (GE I	0		8/31/27 5:00 PM*	21
GE MLI 9019	Received - GT Pkg - PPG ARR Impingement Cooling Piping (GE	0		8/31/27 5:00 PM*	21
GE MLI 9024	Received - GT Pkg - Hardwares, Piping Inlet Dehumidification (G	0		8/31/27 5:00 PM*	21
GE MLI 9024	Received - GT Pkg - Piping, Inlet Dehumidification Piping (GE M	0		8/31/27 5:00 PM*	21
GE MLI 9024	Received - GT Pkg - Piping, Inlet Dehumidification Support (GE	0		8/31/27 5:00 PM*	21
GE MLI 924A	Received - GT Pkg - PPG ARR IBH Air Extraction Hardware (GE	0		8/31/27 5:00 PM*	21
GE MLI 924A	Received - GT Pkg - PPG ARR IBH Air Extraction Insulation (GE	0		8/31/27 5:00 PM*	21
GE MLI 924A	Received - GT Pkg - PPG ARR IBH Air Extraction Piping (GE ML	0		8/31/27 5:00 PM*	21
GE MLI 924B	Received - GT Pkg - PPG ARR Air Extraction OBB Piping (GE M	0		8/31/27 5:00 PM*	21
GE MLI 924B	Received - GT Pkg - PPG ARR Air Extraction OBB Supports (GE	0		8/31/27 5:00 PM*	21
GE MLI 924D	Received - GT Pkg - PPG ARR, Air Extraction Flexhose (GE MLI	0		8/31/27 5:00 PM*	21
GE MLI 924D	Received - GT Pkg - PPG ARR, Air Extraction Hardware (GE ML	0		8/31/27 5:00 PM*	21
GE MLI 924D	Received - GT Pkg - PPG ARR, Air Extraction Piping (GE MLI 92	0		8/31/27 5:00 PM*	21
GE MLI 924D	Received - GT Pkg - PPG ARR, Air Extraction Supports (GE MLI	0		8/31/27 5:00 PM*	21
GE MLI 924D	Received - GT Pkg - PPG ARR, Air Extraction Tubing (GE MLI 9	0		8/31/27 5:00 PM*	21
GE MLI 969A	Received - GT Pkg - INTC PPG Lube Oil Hardware (GE MLI 969	0		8/31/27 5:00 PM*	21
GE MLI 969A	Received - GT Pkg - INTC PPG Lube Oil Piping (GE MLI 969AP	0		8/31/27 5:00 PM*	21
GE MLI 969G	Received - GT Pkg - Piping ARR Gas Skid Flexhose (GE MLI 96	0		8/31/27 5:00 PM*	21
GE MLI 969G	Received - GT Pkg - Piping ARR Gas Skid Hardware (GE MLI 96	0		8/31/27 5:00 PM*	21
GE MLI 969G	Received - GT Pkg - Piping Insulation, Cooled Cooling Air (GE M	0		8/31/27 5:00 PM*	21



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI 969(	Received - GT Pkg - Piping ARR Gas Skid Piping (GE MLI 969G	0		8/31/27 5:00 PM*	21
GE MLI 969I	Received - GT Pkg - PPG ARR INTC PPG Ctrl Oil Hardware (GE	0		8/31/27 5:00 PM*	21
GE MLI 969I	Received - GT Pkg - PPG ARR INTC PPG Ctrl Oil Piping (GE ML	0		8/31/27 5:00 PM*	21
GE MLI A184	Received - GT Pkg - INTC PPG Inlet Heating Hardware (GE MLI	0		8/31/27 5:00 PM*	21
GE MLI A184	Received - GT Pkg - INTC PPG Inlet Heating Piping (GE MLI A1	0		8/31/27 5:00 PM*	21
GE MLI A184	Received - GT Pkg - INTC PPG Inlet Heating Support (GE MLI A	0		8/31/27 5:00 PM*	21
GE MLI A341	Received - GT Pkg - PPG ARR Duct Inlet Bleed Heating Hardwa	0		8/31/27 5:00 PM*	21
GE MLI A341	Received - GT Pkg - PPG ARR Duct Inlet Bleed Heating Piping (	0		8/31/27 5:00 PM*	21
GE MLI A341	Received - GT Pkg - PPG ARR Duct Inlet Bleed Heating Suppor	0		8/31/27 5:00 PM*	21
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,02,03 PRO - OFE / GE Provided - Gas Turbine - Train 2 - Valves					
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Valves (GE I	0		8/2/27 7:00 AM*	43
GE MLI 0572	Received - GT Pkg - Fuel Gas Emergency Stop Valve (GE MLI (	0		8/31/27 5:00 PM*	21
GE MLI 092(	Received - GT Pkg - PPG ARR False Start Drain Valve (GE MLI	0		8/31/27 5:00 PM*	21
GE MLI 0953	Received - GT Pkg - Valve Kit Part (GE MLI 0953VV) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI 1022	Received - GT Pkg - Compressor Bleed Valve (GE MLI 1022) - T	0		8/31/27 5:00 PM*	21
GE MLI 1026	Received - GT Pkg - Valves, Regulator False Start Drain (GE ML	0		8/31/27 5:00 PM*	21
GE MLI 1087	Received - GT Pkg - Valves (GE MLI 1087VV) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI 510(	Received - GT Pkg - Drains Module Valves (GE MLI 510C) - Trai	0		8/31/27 5:00 PM*	21
GE MLI 924E	Received - GT Pkg - PPG ARR, Air Extraction Valves (GE MLI 92	0		8/31/27 5:00 PM*	21
GE MLI 924I	Received - GT Pkg - PPG ARR, Air Extraction Valves (GE MLI 92	0		8/31/27 5:00 PM*	21
GE MLI 969A	Received - GT Pkg - Valve, INTC Lube Oil (GE MLI 969AVV) - Tr	0		8/31/27 5:00 PM*	21
GE MLI A037	Received - GT Pkg - Inlet Bleed Heat Valve (GE MLI A037) - Tra	0		8/31/27 5:00 PM*	21
GE MLI A278	Received - GT Pkg - Valves CTM CTRL Stop (GE MLI A278) - Tr	0		8/31/27 5:00 PM*	21
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,02,04 PRO - OFE / GE Provided - Gas Turbine - Train 2 - Misc					
GE MLI 1603	Received - GT Pkg - Foundation Bolting Arrangement (GE MLI	0		6/30/27 5:00 PM*	64
GE MLI 1604	Received - GT Pkg - Bolting & Doweling ARR (GE MLI 1604) - Tr	0		6/30/27 5:00 PM*	64
GE MLI 1121	Received - GT Pkg - Flame Detector (GE MLI 1121) - Train 2	0		7/2/27 5:00 PM*	62
GE MLI 1261	Received - GT Pkg - Combustion Dynamics Monitoring (GE MLI	0		7/2/27 5:00 PM*	62
GE MLI 595A	Received - GT Pkg - Emuls Fuel Solenoid Assy (GE MLI 595A) -	0		7/2/27 5:00 PM*	62
GE MLI A273	Received - GT Pkg - Watermist Fire Protection Skid (GE MLI A2	0		7/2/27 5:00 PM*	62
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Misc (GE MI	0		8/2/27 7:00 AM*	43
GE MLI A209	Received - GT Pkg - Universal On Site Monitoring (GE MLI A209	0		8/2/27 7:00 AM*	43
GE MLI A258	Received - GT Pkg - Station, Vibration Analysis (GE MLI A258) -	0		8/2/27 7:00 AM*	43
GE MLI A315	Received - GT Pkg - TCP Aux Panel For Gas Chromatograph (G	0		8/2/27 7:00 AM*	43
GE MLI A33I	Received - GT Pkg - Major Inspection : Tool Kit For GT Casing D	0		8/2/27 7:00 AM*	43
GE MLI A33H	Received - GT Pkg - Basic Tool Kit & Cart (GE MLI A33H) - Train	0		8/2/27 7:00 AM*	43
GE MLI A33I	Received - GT Pkg - Hydraulic Torque Wrench For GT Casing Di	0		8/2/27 7:00 AM*	43
GE MLI A33J	Received - GT Pkg - Hydraulic Tensioner (GE MLI A33J) - Train 2	0		8/2/27 7:00 AM*	43
GE MLI A33K	Received - GT Pkg - Lifting Beam GT Rotor Plus Guides (GE MI	0		8/2/27 7:00 AM*	43
GE MLI E025	Received - GT Pkg - Water Wash Skid (GE MLI E025) - GA019	0		8/2/27 7:00 AM*	43
GE MLI 1647	Received - GT Pkg - Damper Door (GE MLI 1647) - Train 2	0		8/11/27 5:00 PM*	35
GE MLI 1213	Received - GT Pkg - Transformer, PWR Stepup, LGN (GE MLI 1	0		8/30/27 7:00 AM*	23
GE MLI 0401	Received - GT Pkg - Wire List Field Wiring (GE MLI 0401) - Trai	0		8/31/27 5:00 PM*	21
GE MLI 0585	Received - GT Pkg - Panel, Gas Detector (GE MLI 0585) - Train	0		8/31/27 5:00 PM*	21
GE MLI 0623	Received - GT Pkg - Exhaust Thermocouple (GE MLI 0623) - Tra	0		8/31/27 5:00 PM*	21
GE MLI 0706	Received - GT Pkg - Diffuser Assy, Exhaust (GE MLI 0706) - Tra	0		8/31/27 5:00 PM*	21
GE MLI 0726	Received - GT Pkg - Dynamics Monitor Combustion (GE MLI 07	0		8/31/27 5:00 PM*	21
GE MLI 0953	Received - GT Pkg - Support Fab Kit Part (GE MLI 0953SU) - Tr	0		8/31/27 5:00 PM*	21
GE MLI 0953	Received - GT Pkg - Tubing Kit Part (GE MLI 0953TU) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI 0962	Received - GT Pkg - Support Kit (GE MLI 0962SU) - Train 2	0		8/31/27 5:00 PM*	21



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI 0987	Received - GT Pkg - Tubing ARR, Performance Monitoring (GE I	0		8/31/27 5:00 PM*	21
GE MLI 1049	Received - GT Pkg - Inlet Dehumidification (GE MLI 1049) - GA(	0		8/31/27 5:00 PM*	21
GE MLI 1087	Received - GT Pkg - Hardware (GE MLI 1087HW) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI 1155	Received - GT Pkg - Junction Box AR (GE MLI 1155) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI 1309	Received - GT Pkg - Load Coupling Hardware Kit (GE MLI 1309	0		8/31/27 5:00 PM*	21
GE MLI 1311	Received - GT Pkg - Load Coupling Guard Assembly (GE MLI 1	0		8/31/27 5:00 PM*	21
GE MLI 1319	Received - GT Pkg - Rigid Load Coupling Machining (GE MLI 1	0		8/31/27 5:00 PM*	21
GE MLI 1323	Received - GT Pkg - Load Coupling Tooling Kit (GE MLI 1323) -	0		8/31/27 5:00 PM*	21
GE MLI 1612	Received - GT Pkg - Inlet Plenum Assembly (GE MLI 1612) - Tra	0		8/31/27 5:00 PM*	21
GE MLI 1627	Received - GT Pkg - Acoustic Barrier Wall (GE MLI 1627) - Train	0		8/31/27 5:00 PM*	21
GE MLI 1635	Received - GT Pkg - Duct Assy, External CLG & SLG Air (GE ML	0		8/31/27 5:00 PM*	21
GE MLI 1643	Received - GT Pkg - Ventilation Fans For Enclosures (GE MLI 1(	0		8/31/27 5:00 PM*	21
GE MLI 1645	Received - GT Pkg - Floorunit Grating ARR (GE MLI 1645) - Trai	0		8/31/27 5:00 PM*	21
GE MLI 1652	Received - GT Pkg - Ladder T/C Access (GE MLI 1652) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI 557A	Received - GT Pkg - Turbine Transmitter Arrangement (GE MLI	0		8/31/27 5:00 PM*	21
GE MLI 557T	Received - GT Pkg - Transducer Arrangement (GE MLI 557T) - T	0		8/31/27 5:00 PM*	21
GE MLI 9010	Received - GT Pkg - 9010 Hardware (GE MLI 9010HW) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI 9010	Received - GT Pkg - 9010 Suppport (GE MLI 9010SU) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Misc (GE MLI 9(	0		8/31/27 5:00 PM*	21
GE MLI 969A	Received - GT Pkg - Supports, INTC Lube Oil (GE MLI 969ASU)	0		8/31/27 5:00 PM*	21
GE MLI 969M	Received - GT Pkg - Supports 969M (GE MLI 969MSU) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI A035	Received - GT Pkg - Water Injection Module (Pumping Skid) (GI	0		8/31/27 5:00 PM*	21
GE MLI A042	Received - GT Pkg - Exhaust Diffuser General ARR (GE MLI A04	0		8/31/27 5:00 PM*	21
GE MLI A070	Received - GT Pkg - Filter Elementair Inlet (GE MLI A070) - Trai	0		8/31/27 5:00 PM*	21
GE MLI A122	Received - GT Pkg - Humidity Sensory (GE MLI A122) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI A151	Received - GT Pkg - External Insulation (GE MLI A151) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI A179	Received - GT Pkg - Strainer Field Temporary (GE MLI A179) - T	0		8/31/27 5:00 PM*	21
GE MLI A252	Received - GT Pkg - Consumables LO Flush (GE MLI A252) - Tr	0		8/31/27 5:00 PM*	21
GE MLI A40T	Received - GT Pkg - Inlet System Caulk (GE MLI A40T) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI A998	Received - GT Pkg - KKS Hardware Tags For Unit-2 (GE MLI A9	0		8/31/27 5:00 PM*	21
GE MLI MSS	Received - GT Pkg - Gt Summary Sheet Container (GE MLI MS	0		8/31/27 5:00 PM*	21
GE MLI N32C	Received - GT Pkg - Lci Compartment Fire Protection (GE MLI N	0		8/31/27 5:00 PM*	21
GE MLI QCF0	Received - GT Pkg - Touchup Paint (GE MLI QCF0) - Train 2	0		8/31/27 5:00 PM*	21
GE MLI A041	Received - GT Pkg - Inlet Duct Assembly (GE MLI A041) - Train	0		9/1/27 5:00 PM*	20
GE MLI A980	Received - GT Pkg - Inlet Support Structure (GE MLI A980) - Tra	0		9/1/27 5:00 PM*	20
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,03 PRO - OFE / GE Provided - Gas Turbine - Train 3					
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,03,01 PRO - OFE / GE Provided - Gas Turbine - Train 3 - Equip					
GE MLI G023	Received - GT Pkg - Fuel Gas Chromatograph (GE MLI G023) -	0		8/2/27 7:00 AM*	64
GE MLI A130	Received - GT Pkg - APU (Air Processing Unit) (GE MLI A130) -	0		9/13/27 5:00 PM*	34
GE MLI 0639	Received - GT Pkg - Fuel Gas Coriolis Flow Meter (GE MLI 0639	0		10/1/27 5:00 PM*	20
GE MLI 0992	Received - GT Pkg - Liquid Fuel Module (Pump) (GE MLI 0992)	0		10/1/27 5:00 PM*	20
GE MLI 1617	Received - GT Pkg - Load Compartment Enclosure Assembly (G	0		10/1/27 5:00 PM*	20
GE MLI 1634	Received - GT Pkg - Enclosure, Gas Turbine (GE MLI 1634) - Tr	0		10/1/27 5:00 PM*	20
GE MLI 1648	Received - GT Pkg - Overhead Travel Crane (GE MLI 1648) - Tra	0		10/1/27 5:00 PM*	20
GE MLI A040	Received - GT Pkg - Inlet Filter House (GE MLI A040) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI A076	Received - GT Pkg - CWM (Cooling Water Modules Unit) (GE M	0		10/1/27 5:00 PM*	20
GE MLI A132	Received - GT Pkg - Cooling Fan Module (GE MLI A132) - Train	0		10/1/27 5:00 PM*	20
GE MLI A160	Received - GT Pkg - Oil & Gas Accessory Module (GE MLI A160	0		10/1/27 5:00 PM*	20
GE MLI A295	Received - GT Pkg - LF Emulsion Control Skid (GE MLI A295) -	0		10/1/27 5:00 PM*	20
GE MLI A40F	Received - GT Pkg - Inlet Filter House Evaporative Cooler ME (C	0		10/1/27 5:00 PM*	20




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI G01	Received - GT Pkg - Fuel Gas Absolute Separator Skid (GE MLI	0		10/1/27 5:00 PM*	20
GE MLI N32	Received - GT Pkg - PEECC Fire Protection (GE MLI N32A) - Tra	0		10/1/27 5:00 PM*	20
GE MLI 7F.0	Received - GT Pkg - Gas Turbine (GE MLI 7F.04) - Train 3	0		11/1/27 7:00 AM*	0
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,03,02 PRO - OFE / GE Provided - Gas Turbine - Train 3 - Piping					
GE MLI 924E	Received - GT Pkg - PPG ARR, Air Extraction OBB-Insulation (G	0		6/14/27 7:00 AM*	98
GE MLI A12E	Received - GT Pkg - PPG ARR Lube Oil Flush Field Hardware (G	0		8/2/27 7:00 AM*	64
GE MLI A12E	Received - GT Pkg - PPG ARR Lube Oil Flush Field Piping (GE I	0		8/2/27 7:00 AM*	64
GE MLI A12E	Received - GT Pkg - PPG ARR Lube Oil Flush Field Tubing (GE	0		8/2/27 7:00 AM*	64
GE MLI 924A	Received - GT Pkg - PPG ARR IBH Air Extraction Flexhoses (GE	0		8/2/27 5:00 PM*	63
GE MLI 924E	Received - GT Pkg - PPG ARR, Air Extraction OBB-Hardware (G	0		8/2/27 5:00 PM*	63
GE MLI 090E	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Hardware	0		10/1/27 5:00 PM*	20
GE MLI 090E	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Piping (GI	0		10/1/27 5:00 PM*	20
GE MLI 090E	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Support (	0		10/1/27 5:00 PM*	20
GE MLI 090E	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Load Pipi	0		10/1/27 5:00 PM*	20
GE MLI 090E	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Load Sup	0		10/1/27 5:00 PM*	20
GE MLI 0907	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Hardware	0		10/1/27 5:00 PM*	20
GE MLI 0907	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Piping (GI	0		10/1/27 5:00 PM*	20
GE MLI 0907	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain 2 BRG (G	0		10/1/27 5:00 PM*	20
GE MLI 090S	Received - GT Pkg - PPG ARR Cooling & Sealing Air Flexhose (	0		10/1/27 5:00 PM*	20
GE MLI 090S	Received - GT Pkg - PPG ARR Cooling & Sealing Air Hardware (	0		10/1/27 5:00 PM*	20
GE MLI 090S	Received - GT Pkg - PPG ARR Cooling & Sealing - Piping Insula	0		10/1/27 5:00 PM*	20
GE MLI 090S	Received - GT Pkg - PPG ARR Cooling & Sealing Air Piping (GE	0		10/1/27 5:00 PM*	20
GE MLI 090S	Received - GT Pkg - PPG ARR Cooling & Sealing Air Supports (	0		10/1/27 5:00 PM*	20
GE MLI 092(	Received - GT Pkg - PPG ARR False Start Drain Hardware (GE I	0		10/1/27 5:00 PM*	20
GE MLI 092(	Received - GT Pkg - PPG ARR False Start Drain Piping (GE MLI	0		10/1/27 5:00 PM*	20
GE MLI 092(	Received - GT Pkg - PPG ARR False Start Drain Hardware (GE I	0		10/1/27 5:00 PM*	20
GE MLI 092(	Received - GT Pkg - PPG ARR False Start Drain Piping (GE MLI	0		10/1/27 5:00 PM*	20
GE MLI 092(	Received - GT Pkg - PPG ARR, False Start Drain Supports (GE I	0		10/1/27 5:00 PM*	20
GE MLI 092(	Received - GT Pkg - PPG ARR False Start Drain Tubing (GE ML	0		10/1/27 5:00 PM*	20
GE MLI 0953	Received - GT Pkg - PPG, Comprwash Hardware (GE MLI 0953	0		10/1/27 5:00 PM*	20
GE MLI 0953	Received - GT Pkg - PPG, Comprwash Piping (GE MLI 0953PG	0		10/1/27 5:00 PM*	20
GE MLI 0962	Received - GT Pkg - PPG ARR Fuel Gas Turb Sysflexhose (GE I	0		10/1/27 5:00 PM*	20
GE MLI 0962	Received - GT Pkg - PPG ARR Fuel Gas Turb Syshardware (GE	0		10/1/27 5:00 PM*	20
GE MLI 0962	Received - GT Pkg - PPG ARR Fuel Gas Turb Syspiping (GE ML	0		10/1/27 5:00 PM*	20
GE MLI 0964	Received - GT Pkg - PPG ARR Fire Prot GT Compt Hardware (G	0		10/1/27 5:00 PM*	20
GE MLI 0964	Received - GT Pkg - PPG ARR Fire Prot GT Compt Supports (GI	0		10/1/27 5:00 PM*	20
GE MLI 0964	Received - GT Pkg - PPG ARR Fire Prot GT Compt Tubing (GE I	0		10/1/27 5:00 PM*	20
GE MLI 0972	Received - GT Pkg - PPG ARR Cooling Air EXH FR Flexhose (GI	0		10/1/27 5:00 PM*	20
GE MLI 0972	Received - GT Pkg - PPG ARR Cooling Air EXH FR Hardware (G	0		10/1/27 5:00 PM*	20
GE MLI 0972	Received - GT Pkg - PPG ARR Cooling Air EXH FR Piping (GE M	0		10/1/27 5:00 PM*	20
GE MLI 097E	Received - GT Pkg - PPG Exhaust Plenum Drain Hardware (GE	0		10/1/27 5:00 PM*	20
GE MLI 097E	Received - GT Pkg - PPG Exhaust Plenum Drain Piping (GE ML	0		10/1/27 5:00 PM*	20
GE MLI 097S	Received - GT Pkg - PPG ARR Inlet Plenum Drain (GE MLI 097S	0		10/1/27 5:00 PM*	20
GE MLI 097S	Received - GT Pkg - PPG ARR Inlet Plenum Drain Piping (GE M	0		10/1/27 5:00 PM*	20
GE MLI 099S	Received - GT Pkg - PPG ARR Fire Protection EXH Compt Hard	0		10/1/27 5:00 PM*	20
GE MLI 099S	Received - GT Pkg - PPG ARR Fire Protection EXH Compt Supp	0		10/1/27 5:00 PM*	20
GE MLI 099S	Received - GT Pkg - PPG ARR Fire Protection EXH Compt Tubir	0		10/1/27 5:00 PM*	20
GE MLI 901E	Received - GT Pkg - PPG Liquid Fuel Emulsion Hardware (GE M	0		10/1/27 5:00 PM*	20
GE MLI 901E	Received - GT Pkg - PPG Liquid Fuel Emulsion Piping (GE MLI	0		10/1/27 5:00 PM*	20
GE MLI 901E	Received - GT Pkg - PPG Liquid Fuel Emulsion Supports (GE M	0		10/1/27 5:00 PM*	20
GE MLI 901E	Received - GT Pkg - PPG Liquid Fuel Emulsion Tubing (GE MLI	0		10/1/27 5:00 PM*	20
GE MLI 901E	Received - GT Pkg - PPG Liquid Fuel Emulsion Tubing (GE MLI	0		10/1/27 5:00 PM*	20

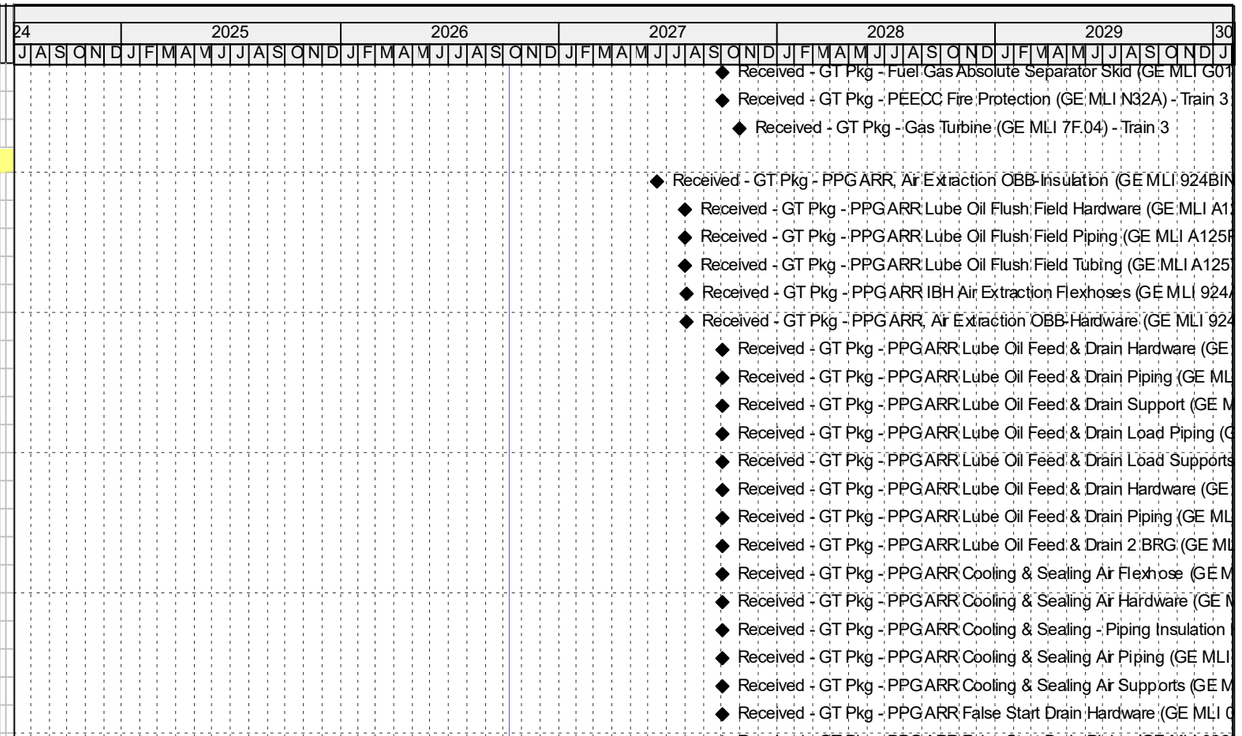

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI 901	Received - GT Pkg - PPG ARR Impingement Cooling Hardware	0		10/1/27 5:00 PM*	20
GE MLI 901	Received - GT Pkg - PP ARR Impgmnt Clg Casing Manifold (GE	0		10/1/27 5:00 PM*	20
GE MLI 901	Received - GT Pkg - PP ARR Impgmnt Clg Bendable Duct (GE I	0		10/1/27 5:00 PM*	20
GE MLI 901	Received - GT Pkg - PPG ARR Impingement Cooling Piping (GE	0		10/1/27 5:00 PM*	20
GE MLI 902	Received - GT Pkg - Hardwares, Piping Inlet Dehumidification (G	0		10/1/27 5:00 PM*	20
GE MLI 902	Received - GT Pkg - Piping, Inlet Dehumidification Piping (GE M	0		10/1/27 5:00 PM*	20
GE MLI 902	Received - GT Pkg - Piping, Inlet Dehumidification Support (GE	0		10/1/27 5:00 PM*	20
GE MLI 924	Received - GT Pkg - PPG ARR IBH Air Extraction Hardware (GE	0		10/1/27 5:00 PM*	20
GE MLI 924	Received - GT Pkg - PPG ARR IBH Air Extraction Insulation (GE	0		10/1/27 5:00 PM*	20
GE MLI 924	Received - GT Pkg - PPG ARR IBH Air Extraction Piping (GE ML	0		10/1/27 5:00 PM*	20
GE MLI 924	Received - GT Pkg - PPG ARR Air Extraction OBB Flexhose (GE	0		10/1/27 5:00 PM*	20
GE MLI 924	Received - GT Pkg - PPG ARR Air Extraction OBB Piping (GE M	0		10/1/27 5:00 PM*	20
GE MLI 924	Received - GT Pkg - PPG ARR Air Extraction OBB Supports (GE	0		10/1/27 5:00 PM*	20
GE MLI 924	Received - GT Pkg - PPG ARR, Air Extraction Flexhose (GE MLI	0		10/1/27 5:00 PM*	20
GE MLI 924	Received - GT Pkg - PPG ARR, Air Extraction Hardware (GE ML	0		10/1/27 5:00 PM*	20
GE MLI 924	Received - GT Pkg - PPG ARR, Air Extraction Piping (GE MLI 92	0		10/1/27 5:00 PM*	20
GE MLI 924	Received - GT Pkg - PPG ARR, Air Extraction Supports (GE MLI	0		10/1/27 5:00 PM*	20
GE MLI 924	Received - GT Pkg - PPG ARR, Air Extraction Tubing (GE MLI 9	0		10/1/27 5:00 PM*	20
GE MLI 969	Received - GT Pkg - INTC PPG Lube Oil Hardware (GE MLI 969	0		10/1/27 5:00 PM*	20
GE MLI 969	Received - GT Pkg - INTC PPG Lube Oil Piping (GE MLI 969AP	0		10/1/27 5:00 PM*	20
GE MLI 969	Received - GT Pkg - Piping ARR Gas Skid Flexhose (GE MLI 96	0		10/1/27 5:00 PM*	20
GE MLI 969	Received - GT Pkg - Piping ARR Gas Skid Hardware (GE MLI 96	0		10/1/27 5:00 PM*	20
GE MLI 969	Received - GT Pkg - Piping Insulation, Cooled Cooling Air (GE M	0		10/1/27 5:00 PM*	20
GE MLI 969	Received - GT Pkg - Piping ARR Gas Skid Piping (GE MLI 969G	0		10/1/27 5:00 PM*	20
GE MLI 969	Received - GT Pkg - PPG ARR INTC PPG Ctrl Oil Hardware (GE	0		10/1/27 5:00 PM*	20
GE MLI 969	Received - GT Pkg - PPG ARR INTC PPG Ctrl Oil Piping (GE ML	0		10/1/27 5:00 PM*	20
GE MLI A184	Received - GT Pkg - INTC PPG Inlet Heating Hardware (GE MLI	0		10/1/27 5:00 PM*	20
GE MLI A184	Received - GT Pkg - INTC PPG Inlet Heating Piping (GE MLI A1	0		10/1/27 5:00 PM*	20
GE MLI A184	Received - GT Pkg - INTC PPG Inlet Heating Support (GE MLI A	0		10/1/27 5:00 PM*	20
GE MLI A341	Received - GT Pkg - PPG ARR Duct Inlet Bleed Heating Hardwa	0		10/1/27 5:00 PM*	20
GE MLI A341	Received - GT Pkg - PPG ARR Duct Inlet Bleed Heating Piping (	0		10/1/27 5:00 PM*	20
GE MLI A341	Received - GT Pkg - PPG ARR Duct Inlet Bleed Heating Suppor	0		10/1/27 5:00 PM*	20
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,03,03 PRO - OFE / GE Provided - Gas Turbine - Train 3 - Valves					
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Valves (GE	0		8/2/27 7:00 AM*	64
GE MLI 0572	Received - GT Pkg - Fuel Gas Emergency Stop Valve (GE MLI (	0		10/1/27 5:00 PM*	20
GE MLI 0920	Received - GT Pkg - PPG ARR False Start Drain Valve (GE MLI	0		10/1/27 5:00 PM*	20
GE MLI 0953	Received - GT Pkg - Valve Kit Part (GE MLI 0953VV) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI 1022	Received - GT Pkg - Compressor Bleed Valve (GE MLI 1022) - T	0		10/1/27 5:00 PM*	20
GE MLI 1026	Received - GT Pkg - Valves, Regulator False Start Drain (GE ML	0		10/1/27 5:00 PM*	20
GE MLI 1087	Received - GT Pkg - Valves (GE MLI 1087VV) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI 510	Received - GT Pkg - Drains Module Valves (GE MLI 510C) - Trai	0		10/1/27 5:00 PM*	20
GE MLI 924	Received - GT Pkg - PPG ARR, Air Extraction Valves (GE MLI 9	0		10/1/27 5:00 PM*	20
GE MLI 924	Received - GT Pkg - PPG ARR, Air Extraction Valves (GE MLI 9	0		10/1/27 5:00 PM*	20
GE MLI 969	Received - GT Pkg - Valve, INTC Lube Oil (GE MLI 969AVV) - Tr	0		10/1/27 5:00 PM*	20
GE MLI A037	Received - GT Pkg - Inlet Bleed Heat Valve (GE MLI A037) - Tra	0		10/1/27 5:00 PM*	20
GE MLI A278	Received - GT Pkg - Valves CTM CTRL Stop (GE MLI A278) - Tr	0		10/1/27 5:00 PM*	20
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,03,04 PRO - OFE / GE Provided - Gas Turbine - Train 3 - Misc					
GE MLI 1603	Received - GT Pkg - Foundation Bolting Arrangement (GE MLI	0		8/2/27 7:00 AM*	64
GE MLI 1604	Received - GT Pkg - Bolting & Doweling ARR (GE MLI 1604) - Tr	0		8/2/27 7:00 AM*	64
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Misc (GE MI	0		8/2/27 7:00 AM*	64



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI A209	Received - GT Pkg - Universal On Site Monitoring (GE MLI A209	0		8/2/27 7:00 AM*	64
GE MLI A258	Received - GT Pkg - Station, Vibration Analysis (GE MLI A258) -	0		8/2/27 7:00 AM*	64
GE MLI A315	Received - GT Pkg - TCP Aux Panel For Gas Chromatograph (G	0		8/2/27 7:00 AM*	64
GE MLI A33D	Received - GT Pkg - Major Inspection : Tool Kit For GT Casing D	0		8/2/27 7:00 AM*	64
GE MLI A33H	Received - GT Pkg - Basic Tool Kit & Cart (GE MLI A33H) - Train	0		8/2/27 7:00 AM*	64
GE MLI A33I	Received - GT Pkg - Hydraulic Torque Wrench For GT Casing Di	0		8/2/27 7:00 AM*	64
GE MLI A33J	Received - GT Pkg - Hydraulic Tensioner (GE MLI A33J) - Train 3	0		8/2/27 7:00 AM*	64
GE MLI A33K	Received - GT Pkg - Lifting Beam GT Rotor Plus Guides (GE MI	0		8/2/27 7:00 AM*	64
GE MLI 1121	Received - GT Pkg - Flame Detector (GE MLI 1121) - Train 3	0		8/2/27 5:00 PM*	63
GE MLI 1261	Received - GT Pkg - Combustion Dynamics Monitoring (GE MLI	0		8/2/27 5:00 PM*	63
GE MLI 595A	Received - GT Pkg - Emuls Fuel Solenoid Assy (GE MLI 595A) -	0		8/2/27 5:00 PM*	63
GE MLI A273	Received - GT Pkg - Watermist Fire Protection Skid (GE MLI A2	0		8/2/27 5:00 PM*	63
GE MLI 1647	Received - GT Pkg - Damper Door (GE MLI 1647) - Train 3	0		9/13/27 5:00 PM*	34
GE MLI 0585	Received - GT Pkg - Panel, Gas Detector (GE MLI 0585) - Train	0		9/30/27 5:00 PM*	21
GE MLI 0401	Received - GT Pkg - Wire List Field Wiring (GE MLI 0401) - Trai	0		10/1/27 5:00 PM*	20
GE MLI 0623	Received - GT Pkg - Exhaust Thermocouple (GE MLI 0623) - Tr	0		10/1/27 5:00 PM*	20
GE MLI 0706	Received - GT Pkg - Diffuser Assy, Exhaust (GE MLI 0706) - Tra	0		10/1/27 5:00 PM*	20
GE MLI 0726	Received - GT Pkg - Dynamics Monitor Combustion (GE MLI 07	0		10/1/27 5:00 PM*	20
GE MLI 0953	Received - GT Pkg - Support Fab Kit Part (GE MLI 0953SU) - Tr	0		10/1/27 5:00 PM*	20
GE MLI 0953	Received - GT Pkg - Tubing Kit Part (GE MLI 0953TU) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI 0962	Received - GT Pkg - Support Kit (GE MLI 0962SU) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI 0987	Received - GT Pkg - Tubing ARR, Performance Monitoring (GE I	0		10/1/27 5:00 PM*	20
GE MLI 1049	Received - GT Pkg - Inlet Dehumidification (GE MLI 1049) - GA(	0		10/1/27 5:00 PM*	20
GE MLI 1087	Received - GT Pkg - Hardware (GE MLI 1087HW) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI 1155	Received - GT Pkg - Junction Box AR (GE MLI 1155) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI 1213	Received - GT Pkg - Transformer, PWR Stepup, LGN (GE MLI 1	0		10/1/27 5:00 PM*	20
GE MLI 1309	Received - GT Pkg - Load Coupling Hardware Kit (GE MLI 1309	0		10/1/27 5:00 PM*	20
GE MLI 1311	Received - GT Pkg - Load Coupling Guard Assembly (GE MLI 1	0		10/1/27 5:00 PM*	20
GE MLI 1319	Received - GT Pkg - Rigid Load Coupling Machining (GE MLI 13	0		10/1/27 5:00 PM*	20
GE MLI 1323	Received - GT Pkg - Load Coupling Tooling Kit (GE MLI 1323) -	0		10/1/27 5:00 PM*	20
GE MLI 1612	Received - GT Pkg - Inlet Plenum Assembly (GE MLI 1612) - Tra	0		10/1/27 5:00 PM*	20
GE MLI 1627	Received - GT Pkg - Acoustic Barrier Wall (GE MLI 1627) - Train	0		10/1/27 5:00 PM*	20
GE MLI 1635	Received - GT Pkg - Duct Assy, External CLG & SLG Air (GE ML	0		10/1/27 5:00 PM*	20
GE MLI 1643	Received - GT Pkg - Ventilation Fans For Enclosures (GE MLI 1(	0		10/1/27 5:00 PM*	20
GE MLI 1645	Received - GT Pkg - Floorunit Grating ARR (GE MLI 1645) - Trai	0		10/1/27 5:00 PM*	20
GE MLI 1652	Received - GT Pkg - Ladder T/C Access (GE MLI 1652) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI 557A	Received - GT Pkg - Turbine Transmitter Arrangement (GE MLI	0		10/1/27 5:00 PM*	20
GE MLI 557T	Received - GT Pkg - Transducer Arrangement (GE MLI 557T) - T	0		10/1/27 5:00 PM*	20
GE MLI 9010	Received - GT Pkg - 9010 Hardware (GE MLI 9010HW) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI 9010	Received - GT Pkg - 9010 Suppport (GE MLI 9010SU) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Misc (GE MLI 9(	0		10/1/27 5:00 PM*	20
GE MLI 969A	Received - GT Pkg - Supports, INTC Lube Oil (GE MLI 969ASU	0		10/1/27 5:00 PM*	20
GE MLI 969M	Received - GT Pkg - Supports 969M (GE MLI 969MSU) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI A035	Received - GT Pkg - Water Injection Module (Pumping Skid) (GE	0		10/1/27 5:00 PM*	20
GE MLI A041	Received - GT Pkg - Inlet Duct Assembly (GE MLI A041) - Train	0		10/1/27 5:00 PM*	20
GE MLI A042	Received - GT Pkg - Exhaust Diffuser General ARR (GE MLI A04	0		10/1/27 5:00 PM*	20
GE MLI A070	Received - GT Pkg - Filter Elementair Inlet (GE MLI A070) - Trai	0		10/1/27 5:00 PM*	20
GE MLI A122	Received - GT Pkg - Humidity Sensory (GE MLI A122) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI A151	Received - GT Pkg - External Insulation (GE MLI A151) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI A179	Received - GT Pkg - Strainer Field Temporary (GE MLI A179) - T	0		10/1/27 5:00 PM*	20




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI A252	Received - GT Pkg - Consumables LO Flush (GE MLI A252) - Tr	0		10/1/27 5:00 PM*	20
GE MLI A40T	Received - GT Pkg - Inlet System Caulk (GE MLI A40T) - Train 3	0		10/1/27 5:00 PM*	20
GE MLI A980	Received - GT Pkg - Inlet Support Structure (GE MLI A980) - Tra	0		10/1/27 5:00 PM*	20
GE MLI A998	Received - GT Pkg - KKS Hardware Tags For Unit-3 (GE MLI A9	0		10/1/27 5:00 PM*	20
GE MLI MSS	Received - GT Pkg - Gt Summary Sheet Container (GE MLI MS	0		10/1/27 5:00 PM*	20
GE MLI N32(	Received - GT Pkg - Lci Compartment Fire Protection (GE MLI N	0		10/1/27 5:00 PM*	20
GE MLI QCF	Received - GT Pkg - Touchup Paint (GE MLI QCF0) - Train 3	0		10/1/27 5:00 PM*	20
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,04 PRO - OFE / GE Provided - Gas Turbine - Train 4					
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,04,01 PRO - OFE / GE Provided - Gas Turbine - Train 4 - Equip					
GE MLI G02	Received - GT Pkg - Fuel Gas Chromatograph (GE MLI G023) -	0		8/2/27 7:00 AM*	85
GE MLI A13(	Received - GT Pkg - APU (Air Processing Unit) (GE MLI A130) -	0		10/11/27 5:00 PM*	35
GE MLI 063	Received - GT Pkg - Fuel Gas Coriolis Flow Meter (GE MLI 063	0		11/1/27 7:00 AM*	21
GE MLI 099	Received - GT Pkg - Liquid Fuel Module (Pump) (GE MLI 0992)	0		11/1/27 7:00 AM*	21
GE MLI 161	Received - GT Pkg - Load Compartment Enclosure Assembly (G	0		11/1/27 7:00 AM*	21
GE MLI 163	Received - GT Pkg - Enclosure, Gas Turbine (GE MLI 1634) - Tr	0		11/1/27 7:00 AM*	21
GE MLI 164	Received - GT Pkg - Overhead Travel Crane (GE MLI 1648) - Tra	0		11/1/27 7:00 AM*	21
GE MLI A04(	Received - GT Pkg - Inlet Filter House (GE MLI A040) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI A132	Received - GT Pkg - Cooling Fan Module (GE MLI A132) - Train	0		11/1/27 7:00 AM*	21
GE MLI A16(	Received - GT Pkg - Oil & Gas Accessory Module (GE MLI A16(	0		11/1/27 7:00 AM*	21
GE MLI A29	Received - GT Pkg - LF Emulsion Control Skid (GE MLI A295) -	0		11/1/27 7:00 AM*	21
GE MLI A40F	Received - GT Pkg - Inlet Filter House Evaporative Cooler ME (G	0		11/1/27 7:00 AM*	21
GE MLI G01	Received - GT Pkg - Fuel Gas Absolute Separator Skid (GE MLI	0		11/1/27 7:00 AM*	21
GE MLI N32/	Received - GT Pkg - PEECC Fire Protection (GE MLI N32A) - Tra	0		11/1/27 7:00 AM*	21
GE MLI A07(	Received - GT Pkg - CWM (Cooling Water Modules Unit) (GE M	0		11/1/27 5:00 PM*	20
GE MLI 7F.0	Received - GT Pkg - Gas Turbine (GE MLI 7F.04) - Train 4	0		11/30/27 5:00 PM*	0
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,04,02 PRO - OFE / GE Provided - Gas Turbine - Train 4 - Piping					
GE MLI 924E	Received - GT Pkg - PPG ARR, Air Extraction OBB-Insulation (G	0		6/14/27 7:00 AM*	119
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Hardware (G	0		8/2/27 7:00 AM*	85
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Piping (GE I	0		8/2/27 7:00 AM*	85
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Tubing (GE	0		8/2/27 7:00 AM*	85
GE MLI 924A	Received - GT Pkg - PPG ARR IBH Air Extraction Flexhoses (GE	0		9/1/27 5:00 PM*	62
GE MLI 924E	Received - GT Pkg - PPG ARR, Air Extraction OBB-Hardware (G	0		9/1/27 5:00 PM*	62
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Hardware	0		11/1/27 7:00 AM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Piping (GI	0		11/1/27 7:00 AM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Support (	0		11/1/27 7:00 AM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Load Pipi	0		11/1/27 7:00 AM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Load Sup	0		11/1/27 7:00 AM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Hardware	0		11/1/27 7:00 AM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain Piping (GI	0		11/1/27 7:00 AM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Lube Oil Feed & Drain 2 BRG (G	0		11/1/27 7:00 AM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Cooling & Sealing Air Flexhose (	0		11/1/27 7:00 AM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Cooling & Sealing Air Hardware (	0		11/1/27 7:00 AM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Cooling & Sealing - Piping Insula	0		11/1/27 7:00 AM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Cooling & Sealing Air Piping (GE	0		11/1/27 7:00 AM*	21
GE MLI 090	Received - GT Pkg - PPG ARR Cooling & Sealing Air Supports (	0		11/1/27 7:00 AM*	21
GE MLI 092(	Received - GT Pkg - PPG ARR False Start Drain Hardware (GE I	0		11/1/27 7:00 AM*	21
GE MLI 092(	Received - GT Pkg - PPG ARR False Start Drain Piping (GE MLI	0		11/1/27 7:00 AM*	21
GE MLI 092(	Received - GT Pkg - PPG ARR, False Start Drain Supports (GE I	0		11/1/27 7:00 AM*	21
GE MLI 092(	Received - GT Pkg - PPG ARR False Start Drain Tubing (GE ML	0		11/1/27 7:00 AM*	21
GE MLI 095	Received - GT Pkg - PPG, Comprwash Hardware (GE MLI 0953	0		11/1/27 7:00 AM*	21

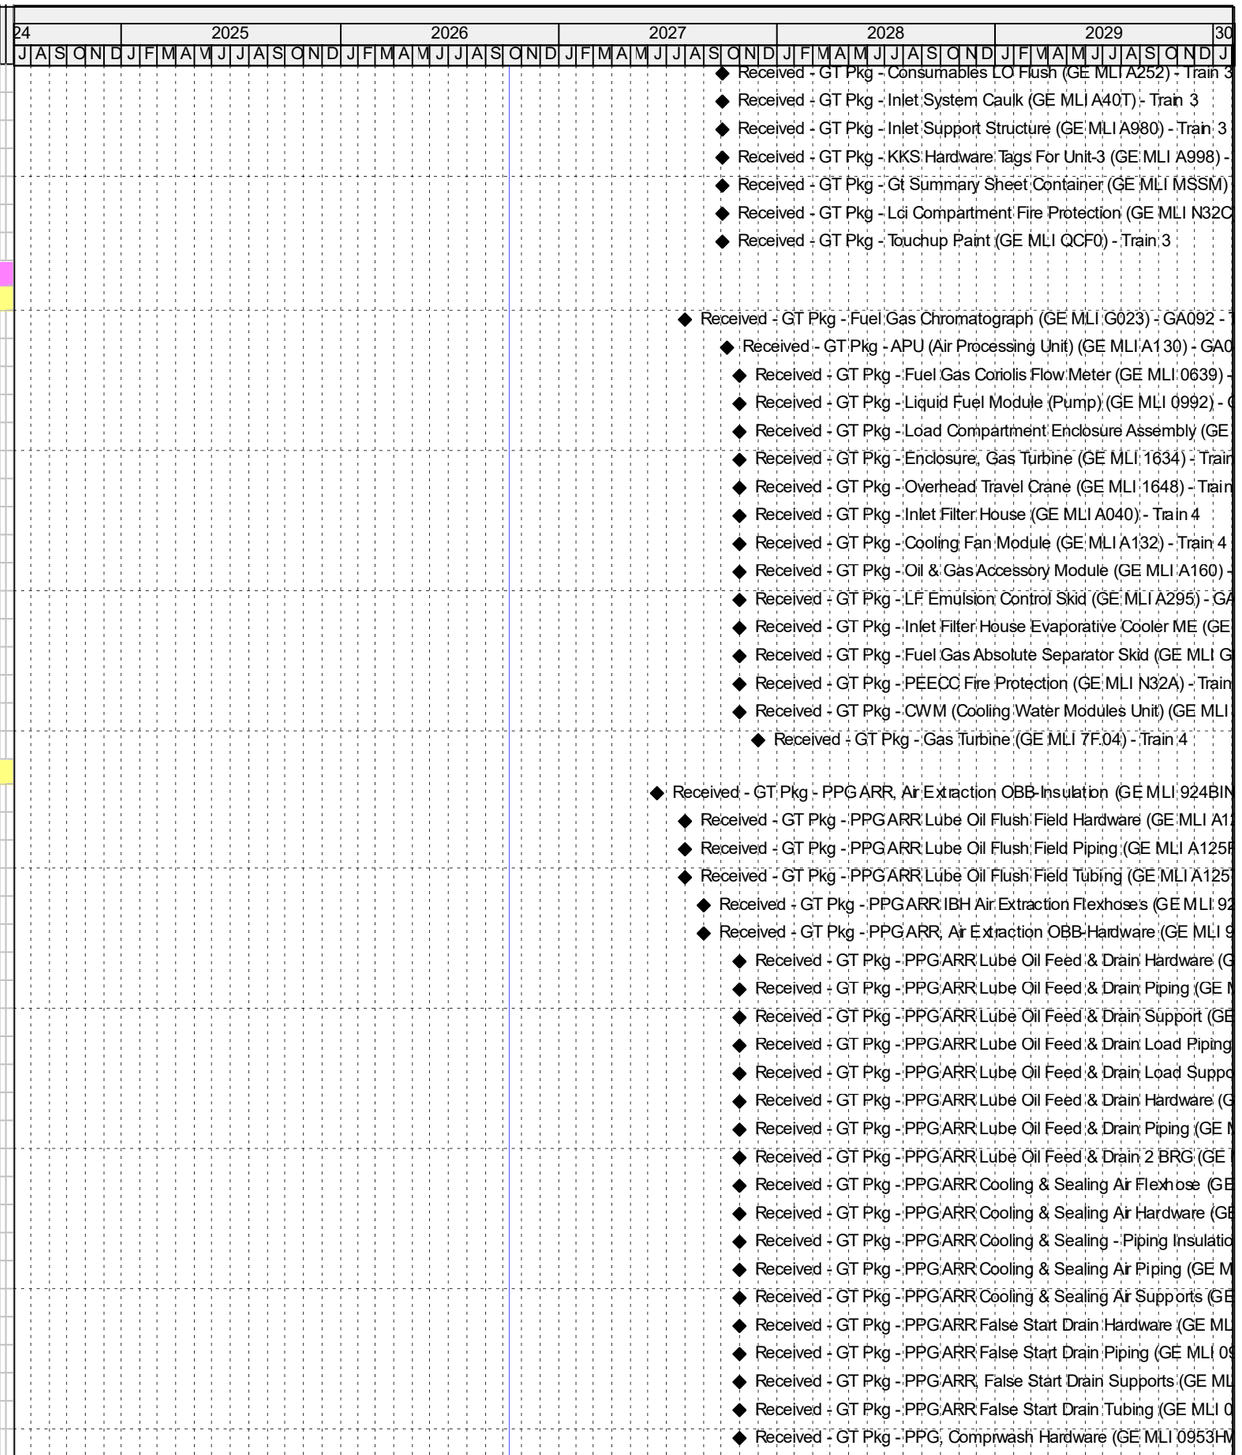

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI 0953	Received - GT Pkg - PPG, Comprwash Piping (GE MLI 0953PG	0		11/1/27 7:00 AM*	21
GE MLI 0962	Received - GT Pkg - PPG ARR Fuel Gas Turb Sysflexhose (GE I	0		11/1/27 7:00 AM*	21
GE MLI 0962	Received - GT Pkg - PPG ARR Fuel Gas Turb Syshardware (GE	0		11/1/27 7:00 AM*	21
GE MLI 0962	Received - GT Pkg - PPG ARR Fuel Gas Turb Syspiping (GE ML	0		11/1/27 7:00 AM*	21
GE MLI 0964	Received - GT Pkg - PPG ARR Fire Prot GT Compt Hardware (G	0		11/1/27 7:00 AM*	21
GE MLI 0964	Received - GT Pkg - PPG ARR Fire Prot GT Compt Supports (GI	0		11/1/27 7:00 AM*	21
GE MLI 0964	Received - GT Pkg - PPG ARR Fire Prot GT Compt Tubing (GE I	0		11/1/27 7:00 AM*	21
GE MLI 0972	Received - GT Pkg - PPG ARR Cooling Air EXH FR Flexhose (GI	0		11/1/27 7:00 AM*	21
GE MLI 0972	Received - GT Pkg - PPG ARR Cooling Air EXH FR Hardware (G	0		11/1/27 7:00 AM*	21
GE MLI 0972	Received - GT Pkg - PPG ARR Cooling Air EXH FR Piping (GE M	0		11/1/27 7:00 AM*	21
GE MLI 0976	Received - GT Pkg - PPG Exhaust Plenum Drain Hardware (GE	0		11/1/27 7:00 AM*	21
GE MLI 0976	Received - GT Pkg - PPG Exhaust Plenum Drain Piping (GE ML	0		11/1/27 7:00 AM*	21
GE MLI 0979	Received - GT Pkg - PPG ARR Inlet Plenum Drain (GE MLI 097	0		11/1/27 7:00 AM*	21
GE MLI 0979	Received - GT Pkg - PPG ARR Inlet Plenum Drain Piping (GE M	0		11/1/27 7:00 AM*	21
GE MLI 0995	Received - GT Pkg - PPG ARR Fire Protection EXH Compt Hard	0		11/1/27 7:00 AM*	21
GE MLI 0995	Received - GT Pkg - PPG ARR Fire Protection EXH Compt Supp	0		11/1/27 7:00 AM*	21
GE MLI 0995	Received - GT Pkg - PPG ARR Fire Protection EXH Compt Tubir	0		11/1/27 7:00 AM*	21
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Hardware (GE M	0		11/1/27 7:00 AM*	21
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Piping (GE MLI	0		11/1/27 7:00 AM*	21
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Supports (GE M	0		11/1/27 7:00 AM*	21
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Tubing (GE MLI	0		11/1/27 7:00 AM*	21
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Tubing (GE MLI	0		11/1/27 7:00 AM*	21
GE MLI 9019	Received - GT Pkg - PPG ARR Impingement Cooling Hardware	0		11/1/27 7:00 AM*	21
GE MLI 9019	Received - GT Pkg - PP ARR Impgmnt Clg Casing Manifold (GE	0		11/1/27 7:00 AM*	21
GE MLI 9019	Received - GT Pkg - PP ARR Impgmnt Clg Bendable Duct (GE I	0		11/1/27 7:00 AM*	21
GE MLI 9019	Received - GT Pkg - PPG ARR Impingement Cooling Piping (GE	0		11/1/27 7:00 AM*	21
GE MLI 9024	Received - GT Pkg - Hardwares, Piping Inlet Dehumidification (G	0		11/1/27 7:00 AM*	21
GE MLI 9024	Received - GT Pkg - Piping, Inlet Dehumidification Piping (GE M	0		11/1/27 7:00 AM*	21
GE MLI 9024	Received - GT Pkg - Piping, Inlet Dehumidification Support (GE	0		11/1/27 7:00 AM*	21
GE MLI 9247	Received - GT Pkg - PPG ARR IBH Air Extraction Hardware (GE	0		11/1/27 7:00 AM*	21
GE MLI 9247	Received - GT Pkg - PPG ARR IBH Air Extraction Insulation (GE	0		11/1/27 7:00 AM*	21
GE MLI 9247	Received - GT Pkg - PPG ARR IBH Air Extraction Piping (GE ML	0		11/1/27 7:00 AM*	21
GE MLI 9248	Received - GT Pkg - PPG ARR Air Extraction OBB Flexhose (GE	0		11/1/27 7:00 AM*	21
GE MLI 9248	Received - GT Pkg - PPG ARR Air Extraction OBB Piping (GE M	0		11/1/27 7:00 AM*	21
GE MLI 9248	Received - GT Pkg - PPG ARR Air Extraction OBB Supports (GE	0		11/1/27 7:00 AM*	21
GE MLI 9241	Received - GT Pkg - PPG ARR, Air Extraction Flexhose (GE MLI	0		11/1/27 7:00 AM*	21
GE MLI 9241	Received - GT Pkg - PPG ARR, Air Extraction Hardware (GE ML	0		11/1/27 7:00 AM*	21
GE MLI 9241	Received - GT Pkg - PPG ARR, Air Extraction Piping (GE MLI 92	0		11/1/27 7:00 AM*	21
GE MLI 9241	Received - GT Pkg - PPG ARR, Air Extraction Supports (GE MLI	0		11/1/27 7:00 AM*	21
GE MLI 9241	Received - GT Pkg - PPG ARR, Air Extraction Tubing (GE MLI 9	0		11/1/27 7:00 AM*	21
GE MLI 9694	Received - GT Pkg - INTC PPG Lube Oil Hardware (GE MLI 969	0		11/1/27 7:00 AM*	21
GE MLI 9694	Received - GT Pkg - INTC PPG Lube Oil Piping (GE MLI 969AP	0		11/1/27 7:00 AM*	21
GE MLI 9690	Received - GT Pkg - Piping ARR Gas Skid Flexhose (GE MLI 96	0		11/1/27 7:00 AM*	21
GE MLI 9690	Received - GT Pkg - Piping ARR Gas Skid Hardware (GE MLI 96	0		11/1/27 7:00 AM*	21
GE MLI 9690	Received - GT Pkg - Piping Insulation, Cooled Cooling Air (GE M	0		11/1/27 7:00 AM*	21
GE MLI 9690	Received - GT Pkg - Piping ARR Gas Skid Piping (GE MLI 969G	0		11/1/27 7:00 AM*	21
GE MLI 969M	Received - GT Pkg - PPG ARR INTC PPG Ctrl Oil Hardware (GE	0		11/1/27 7:00 AM*	21
GE MLI 969M	Received - GT Pkg - PPG ARR INTC PPG Ctrl Oil Piping (GE ML	0		11/1/27 7:00 AM*	21
GE MLI A184	Received - GT Pkg - INTC PPG Inlet Heating Hardware (GE MLI	0		11/1/27 7:00 AM*	21
GE MLI A184	Received - GT Pkg - INTC PPG Inlet Heating Piping (GE MLI A1	0		11/1/27 7:00 AM*	21




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI A184	Received - GT Pkg - INTC PPG Inlet Heating Support (GE MLI A	0		11/1/27 7:00 AM*	21
GE MLI A341	Received - GT Pkg - PPG ARR Duct Inlet Bleed Heating Hardwa	0		11/1/27 7:00 AM*	21
GE MLI A341	Received - GT Pkg - PPG ARR Duct Inlet Bleed Heating Piping (	0		11/1/27 7:00 AM*	21
GE MLI A341	Received - GT Pkg - PPG ARR Duct Inlet Bleed Heating Suppor	0		11/1/27 7:00 AM*	21
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,04,03 PRO - OFE / GE Provided - Gas Turbine - Train 4 - Valves					
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Valves (GE I	0		8/2/27 7:00 AM*	85
GE MLI 0572	Received - GT Pkg - Fuel Gas Emergency Stop Valve (GE MLI (	0		11/1/27 7:00 AM*	21
GE MLI 092(	Received - GT Pkg - PPG ARR False Start Drain Valve (GE MLI	0		11/1/27 7:00 AM*	21
GE MLI 095	Received - GT Pkg - Valve Kit Part (GE MLI 0953VV) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI 102	Received - GT Pkg - Compressor Bleed Valve (GE MLI 1022) - T	0		11/1/27 7:00 AM*	21
GE MLI 102(	Received - GT Pkg - Valves, Regulator False Start Drain (GE ML	0		11/1/27 7:00 AM*	21
GE MLI 1087	Received - GT Pkg - Valves (GE MLI 1087VV) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI 510(	Received - GT Pkg - Drains Module Valves (GE MLI 510C) - Trai	0		11/1/27 7:00 AM*	21
GE MLI 924E	Received - GT Pkg - PPG ARR, Air Extraction Valves (GE MLI 92	0		11/1/27 7:00 AM*	21
GE MLI 924I	Received - GT Pkg - PPG ARR, Air Extraction Valves (GE MLI 92	0		11/1/27 7:00 AM*	21
GE MLI 969A	Received - GT Pkg - Valve, INTC Lube Oil (GE MLI 969AVV) - Tr	0		11/1/27 7:00 AM*	21
GE MLI A037	Received - GT Pkg - Inlet Bleed Heat Valve (GE MLI A037) - Tra	0		11/1/27 7:00 AM*	21
GE MLI A278	Received - GT Pkg - Valves CTM CTRL Stop (GE MLI A278) - Tr	0		11/1/27 7:00 AM*	21
BH CNN-KPJV-MAST-LIVE,20,01,GE,02,04,04 PRO - OFE / GE Provided - Gas Turbine - Train 4 - Misc					
GE MLI A125	Received - GT Pkg - PPG ARR Lube Oil Flush Field Misc (GE MI	0		8/2/27 7:00 AM*	85
GE MLI A209	Received - GT Pkg - Universal On Site Monitoring (GE MLI A209	0		8/2/27 7:00 AM*	85
GE MLI A258	Received - GT Pkg - Station, Vibration Analysis (GE MLI A258) -	0		8/2/27 7:00 AM*	85
GE MLI A315	Received - GT Pkg - TCP Aux Panel For Gas Chromatograph (G	0		8/2/27 7:00 AM*	85
GE MLI A33I	Received - GT Pkg - Major Inspection : Tool Kit For GT Casing D	0		8/2/27 7:00 AM*	85
GE MLI A33H	Received - GT Pkg - Basic Tool Kit & Cart (GE MLI A33H) - Train	0		8/2/27 7:00 AM*	85
GE MLI A33I	Received - GT Pkg - Hydraulic Torque Wrench For GT Casing Di	0		8/2/27 7:00 AM*	85
GE MLI A33J	Received - GT Pkg - Hydraulic Tensioner (GE MLI A33J) - Train 4	0		8/2/27 7:00 AM*	85
GE MLI A33K	Received - GT Pkg - Lifting Beam GT Rotor Plus Guides (GE MI	0		8/2/27 7:00 AM*	85
GE MLI 1603	Received - GT Pkg - Foundation Bolting Arrangement (GE MLI	0		8/31/27 5:00 PM*	63
GE MLI 1604	Received - GT Pkg - Bolting & Doweling ARR (GE MLI 1604) - Tr	0		8/31/27 5:00 PM*	63
GE MLI 1121	Received - GT Pkg - Flame Detector (GE MLI 1121) - Train 4	0		9/1/27 5:00 PM*	62
GE MLI 1261	Received - GT Pkg - Combustion Dynamics Monitoring (GE MLI	0		9/1/27 5:00 PM*	62
GE MLI 595A	Received - GT Pkg - Emuls Fuel Solenoid Assy (GE MLI 595A) -	0		9/1/27 5:00 PM*	62
GE MLI 1647	Received - GT Pkg - Damper Door (GE MLI 1647) - Train 4	0		10/11/27 5:00 PM*	35
GE MLI 0585	Received - GT Pkg - Panel, Gas Detector (GE MLI 0585) - Train	0		10/28/27 5:00 PM*	22
GE MLI 0401	Received - GT Pkg - Wire List Field Wiring (GE MLI 0401) - Trai	0		11/1/27 7:00 AM*	21
GE MLI 0623	Received - GT Pkg - Exhaust Thermocouple (GE MLI 0623) - Tra	0		11/1/27 7:00 AM*	21
GE MLI 0706	Received - GT Pkg - Diffuser Assy, Exhaust (GE MLI 0706) - Tra	0		11/1/27 7:00 AM*	21
GE MLI 0726	Received - GT Pkg - Dynamics Monitor Combustion (GE MLI 07	0		11/1/27 7:00 AM*	21
GE MLI 0953	Received - GT Pkg - Support Fab Kit Part (GE MLI 0953SU) - Tr	0		11/1/27 7:00 AM*	21
GE MLI 0953	Received - GT Pkg - Tubing Kit Part (GE MLI 0953TU) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI 0962	Received - GT Pkg - Support Kit (GE MLI 0962SU) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI 0987	Received - GT Pkg - Tubing ARR, Performance Monitoring (GE I	0		11/1/27 7:00 AM*	21
GE MLI 1049	Received - GT Pkg - Inlet Dehumidification (GE MLI 1049) - GA(	0		11/1/27 7:00 AM*	21
GE MLI 1087	Received - GT Pkg - Hardware (GE MLI 1087HW) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI 1155	Received - GT Pkg - Junction Box AR (GE MLI 1155) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI 1213	Received - GT Pkg - Transformer, PWR Stepup, LGN (GE MLI 1	0		11/1/27 7:00 AM*	21
GE MLI 1309	Received - GT Pkg - Load Coupling Hardware Kit (GE MLI 1309	0		11/1/27 7:00 AM*	21
GE MLI 1311	Received - GT Pkg - Load Coupling Guard Assembly (GE MLI 1	0		11/1/27 7:00 AM*	21
GE MLI 1319	Received - GT Pkg - Rigid Load Coupling Machining (GE MLI 13	0		11/1/27 7:00 AM*	21

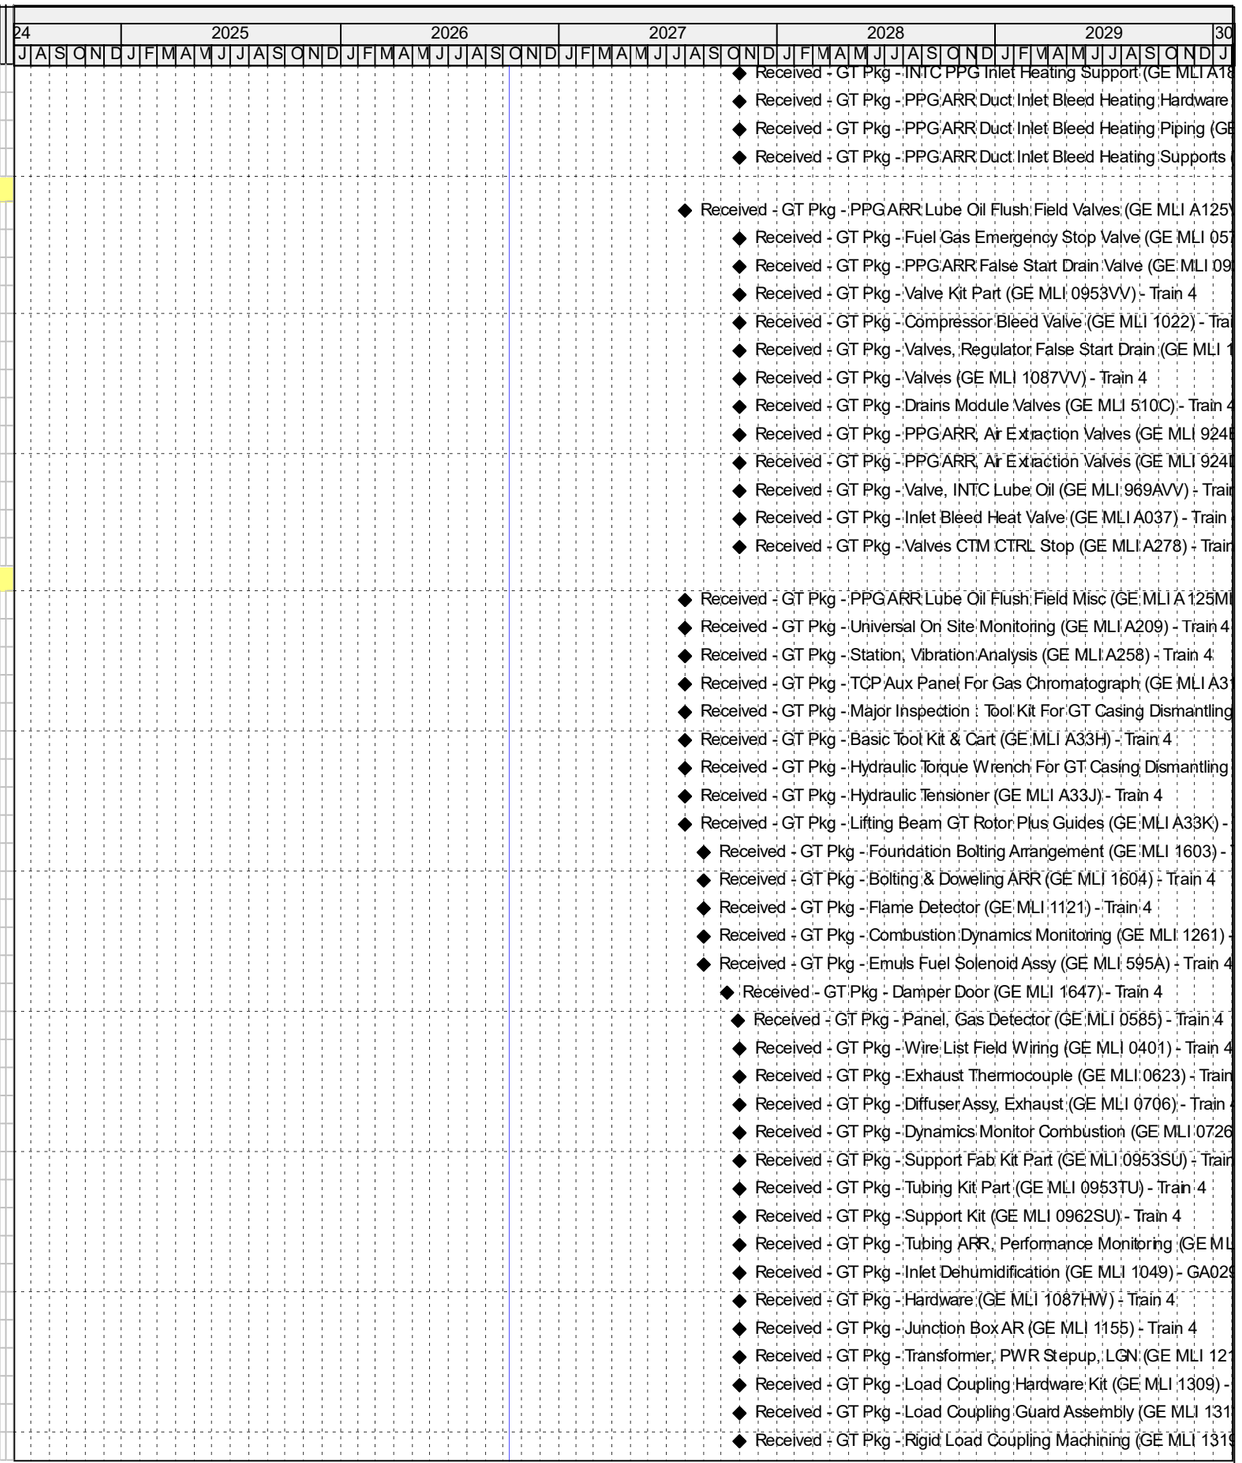


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
GE MLI 1323	Received - GT Pkg - Load Coupling Tooling Kit (GE MLI 1323) -	0		11/1/27 7:00 AM*	21
GE MLI 1612	Received - GT Pkg - Inlet Plenum Assembly (GE MLI 1612) - Tra	0		11/1/27 7:00 AM*	21
GE MLI 1627	Received - GT Pkg - Acoustic Barrier Wall (GE MLI 1627) - Train	0		11/1/27 7:00 AM*	21
GE MLI 1635	Received - GT Pkg - Duct Assy, External CLG & SLG Air (GE ML	0		11/1/27 7:00 AM*	21
GE MLI 1643	Received - GT Pkg - Ventilation Fans For Enclosures (GE MLI 1(	0		11/1/27 7:00 AM*	21
GE MLI 1645	Received - GT Pkg - Floorunit Grating ARR (GE MLI 1645) - Trai	0		11/1/27 7:00 AM*	21
GE MLI 1652	Received - GT Pkg - Ladder T/C Access (GE MLI 1652) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI 557A	Received - GT Pkg - Turbine Transmitter Arrangement (GE MLI	0		11/1/27 7:00 AM*	21
GE MLI 557T	Received - GT Pkg - Transducer Arrangement (GE MLI 557T) - T	0		11/1/27 7:00 AM*	21
GE MLI 9010	Received - GT Pkg - 9010 Hardware (GE MLI 9010HW) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI 9010	Received - GT Pkg - 9010 Suppport (GE MLI 9010SU) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI 9016	Received - GT Pkg - PPG Liquid Fuel Emulsion Misc (GE MLI 9(	0		11/1/27 7:00 AM*	21
GE MLI 969A	Received - GT Pkg - Supports, INTC Lube Oil (GE MLI 969ASU)	0		11/1/27 7:00 AM*	21
GE MLI 969M	Received - GT Pkg - Supports 969M (GE MLI 969MSU) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI A035	Received - GT Pkg - Water Injection Module (Pumping Skid) (GI	0		11/1/27 7:00 AM*	21
GE MLI A041	Received - GT Pkg - Inlet Duct Assembly (GE MLI A041) - Train	0		11/1/27 7:00 AM*	21
GE MLI A042	Received - GT Pkg - Exhaust Diffuser General ARR (GE MLI A04	0		11/1/27 7:00 AM*	21
GE MLI A070	Received - GT Pkg - Filter Elementair Inlet (GE MLI A070) - Trai	0		11/1/27 7:00 AM*	21
GE MLI A122	Received - GT Pkg - Humidity Sensory (GE MLI A122) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI A151	Received - GT Pkg - External Insulation (GE MLI A151) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI A179	Received - GT Pkg - Strainer Field Temporary (GE MLI A179) - T	0		11/1/27 7:00 AM*	21
GE MLI A252	Received - GT Pkg - Consumables LO Flush (GE MLI A252) - Tr	0		11/1/27 7:00 AM*	21
GE MLI A273	Received - GT Pkg - Watermist Fire Protection Skid (GE MLI A2	0		11/1/27 7:00 AM*	21
GE MLI A40T	Received - GT Pkg - Inlet System Caulk (GE MLI A40T) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI A998	Received - GT Pkg - KKS Hardware Tags For Unit-4 (GE MLI A9	0		11/1/27 7:00 AM*	21
GE MLI MSS	Received - GT Pkg - Gt Summary Sheet Container (GE MLI MS	0		11/1/27 7:00 AM*	21
GE MLI N32(	Received - GT Pkg - Lci Compartment Fire Protection (GE MLI M	0		11/1/27 7:00 AM*	21
GE MLI QCF	Received - GT Pkg - Touchup Paint (GE MLI QCF0) - Train 4	0		11/1/27 7:00 AM*	21
GE MLI A980	Received - GT Pkg - Inlet Support Structure (GE MLI A980) - Tra	0		11/1/27 5:00 PM*	20
BH CNN-KPJV-MAST-LIVE,20,01,GE,03 PRO - OFE / GE Provided - Control System					
GE MLI Q014H	Received - Plant Control System - PLANT CONTROL PANELS (	0		11/1/27 5:00 PM*	103
GE MLI Q014F	Received - Plant Control System - PANEL COMMISSIONING SF	0		11/1/27 5:00 PM*	149
GE MLI Q065-I	Received - Plant Control System - MARSHALLING PANELS (GE	0		11/1/27 5:00 PM*	103
GE MLI Q108A	Received - Plant Control System - HISTORIAN SERVERS SWIT	0		11/1/27 5:00 PM*	103
GE MLI Q108T	Received - Plant Control System - RACK PANEL (NETWORK PA	0		11/1/27 5:00 PM*	103
GE MLI Q109-I	Received - Plant Control System - CONSOLES (GE MLI Q109) -	0		11/1/27 5:00 PM*	103
GE MLI Q408-I	Received - Plant Control System - CYBER SECURITY (GE MLI (	0		11/1/27 5:00 PM*	103
GE MLI Q411-I	Received - Plant Control System - OPERATOR TRAINING SIMU	0		11/1/27 5:00 PM*	103
GE MLI Q508-I	Received - Plant Control System - REMOTE OPERATION (GE M	0		11/1/27 5:00 PM*	103
BH CNN-KPJV-MAST-LIVE,20,01,SCR PRO - OFE / NOOTER Provided - SCR (Selective Catalytic Reduction)					
KPA.MS.NT.100	Received - MS - All Nooter - SCR - Train 1	0		4/15/27 5:00 PM	285
KPA.MS.NT.100	Received - MS - All Nooter - SCR - Train 2	0		4/15/27 5:00 PM	302
KPA.MS.NT.101	Received - MS - All Nooter - SCR - Train 3	0		5/4/27 5:00 PM	300
KPA.MS.NT.101	Received - MS - All Nooter - SCR - Train 4	0		5/4/27 5:00 PM	315
BH CNN-KPJV-MAST-LIVE,20,01,SCR,01 PRO - OFE - SCR - Mix Duct & Lances					
KPA.OFE.SCR	Received - OFE SCR Mixing Duct & Lances - Train 1 Milestone	0		12/16/26 5:00 PM	288
KPA.OFE.SCR	Received - OFE SCR Mixing Duct & Lances - Train 2 Milestone	0		1/11/27 5:00 PM	277
KPA.OFE.SCR	Received - OFE SCR Mixing Duct & Lances - Train 3 Milestone	0		1/29/27 5:00 PM	233
KPA.OFE.SCR	Received - OFE SCR Mixing Duct & Lances - Train 4 Milestone	0		2/12/27 5:00 PM	212
BH CNN-KPJV-MAST-LIVE,20,01,SCR,02 PRO - OFE - SCR - Inlet Duct with Distribution Grids					

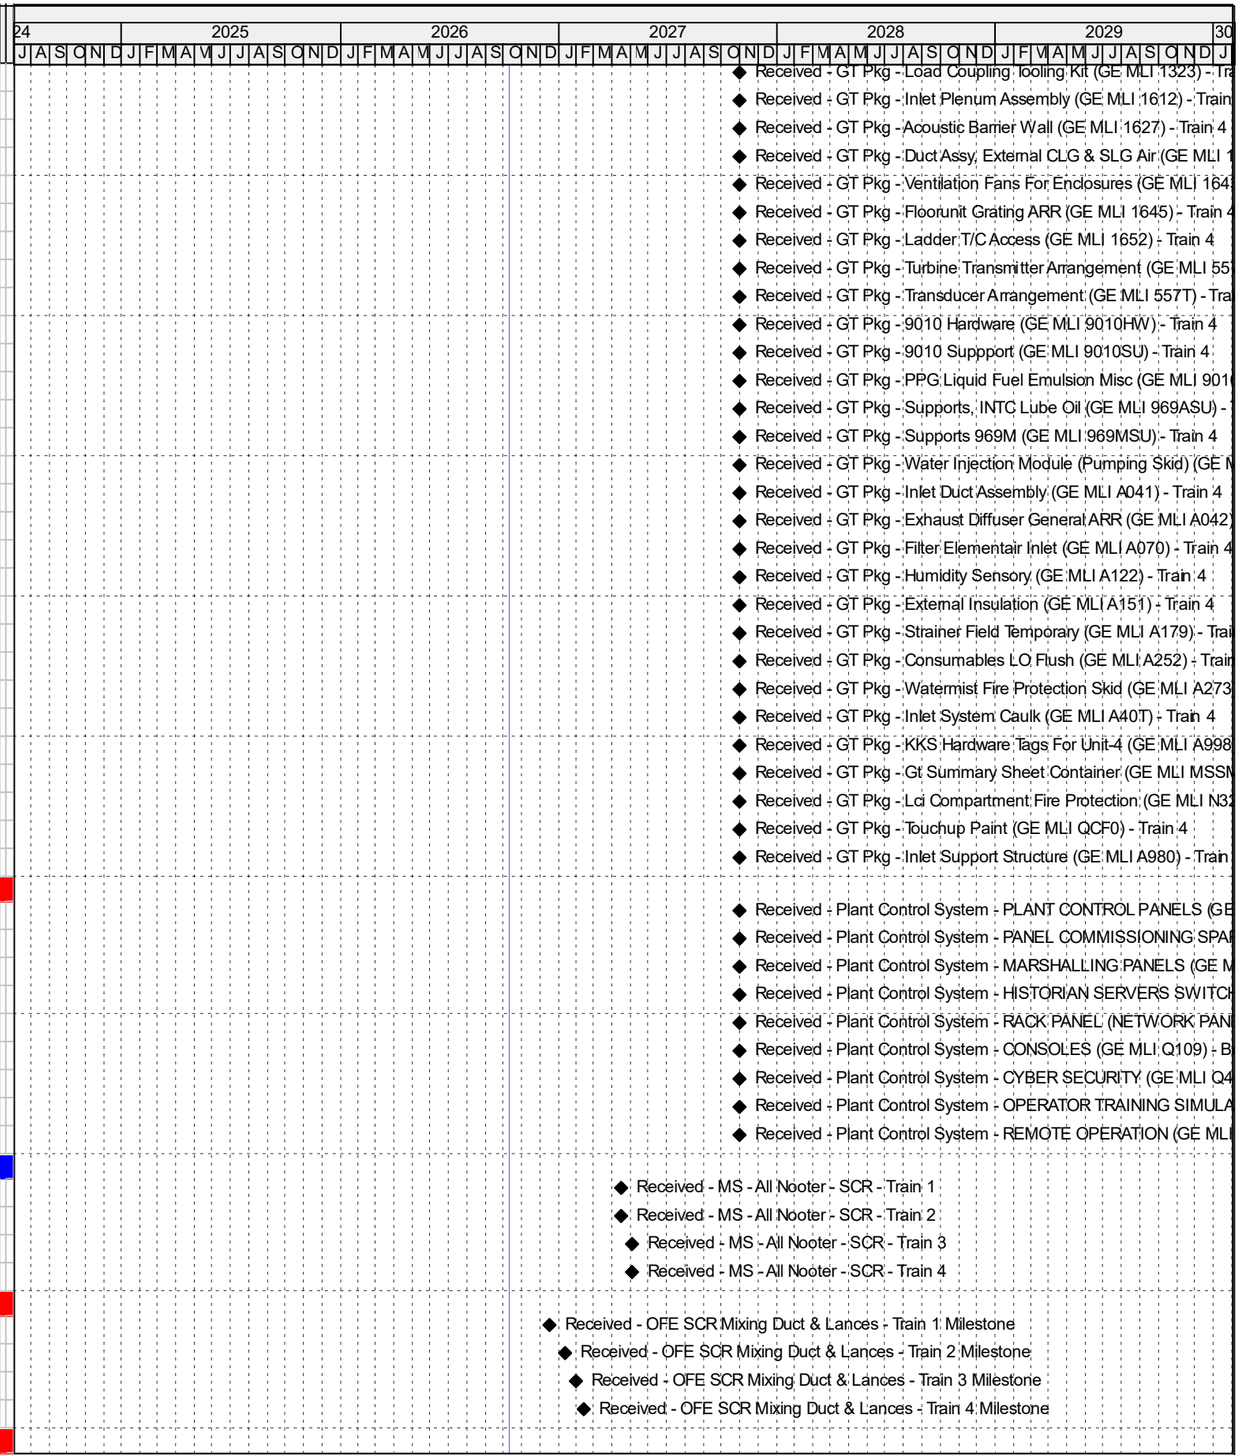


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.OFE.SCR.	Received - OFE SCR Inlet Duct with Distribution Grids - Train 1 M	0		12/15/26 5:00 PM	289
KPA.OFE.SCR.	Received - OFE SCR Inlet Duct with Distribution Grids - Train 2 M	0		12/31/26 5:00 PM	283
KPA.OFE.SCR.	Received - OFE SCR Inlet Duct with Distribution Grids - Train 3 M	0		1/28/27 5:00 PM	234
KPA.OFE.SCR.	Received - OFE SCR Inlet Duct with Distribution Grids - Train 4 M	0		2/16/27 5:00 PM	211
BH CNN-KPJV-MAST-LIVE,20,01,SCR,03 PRO - OFE - SCR - SCR Duct					
KPA.OFE.SCR.	Received - OFE SCR Duct - Train 1 Milestone	0		12/15/26 5:00 PM	289
KPA.OFE.SCR.	Received - OFE SCR Duct - Train 2 Milestone	0		1/8/27 5:00 PM	278
KPA.OFE.SCR.	Received - OFE SCR Duct - Train 3 Milestone	0		2/1/27 5:00 PM	232
KPA.OFE.SCR.	Received - OFE SCR Duct - Train 4 Milestone	0		2/17/27 5:00 PM	210
BH CNN-KPJV-MAST-LIVE,20,01,SCR,04 PRO - OFE - SCR - Tempering Air Duct From Fans					
KPA.OFE.SCR.	Received - OFE SCR Tempering Air Duct - Train 1 Milestone	0		12/15/26 5:00 PM	289
KPA.OFE.SCR.	Received - OFE SCR Tempering Air Duct - Train 2 Milestone	0		1/8/27 5:00 PM	278
KPA.OFE.SCR.	Received - OFE SCR Tempering Air Duct - Train 3 Milestone	0		1/29/27 5:00 PM	233
KPA.OFE.SCR.	Received - OFE SCR Tempering Air Duct - Train 4 Milestone	0		2/16/27 5:00 PM	211
BH CNN-KPJV-MAST-LIVE,20,01,SCR,05 PRO - OFE - SCR - CO System					
KPA.OFE.SCR.	Received - OFE SCR CO Support Frames - Train 1 Milestone	0		12/15/26 5:00 PM	289
KPA.OFE.SCR.	Received - OFE SCR CO Support Frames - Train 2 Milestone	0		1/8/27 5:00 PM	278
KPA.OFE.SCR.	Received - OFE SCR CO Support Frames - Train 3 Milestone	0		1/29/27 5:00 PM	233
KPA.OFE.SCR.	Received - OFE SCR CO Support Frames - Train 4 Milestone	0		2/16/27 5:00 PM	211
KPA.OFE.SCR.	Received - OFE SCR CO Catalyst - Train 1 Milestone	0		1/31/28 5:00 PM	84
KPA.OFE.SCR.	Received - OFE SCR CO Catalyst - Train 2 Milestone	0		1/31/28 5:00 PM	92
KPA.OFE.SCR.	Received - OFE SCR CO Catalyst - Train 3 Milestone	0		1/31/28 5:00 PM	81
KPA.OFE.SCR.	Received - OFE SCR CO Catalyst - Train 4 Milestone	0		1/31/28 5:00 PM	64
BH CNN-KPJV-MAST-LIVE,20,01,SCR,06 PRO - OFE - SCR - NH3 System					
KPA.OFE.SCR.	Received - OFE SCR NH3 SCR Support Frames - Train 1 Milest	0		12/16/26 5:00 PM	288
KPA.OFE.SCR.	Received - OFE SCR NH3 SCR Support Frames - Train 2 Milest	0		1/11/27 5:00 PM	277
KPA.OFE.SCR.	Received - OFE SCR NH3 AFCU Skid - Train 1 Milestone	0		2/1/27 5:00 PM	337
KPA.OFE.SCR.	Received - OFE SCR NH3 AFCU Skid - Train 2 Milestone	0		2/1/27 5:00 PM	354
KPA.OFE.SCR.	Received - OFE SCR NH3 SCR Support Frames - Train 3 Milest	0		2/2/27 5:00 PM	231
KPA.OFE.SCR.	Received - OFE SCR NH3 SCR Support Frames - Train 4 Milest	0		2/17/27 5:00 PM	210
KPA.OFE.SCR.	Received - OFE SCR NH3 AFCU Skid - Train 3 Milestone	0		3/1/27 5:00 PM	346
KPA.OFE.SCR.	Received - OFE SCR NH3 AFCU Skid - Train 4 Milestone	0		3/1/27 5:00 PM	361
KPA.OFE.SCR.	Received - OFE SCR NH3 SCR Manifold w/Piping - Train 1 Miles	0		3/1/27 5:00 PM	151
KPA.OFE.SCR.	Received - OFE SCR NH3 SCR Manifold w/Piping - Train 2 Miles	0		3/1/27 5:00 PM	162
KPA.OFE.SCR.	Received - OFE SCR NH3 A/G Assemblies & Piping - Train 1 Mil	0		4/1/27 5:00 PM	128
KPA.OFE.SCR.	Received - OFE SCR NH3 SCR Manifold w/Piping - Train 3 Miles	0		4/1/27 5:00 PM	169
KPA.OFE.SCR.	Received - OFE SCR NH3 SCR Manifold w/Piping - Train 4 Miles	0		4/1/27 5:00 PM	144
KPA.OFE.SCR.	Received - OFE SCR NH3 A/G Assemblies & Piping - Train 2 Mil	0		4/2/27 5:00 PM	138
KPA.OFE.SCR.	Received - OFE SCR NH3 A/G Assemblies & Piping - Train 4 Mil	0		5/3/27 5:00 PM	122
KPA.OFE.SCR.	Received - OFE SCR NH3 A/G Assemblies & Piping - Train 3 Mil	0		5/4/27 5:00 PM	146
BH CNN-KPJV-MAST-LIVE,20,01,SCR,30 PRO - OFE - SCR - SCR Catalyst					
KPA.OFE.SCR(	Received - OFE SCR Catalyst - SCR - Train 1 Milestone	0		1/31/28 5:00 PM	84
KPA.OFE.SCR(	Received - OFE SCR Catalyst - SCR - Train 2 Milestone	0		1/31/28 5:00 PM	92
KPA.OFE.SCR(	Received - OFE SCR Catalyst - SCR - Train 3 Milestone	0		1/31/28 5:00 PM	81
KPA.OFE.SCR(	Received - OFE SCR Catalyst - SCR - Train 4 Milestone	0		1/31/28 5:00 PM	17
BH CNN-KPJV-MAST-LIVE,20,01,SCR,07 PRO - OFE - SCR - Exhaust Stack Expansion Joints					
KPA.OFE.SCR.	Received - OFE SCR Exhaust Stack Expansion Joints - Train 1 I	0		4/2/27 5:00 PM	294
KPA.OFE.SCR.	Received - OFE SCR Exhaust Stack Expansion Joints - Train 2 I	0		4/2/27 5:00 PM	311
KPA.OFE.SCR.	Received - OFE SCR Exhaust Stack Expansion Joints - Train 3 I	0		5/4/27 5:00 PM	300
KPA.OFE.SCR.	Received - OFE SCR Exhaust Stack Expansion Joints - Train 4 I	0		5/4/27 5:00 PM	315
BH CNN-KPJV-MAST-LIVE,20,01,SCR,08 PRO - OFE - SCR - Exhaust Stacks					

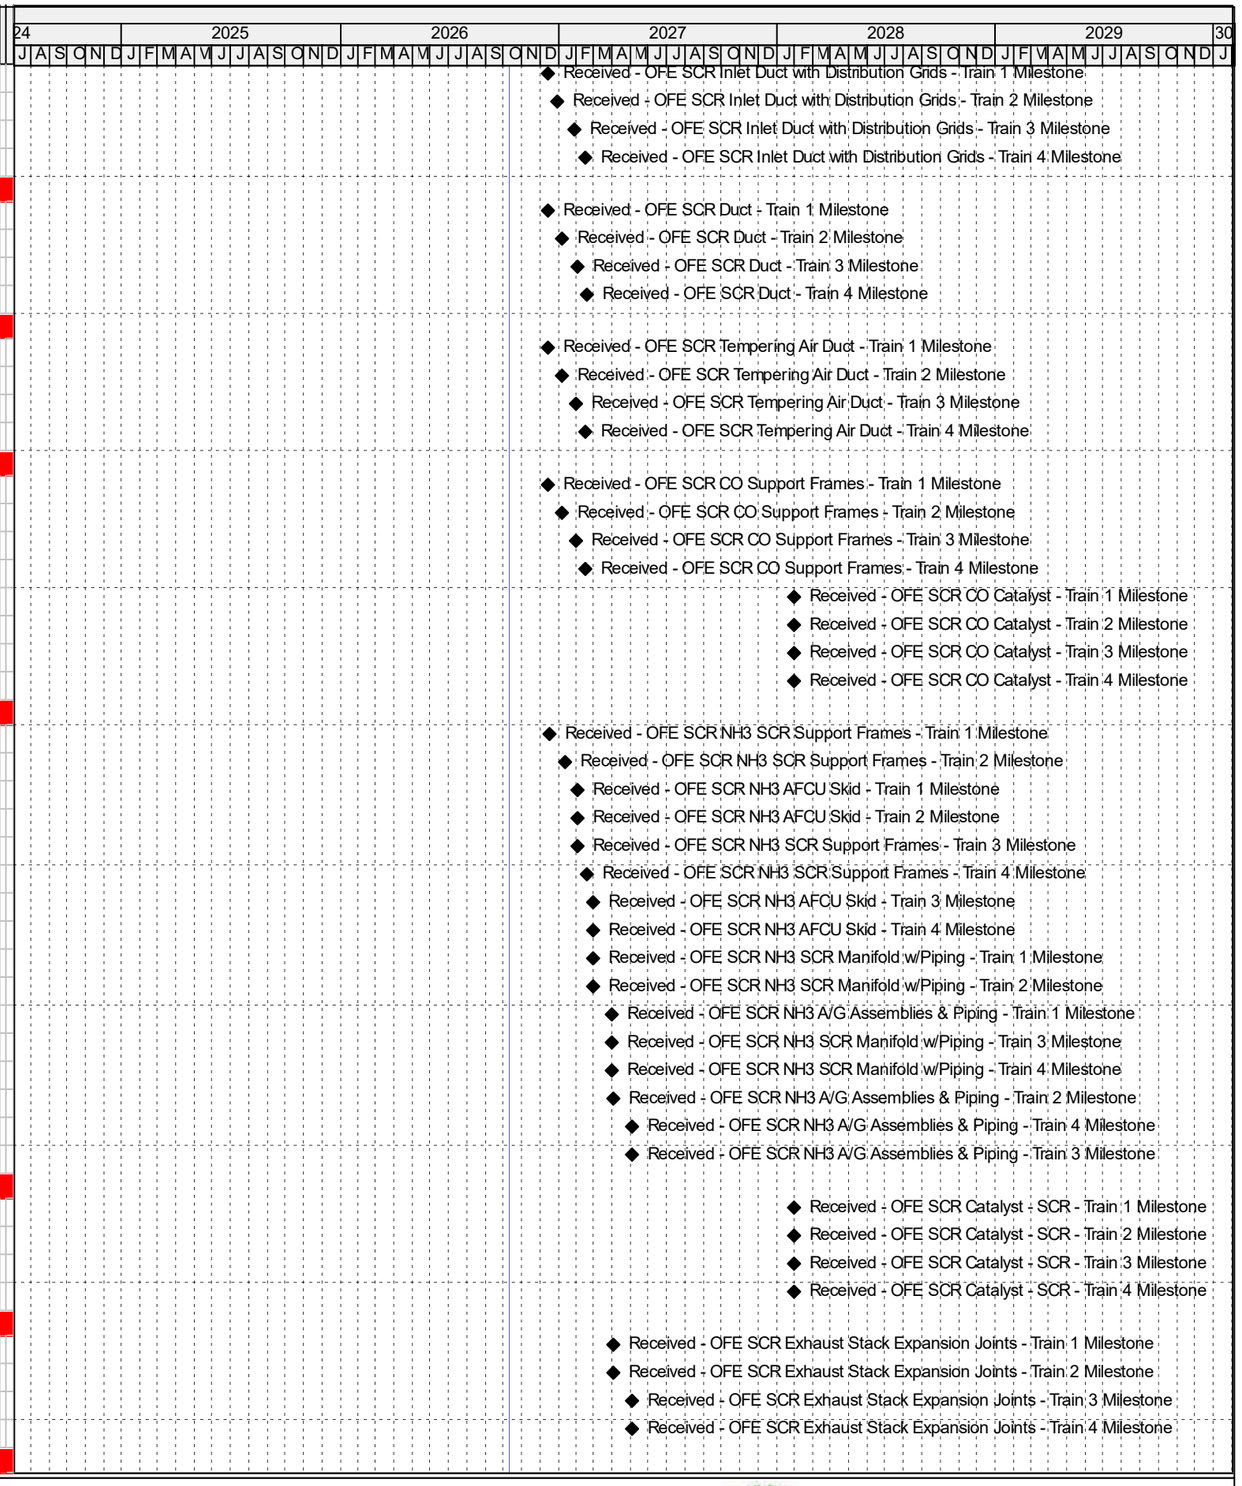


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.OFE.STAC	Received - OFE SCR Exhaust Stack - Train 1 Milestone	0		12/15/26 5:00 PM	245
KPA.OFE.STAC	Received - OFE SCR Exhaust Stack - Train 2 Milestone	0		1/8/27 5:00 PM	278
KPA.OFE.STAC	Received - OFE SCR Stack Silencer - Train 1 Milestone	0		1/15/27 5:00 PM	294
KPA.OFE.STAC	Received - OFE SCR Stack Silencer - Train 2 Milestone	0		1/15/27 5:00 PM	299
KPA.OFE.STAC	Received - OFE SCR Exhaust Stack - Train 3 Milestone	0		1/29/27 5:00 PM	233
KPA.OFE.STAC	Received - OFE SCR Exhaust Stack - Train 4 Milestone	0		2/16/27 5:00 PM	211
KPA.OFE.STAC	Received - OFE SCR Stack Silencer - Train 3 Milestone	0		2/16/27 5:00 PM	248
KPA.OFE.STAC	Received - OFE SCR Stack Silencer - Train 4 Milestone	0		2/16/27 5:00 PM	237
BH CNN-KPJV-MAST-LIVE,20,01,SCR,09 PRO - OFE - SCR - SB Piping					
KPA.OFE.SCR.	Received - OFE SCR SB Piping Material (Pipe & Fittings) - All Tr	0		4/15/27 5:00 PM	118
BH CNN-KPJV-MAST-LIVE,20,01,SCR,10 PRO - OFE - SCR - Valves, Instruments & Controls					
KPA.OFE.SCR.	Received - OFE SCR Valves - All Trains Milestone	0		4/1/27 5:00 PM	295
KPA.OFE.SCR.	Received - OFE SCR Instruments & Controls - All Trains Milestor	0		4/2/27 5:00 PM	294
BH CNN-KPJV-MAST-LIVE,20,01,SCR,12 PRO - OFE - SCR - (GA016) Tempering Air Fans W/ Damper, Inlet Filter, and Silencer					
KPA.OFE.GA0	Received - OFE SCR Tempering Air Fans w/ Damper, Inlet Filter	0		12/1/26 4:00 PM	287
KPA.OFE.GA0	Received - OFE SCR Tempering Air Fans w/ Damper, Inlet Filter	0		12/14/26 5:00 PM	283
KPA.OFE.GA0	Received - OFE SCR Tempering Air Fans w/ Damper, Inlet Filter	0		1/15/27 5:00 PM	231
KPA.OFE.GA0	Received - OFE SCR Tempering Air Fans w/ Damper, Inlet Filter	0		2/2/27 5:00 PM	208
BH CNN-KPJV-MAST-LIVE,20,01,SCR,11 PRO - OFE - SCR - All Other Remaining Components					
KPA.OFE.STAC	Received - OFE SCR Ladders & Platforms - Train 1 Milestone	0		12/15/26 4:00 PM	289
KPA.OFE.STAC	Received - OFE SCR Stairtower - Train 1 Milestone	0		12/15/26 5:00 PM	289
KPA.OFE.STAC	Received - OFE SCR Safety Gates - Train 1 Milestone	0		12/16/26 5:00 PM	288
KPA.OFE.STAC	Received - OFE SCR Safety Gates - Train 2 Milestone	0		12/16/26 5:00 PM	293
KPA.OFE.STAC	Received - OFE SCR Safety Gates - Train 3 Milestone	0		12/31/26 5:00 PM	253
KPA.OFE.STAC	Received - OFE SCR Safety Gates - Train 4 Milestone	0		12/31/26 5:00 PM	242
KPA.OFE.STAC	Received - OFE SCR Stairtower - Train 2 Milestone	0		1/8/27 5:00 PM	278
KPA.OFE.STAC	Received - OFE SCR Ladders & Platforms - Train 2 Milestone	0		1/8/27 5:00 PM	278
KPA.OFE.STAC	Received - OFE SCR Ladders & Platforms - Train 3 Milestone	0		2/11/27 5:00 PM	224
KPA.OFE.STAC	Received - OFE SCR Ladders & Platforms - Train 4 Milestone	0		2/16/27 5:00 PM	211
KPA.OFE.STAC	Received - OFE SCR Stairtower - Train 3 Milestone	0		2/26/27 5:00 PM	214
KPA.OFE.STAC	Received - OFE SCR Stairtower - Train 4 Milestone	0		2/26/27 5:00 PM	203
KPA.OFE.STAC	Received - OFE SCR CEMS Equipment Lifting Hoists - All Trains	0		4/15/27 5:00 PM	313
KPA.OFE.OTHI	Received - OFE All Other Equipment Components - SCR - Train	0		7/13/27 5:00 PM*	157
KPA.OFE.OTHI	Received - OFE All Other Equipment Components - SCR - Train	0		7/13/27 5:00 PM*	157
KPA.OFE.OTHI	Received - OFE All Other Equipment Components - SCR - Train	0		7/13/27 5:00 PM*	157
KPA.OFE.OTHI	Received - OFE All Other Equipment Components - SCR - Train	0		7/13/27 5:00 PM*	157
BH CNN-KPJV-MAST-LIVE,20,01,SCR,15 PRO - OFE - SCR - Casing Panels					
KPA.OFE.PANE	Received - OFE Casing Panels - SCR - Train 1 [02/12/2027] Mile	0		2/12/27 5:00 PM*	289
KPA.OFE.PANE	Received - OFE Casing Panels - SCR - Train 2 [04/27/2027] Mile	0		4/27/27 5:00 PM*	243
KPA.OFE.PANE	Received - OFE Casing Panels - SCR - Train 3 [04/27/2027] Mile	0		4/27/27 5:00 PM*	213
KPA.OFE.PANE	Received - OFE Casing Panels - SCR - Train 4 [04/27/2027] Mile	0		4/27/27 5:00 PM*	202
BH CNN-KPJV-MAST-LIVE,20,01,SCR,20 PRO - OFE - SCR - All Major Remaining Components (Delete?)					
KPA.OFE.MAJ	Received - OFE All Remaining Major Components - SCR - Train	0		5/13/27 5:00 PM*	98
KPA.OFE.MAJ	Received - OFE All Remaining Major Components - SCR - Train	0		5/13/27 5:00 PM*	109
KPA.OFE.MAJ	Received - OFE All Remaining Major Components - SCR - Train	0		5/13/27 5:00 PM*	139
KPA.OFE.MAJ	Received - OFE All Remaining Major Components - SCR - Train	0		5/13/27 5:00 PM*	114
BH CNN-KPJV-MAST-LIVE,20,01,SCR,35 PRO - OFE - SCR - Spare Parts					
KPA.OFE.SPAI	Received - OFE SCR Spare Parts Milestone	0		1/31/28 5:00 PM	17
BH CNN-KPJV-MAST-LIVE,20,01,CTG PRO - OFE - CTG (Combustion Turbine Generator)					
BH CNN-KPJV-MAST-LIVE,20,01,CTG,05 PRO - OFE - CTG - Foundation Embedment Plate					
KPA.OFE.FEP.	Received - OFE CTG Foundation Embedment Plate - CTG - Tra	0		6/1/27 7:00 AM	65

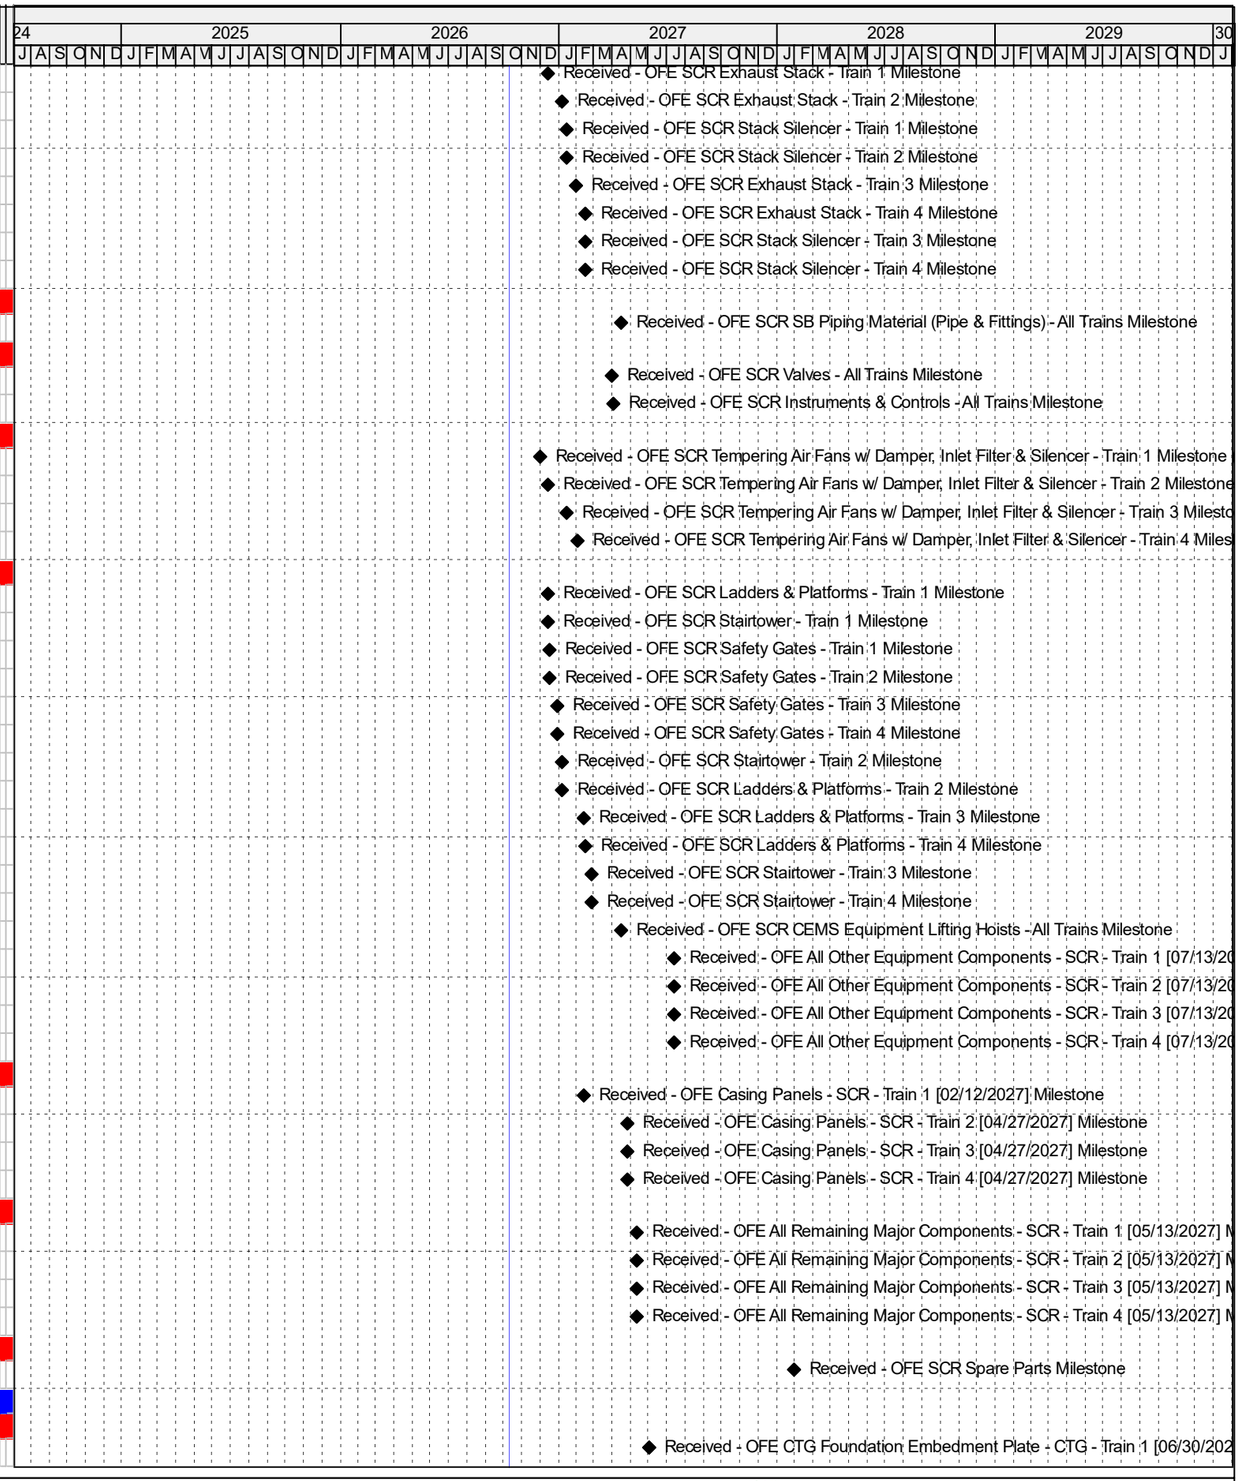


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.OFE.FEP.	Received - OFE CTG Foundation Embedment Plate - CTG - Tra	0		6/30/27 5:00 PM	64
KPA.OFE.FEP.	Received - OFE CTG Foundation Embedment Plate - CTG - Tra	0		8/2/27 7:00 AM	64
KPA.OFE.FEP.	Received - OFE CTG Foundation Embedment Plate - CTG - Tra	0		8/31/27 5:00 PM	63
BH CNN-KPJV-MAST-LIVE,20,01,CTG,10 PRO - OFE - CTG - GT (Gas Turbine)					
KPA.OFE.GT.1(	Received - OFE (via Rail) Gas Turbine - CTG - Train 1 [09/30/20	0		8/31/27 5:00 PM	0
KPA.OFE.GT.1(	Received - OFE (via Rail) Gas Turbine - CTG - Train 2 [10/30/20	0		9/30/27 5:00 PM	0
KPA.OFE.GT.1(	Received - OFE (via Rail) Gas Turbine - CTG - Train 3 [11/30/20	0		11/1/27 7:00 AM	0
KPA.OFE.GT.1(	Received - OFE (via Rail) Gas Turbine - CTG - Train 4 [12/30/20	0		11/30/27 5:00 PM	0
BH CNN-KPJV-MAST-LIVE,20,01,CTG,15 PRO - OFE - CTG - Generator					
KPA.OFE.GEN	Received - OFE (via Rail) Generator - CTG - Train 1 [09/30/2027	0		8/31/27 5:00 PM	0
KPA.OFE.GEN	Received - OFE (via Rail) Generator - CTG - Train 2 [10/30/2027	0		9/30/27 5:00 PM	0
KPA.OFE.GEN	Received - OFE (via Rail) Generator - CTG - Train 3 [11/30/2027	0		11/1/27 7:00 AM	0
KPA.OFE.GEN	Received - OFE (via Rail) Generator - CTG - Train 4 [12/30/2027	0		11/30/27 5:00 PM	0
BH CNN-KPJV-MAST-LIVE,20,01,CTG,20 PRO - OFE - CTG - Inlet Filter House Main Structure					
KPA.OFE.IFHS	Received - OFE Inlet Filter House Structure - CTG - Train 1 [10/3	0		8/2/27 7:00 AM	64
KPA.OFE.IFHS	Received - OFE Inlet Filter House Structure - CTG - Train 2 [11/3	0		9/1/27 5:00 PM	62
KPA.OFE.IFHS	Received - OFE Inlet Filter House Structure - CTG - Train 3 [12/3	0		10/1/27 5:00 PM	62
KPA.OFE.IFHS	Received - OFE Inlet Filter House Structure - CTG - Train 4 [01/3	0		11/1/27 7:00 AM	63
BH CNN-KPJV-MAST-LIVE,20,01,CTG,31 PRO - OFE - CTG - (GA031) LEC (Load Commutative Inverter & Excitation Compartment)					
KPA.OFE.GA0(	Received - OFE GE LEC - CTG - Train 1 [10/30/2027] Milestone	0		8/2/27 7:00 AM	64
KPA.OFE.GA0(	Received - OFE GE LEC - CTG - Train 2 [11/30/2027] Milestone	0		9/1/27 5:00 PM	62
KPA.OFE.GA0(	Received - OFE GE LEC - CTG - Train 3 [12/30/2027] Milestone	0		10/1/27 5:00 PM	62
KPA.OFE.GA0(	Received - OFE GE LEC - CTG - Train 4 [01/30/2028] Milestone	0		11/1/27 5:00 PM	62
BH CNN-KPJV-MAST-LIVE,20,01,CTG,40 PRO - OFE - CTG - BoP DCS					
KPA.OFE.DCS.	Received - OFE DCS - BoP CTG [12/30/2027] Milestone	0		11/1/27 5:00 PM	213
BH CNN-KPJV-MAST-LIVE,20,01,CTG,45 PRO - OFE - CTG - Miscellaneous Components					
KPA.OFE.GA0(	Fab & Deliver - Fuel Gas Knockout Drum (GA093)	7	7/16/27 7:00 AM	7/26/27 5:00 PM*	136
KPA.OFE.MISC	Received - OFE All Other Equipment Components - CTG - Train	0		11/1/27 7:00 AM*	0
KPA.OFE.MISC	Received - OFE All Other Equipment Components - CTG - Train	0		11/30/27 5:00 PM*	0
KPA.OFE.MISC	Received - OFE All Other Equipment Components - CTG - Train	0		12/30/27 5:00 PM*	0
KPA.OFE.MISC	Received - OFE All Other Equipment Components - CTG - Train	0		1/31/28 5:00 PM*	0
BH CNN-KPJV-MAST-LIVE,20,01,GC PRO - OFE - Gas Compressors					
KPA.OFE.GC.1(	Received - OFE Gas Compressors (Atlas) - Train 1 [07/22/2027]	0		7/22/27 5:00 PM*	104
KPA.OFE.GC.1(	Received - OFE Gas Compressors (Atlas) - Train 2 [08/01/2027]	0		7/22/27 5:00 PM*	104
KPA.OFE.GC.1(	Received - OFE Gas Compressors (Atlas) - Train 3 [08/01/2027]	0		7/22/27 5:00 PM*	104
KPA.OFE.GC.1(	Received - OFE Gas Compressors (Atlas) - Train 4 [08/01/2027]	0		7/22/27 5:00 PM*	104
BH CNN-KPJV-MAST-LIVE,20,01,GCB PRO - OFE - GCB (General Circuit Breaker)					
KPA.OFE.GCB.1	Received - OFE Generator Circuit Breaker - Train 1 [11/30/2026]	0		11/30/26 5:00 PM*	298
KPA.OFE.GCB.1	Received - OFE Generator Circuit Breaker - Train 2 [12/17/2026	0		12/17/26 5:00 PM*	285
KPA.OFE.GCB.1	Received - OFE Generator Circuit Breaker - Train 3 [01/15/2027	0		1/15/27 5:00 PM*	307
KPA.OFE.GCB.1	Received - OFE Generator Circuit Breaker - Train 4 [02/15/2027	0		2/16/27 7:00 AM*	287
BH CNN-KPJV-MAST-LIVE,20,01,PDC PRO - OFE - PDC (Power Distribution Center)					
KPA.OFE.PDC.1	Received - OFE Power Distribution Center (PDC) - Train 1 [Orig (	0		1/22/27 5:00 PM	199
KPA.OFE.PDC.1	Received - OFE Power Distribution Center (PDC) - Train 2 [Orig (	0		2/25/27 5:00 PM	187
KPA.OFE.PDC.1	Received - OFE Loose Transformers - Train 1 [03/05/2027] Mile	0		3/5/27 5:00 PM*	237
KPA.OFE.PDC.1	Received - OFE Loose Transformers - Train 2 [03/05/2027] Mile	0		3/5/27 5:00 PM*	248
KPA.OFE.PDC.1	Received - OFE Loose Transformers - Train 3 [03/05/2027] Mile	0		3/5/27 5:00 PM*	278
KPA.OFE.PDC.1	Received - OFE Loose Transformers - Train 4 [03/05/2027] Mile	0		3/5/27 5:00 PM*	206
KPA.OFE.PDC.1	Received - OFE Power Distribution Center (PDC) - Train 3 [Orig (	0		5/28/27 5:00 PM	151
KPA.OFE.PDC.1	Received - OFE Power Distribution Center (PDC) - Train 4 [Orig (	0		6/9/27 5:00 PM	139
BH CNN-KPJV-MAST-LIVE,20,01,TR PRO - OFE - Transformers					

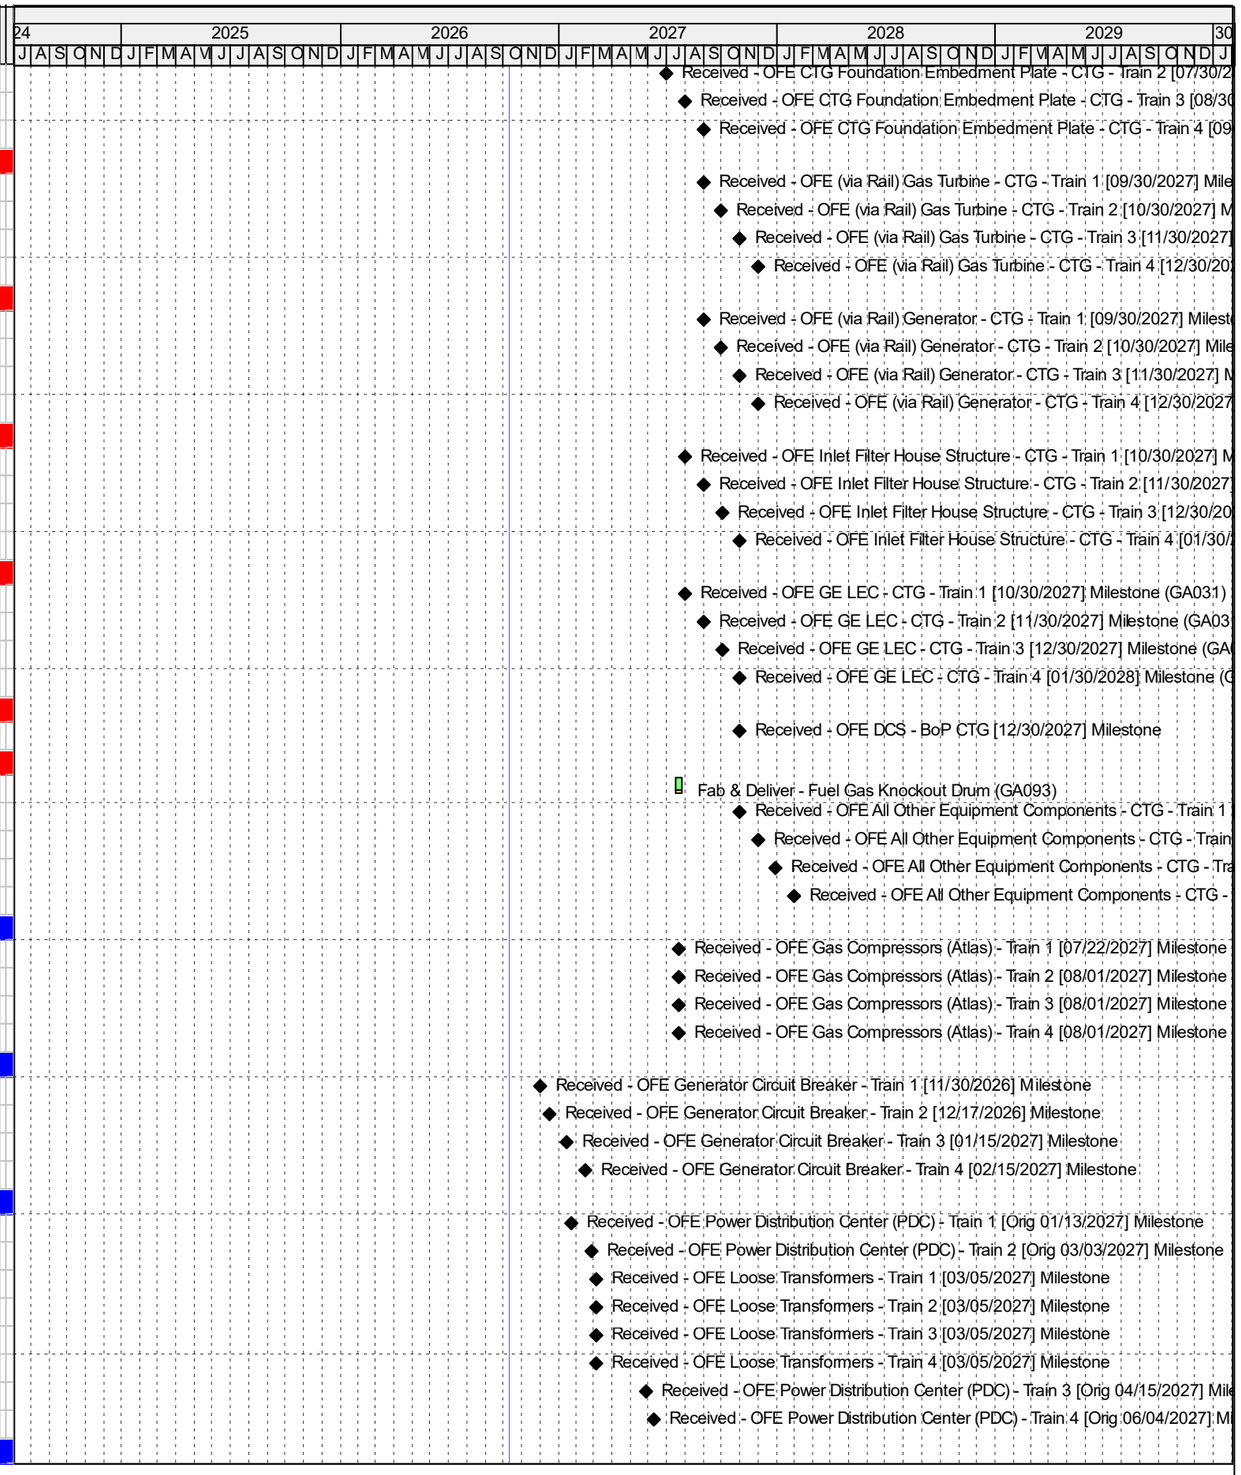

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.OFE.TRAN	Received - OFE 138KV Station Service Transformers (SSTs) (Tra	0	5/4/26 7:00 AM A		
KPA.OFE.TRAN	Received - OFE GSU (Generator Step Up) - Train 1 (Transfer Cu	0		5/16/26 5:00 PM A	
KPA.OFE.TRAN	Received - OFE 345KV Station Service Transformers (SSTs) (Tra	0		5/16/26 5:00 PM A	
KPA.OFE.TRAN	Received - OFE GSU (Generator Step Up) - (Transfer of Custody	0		5/16/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,20,01,MI PRO - OFE - Misc					
KPA.OFE.GA01	Received - OFE CEMS - Train 1 [08/01/2027] Milestone (GA018	0		8/2/27 7:00 AM*	241
KPA.OFE.GA01	Received - OFE CEMS - Train 2 [08/01/2027] Milestone (GA018	0		8/2/27 7:00 AM*	239
KPA.OFE.GA01	Received - OFE CEMS - Train 3 [08/01/2027] Milestone (GA018	0		8/2/27 7:00 AM*	241
KPA.OFE.GA01	Received - OFE CEMS - Train 4 [08/01/2027] Milestone (GA018	0		8/2/27 7:00 AM*	241
BH CNN-KPJV-MAST-LIVE,20,38 PRO - Long Lead Contractor Furnished Items					
KPA.LL.1006	Procure - Long Lead item - Pile	0	6/8/26 7:00 AM A	6/26/26 5:00 PM A	
KPA.LL.1000	Fab & Deliver - False Start Drain Tank - CTG - Train 1 (GA050)	0	5/26/26 7:00 AM A	7/10/26 5:00 PM A	
KPA.LL.1005	Fab & Deliver - False Start Drain Tank - CTG - Train 2 (GA050)	0	5/26/26 7:00 AM A	7/10/26 5:00 PM A	
KPA.LL.1010	Fab & Deliver - False Start Drain Tank - CTG - Train 3 (GA050)	0	5/26/26 7:00 AM A	7/10/26 5:00 PM A	
KPA.LL.1015	Fab & Deliver - False Start Drain Tank - CTG - Train 4 (GA050)	0	5/26/26 7:00 AM A	7/10/26 5:00 PM A	
KPA.LL.1020	Procure - Long Lead Item - Natrual Gas Pipe	0	6/15/26 7:00 AM A	8/14/26 5:00 PM A	
KPA.LL.1050	Procure - Long Lead Item - Storm Water Pipe	0	6/15/26 7:00 AM A	9/18/26 5:00 PM A	
KPA.LL.1041	Procure - Long Lead Item - Electrical Precast Manhole Structure	15	8/3/26 7:00 AM A	10/30/26 5:00 PM	18
KPA.LL.1036	Procure - Long Lead Item - MV / LV / IO Cable	89	8/3/26 7:00 AM A	2/18/27 5:00 PM	74
KPA.LL.GA072.1	Procure - Long Lead item - PEMB - PSE (Plant Services Enclos	100	10/12/26 7:00 AM	3/5/27 5:00 PM	201
KPA.LL.1045	Procure - Long Lead item - PEMB - Admin/Warehouse (AMWB	100	10/13/26 7:00 AM	3/8/27 5:00 PM	98
KPA.LL.1060	Procure - Long Lead item - Valves	107	10/12/26 7:00 AM	3/16/27 5:00 PM	58
KPA.OFE.GA069	Fab & Deliver - Fire Water Pump House Materials (GA069)	105	10/12/26 7:00 AM	3/17/27 5:00 PM	256
KPA.LL.1070	Procure - Long Lead item - PEMB - Fire Water Pump House - S	100	12/1/26 7:00 AM	4/22/27 5:00 PM	236
KPA.LL.1065	Procure - Long Lead item - PEMB - Liquid Fuel Enclosure (GA0	150	10/12/26 7:00 AM	5/14/27 5:00 PM	161
KPA.LL.1025	Procure - Long Lead item - Fire Pumps	151	10/12/26 7:00 AM	5/17/27 5:00 PM	219
KPA.LL.1075	Procure - Long Lead item - PEMB - FGCE (Fuel Gas Compressc	190	11/2/26 7:00 AM	8/3/27 5:00 PM	2
KPA.LL.1030	Procure - Long Lead item - Isophase Duct / 15kV Cable / 15kV	256	8/3/26 7:00 AM A	10/14/27 5:00 PM	76
KPA.OFE.GA094	Fab & Deliver - Weather Station Materials (GA094)	13	11/1/27 7:00 AM	11/18/27 5:00 PM	82
BH CNN-KPJV-MAST-LIVE,40 CONSTRUCTION					
BH CNN-KPJV-MAST-LIVE,40,00 CONST - Milestones					
KPA.CTG1.MSDF	MS - Drive Pile - Complete - Train 1	0		3/4/27 5:00 PM	54
KPA.CTG2.MSDF	MS - Drive Pile - Complete - Train 2	0		5/13/27 5:00 PM	77
BH CNN-KPJV-MAST-LIVE,40,01 CONST - Mobilization					
KPA.MBL.1020	Mobilize - Site - Guarantee Electric (GECO) [05/11/26]	0	5/11/26 7:00 AM A	6/8/26 5:00 PM A	
KPA.MBL.1000	Mobilize - Site - Kokosing Plocher II (KPII) [05/04/26]	0	5/4/26 7:00 AM A	6/11/26 5:00 PM A	
KPA.MBL.1025	Mobilize - Site - Corrigan Haberberger (CH) [07/27/26]	0	7/27/26 7:00 AM A	8/21/26 5:00 PM A	
KPA.MBL.1005	Mobilize - Site - Boyer (BRP) [09/14/26]	0	9/14/26 7:00 AM A	9/15/26 5:00 PM A	
KPA.MBL.1010	Mobilize - Site - Madison Industrial (MI) [11/16/26]	8	11/16/26 7:00 AM*	11/25/26 5:00 PM	253
KPA.MBL.1030	Mobilize - Site - Chattanooga (CBT) [01/04/27]	10	1/4/27 7:00 AM*	1/15/27 5:00 PM	115
BH CNN-KPJV-MAST-LIVE,40,02 CONST - Site					
KPA.SW.1010	Clear Laydown, Trailers, & Parking Areas	0	5/5/26 7:00 AM A	6/19/26 5:00 PM A	
KPA.SW.1000	Grade & Level Laydown, Trailers, & Parking Areas	0	5/4/26 7:00 AM A	6/19/26 5:00 PM A	
KPA.SW.1020	Establish - Laydown, Trailers, & Parking Areas	0	5/18/26 7:00 AM A	6/19/26 5:00 PM A	
KPA.SW.1030	Site Mass Ex/Earthwork	0	6/8/26 7:00 AM A	7/30/26 5:00 PM A	
KPA.BOA.FWL.1	Install - U/G Pipe - Service Water - North Road	0	9/22/26 7:00 AM A	10/6/26 5:00 PM A	
KPA.BOA.FWL.1	Install - U/G Pipe - Potable Water Feed (Partial Install Next to 2(	15	11/19/26 7:00 AM	12/11/26 5:00 PM	308
KPA.SW.GA095.	Install - U/G Process Pipe - (Str B6 to Str B10A) - North Main - E	25	12/2/26 7:00 AM	1/7/27 5:00 PM	291
KPA.SW.1100	Site Paving	30	10/28/27 7:00 AM	12/9/27 5:00 PM	86
BH CNN-KPJV-MAST-LIVE,40,02,005 CONST - Site - Storm Water System					




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.BOA.STW.	Install - U/G Pipe - Storm Water - (Str B10A to Str B2) - North Rc	16	9/21/26 7:00 AM A	11/2/26 5:00 PM	550
KPA.BOA.STW.	Install - U/G Pipe - Storm Water - (Str B2 to Str A7) - West Roac	13	11/9/26 7:00 AM	11/25/26 5:00 PM	289
KPA.BOA.STW.	Install - U/G Pipe - Storm Water - (Structure A7 to A10) - South I	13	12/7/26 7:00 AM	12/23/26 5:00 PM	284
KPA.BOA.STW.	Install - U/G Pipe - Storm Water - (Structure A9 to A19) - Betwee	5	12/24/26 7:00 AM	12/31/26 5:00 PM	284
BH CNN-KPJV-MAST-LIVE,40,02,020 CONST - Site - Fire Protection System					
KPA.BOA.FWL.	Install - U/G Fire Water Piping - Loop - North Road Up To Admin	6	9/21/26 7:00 AM A	10/19/26 5:00 PM	145
KPA.BOA.FWL.	Install - U/G Fire Water Piping - Loop - Around Fuel Oil Tanks Ar	20	11/3/26 7:00 AM	12/2/26 5:00 PM	145
KPA.BOA.FWL.	Install - U/G Fire Water Piping - West Road (North to South) - Bc	10	12/3/26 7:00 AM	12/16/26 5:00 PM	240
KPA.BOA.FWL.	Install - U/G Fire Water Piping - Fire Water Pumphouse - BoP	15	12/17/26 7:00 AM	1/8/27 5:00 PM	240
KPA.BOA.FWL.	Connect - U/G Fire Water Piping to BESS Fire Protective Syster	1	10/26/27 7:00 AM	10/26/27 5:00 PM	87
BH CNN-KPJV-MAST-LIVE,40,02,095 CONST - Site - (GA095) Fuel Gas Metering & Regulation Yard					
KPA.SW.GA095	Install - U/G Process Pipe - Fuel Gas Line 20" - (Yard to Fuel Ga	43	10/5/26 7:00 AM A	12/11/26 5:00 PM	308
KPA.SW.GA095	Install - Fuel Gas Metering & Regulation Site Pad (GA095)	5	8/9/27 7:00 AM	8/13/27 5:00 PM	158
BH CNN-KPJV-MAST-LIVE,40,02,104 CONST - Site - (GA104) Plant Entrance Gate					
KPA.SW.1140	Install - U/G Control / Power Cable to Entrance Gate (GA104)	5	6/1/27 7:00 AM	6/7/27 5:00 PM	186
BH CNN-KPJV-MAST-LIVE,40,02,105 CONST - Site - (GA105) Guard Shack					
KPA.SW.1130	Install - U/G Control / Power Cable to Guard Shack (GA105)	5	4/22/27 7:00 AM	4/28/27 5:00 PM	186
KPA.BOP.GA10	MFRP - Foundation - Guard Shack (GA105)	2	4/29/27 7:00 AM	4/30/27 5:00 PM	186
KPA.SW.1170	Install - Guard Shack (GA105)	15	5/3/27 7:00 AM	5/21/27 5:00 PM	186
KPA.SW.1120	Install - Plant Entrance Gate (GA104)	5	5/24/27 7:00 AM	5/28/27 5:00 PM	186
BH CNN-KPJV-MAST-LIVE,40,02,SS CONST - Site - Site Security					
KPA.SW.1090	Install - Permanent Fencing/Gate	20	10/28/27 7:00 AM	11/24/27 5:00 PM	86
BH CNN-KPJV-MAST-LIVE,40,04 CONST - BoP					
KPA.SW.GA095.	Install - U/G Process Pipe - (Str B6 to Str B2) - North Main - Wes	25	10/26/26 7:00 AM*	12/1/26 5:00 PM	291
KPA.SW.GA095.	Install - U/G Process Pipe - (Str B2 to Str A7) - West Road	30	11/9/26 7:00 AM	12/22/26 5:00 PM	18
BH CNN-KPJV-MAST-LIVE,40,04,AMW CONST - BoP - AD/MS/WB/MI AREA					
KPA.CTG4.ELEI	Install - U/G Electrical Duct Bank - (DB507A/B/C, 508, 509) - Adr	25	12/10/26 7:00 AM	1/15/27 5:00 PM	305
BH CNN-KPJV-MAST-LIVE,40,04,AMW,082 CONST - BoP AREA - (GA082) Auxiliary Transformer (Admin Area)					
KPA.BOA.GA0	MFRP - Foundation & Pedestal - Aux Transformer - Admin Area	10	2/8/27 7:00 AM	2/22/27 5:00 PM	220
KPA.BOA.GA0	Excavate - U/G Interconnect Utilities - Aux Transformer - Admin A	5	3/18/27 7:00 AM	3/24/27 5:00 PM	423
KPA.BOA.GA0	Install - U/G Pipe - Aux Transformer - Admin Area (GA082)	5	3/18/27 7:00 AM	3/24/27 5:00 PM	423
KPA.BOA.GA0	Install - OFE Equipment Package - Aux Transformer - Admin Are	10	11/1/27 7:00 AM	11/12/27 5:00 PM	94
BH CNN-KPJV-MAST-LIVE,40,04,AMW,094 CONST - BoP AREA - (GA094) Weather Station					
KPA.BOA.GA0	Install - Weather Station (GA094)	5	11/19/27 7:00 AM	11/26/27 5:00 PM	85
BH CNN-KPJV-MAST-LIVE,40,04,AMW,096 CONST - BoP AREA - (GA096) Admin Building & Maintenance Shop					
KPA.BOA.GA0	Install - U/G Fire Water Piping - Admin/Warehouse (AMWB) (GA	10	10/20/26 7:00 AM	11/2/26 5:00 PM	145
KPA.BOA.GA0	Drive Pile - Admin/Warehouse (AMWB) (GA096-7) - Crane 1	24	11/4/26 7:00 AM	12/9/26 5:00 PM	2
KPA.BOA.GA0	Install - U/G Pipe - M&P (Mechanical & Plumbing) - Admin/Ware	20	12/10/26 7:00 AM	1/8/27 5:00 PM	118
KPA.BOA.AMS	Install - Grounding - Admin/Warehouse (AMWB) (GA096-7)	14	1/5/27 7:00 AM	1/22/27 5:00 PM	218
KPA.BOA.GA0	MFRP - Foundation - Admin/Warehouse (AMWB) (GA096-7)	30	12/24/26 7:00 AM	2/5/27 5:00 PM	118
KPA.BOA.GA0	Install - PEMB - Admin/Warehouse (AMWB) (GA096-7)	90	5/3/27 7:00 AM	9/8/27 5:00 PM	59
BH CNN-KPJV-MAST-LIVE,40,04,AMW,106 CONST - BoP AREA - (GA106) Septic Field					
KPA.BOA.GA1	Install - Connect & Inspect - Septic Field (GA106)	25	1/28/27 7:00 AM	3/4/27 5:00 PM	100
BH CNN-KPJV-MAST-LIVE,40,04,FG CONST - BoP - Fuel Gas AREA					
BH CNN-KPJV-MAST-LIVE,40,04,FG,085 CONST - BoP AREA - (GA085) Fuel Gas Compressor Enclosure					
KPA.BOA.GA0	Drive Pile - FGCE (Fuel Gas Compressor Enclosure) (GA085) - C	19	5/20/27 7:00 AM	6/16/27 5:00 PM	0
KPA.BOA.GA0	Install - U/G Pipe - FGCE (Fuel Gas Compressor Enclosure) (GA	15	6/17/27 7:00 AM	7/8/27 5:00 PM	0
KPA.BOA.GA0	MFRP - Foundation - FGCE (Fuel Gas Compressor Enclosure) (	20	7/9/27 7:00 AM	8/5/27 5:00 PM	0
KPA.BOA.GA0	Install - PEMB - FGCE (Fuel Gas Compressor Enclosure) Buildir	50	8/6/27 7:00 AM	10/15/27 5:00 PM	0
KPA.BOA.GA0	Install - Fuel Gas Compressor Equipment / Piping (GA085)	70	8/27/27 7:00 AM	12/6/27 5:00 PM	79
BH CNN-KPJV-MAST-LIVE,40,04,FG,087 CONST - BoP AREA - (GA087) Fuel Gas Compressor					

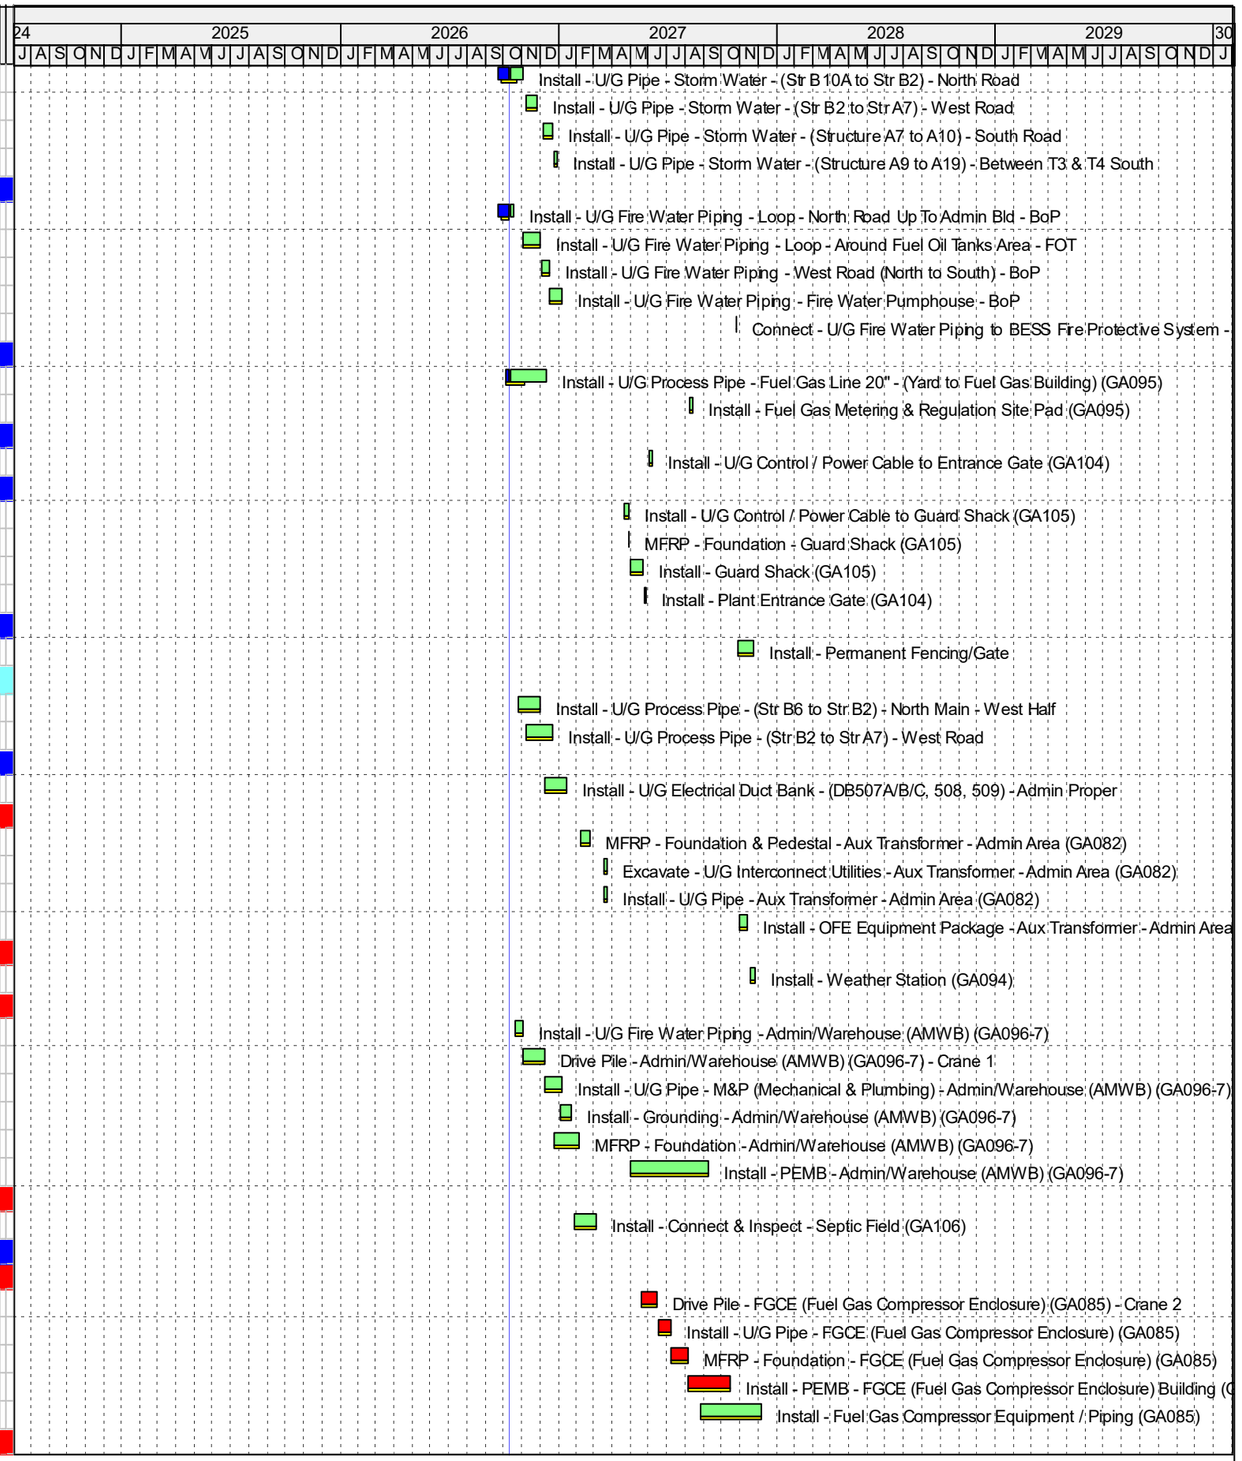

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.BOA.GA0	Install - Fuel Gas Compressor (Qty. 4) (GA087)	25	8/27/27 7:00 AM	10/1/27 5:00 PM	124
BH CNN-KPJV-MAST-LIVE,40,04,FG,090 CONST - BoP AREA - (GA090) Nitrogen Generator Skid					
KPA.BOA.GA0	Install - A/G Pipe - Nitrogen Generator Skid (GA090)	110	6/23/27 7:00 AM	11/26/27 5:00 PM	85
BH CNN-KPJV-MAST-LIVE,40,04,FG,091 CONST - BoP AREA - (GA091) Fuel Gas Compressor Heat Exchangers					
KPA.BOA.GA0	Install - Fuel Gas Compressor Heat Exchangers 4ea (GA091)	15	8/27/27 7:00 AM	9/17/27 5:00 PM	134
BH CNN-KPJV-MAST-LIVE,40,04,FG,092 CONST - BoP AREA - (GA092) Fuel Gas Chromatograph (GE MLI G023)					
KPA.BOA.GA0	Install - GE Fuel Gas Chromatograph (GA092)	15	11/10/27 7:00 AM	12/1/27 5:00 PM	82
BH CNN-KPJV-MAST-LIVE,40,04,FG,093 CONST - BoP AREA - (GA093) Fuel Gas Knockout Drum					
KPA.BOA.GA0	Install - Equipment - Fuel Gas Knockout Drum (GA093)	2	10/18/27 7:00 AM	10/19/27 5:00 PM	82
KPA.BOA.GA0	Install - U/G Process Pipe - Fuel Gas Knockout Drum (GA093)	15	10/20/27 7:00 AM	11/9/27 5:00 PM	82
BH CNN-KPJV-MAST-LIVE,40,04,FO CONST - BoP - Fuel Oil AREA					
BH CNN-KPJV-MAST-LIVE,40,04,FO,053 CONST - BoP AREA - (GA053) Fuel Oil Unloading Stations					
BH CNN-KPJV-MAST-LIVE,40,04,FO,053,1 CONST - BoP AREA - (GA053) Fuel Oil Unloading Station 1					
KPA.BOA.GA(	Install - U/G Pipe - Fuel Oil Unloading Station 1 (GA053)	5	3/19/27 7:00 AM	3/25/27 5:00 PM	137
KPA.BOP.ELE	Install - U/G Electrical Duct Bank - Fuel Oil Unloading Station 1 (	5	3/19/27 7:00 AM	3/25/27 5:00 PM	137
KPA.BOA.GA(	MFRP - Foundation - Fuel Oil Unloading Station 1 (GA053)	20	3/26/27 7:00 AM	4/22/27 5:00 PM	137
KPA.BOA.GA(	Install - Fuel Oil Unloading Station 1 (GA053)	15	9/28/27 7:00 AM	10/18/27 5:00 PM	113
BH CNN-KPJV-MAST-LIVE,40,04,FO,053,2 CONST - BoP AREA - (GA053) Fuel Oil Unloading Station 2					
KPA.BOA.GA(	Install - U/G Pipe - Fuel Oil Unloading Station 2 (GA053)	5	3/19/27 7:00 AM	3/25/27 5:00 PM	157
KPA.BOP.ELE	Install - U/G Electrical Duct Bank - Fuel Oil Unloading Station 2 (	5	3/19/27 7:00 AM	3/25/27 5:00 PM	157
KPA.BOA.GA(	MFRP - Foundation - Fuel Oil Unloading Station 2 (GA053)	20	4/23/27 7:00 AM	5/20/27 5:00 PM	137
KPA.BOA.GA(	Install - Fuel Oil Unloading Station 2 (GA053)	15	9/28/27 7:00 AM	10/18/27 5:00 PM	113
BH CNN-KPJV-MAST-LIVE,40,04,FO,053,3 CONST - BoP AREA - (GA053) Fuel Oil Unloading Station 3					
KPA.BOA.GA(	Install - U/G Pipe - Fuel Oil Unloading Station 3 (GA053)	5	3/19/27 7:00 AM	3/25/27 5:00 PM	177
KPA.BOP.ELE	Install - U/G Electrical Duct Bank - Fuel Oil Unloading Station 3 (	5	3/19/27 7:00 AM	3/25/27 5:00 PM	177
KPA.BOA.GA(	MFRP - Foundation - Fuel Oil Unloading Station 3 (GA053)	20	5/21/27 7:00 AM	6/18/27 5:00 PM	137
KPA.BOA.GA(	Install - Fuel Oil Unloading Station 3 (GA053)	15	9/28/27 7:00 AM	10/18/27 5:00 PM	113
BH CNN-KPJV-MAST-LIVE,40,04,FO,054 CONST - BoP AREA - (GA054) Fuel Oil Unloading Pumps					
KPA.BOA.GA0	Install - Fuel Oil Unloading Tank Pumps (GA054)	15	11/22/27 7:00 AM	12/13/27 5:00 PM	74
BH CNN-KPJV-MAST-LIVE,40,04,FO,056 CONST - BoP AREA - (GA056) Fuel Oil Tanks					
KPA.BOA.GA0	MFRP - Foundation - Fuel Oil Tank (A&B) (GA056)	0	8/3/26 7:00 AM A	9/22/26 5:00 PM A	
KPA.BOA.STW	Install - U/G Pipe - Storm Water - Fuel Oil Area (GA056)	14	10/5/26 7:00 AM A	10/29/26 5:00 PM	167
KPA.BOA.GA0	LOE - Install - Fuel Oil Tank (A&B) (GA056)	186	1/16/27 7:00 AM	8/20/27 5:00 PM	172
BH CNN-KPJV-MAST-LIVE,40,04,FO,056,056A CONST - BoP AREA - (GA056) Fuel Oil Tank A					
KPA.BOA.GA(	Drive Pile - Fuel Oil Tank (A) (GA056) - Crane 1	0	7/29/26 7:00 AM A	8/26/26 5:00 PM A	
KPA.BOA.GA(	Start Tank - CBT - Fuel Oil Tank A [01/04/27] (GA056)	0	1/16/27 7:00 AM		141
KPA.BOA.GA(	Survey - Foundation - Fuel Oil Tank A (GA056)	1	1/16/27 7:00 AM	1/16/27 5:00 PM	181
KPA.BOA.GA(	Install - Bottom Plates - Fuel Oil Tank A (GA056)	2	1/18/27 7:00 AM	1/19/27 5:00 PM	181
KPA.BOA.GA(	Weld - Bottom Plates - Fuel Oil Tank A (GA056)	15	1/20/27 7:00 AM	2/5/27 5:00 PM	181
KPA.BOA.GA(	Install - Stiffener Ring 1 - Fuel Oil Tank A (GA056)	15	1/20/27 7:00 AM	2/5/27 5:00 PM	181
KPA.BOA.GA(	Install - Stiffener Ring 2 - Fuel Oil Tank A (GA056)	10	1/26/27 7:00 AM	2/5/27 5:00 PM	181
KPA.BOA.GA(	Cut - Door Sheet - Fuel Oil Tank A (GA056)	1	2/6/27 7:00 AM	2/6/27 5:00 PM	181
KPA.BOA.GA(	Install - Stiffener Ring 3 - Fuel Oil Tank A (GA056)	10	2/8/27 7:00 AM	2/18/27 5:00 PM	181
KPA.BOA.GA(	Install - Wind Protection - Fuel Oil Tank A (GA056)	3	2/19/27 7:00 AM	2/22/27 5:00 PM	188
KPA.BOA.GA(	Install - Stiffener Ring 4 - Fuel Oil Tank A (GA056)	10	2/19/27 7:00 AM	3/2/27 5:00 PM	181
KPA.BOA.GA(	Install - Stiffener Ring 5 - Fuel Oil Tank A (GA056)	10	3/3/27 7:00 AM	3/13/27 5:00 PM	181
KPA.BOA.GA(	Install - Nozzles & Manways - Fuel Oil Tank A (GA056)	40	2/8/27 7:00 AM	3/25/27 5:00 PM	181
KPA.BOA.GA(	Install - Lugs / Pipe Supports / Clips - Fuel Oil Tank A (GA056)	40	2/8/27 7:00 AM	3/25/27 5:00 PM	181
KPA.BOA.GA(	Install - Stiffener Ring 6 - Fuel Oil Tank A (GA056)	10	3/15/27 7:00 AM	3/25/27 5:00 PM	181
KPA.BOA.GA(	Install - Rim Angle - Fuel Oil Tank A (GA056)	5	3/26/27 7:00 AM	3/31/27 5:00 PM	181
KPA.BOA.GA(	Install - Install Girders / Rafters / Columns - Fuel Oil Tank A (GA0	9	4/1/27 7:00 AM	4/10/27 5:00 PM	181




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.BOA.GA(	Install - Install Roof Plates - Fuel Oil Tank A (GA056)	12	4/12/27 7:00 AM	4/24/27 5:00 PM	181
KPA.BOA.GA(	Install - Roof Insulation Rings - Fuel Oil Tank A (GA056)	7	4/26/27 7:00 AM	5/3/27 5:00 PM	181
KPA.BOA.GA(	Install - Roof Handrail & Platform - Fuel Oil Tank A (GA056)	3	5/4/27 7:00 AM	5/6/27 5:00 PM	181
KPA.BOA.GA(	Install - Insulation Angle on Stiffener Ring 1 - Fuel Oil Tank A (G/	4	5/4/27 7:00 AM	5/7/27 5:00 PM	181
KPA.BOA.GA(	Install - Spiral Staircase - Fuel Oil Tank A (GA056)	5	5/7/27 7:00 AM	5/12/27 5:00 PM	181
KPA.BOA.GA(	Install - Heaters - Fuel Oil Tank A (GA056)	1	5/13/27 7:00 AM	5/13/27 5:00 PM	181
KPA.BOA.GA(	Paint - Interior - Fuel Oil Tank A (GA056)	15	5/14/27 7:00 AM	5/31/27 5:00 PM	181
KPA.BOA.GA(	Install - Door Sheet - Fuel Oil Tank A (GA056)	5	6/1/27 7:00 AM	6/5/27 5:00 PM	181
KPA.BOA.GA(	Paint - Exterior - Fuel Oil Tank A (GA056)	15	6/7/27 7:00 AM	6/23/27 5:00 PM	181
KPA.BOA.GA(	Test - Hydro - Fuel Oil Tank A (GA056)	5	6/24/27 7:00 AM	6/29/27 5:00 PM	181
KPA.BOA.GA(	Mech Complete - CBT - Fuel Oil Tank A (GA056)	0		6/29/27 5:00 PM	181
KPA.BOA.GA(	Install - Insulation - Fuel Oil Tank A (GA056)	36	6/30/27 7:00 AM	8/10/27 5:00 PM	181
BH CNN-KPJV-MAST-LIVE,40,04,FO,056,056B CONST - BoP AREA - (GA056) Fuel Oil Tank B					
KPA.BOA.GA(	Drive Pile - Fuel Oil Tank (B) (GA056) - Crane 1	0	6/30/26 7:00 AM A	7/28/26 5:00 PM A	
KPA.BOA.GA(	Start Tank - CBT - Fuel Oil Tank B [01/13/27] (GA056)	0	1/26/27 7:00 AM		141
KPA.BOA.GA(	Survey - Foundation - Fuel Oil Tank B (GA056)	1	1/26/27 7:00 AM	1/26/27 5:00 PM	141
KPA.BOA.GA(	Install - Bottom Plates - Fuel Oil Tank B (GA056)	2	1/27/27 7:00 AM	1/28/27 5:00 PM	141
KPA.BOA.GA(	Install - Stiffener Ring 2 - Fuel Oil Tank B (GA056)	10	2/3/27 7:00 AM	2/15/27 7:00 AM	141
KPA.BOA.GA(	Weld - Bottom Plates - Fuel Oil Tank B (GA056)	15	1/29/27 7:00 AM	2/15/27 5:00 PM	141
KPA.BOA.GA(	Install - Stiffener Ring 1 - Fuel Oil Tank B (GA056)	15	1/29/27 7:00 AM	2/15/27 5:00 PM	141
KPA.BOA.GA(	Cut - Door Sheet - Fuel Oil Tank B (GA056)	1	2/15/27 7:00 AM	2/15/27 5:00 PM	141
KPA.BOA.GA(	Install - Stiffener Ring 3 - Fuel Oil Tank B (GA056)	10	2/16/27 7:00 AM	2/26/27 5:00 PM	141
KPA.BOA.GA(	Install - Wind Protection - Fuel Oil Tank B (GA056)	3	2/27/27 7:00 AM	3/2/27 5:00 PM	148
KPA.BOA.GA(	Install - Stiffener Ring 4 - Fuel Oil Tank B (GA056)	10	2/27/27 7:00 AM	3/10/27 5:00 PM	141
KPA.BOA.GA(	Install - Stiffener Ring 5 - Fuel Oil Tank B (GA056)	10	3/11/27 7:00 AM	3/22/27 5:00 PM	141
KPA.BOA.GA(	Install - Nozzles & Manways - Fuel Oil Tank B (GA056)	40	2/16/27 7:00 AM	4/2/27 5:00 PM	141
KPA.BOA.GA(	Install - Lugs / Pipe Supports / Clips - Fuel Oil Tank B (GA056)	40	2/16/27 7:00 AM	4/2/27 5:00 PM	141
KPA.BOA.GA(	Install - Stiffener Ring 6 - Fuel Oil Tank B (GA056)	10	3/23/27 7:00 AM	4/2/27 5:00 PM	141
KPA.BOA.GA(	Install - Rim Angle - Fuel Oil Tank B (GA056)	4	4/3/27 7:00 AM	4/7/27 5:00 PM	141
KPA.BOA.GA(	Install - Install Girders / Rafters / Columns - Fuel Oil Tank B (GA(	9	4/8/27 7:00 AM	4/17/27 5:00 PM	141
KPA.BOA.GA(	Install - Install Roof Plates - Fuel Oil Tank B (GA056)	12	4/19/27 7:00 AM	5/1/27 5:00 PM	141
KPA.BOA.GA(	Install - Roof Insulation Rings - Fuel Oil Tank B (GA056)	7	5/3/27 7:00 AM	5/10/27 5:00 PM	141
KPA.BOA.GA(	Install - Insulation Angle on Stiffener Ring 1 - Fuel Oil Tank B (G/	4	5/11/27 7:00 AM	5/14/27 5:00 PM	141
KPA.BOA.GA(	Install - Roof Handrail & Platform - Fuel Oil Tank B (GA056)	3	5/15/27 7:00 AM	5/18/27 5:00 PM	141
KPA.BOA.GA(	Install - Spiral Staircase - Fuel Oil Tank B (GA056)	5	5/19/27 7:00 AM	5/24/27 5:00 PM	141
KPA.BOA.GA(	Install - Heaters - Fuel Oil Tank B (GA056)	1	5/25/27 7:00 AM	5/25/27 5:00 PM	141
KPA.BOA.GA(	Paint - Interior - Fuel Oil Tank B (GA056)	15	5/26/27 7:00 AM	6/11/27 5:00 PM	141
KPA.BOA.GA(	Install - Door Sheet - Fuel Oil Tank B (GA056)	4	6/12/27 7:00 AM	6/16/27 5:00 PM	141
KPA.BOA.GA(	Paint - Exterior - Fuel Oil Tank B (GA056)	15	6/17/27 7:00 AM	7/3/27 5:00 PM	141
KPA.BOA.GA(	Test - Hydro - Fuel Oil Tank B (GA056)	5	7/5/27 7:00 AM	7/9/27 5:00 PM	141
KPA.BOA.GA(	Mech Complete - CBT - Fuel Oil Tank B (GA056)	0		7/9/27 5:00 PM	141
KPA.BOA.GA(	Install - Insulation - Fuel Oil Tank B (GA056)	36	7/10/27 7:00 AM	8/20/27 5:00 PM	141
BH CNN-KPJV-MAST-LIVE,40,04,FO,057 CONST - BoP AREA - (GA057) Fuel Oil Tank Containment Berm					
KPA.BOA.GA0:	Install - Fire Water Loop Around Containment Berm (GA056)	30	8/23/27 7:00 AM	10/4/27 5:00 PM	123
KPA.BOA.GA0:	Build - Containment Berm (GA057) [8/15]	40	8/23/27 7:00 AM	10/18/27 5:00 PM	113
BH CNN-KPJV-MAST-LIVE,40,04,LF CONST - BoP - Liquid Fuel AREA					
BH CNN-KPJV-MAST-LIVE,40,04,LF,059 CONST - BoP AREA - (GA059) Liquid Fuel Enclosure					
KPA.BOA.GA0:	Drive Pile - Liquid Fuel Enclosure (GA059) - Crane 2	4	11/30/26 7:00 AM*	12/3/26 5:00 PM	2
KPA.BOP.ELE[	Install - U/G Electrical Duct Bank - Liquid Fuel Enclosure (GA05	5	3/18/27 7:00 AM	3/24/27 5:00 PM	178
KPA.BOA.GA0:	Install - U/G Fireprotection Piping - Liquid Fuel Enclosure (GA05	5	3/18/27 7:00 AM	3/24/27 5:00 PM	178

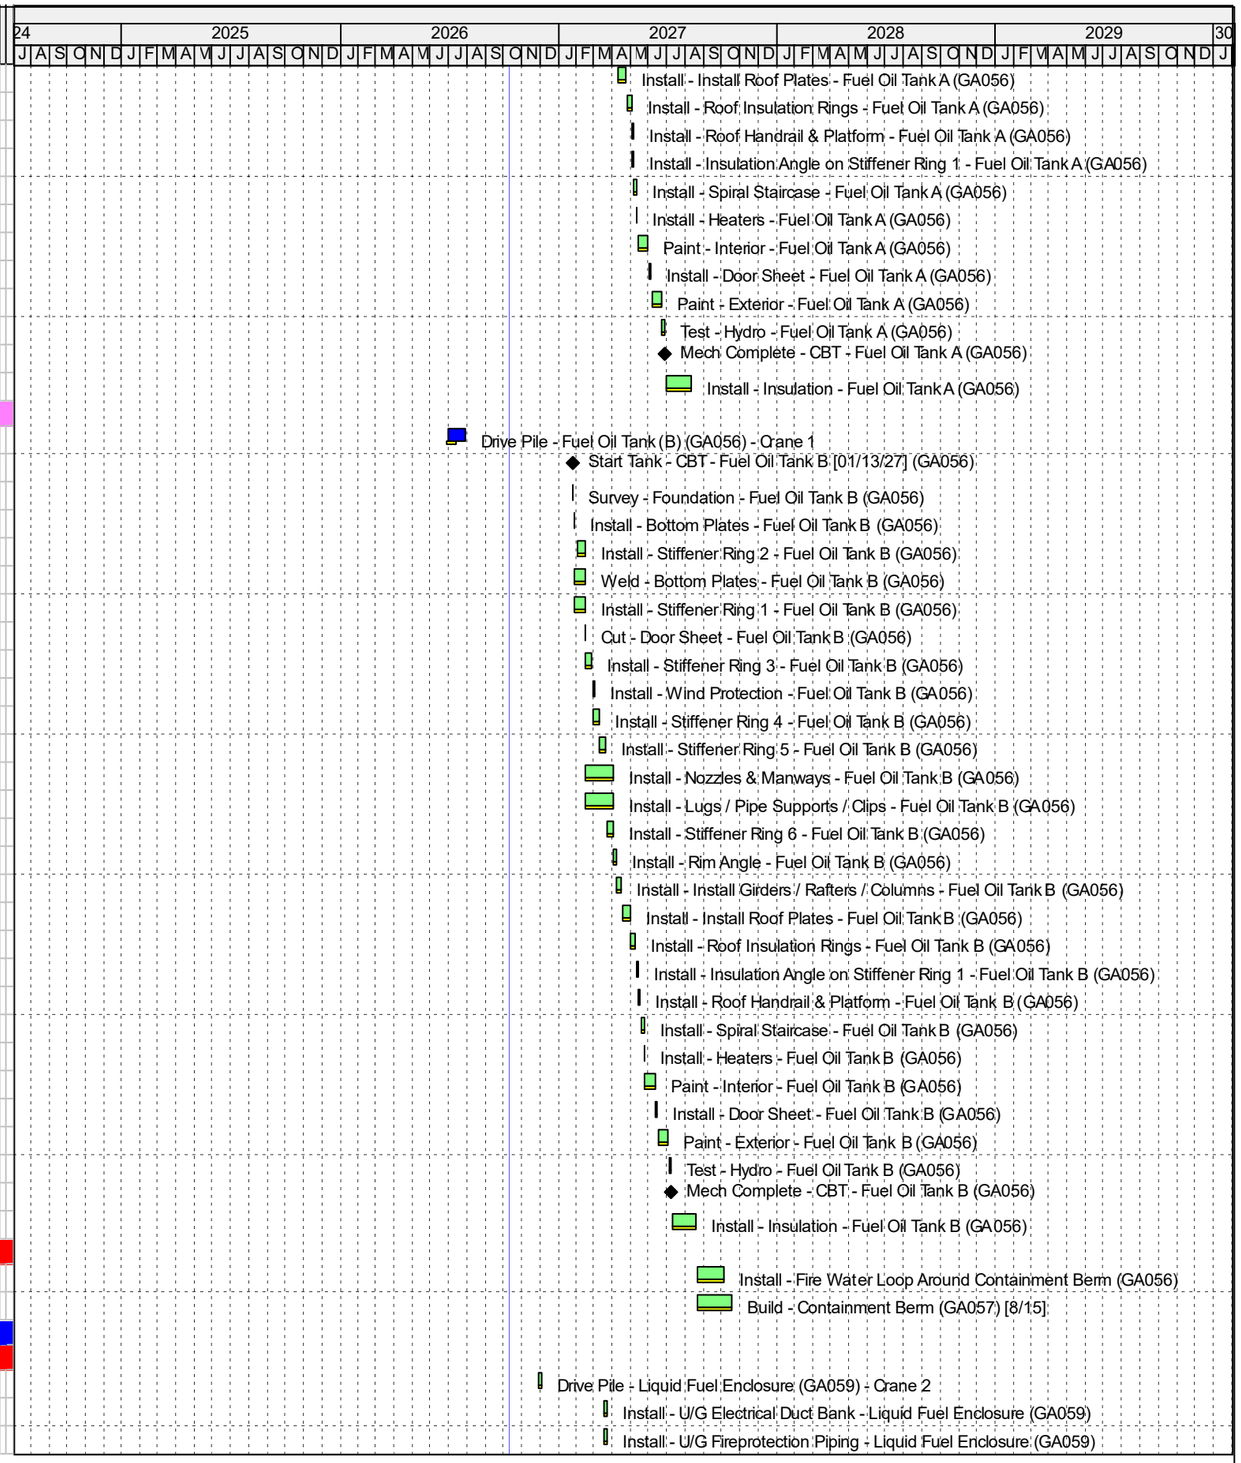

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.BOA.GA0	Install - U/G Process Pipe - Liquid Fuel Enclosure (GA059)	20	3/18/27 7:00 AM	4/14/27 5:00 PM	163
KPA.BOA.GA0	MFRP - Foundation - Liquid Fuel Enclosure (GA059) (Crew 2)	20	6/11/27 7:00 AM	7/9/27 5:00 PM	123
KPA.BOA.GA0	Install - PEMB - Liquid Fuel Enclosure (GA059)	60	7/12/27 7:00 AM	10/4/27 5:00 PM	123
BH CNN-KPJV-MAST-LIVE,40,04,LF,061 CONST - BoP AREA - (GA061) Liquid Fuel Pump (GE MLI 0092)					
KPA.BOA.GA0	Install - GE Liquid Fuel Pumps (Qty 4) (GA061)	15	11/1/27 7:00 AM	11/19/27 5:00 PM	74
BH CNN-KPJV-MAST-LIVE,40,04,N4 CONST - BoP - Ammonia AREA					
BH CNN-KPJV-MAST-LIVE,40,04,N4,063 CONST - BoP AREA - (GA063) Ammonia Unloading Station					
KPA.BOA.GA0	Drive Pile - Ammonia Unloading Station (GA063) - Crane 1	5	2/24/27 7:00 AM	3/2/27 5:00 PM	2
KPA.BOA.GA0	MFRP - Foundation - Ammonia Unloading Station (GA063)	10	3/3/27 7:00 AM	3/16/27 5:00 PM	204
KPA.BOA.GA0	Install - Ammonia Storage Skid (GA063)	15	8/23/27 7:00 AM	9/13/27 5:00 PM	138
KPA.BOA.GA0	Install - A/G Pipe - Ammonia Unloading Station (GA063)	140	4/23/27 7:00 AM	11/9/27 5:00 PM	97
BH CNN-KPJV-MAST-LIVE,40,04,N4,064 CONST - BoP AREA - (GA064) Ammonia Storage Tanks					
KPA.BOA.GA0	Install - A/G Pipe - Ammonia Storage Tanks (GA064)	140	4/23/27 7:00 AM	11/9/27 5:00 PM	97
BH CNN-KPJV-MAST-LIVE,40,04,N4,065 CONST - BoP AREA - (GA065) Ammonia Forwarding Pump					
KPA.BOA.GA0	Install - A/G Pipe - Ammonia Forwarding Pumps (GA065)	140	4/23/27 7:00 AM	11/9/27 5:00 PM	97
BH CNN-KPJV-MAST-LIVE,40,04,N4,066 CONST - BoP AREA - (GA066) Ammonia Unloading Pump					
KPA.BOA.GA0	Install - A/G Pipe - Ammonia Unloading Sump (GA066)	140	4/23/27 7:00 AM	11/9/27 5:00 PM	97
BH CNN-KPJV-MAST-LIVE,40,04,PS CONST - BoP - Plant Services AREA					
BH CNN-KPJV-MAST-LIVE,40,04,PS,069 CONST - BoP AREA - (GA069) Fire Pump House					
KPA.BOP.ELE	Install - U/G Electrical Duct Bank - Fire Water Pump House (GA	5	6/11/27 7:00 AM	6/17/27 5:00 PM	197
KPA.BOA.GA0	Install - U/G Fire Water Piping - Loop (GA069)	10	6/11/27 7:00 AM	6/24/27 5:00 PM	173
KPA.BOA.GA0	MFRP - Foundation - Fire Water Pump House (GA069)	10	6/11/27 7:00 AM	6/24/27 5:00 PM	133
KPA.BOA.GA0	Install - PEMB - Fire Water Pump House - Small Enclosure (GA	1	6/25/27 7:00 AM	6/25/27 5:00 PM	192
BH CNN-KPJV-MAST-LIVE,40,04,PS,070 CONST - BoP AREA - (GA070) Service Water / Fire Protection Tank					
KPA.BOA.GA0	Drive Pile - SW / FW Tank (GA070) - Crane 2	7	5/11/27 7:00 AM	5/19/27 5:00 PM	0
KPA.BOA.GA0	MFRP - Foundation - SW / FW Tank (GA070)	10	5/27/27 7:00 AM	6/10/27 5:00 PM	123
KPA.BOA.GA0	Start Tank - CBT - SW / FW Tank (GA070)	0	6/11/27 7:00 AM		357
KPA.BOA.GA0	Survey - Foundation - SW / FW Tank (GA070)	1	6/11/27 7:00 AM	6/11/27 5:00 PM	357
KPA.BOA.GA0	Install - Bottom Plates - SW / FW Tank (GA070)	2	6/12/27 7:00 AM	6/14/27 5:00 PM	357
KPA.BOA.GA0	Install - Stiffener Ring 1 - SW / FW Tank (GA070)	4	6/12/27 7:00 AM	6/16/27 5:00 PM	357
KPA.BOA.GA0	Install - Stiffener Ring 2 - SW / FW Tank (GA070)	4	6/17/27 7:00 AM	6/21/27 5:00 PM	357
KPA.BOA.GA0	Cut - Door Sheet - SW / FW Tank (GA070)	1	6/22/27 7:00 AM	6/22/27 5:00 PM	357
KPA.BOA.GA0	Weld - Bottom Plates - SW / FW Tank (GA070)	10	6/12/27 7:00 AM	6/23/27 5:00 PM	357
KPA.BOA.GA0	Install - Stiffener Ring 3 - SW / FW Tank (GA070)	4	6/23/27 7:00 AM	6/26/27 5:00 PM	357
KPA.BOA.GA0	Install - Anchor Chairs - SW / FW Tank (GA070)	5	6/28/27 7:00 AM	7/2/27 5:00 PM	357
KPA.BOA.GA0	Install - Stiffener Ring 4 - SW / FW Tank (GA070)	4	7/3/27 7:00 AM	7/7/27 5:00 PM	357
KPA.BOA.GA0	Install - Wind Protection - SW / FW Tank (GA070)	3	7/8/27 7:00 AM	7/10/27 5:00 PM	357
KPA.BOA.GA0	Install - Stiffener Ring 5 - SW / FW Tank (GA070)	4	7/12/27 7:00 AM	7/15/27 5:00 PM	357
KPA.BOA.GA0	Install - Rim Angle - SW / FW Tank (GA070)	4	7/16/27 7:00 AM	7/20/27 5:00 PM	357
KPA.BOA.GA0	Install - Interior NACE Grinding - SW / FW Tank (GA070)	21	6/28/27 7:00 AM	7/21/27 5:00 PM	357
KPA.BOA.GA0	Install - Nozzles & Manways - SW / FW Tank (GA070)	21	6/28/27 7:00 AM	7/21/27 5:00 PM	357
KPA.BOA.GA0	Build - Roof on Ground - SW / FW Tank (GA070)	5	7/21/27 7:00 AM	7/26/27 5:00 PM	357
KPA.BOA.GA0	Install - Roof Insulation Rings - SW / FW Tank (GA070)	3	7/27/27 7:00 AM	7/29/27 5:00 PM	357
KPA.BOA.GA0	Install - Insulation Angle on Stiffener Ring 1 - SW / FW Tank (G	3	7/30/27 7:00 AM	8/2/27 5:00 PM	357
KPA.BOA.GA0	Install - Roof - SW / FW Tank (GA070)	3	7/30/27 7:00 AM	8/2/27 5:00 PM	357
KPA.BOA.GA0	Install - Platform & Handrail - SW / FW Tank (GA070)	3	8/3/27 7:00 AM	8/5/27 5:00 PM	357
KPA.BOA.GA0	Install - Spiral Staircase - SW / FW Tank (GA070)	5	8/6/27 7:00 AM	8/11/27 5:00 PM	357
KPA.BOA.GA0	Install - Heaters - SW / FW Tank (GA070)	1	8/12/27 7:00 AM	8/12/27 5:00 PM	357
KPA.BOA.GA0	Paint - Interior - SW / FW Tank (GA070)	10	8/13/27 7:00 AM	8/24/27 5:00 PM	357
KPA.BOA.GA0	Install - Door Sheet - SW / FW Tank (GA070)	3	8/25/27 7:00 AM	8/27/27 5:00 PM	357
KPA.BOA.GA0	Paint - Exterior - SW / FW Tank (GA070)	7	8/28/27 7:00 AM	9/4/27 5:00 PM	357




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.BOA.GA0	Test - Hydro - SW / FW Tank (GA070)	5	9/6/27 7:00 AM	9/10/27 5:00 PM	357
KPA.BOA.GA0	Mech Complete - CBT - SW / FW Tank (GA070)	0		9/10/27 5:00 PM	357
KPA.BOA.GA0	LOE - Install - Tank - Service Water / Fire Water Tank (GA070)	99	6/11/27 7:00 AM	10/4/27 5:00 PM	357
KPA.BOA.GA0	Install - Insulation - SW / FW Tank (GA070)	20	9/11/27 7:00 AM	10/4/27 5:00 PM	357
BH CNN-KPJV-MAST-LIVE,40,04,PS,072 CONST - BoP AREA - (GA072) Plant Services Enclosure					
KPA.BOA.GA0	Drive Pile - PSE (Plant Services Enclosure) (GA072) - Crane 2	8	4/29/27 7:00 AM	5/10/27 5:00 PM	0
KPA.BOA.GA0	Install - U/G Pipe - PSE (Plant Services Enclosure) (GA072)	30	5/11/27 7:00 AM	6/22/27 5:00 PM	110
KPA.BOA.GA0	MFRP - Foundation - PSE (Plant Services Enclosure) (GA072)	15	6/23/27 7:00 AM	7/14/27 5:00 PM	110
KPA.BOA.GA0	Install - PEMB - PSE (Plant Services Enclosure) (GA072)	70	7/15/27 7:00 AM	10/21/27 5:00 PM	110
KPA.BOA.GA0	Install - Equipment - PSE (Plant Services Enclosure) (GA072)	100	6/2/27 7:00 AM	10/21/27 5:00 PM	110
BH CNN-KPJV-MAST-LIVE,40,04,PS,083 CONST - BoP AREA - (GA083) Demineralized Water Tanks Area					
KPA.BOA.GA0	Install - U/G Pipe - (Demineralized Water Sump/Tanks) (GA083)	10	4/29/27 7:00 AM	5/12/27 5:00 PM	213
KPA.BOP.ELE	Install - U/G Electrical Duct Bank - Demineralized Water Sump /	10	5/13/27 7:00 AM	5/26/27 5:00 PM	213
KPA.BOA.GA0	LOE - Install - Tanks - DWT (Demineralized Water Tanks) - Both	153	4/29/27 7:00 AM	10/23/27 5:00 PM	135
BH CNN-KPJV-MAST-LIVE,40,04,PS,083,1 CONST - BoP AREA - (GA083) Demineralized Water - South Tank					
KPA.BOA.GA(	Drive Pile - DWT (Demineralized Water Tank B) - South (GA083	20	3/4/27 7:00 AM	3/31/27 5:00 PM	0
KPA.BOA.GA(	MFRP - Foundation - DWT (Demineralized Water Tank) - South	20	4/1/27 7:00 AM	4/28/27 5:00 PM	109
KPA.BOA.GA(	Start Tank - CBT - Demineralized Water Tank South (GA083)	0	4/29/27 7:00 AM		158
KPA.BOA.GA(	Survey - Foundation - Demineralized Water Tank South (GA083	1	4/29/27 7:00 AM	4/29/27 5:00 PM	158
KPA.BOA.GA(	Install - Annular Ring - Demineralized Water Tank South (GA083	4	4/30/27 7:00 AM	5/4/27 5:00 PM	158
KPA.BOA.GA(	Install - Bottom Plates - Demineralized Water Tank South (GA08	2	5/5/27 7:00 AM	5/6/27 5:00 PM	158
KPA.BOA.GA(	Install - Stiffener Ring 1 - Demineralized Water Tank South (GA(	8	5/5/27 7:00 AM	5/13/27 5:00 PM	158
KPA.BOA.GA(	Weld - Bottom Plates - Demineralized Water Tank South (GA08	10	5/5/27 7:00 AM	5/15/27 5:00 PM	158
KPA.BOA.GA(	Install - Stiffener Ring 2 - Demineralized Water Tank South (GA(	8	5/10/27 7:00 AM	5/18/27 5:00 PM	158
KPA.BOA.GA(	Cut - Door sheet - Demineralized Water Tank South (GA083)	1	5/19/27 7:00 AM	5/19/27 5:00 PM	158
KPA.BOA.GA(	Install - Stiffener Ring 3 - Demineralized Water Tank South (GA(	7	5/19/27 7:00 AM	5/26/27 5:00 PM	158
KPA.BOA.GA(	Install - Wind Protection - Demineralized Water Tank South (GA	4	5/27/27 7:00 AM	5/31/27 5:00 PM	161
KPA.BOA.GA(	Install - Stiffener Ring 4 - Demineralized Water Tank South (GA(	8	5/27/27 7:00 AM	6/4/27 5:00 PM	158
KPA.BOA.GA(	Install - Stiffener Ring 5 - Demineralized Water Tank South (GA(	7	6/5/27 7:00 AM	6/12/27 5:00 PM	158
KPA.BOA.GA(	Install - Stiffener Ring 6 - Demineralized Water Tank South (GA(	7	6/12/27 7:00 AM	6/19/27 5:00 PM	158
KPA.BOA.GA(	Install - Stiffener Ring 7 - Demineralized Water Tank South (GA(	7	6/21/27 7:00 AM	6/28/27 5:00 PM	158
KPA.BOA.GA(	Install - Stiffener Ring 8 - Demineralized Water Tank South (GA(	7	6/29/27 7:00 AM	7/6/27 5:00 PM	158
KPA.BOA.GA(	Install - Rim Angle - Demineralized Water Tank South (GA083)	4	7/7/27 7:00 AM	7/10/27 5:00 PM	158
KPA.BOA.GA(	Install - Nozzles & Manways - Demineralized Water Tank South	41	5/27/27 7:00 AM	7/13/27 5:00 PM	161
KPA.BOA.GA(	Install - Lugs / Pipe Supports / Clips - Demineralized Water Tank	41	5/27/27 7:00 AM	7/13/27 5:00 PM	161
KPA.BOA.GA(	Install - Girders / Rafters / Columns - Demineralized Water Tank	5	7/12/27 7:00 AM	7/16/27 5:00 PM	158
KPA.BOA.GA(	Install - Insulation Angle on Stiffener Ring 1 - Demineralized Wa	4	7/17/27 7:00 AM	7/21/27 5:00 PM	162
KPA.BOA.GA(	Install - Roof Plates - Demineralized Water Tank South (GA083)	8	7/17/27 7:00 AM	7/26/27 5:00 PM	158
KPA.BOA.GA(	Install - Roof Handrail & Platform - Demineralized Water Tank Sc	3	7/27/27 7:00 AM	7/29/27 5:00 PM	158
KPA.BOA.GA(	Install - Insulation Rings on Roof - Demineralized Water Tank Sc	5	7/27/27 7:00 AM	7/31/27 5:00 PM	158
KPA.BOA.GA(	Install - Sprial Staircase - Demineralized Water Tank South (GA(	5	7/30/27 7:00 AM	8/4/27 5:00 PM	158
KPA.BOA.GA(	Clean Interior - Demineralized Water Tank South (GA083)	2	8/5/27 7:00 AM	8/6/27 5:00 PM	158
KPA.BOA.GA(	Install - Door sheet - Demineralized Water Tank South (GA083)	3	8/7/27 7:00 AM	8/10/27 5:00 PM	158
KPA.BOA.GA(	Install - Heaters - Demineralized Water Tank South (GA083)	1	8/11/27 7:00 AM	8/11/27 5:00 PM	158
KPA.BOA.GA(	Test - Hydro - Demineralized Water Tank South (GA083)	5	8/11/27 7:00 AM	8/16/27 5:00 PM	158
KPA.BOA.GA(	Mech Complete - CBT - Demineralized Water Tank South (GA08	0		8/16/27 5:00 PM	399
KPA.BOA.GA(	Install - Insulation - Demineralized Water Tank South (GA083)	36	8/17/27 7:00 AM	9/27/27 5:00 PM	158
BH CNN-KPJV-MAST-LIVE,40,04,PS,083,2 CONST - BoP AREA - (GA083) Demineralized Water - North Tank					
KPA.BOA.GA(	Drive Pile - DWT (Demineralized Water Tank A) - North (GA083)	20	4/1/27 7:00 AM	4/28/27 5:00 PM	0
KPA.BOA.GA(	MFRP - Foundation - DWT (Demineralized Water Tank) - North (	20	4/29/27 7:00 AM	5/26/27 5:00 PM	109

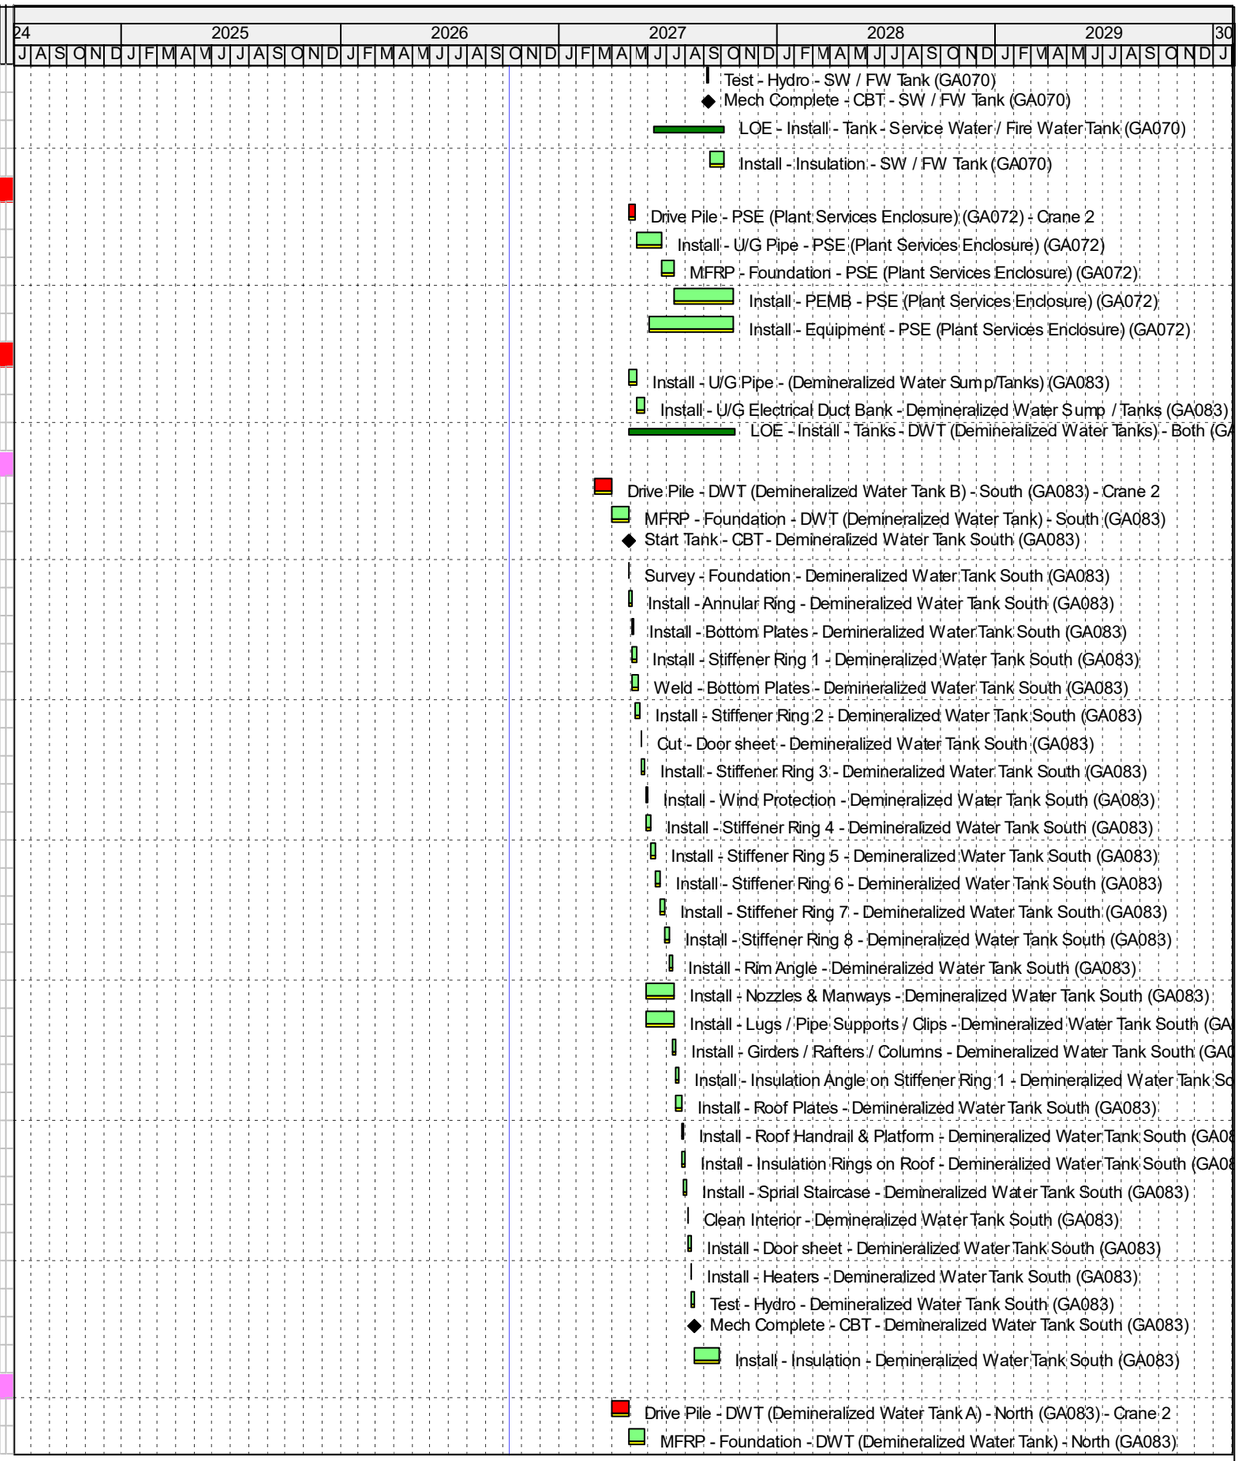


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.BOA.GA(	Start Tank - CBT - Demineralized Water Tank North (GA083)	0	5/27/27 7:00 AM		135
KPA.BOA.GA(	Survey - Foundation - Demineralized Water Tank North (GA083)	1	5/27/27 7:00 AM	5/27/27 5:00 PM	135
KPA.BOA.GA(	Install - Annular Ring - Demineralized Water Tank North (GA083)	4	5/28/27 7:00 AM	6/1/27 5:00 PM	135
KPA.BOA.GA(	Install - Bottom Plates - Demineralized Water Tank North (GA08	2	6/2/27 7:00 AM	6/3/27 5:00 PM	135
KPA.BOA.GA(	Install - Stiffener Ring 1 - Demineralized Water Tank North (GA0	8	6/2/27 7:00 AM	6/10/27 5:00 PM	135
KPA.BOA.GA(	Weld - Bottom Plates - Demineralized Water Tank North (GA08	10	6/2/27 7:00 AM	6/12/27 5:00 PM	135
KPA.BOA.GA(	Install - Stiffener Ring 2 - Demineralized Water Tank North (GA0	8	6/7/27 7:00 AM	6/15/27 5:00 PM	135
KPA.BOA.GA(	Cut - Door sheet - Demineralized Water Tank North (GA083)	1	6/16/27 7:00 AM	6/16/27 5:00 PM	135
KPA.BOA.GA(	Install - Stiffener Ring 3 - Demineralized Water Tank North (GA0	7	6/16/27 7:00 AM	6/23/27 5:00 PM	135
KPA.BOA.GA(	Install - Wind Protection - Demineralized Water Tank North (GA(	4	6/24/27 7:00 AM	6/28/27 5:00 PM	138
KPA.BOA.GA(	Install - Stiffener Ring 4 - Demineralized Water Tank North (GA0	8	6/24/27 7:00 AM	7/2/27 5:00 PM	135
KPA.BOA.GA(	Install - Stiffener Ring 5 - Demineralized Water Tank North (GA0	7	7/3/27 7:00 AM	7/10/27 5:00 PM	135
KPA.BOA.GA(	Install - Stiffener Ring 6 - Demineralized Water Tank North (GA0	7	7/10/27 7:00 AM	7/17/27 5:00 PM	135
KPA.BOA.GA(	Install - Stiffener Ring 7 - Demineralized Water Tank North (GA0	7	7/19/27 7:00 AM	7/26/27 5:00 PM	135
KPA.BOA.GA(	Install - Stiffener Ring 8 - Demineralized Water Tank North (GA0	7	7/27/27 7:00 AM	8/3/27 5:00 PM	135
KPA.BOA.GA(	Install - Rim Angle - Demineralized Water Tank North (GA083)	4	8/4/27 7:00 AM	8/7/27 5:00 PM	135
KPA.BOA.GA(	Install - Nozzles & Manways - Demineralized Water Tank North (	41	6/24/27 7:00 AM	8/10/27 5:00 PM	138
KPA.BOA.GA(	Install - Lugs / Pipe Supports / Clips - Demineralized Water Tank	41	6/24/27 7:00 AM	8/10/27 5:00 PM	138
KPA.BOA.GA(	Install - Girders / Rafters / Columns - Demineralized Water Tank	5	8/9/27 7:00 AM	8/13/27 5:00 PM	135
KPA.BOA.GA(	Install - Insulation Angle on Stiffener Ring 1 - Demineralized Wa	4	8/14/27 7:00 AM	8/18/27 5:00 PM	139
KPA.BOA.GA(	Install - Roof Plates - Demineralized Water Tank North (GA083)	8	8/14/27 7:00 AM	8/23/27 5:00 PM	135
KPA.BOA.GA(	Install - Roof Handrail & Platform - Demineralized Water Tank N	3	8/24/27 7:00 AM	8/26/27 5:00 PM	135
KPA.BOA.GA(	Install - Insulation Rings on Roof - Demineralized Water Tank N	5	8/24/27 7:00 AM	8/28/27 5:00 PM	135
KPA.BOA.GA(	Install - Sprial Staircase - Demineralized Water Tank North (GA0	5	8/27/27 7:00 AM	9/1/27 5:00 PM	135
KPA.BOA.GA(	Clean Interior - Demineralized Water Tank North (GA083)	2	9/2/27 7:00 AM	9/3/27 5:00 PM	135
KPA.BOA.GA(	Install - Door sheet - Demineralized Water Tank North (GA083)	3	9/4/27 7:00 AM	9/7/27 5:00 PM	135
KPA.BOA.GA(	Install - Heaters - Demineralized Water Tank North (GA083)	1	9/8/27 7:00 AM	9/8/27 5:00 PM	135
KPA.BOA.GA(	Test - Hydro - Demineralized Water Tank North (GA083)	5	9/8/27 7:00 AM	9/13/27 5:00 PM	135
KPA.BOA.GA(	Mech Complete - CBT - Demineralized Water Tank North (GA08	0		9/13/27 5:00 PM	135
KPA.BOA.GA(	Install - Insulation - Demineralized Water Tank North (GA083)	35	9/14/27 7:00 AM	10/23/27 5:00 PM	135
BH CNN-KPJV-MAST-LIVE,40,04,PS,084 CONST - BoP AREA - (GA084) Wastewater Collection Sump					
KPA.BOA.GA0	Excavate - Waste Water Collection Sump (Demineralized Wate	3	3/8/27 7:00 AM	3/10/27 5:00 PM	188
KPA.BOA.GA0	MFRP - Foundation - Waste Water Collection Sump - (Demineral	20	3/11/27 7:00 AM	4/7/27 5:00 PM	188
BH CNN-KPJV-MAST-LIVE,40,T1 CONST - Train 1					
KPA.CTG3.GA03	Drive Pile - Isophase Bus Supports - Train 1 (GA035) - Crane 2	5	2/25/27 7:00 AM	3/3/27 5:00 PM	0
BH CNN-KPJV-MAST-LIVE,40,T1,007 CONST - Train 1 - (GA007) SCR & SCR Exhaust Stack					
KPA.CTG1.GA0	Drive Pile - SCR & Stack - Train 1 (GA011) - Crane 2	14	12/7/26 7:00 AM	12/24/26 5:00 PM	2
KPA.CTG1.GA0	MFRP - Foundation - SCR & Exhaust Stack - Train 1 (GA007)	25	3/18/27 7:00 AM	4/21/27 5:00 PM	7
KPA.CTG1.GA0	Verify / Survey / Layout - Main Equip - SCR - Train 1	9	4/22/27 7:00 AM	5/4/27 5:00 PM	153
KPA.CTG1.GA0	Fab - Section 1 (Breech Section) - Main Equip - SCR - Train 1	9	5/5/27 7:00 AM	5/17/27 5:00 PM	153
KPA.CTG1.GA0	Install - U/G Interconnect Pipe - SCR - Train 1 (GA011)	20	4/22/27 7:00 AM	5/19/27 5:00 PM	383
KPA.CTG1.GA0	Install - Bottom 49' Breech Stack Section - Main Equip - SCR - T	2	5/18/27 7:00 AM	5/19/27 5:00 PM	153
KPA.CTG1.GA0	Install - Inlet DSCR Duct Through Primary Duct A - Main Equip -	13	5/10/27 7:00 AM	5/26/27 5:00 PM	153
KPA.CTG1.GA0	Fab - Middle Stack Sections - Main Equip - SCR - Train 1	9	5/18/27 7:00 AM	5/28/27 5:00 PM	157
KPA.CTG1.GA0	Weld - Internal & External Ducts - Main Equip - SCR - Train 1	3	5/27/27 7:00 AM	6/1/27 5:00 PM	153
KPA.CTG1.GA0	Install - Middle Section Of 45' Stack - Main Equip - SCR - Train 1	2	6/1/27 7:00 AM	6/2/27 5:00 PM	157
KPA.CTG1.GA0	Fit & Weld - Lower Horizontal Stack Seam - Main Equip - SCR -	2	6/3/27 7:00 AM	6/4/27 5:00 PM	157
KPA.CTG1.GA0	Fab - Upper 45' Section Of Stack With Catwalk - Main Equip - S	7	6/2/27 7:00 AM	6/10/27 5:00 PM	153
KPA.CTG1.GA0	Install - Fan Outlet Dampers & Expansion Joints - Main Equip -	2	6/14/27 7:00 AM	6/15/27 5:00 PM	153
KPA.CTG1.GA0	Install - Upper Top Section Of Stack & Catwalk - Main Equip - S(	2	6/14/27 7:00 AM	6/15/27 5:00 PM	153

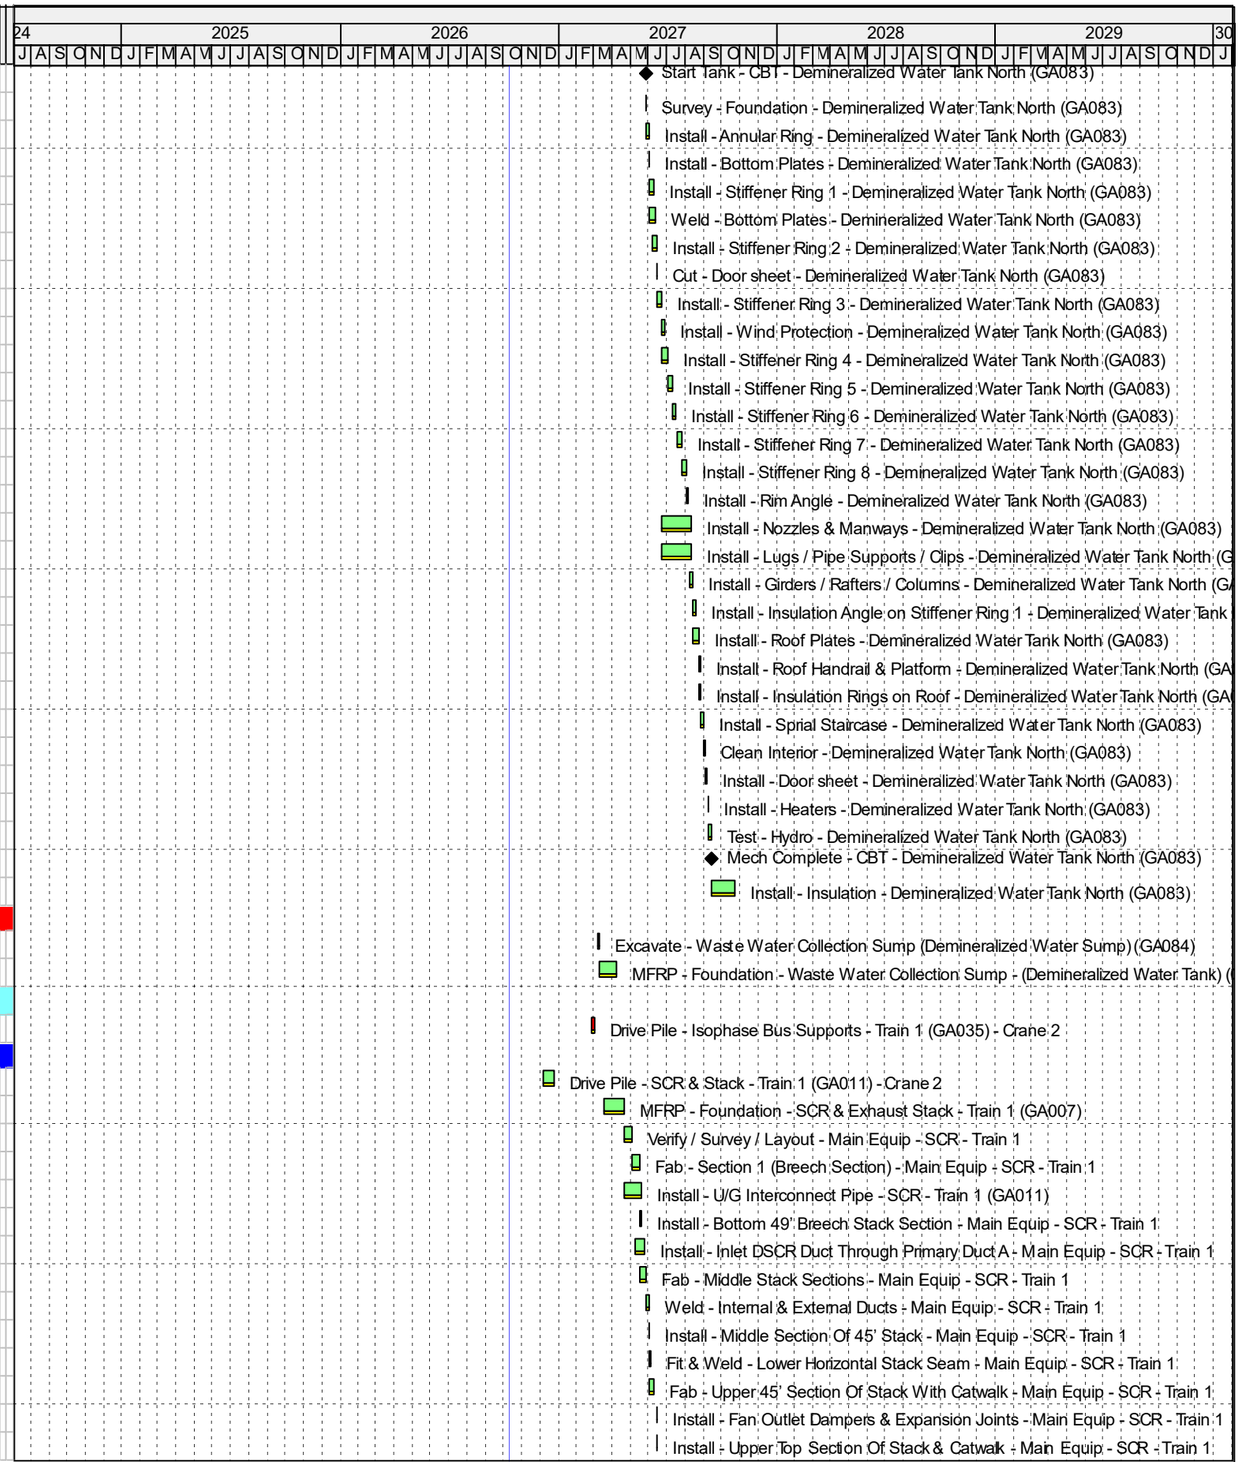


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.CTG1.GA0	Install - Fan Inlet Silencers - Main Equip - SCR - Train 1	3	6/16/27 7:00 AM	6/18/27 5:00 PM	153
KPA.CTG1.GA0	Install - U/G Interconnect Electrical - SCR - Train 1 (GA011)	42	4/22/27 7:00 AM	6/21/27 5:00 PM	122
KPA.CTG1.GA0	Weld - Top Horizontal Stack Seam - Main Equip - SCR - Train 1	2	6/21/27 7:00 AM	6/22/27 5:00 PM	153
KPA.CTG1.GA0	Install - All Inlet Duct Seam Insulation & Liner Plates - Main Equ	7	6/23/27 7:00 AM	7/1/27 5:00 PM	153
KPA.CTG1.GA0	Install - Internal Stack Insulation & Liners - Main Equip - SCR - T	4	6/28/27 7:00 AM	7/1/27 5:00 PM	153
KPA.CTG1.GA0	Install - Cable Pull - SCR - Train 1 (GA011)	50	6/22/27 7:00 AM	8/31/27 5:00 PM	122
KPA.CTG1.GA0	Install - OFE Supplied Piping & Supports Packages - SCR - Trai	100	5/14/27 7:00 AM	10/5/27 5:00 PM	98
KPA.CTG1.GA0	Install - Balance Of Inlet Duct Ladders & Platforms - Main Equip	3	11/3/27 7:00 AM	11/5/27 5:00 PM	75
KPA.CTG1.GA0	Install - Equipment Electrical / Instrumentation - SCR - Train 1 (G	145	4/22/27 7:00 AM	11/15/27 5:00 PM	93
KPA.CTG1.GA0	LOE - Install - OFE Equipment Packages - Misc Major - SCR - Ti	148	4/22/27 7:00 AM	11/18/27 5:00 PM	66
KPA.CTG1.GA0	Load - All SCR Catalyst Blocks - Main Equip - SCR - Train 1	20	2/1/28 7:00 AM	2/29/28 5:00 PM	64
BH CNN-KPJV-MAST-LIVE,40,T1,011 CONST - Train 1 - (GA011) CT Generator					
KPA.CTG1.GA0	Drive Pile - CTG - Train 1 (GA011) - Crane 2	14	12/30/26 7:00 AM	1/19/27 5:00 PM	0
KPA.CTG1.GA0	Install - U/G Electrical Under Mudmat CTG - Train 1	10	1/27/27 7:00 AM	2/9/27 5:00 PM	7
KPA.CTG1.GA0	Install - Grounding - CTG - Train 1 (GA011)	4	2/18/27 7:00 AM	2/23/27 5:00 PM	175
KPA.CTG1.GA0	Install - In Slab Electrical + 5ft - CTG / SCR - Train 1 (GA011)	5	2/19/27 7:00 AM	2/25/27 5:00 PM	116
KPA.CTG1.GA0	Install - In Slab & U/G Pipe + 5ft - CTG - Train 1 (GA011)	5	2/19/27 7:00 AM	2/25/27 5:00 PM	116
KPA.CTG1.GA0	MFRP - Foundation - CTG - Train 1 (GA011)	25	2/10/27 7:00 AM	3/17/27 5:00 PM	7
KPA.CTG1.GA0	FRP - Pedestal - CTG - Train 1 (GA011)	15	3/18/27 7:00 AM	4/7/27 5:00 PM	102
KPA.CTG1.GA0	Excavate - U/G Interconnect Utilities - CTG - Train 1 (GA011)	5	4/6/27 7:00 AM	4/12/27 5:00 PM	136
KPA.CTG1.GA0	Install - U/G Interconnect Pipe - CTG - Train 1 (GA011)	20	4/9/27 7:00 AM	5/6/27 5:00 PM	203
KPA.CTG1.GA0	Install - U/G Interconnect Electrical - CTG - Train 1 (GA011)	42	4/19/27 7:00 AM	6/16/27 5:00 PM	130
KPA.CTG1.GA0	Install - Cable Pull - CTG - Train 1 (GA011)	45	6/17/27 7:00 AM	8/19/27 5:00 PM	130
KPA.CTG1.GA0	Install - OFE Equipment Package - Misc Other - SCR - CTG - Tra	20	11/1/27 7:00 AM	11/29/27 5:00 PM	0
KPA.CTG1.GA0	Install - OFE Equipment Package - Generator / Gas Turbine - C	122	9/1/27 7:00 AM	2/24/28 5:00 PM	0
KPA.CTG1.GA0	Install - Equipment Electrical / Instrumentation - CTG - Train 1 (G	80	11/1/27 7:00 AM	2/24/28 5:00 PM	0
KPA.CTG1.GA0	Install - OFE Supplied Piping & Supports Packages - CTG - Trai	80	11/1/27 7:00 AM	2/24/28 5:00 PM	0
BH CNN-KPJV-MAST-LIVE,40,T1,015 CONST - Train 1 - (GA015) SCR Filter House					
KPA.CTG1.GA0	Drive Pile - Filter House - Train 1 - Crane 2	7	2/11/27 7:00 AM	2/22/27 5:00 PM	0
KPA.CTG1.GA0	Install - (2) Inlet Filter House Transitions - Main Equip - SCR - Tra	6	11/1/27 7:00 AM	11/8/27 5:00 PM	66
KPA.CTG1.GA0	Install - Inlet Filter House Modules - Main Equip - SCR - Train 1	5	11/9/27 7:00 AM	11/15/27 5:00 PM	66
KPA.CTG1.GA0	Install - Inlet House Filters - Main Equip - SCR - Train 1	3	11/16/27 7:00 AM	11/18/27 5:00 PM	66
BH CNN-KPJV-MAST-LIVE,40,T1,016 CONST - Train 1 - (GA016) SCR Tempering Air Fan					
KPA.CTG1.GA0	Set - Tempering Fans (4 Total) - Main Equip - SCR - Train 1	5	5/11/27 7:00 AM	5/17/27 5:00 PM	157
KPA.CTG1.GA0	Install - Tempering Air Duct Support Steel - Main Equip - SCR - T	8	5/20/27 7:00 AM	6/1/27 5:00 PM	153
KPA.CTG1.GA0	Install - Tempering Air Ducts - Main Equip - SCR - Train 1	7	6/2/27 7:00 AM	6/10/27 5:00 PM	153
KPA.CTG1.GA0	Install - Tempering Air Duct Expansion Joints - Main Equip - SCF	1	6/11/27 7:00 AM	6/11/27 5:00 PM	153
BH CNN-KPJV-MAST-LIVE,40,T1,017 CONST - Train 1 - (GA017) SCR Ammonia Flow Control Unit					
KPA.CTG1.GA0	Drive Pile - Ammonia Flow Control - Train 1 (GA017) - Crane 2	1	1/20/27 7:00 AM	1/20/27 5:00 PM	11
BH CNN-KPJV-MAST-LIVE,40,T1,018 CONST - Train 1 - (GA018) CEMS					
KPA.CTG1.GA0	Drive Pile - CEMS - Train 1 (GA018) - Crane 2	1	1/26/27 7:00 AM	1/26/27 5:00 PM	0
KPA.CTG1.GA0	Install - OFE Equipment Package - CEMS - Train 1 (GA018)	10	8/2/27 7:00 AM	8/13/27 5:00 PM	241
KPA.CTG1.GA0	Install - OFE Supplied Piping & Supports Packages - CEMS - Tr	15	8/3/27 7:00 AM	8/23/27 5:00 PM	241
KPA.CTG1.GA0	Install - Equipment Electrical / Instrumentation - CEMS - Train 1	15	8/3/27 7:00 AM	8/23/27 5:00 PM	241
BH CNN-KPJV-MAST-LIVE,40,T1,020 CONST - Train 1 - (GA020) Gas Fuel Filtering Skid (GE MLI G015)					
KPA.CTG1.GA0	Install - GE Supplied Fuel Gas Absolute Separator Skid - Train 1	15	11/1/27 7:00 AM	11/19/27 5:00 PM	65
BH CNN-KPJV-MAST-LIVE,40,T1,021 CONST - Train 1 - (GA021) Fuel Gas CTG Drain Tank					
KPA.CTG1.GA0	Install - Fuel Gas CTG Drain Tank - Train 1 (GA021)	15	11/1/27 7:00 AM	11/19/27 5:00 PM	65
BH CNN-KPJV-MAST-LIVE,40,T1,022 CONST - Train 1 - (GA022) Water Mist Fire Fighting Skid (GE MLI A273)					
KPA.CTG1.GA0	Install - GE Supplied Water Mist Fire Fighting Skid - Train 1 (GA	15	11/1/27 7:00 AM	11/19/27 5:00 PM	65
KPA.CTG1.GA0	Install - A/G Pipe - GE Water Mist Fire Fighting Skid - Train 1 (G	130	6/16/27 7:00 AM	12/17/27 5:00 PM	46

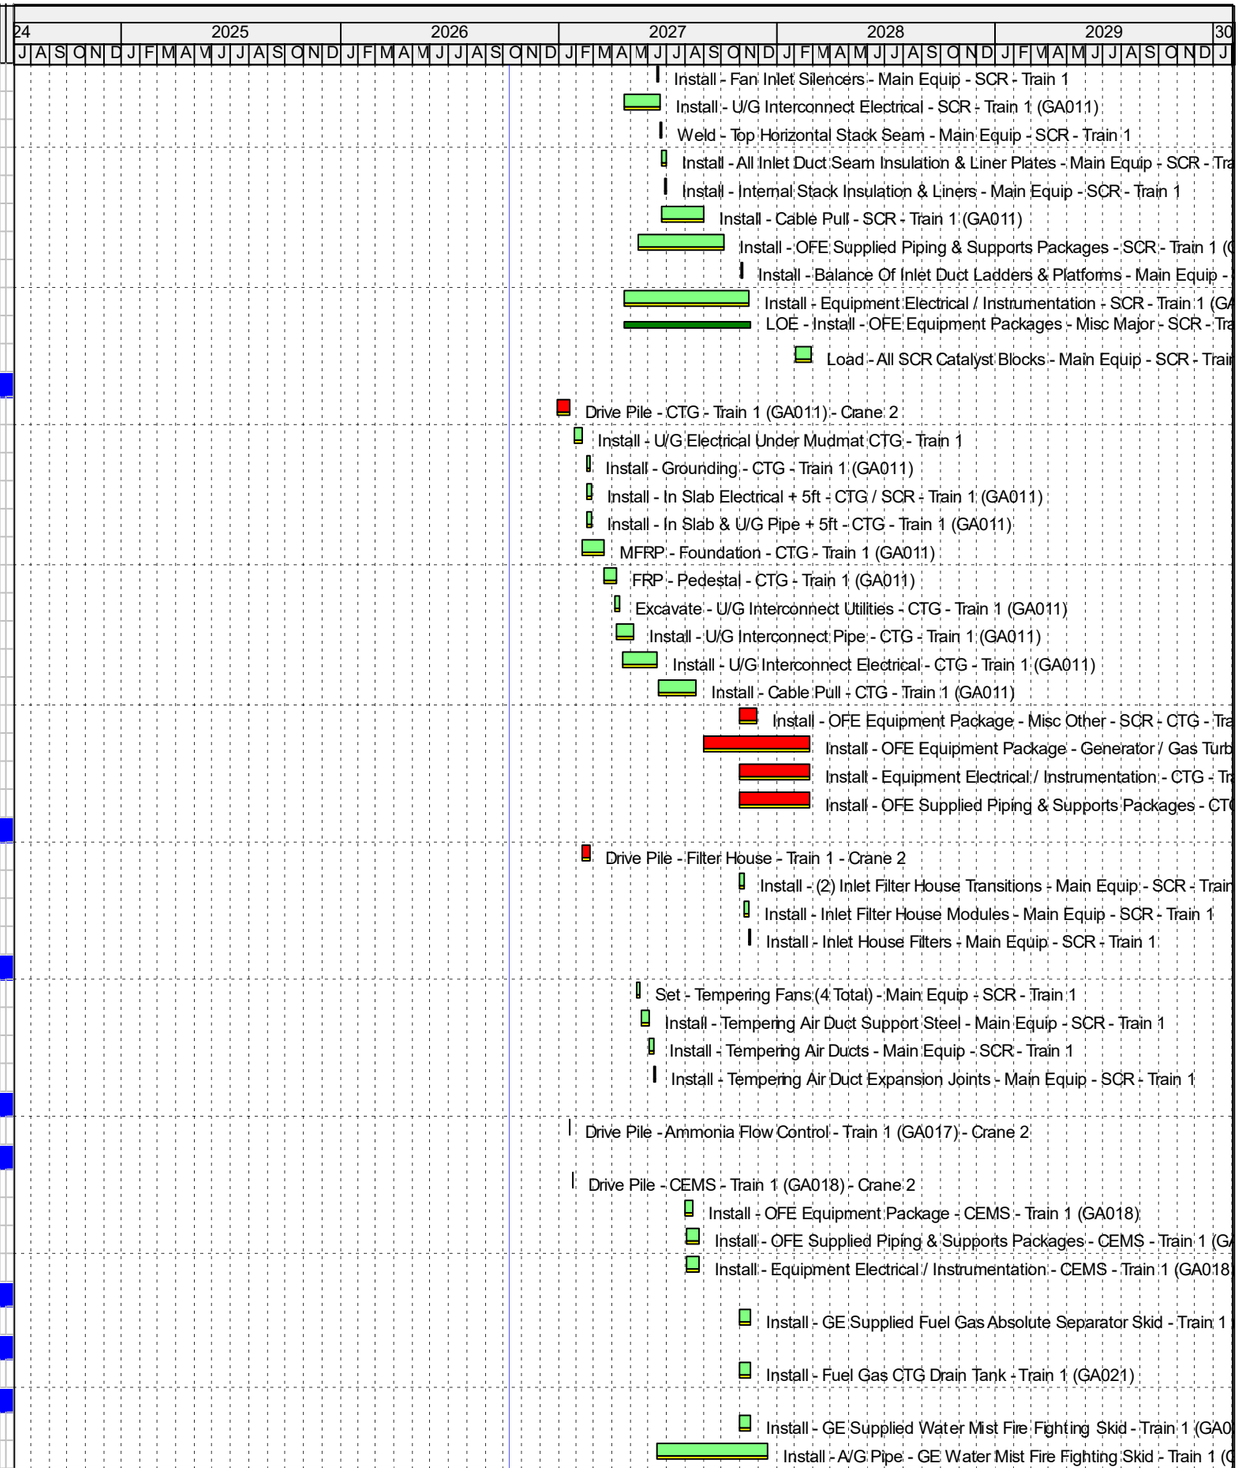

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
BH CNN-KPJV-MAST-LIVE,40,T1,024 CONST - Train 1 - (GA024) Accessory Module (GE MLI A160)					
KPA.CTG1.GA0:	Drive Pile - Accessory Module - Train 1 (GA024) - Crane 2	2	2/5/27 7:00 AM	2/8/27 5:00 PM	0
BH CNN-KPJV-MAST-LIVE,40,T1,026 CONST - Train 1 - (GA026) Lube Oil Conditioner (GE MLI F056)					
KPA.CTG1.GA0:	Install - A/G Pipe - GE Lube Oil Conditioner - Train 1 (GA026)	130	4/30/27 7:00 AM	11/2/27 5:00 PM	78
BH CNN-KPJV-MAST-LIVE,40,T1,027 CONST - Train 1 - (GA027) AC Reactor (GE MLI A140)					
KPA.CTG1.GA0:	Install - OFE Equipment Package - GE AC Reactor - Train 1 (GA	15	11/1/27 7:00 AM	11/19/27 5:00 PM	65
BH CNN-KPJV-MAST-LIVE,40,T1,028 CONST - Train 1 - (GA028) DC Link Reactor (GE MLI A140)					
KPA.CTG1.GA0:	Install - OFE Equipment Package - GE DC Link Reactor - Train 1	15	11/1/27 7:00 AM	11/19/27 5:00 PM	65
BH CNN-KPJV-MAST-LIVE,40,T1,029 CONST - Train 1 - (GA029) Dehumidification Skid (GE MLI 1049)					
KPA.CTG1.GA0:	Install - OFE Equipment Package - GE Dehumidification Skid - T	15	11/1/27 7:00 AM	11/19/27 5:00 PM	65
BH CNN-KPJV-MAST-LIVE,40,T1,030 CONST - Train 1 - (GA030) PEECC (GE MLI A059) / (GA031) LEC (GE MLI A192)					
KPA.CTG1.GA0:	Drive Pile - PEECC/LEC - Train 1 (GA030) - Crane 2	2	2/23/27 7:00 AM	2/24/27 5:00 PM	0
BH CNN-KPJV-MAST-LIVE,40,T1,031 CONST - Train 1 - (GA031) LEC (GE MLI A192)					
KPA.CTG1.GA0:	Install - GE PEECC/LEC - Train 1 (GA030) / (GA031)	15	8/2/27 7:00 AM	8/20/27 5:00 PM	129
BH CNN-KPJV-MAST-LIVE,40,T1,032 CONST - Train 1 - (GA032) CT Excitation Transformer (GE MLI A150)					
KPA.CTG1.GA0:	Install - OFE Equipment Package - GE CT Excitation Transforme	15	8/2/27 7:00 AM	8/20/27 5:00 PM	129
BH CNN-KPJV-MAST-LIVE,40,T1,033 CONST - Train 1 - (GA033) CT Isolation Transformer (GE MLI A141)					
KPA.CTG1.GA0:	Install - OFE Equipment Package - GE CT Isolation Transformer	15	11/1/27 7:00 AM	11/19/27 5:00 PM	65
BH CNN-KPJV-MAST-LIVE,40,T1,034 CONST - Train 1 - (GA034) CT Oil Containing Sump					
KPA.CTG1.GA0:	Install - OFE Equipment Package - CT Oil Containing Sump - Tr	15	11/1/27 7:00 AM	11/19/27 5:00 PM	65
BH CNN-KPJV-MAST-LIVE,40,T1,035 CONST - Train 1 - (GA035) Isophase Bus/Generator Circuit Breaker Supports					
KPA.CTG1.GA0:	Install - Isophase Bus/Generator Circuit Breaker Supports - Trair	15	10/15/27 7:00 AM	11/4/27 5:00 PM	76
BH CNN-KPJV-MAST-LIVE,40,T1,036 CONST - Train 1 - (GA036) Unit Aux Transformer (1&3 Only)					
KPA.CTG1.GA0:	Drive Pile - Unit Aux Transformer - Train 1 (GA036) - Crane 2	2	2/9/27 7:00 AM	2/10/27 5:00 PM	0
KPA.CTG1.GA0:	MFRP - Foundation & Pedestal - Unit Aux - Train 1 (GA036)	10	2/11/27 7:00 AM	2/25/27 5:00 PM	237
KPA.CTG1.GA0:	Install - BoP U/G Electrical - Unit Aux Transformer - Train 1 (GA0	5	2/26/27 7:00 AM	3/4/27 5:00 PM	248
KPA.CTG1.GA0:	Install - U/G Pipe - Unit Aux Transformer - Train 1 (GA036)	5	2/26/27 7:00 AM	3/4/27 5:00 PM	248
KPA.CTG1.GA0:	Install - OFE Equipment Package - Unit Aux Transformer - Train	10	11/1/27 7:00 AM	11/12/27 5:00 PM	64
KPA.CTG1.GA0:	Install - OFE Supplied Piping & Supports Packages - Unit Aux Tr	15	11/2/27 7:00 AM	11/22/27 5:00 PM	64
KPA.CTG1.GA0:	Install - Equipment Electrical / Instrumentation - Unit Aux Transfo	15	11/2/27 7:00 AM	11/22/27 5:00 PM	64
BH CNN-KPJV-MAST-LIVE,40,T1,037 CONST - Train 1 - (GA037) Generator Step-up Transformer (1&3 Only)					
KPA.CTG1.GA0:	Drive Pile - GSU (Generator Step Up) Transformer - CTG - Train	6	2/25/27 7:00 AM	3/4/27 5:00 PM	0
KPA.CTG1.GA0:	MFRP - Foundation & Pedestal - GSU (Generator Step Up) Trar	10	3/5/27 7:00 AM	3/18/27 5:00 PM	220
KPA.CTG1.GA0:	Install - BoP U/G Electrical - GSU (Generator Step Up) Transfom	5	3/19/27 7:00 AM	3/25/27 5:00 PM	233
KPA.CTG1.GA0:	Install - U/G Pipe - GSU (Generator Step Up) Transformer - CTG	5	3/19/27 7:00 AM	3/25/27 5:00 PM	233
KPA.CTG1.GA0:	Install - OFE Equipment Package - GSU (Generator Step Up) Tr	15	6/1/27 7:00 AM	6/21/27 5:00 PM	169
KPA.CTG1.GA0:	Install - Equipment Electrical / Instrumentation - GSU (Generato	15	6/2/27 7:00 AM	6/22/27 5:00 PM	171
KPA.CTG1.GA0:	Install - OFE Supplied Piping & Supports Packages - GSU (Gen	15	6/4/27 7:00 AM	6/24/27 5:00 PM	169
BH CNN-KPJV-MAST-LIVE,40,T1,039 CONST - Train 1 - (GA039) 138kV Station Service Transformer (1 Only)					
KPA.CTG1.GA0:	Drive Pile - 138kV Station Service Transformer - Train 1 (GA039	6	1/27/27 7:00 AM	2/3/27 5:00 PM	0
KPA.CTG1.GA0:	MFRP - Foundation & Pedestal - 138kV Station Service Transfo	10	2/4/27 7:00 AM	2/18/27 5:00 PM	240
KPA.CTG1.GA0:	Install - BoP U/G Electrical - 138kV Station Service Transformer	5	2/19/27 7:00 AM	2/25/27 5:00 PM	253
KPA.CTG1.GA0:	Install - U/G Pipe - 138kV Station Service Transformer - Train 1 (	5	2/19/27 7:00 AM	2/25/27 5:00 PM	253
KPA.CTG1.GA0:	Install - OFE Equipment Package - 138kV Station Service Trans	15	6/1/27 7:00 AM	6/21/27 5:00 PM	169
KPA.CTG1.GA0:	Install - Equipment Electrical / Instrumentation - 138kV Station S	15	6/2/27 7:00 AM	6/22/27 5:00 PM	171
KPA.CTG1.GA0:	Install - OFE Supplied Piping & Supports Packages - 138kV Sta	15	6/4/27 7:00 AM	6/24/27 5:00 PM	169
BH CNN-KPJV-MAST-LIVE,40,T1,041 CONST - Train 1 - (GA041) Power Distribution Center (PDC)					
KPA.CTG1.GA0:	Drive Pile - Power Distribution Center (PDC) - Train 1 (GA041) - C	4	1/20/27 7:00 AM	1/25/27 5:00 PM	0
KPA.CTG1.GA0:	MFRP - Foundation - Power Distribution Center (PDC) (GA041) -	6	1/26/27 7:00 AM	2/2/27 5:00 PM	177
KPA.CTG1.GA0:	FRP - Piers - Power Distribution Center (PDC) (GA041) - Train 1	15	2/3/27 7:00 AM	2/24/27 5:00 PM	177
KPA.CTG1.GA0:	Pick & Set - Power Distribution Center (PDC) (GA041) - Train 1	2	2/25/27 7:00 AM	2/26/27 5:00 PM	177
KPA.CTG1.GA0:	Cable Pull - Power Distribution Center (PDC) (GA041) - Train 1	30	3/22/27 7:00 AM	4/30/27 5:00 PM	162



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.CTG1.GA0	Install - Electrical (Inside) - Power Distribution Center (PDC) (GA(	45	5/3/27 7:00 AM	7/6/27 5:00 PM	162
BH CNN-KPJV-MAST-LIVE,40,T1,042 CONST - Train 1 - (GA042) Secondary Unit Substation Transformer					
KPA.CTG1.GA0	Install - Secondary Unit Substation Transformer - Train 1 (GA04	15	11/1/27 7:00 AM	11/19/27 5:00 PM	65
BH CNN-KPJV-MAST-LIVE,40,T1,043 CONST - Train 1 - (GA043) Carbon Dioxide Bottle Manifold (GE MLI G1F0)					
KPA.CTG1.GA0	Install - A/G Pipe - GE Carbon Dioxide Bottle Manifold - Train 1 (	140	4/30/27 7:00 AM	11/16/27 5:00 PM	68
BH CNN-KPJV-MAST-LIVE,40,T1,045 CONST - Train 1 - (GA045) Air Processing Unit (APU) ((GE MLI A130)					
KPA.CTG1.GA0	Install - OFE Equipment Package - GE Air Processing Unit - Trai	15	11/1/27 7:00 AM	11/19/27 5:00 PM	65
BH CNN-KPJV-MAST-LIVE,40,T1,047 CONST - Train 1 - (GA047) Hydrogen Gas Dryer (GE ML G2MA)					
KPA.CTG1.GA0	Install - A/G Pipe - GE Hydrogen Gas Dryer - Train 1 (GA047)	115	4/23/27 7:00 AM	10/5/27 5:00 PM	98
BH CNN-KPJV-MAST-LIVE,40,T1,048 CONST - Train 1 - (GA048) CT Wastewater Sumps					
KPA.CTG1.GA0	Install - OFE Equipment Package - CT Wastewater Sumps - Tra	15	11/1/27 7:00 AM	11/19/27 5:00 PM	65
BH CNN-KPJV-MAST-LIVE,40,T1,050 CONST - Train 1 - (GA050) Water Wash/False Start Drains Tank					
KPA.CTG1.GA0	Install - CFE Equipment - False Start Drain Tank - CTG - Train 1	5	1/20/27 7:00 AM	1/26/27 5:00 PM	7
BH CNN-KPJV-MAST-LIVE,40,T1,051 CONST - Train 1 - (GA051) Cooling Water Module (GE MLI A076)					
KPA.CTG1.GA0	Drive Pile - Cooling Water Module - Train 1 (GA051) - Crane 2	3	12/28/26 7:00 AM	12/30/26 5:00 PM	24
KPA.CTG1.GA0	Install - OFE Equipment Package - Cooling Water Module - Trai	15	8/2/27 7:00 AM	8/20/27 5:00 PM	129
BH CNN-KPJV-MAST-LIVE,40,T1,052 CONST - Train 1 - (GA052) Chemical Pot Feeder					
KPA.CTG1.GA0	Install - A/G Pipe - CCW / Chemical Pot Feed - Train 1 (GA052)	182	4/28/27 7:00 AM	1/14/28 5:00 PM	28
BH CNN-KPJV-MAST-LIVE,40,T1,082 CONST - Train 1 - (GA082) Aux Transformer					
KPA.CTG1.GA0	Install - OFE Equipment Package - Aux Transformer - Train 1 (G	10	3/8/27 7:00 AM	3/19/27 5:00 PM	237
BH CNN-KPJV-MAST-LIVE,40,T2 CONST - Train 2					
KPA.CTG3.GA03	Drive Pile - Isophase Bus Supports - Train 2 (GA035) - Crane 1	4	3/23/27 7:00 AM	3/26/27 5:00 PM	13
BH CNN-KPJV-MAST-LIVE,40,T2,008 CONST - Train 2 - (GA008) SCR & SCR Exhaust Stack					
KPA.CTG2.GA0	Drive Pile - SCR & Stack - Train 2 (GA012) - Crane 1	10	4/19/27 7:00 AM	4/30/27 5:00 PM	43
KPA.CTG2.GA0	MFRP - Foundation - SCR & Exhaust Stack - Train 2 (GA008)	25	6/15/27 7:00 AM	7/20/27 5:00 PM	13
KPA.CTG2.GA0	Verify / Survey / Layout - Main Equip - SCR - Train 2	9	7/21/27 7:00 AM	8/2/27 5:00 PM	102
KPA.CTG2.GA0	Fab - Section 1 (Breech Section) - Main Equip - SCR - Train 2	9	8/3/27 7:00 AM	8/13/27 5:00 PM	102
KPA.CTG2.GA0	Install - U/G Interconnect Pipe - SCR - Train 2 (GA012)	20	7/21/27 7:00 AM	8/17/27 5:00 PM	143
KPA.CTG2.GA0	Install - Bottom 49' Breech Stack Section - Main Equip - SCR - T	2	8/16/27 7:00 AM	8/17/27 5:00 PM	102
KPA.CTG2.GA0	Install - Inlet DSCR Duct Through Primary Duct A - Main Equip -	13	8/6/27 7:00 AM	8/24/27 5:00 PM	102
KPA.CTG2.GA0	Fab - Middle Stack Sections - Main Equip - SCR - Train 2	9	8/16/27 7:00 AM	8/26/27 5:00 PM	106
KPA.CTG2.GA0	Weld - Internal & External Ducts - Main Equip - SCR - Train 2	3	8/25/27 7:00 AM	8/27/27 5:00 PM	102
KPA.CTG2.GA0	Install - Middle Section Of 45' Stack - Main Equip - SCR - Train 2	2	8/27/27 7:00 AM	8/30/27 5:00 PM	106
KPA.CTG2.GA0	Fit & Weld - Lower Horizontal Stack Seam - Main Equip - SCR -	2	8/31/27 7:00 AM	9/1/27 5:00 PM	106
KPA.CTG2.GA0	Fab - Upper 45' Section Of Stack With Catwalk - Main Equip - S	7	8/30/27 7:00 AM	9/8/27 5:00 PM	102
KPA.CTG2.GA0	Install - Fan Outlet Dampers & Expansion Joints - Main Equip -	2	9/10/27 7:00 AM	9/13/27 5:00 PM	102
KPA.CTG2.GA0	Install - Upper Top Section Of Stack & Catwalk - Main Equip - St	2	9/10/27 7:00 AM	9/13/27 5:00 PM	102
KPA.CTG2.GA0	Install - Fan Inlet Silencers - Main Equip - SCR - Train 2	3	9/14/27 7:00 AM	9/16/27 5:00 PM	102
KPA.CTG2.GA0	Install - U/G Interconnect Electrical - SCR - Train 2 (GA012)	42	7/21/27 7:00 AM	9/17/27 5:00 PM	51
KPA.CTG2.GA0	Weld - Top Horizontal Stack Seam - Main Equip - SCR - Train 2	2	9/17/27 7:00 AM	9/20/27 5:00 PM	102
KPA.CTG2.GA0	Install - All Inlet Duct Seam Insulation & Liner Plates - Main Equ	7	9/21/27 7:00 AM	9/29/27 5:00 PM	102
KPA.CTG2.GA0	Install - Internal Stack Insulation & Liners - Main Equip - SCR - T	4	9/24/27 7:00 AM	9/29/27 5:00 PM	102
KPA.CTG2.GA0	Install - Balance Of Inlet Duct Ladders & Platforms - Main Equip	3	10/6/27 7:00 AM	10/8/27 5:00 PM	106
KPA.CTG2.GA0	LOE - Install - OFE Equipment Packages - Misc Major - SCR - Tr	66	7/21/27 7:00 AM	10/21/27 5:00 PM	97
KPA.CTG2.GA0	Install - OFE Supplied Piping & Supports Packages - SCR - Trair	100	7/21/27 7:00 AM	12/9/27 5:00 PM	63
KPA.CTG2.GA0	Install - Cable Pull - SCR - Train 2 (GA012)	70	9/20/27 7:00 AM	12/28/27 5:00 PM	51
KPA.CTG2.GA0	Install - Equipment Electrical / Instrumentation - SCR - Train 2 (G	150	7/21/27 7:00 AM	2/22/28 5:00 PM	13
KPA.CTG2.GA0	Load - All SCR Catalyst Blocks - Main Equip - SCR - Train 2	20	2/1/28 7:00 AM	2/29/28 5:00 PM	81
BH CNN-KPJV-MAST-LIVE,40,T2,012 CONST - Train 2 - (GA012) CT Generator					
KPA.CTG2.GA0	Drive Pile - CTG - Train 2 (GA012) - Crane 1	15	3/29/27 7:00 AM	4/16/27 5:00 PM	13
KPA.CTG2.GA0	Install - U/G Electrical Under Mudmat CTG - Train 2	10	4/26/27 7:00 AM	5/7/27 5:00 PM	13




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.CTG2.GA0	Install - Grounding - CTG - Train 2 (GA012)	4	5/10/27 7:00 AM	5/13/27 5:00 PM	139
KPA.CTG2.GA0	Install - In Slab Electrical + 5ft - CTG / SCR - Train 2 (GA012)	5	5/18/27 7:00 AM	5/24/27 5:00 PM	75
KPA.CTG2.GA0	Install - In Slab & U/G Pipe + 5ft - CTG - Train 2 (GA012)	5	5/18/27 7:00 AM	5/24/27 5:00 PM	75
KPA.CTG2.GA0	MFRP - Foundation - CTG - Train 2 (GA012)	25	5/10/27 7:00 AM	6/14/27 5:00 PM	13
KPA.CTG2.GA0	Excavate - U/G Interconnect Utilities - CTG - Train 2 (GA012)	5	6/15/27 7:00 AM	6/21/27 5:00 PM	73
KPA.CTG2.GA0	FRP - Pedestal - CTG - Train 2 (GA012)	15	6/15/27 7:00 AM	7/6/27 5:00 PM	61
KPA.CTG2.GA0	Install - U/G Interconnect Pipe - CTG - Train 2 (GA012)	20	6/18/27 7:00 AM	7/16/27 5:00 PM	165
KPA.CTG2.GA0	Install - U/G Interconnect Electrical - CTG - Train 2 (GA012)	42	6/18/27 7:00 AM	8/17/27 5:00 PM	73
KPA.CTG2.GA0	Install - Cable Pull - CTG - Train 2 (GA012)	70	8/18/27 7:00 AM	11/24/27 5:00 PM	73
KPA.CTG2.GA0	Install - OFE Equipment Package - Misc Other - SCR - CTG - Tra	20	12/1/27 7:00 AM	12/29/27 5:00 PM	0
KPA.CTG2.GA0	Install - OFE Equipment Package - Generator / Gas Turbine - C	112	10/1/27 7:00 AM	3/10/28 5:00 PM	0
KPA.CTG2.GA0	Install - OFE Supplied Piping & Supports Packages - CTG - Trair	70	12/1/27 7:00 AM	3/10/28 5:00 PM	0
KPA.CTG2.GA0	Install - Equipment Electrical / Instrumentation - CTG - Train 2 (G	70	12/1/27 7:00 AM	3/10/28 5:00 PM	0
BH CNN-KPJV-MAST-LIVE,40,T2,016 CONST - Train 2 - (GA016) SCR Tempering Air Fan					
KPA.CTG2.GA0	Set - Tempering Fans (4 Total) - Main Equip - SCR - Train 2	5	8/9/27 7:00 AM	8/13/27 5:00 PM	106
KPA.CTG2.GA0	Install - Tempering Air Duct Support Steel - Main Equip - SCR - T	8	8/18/27 7:00 AM	8/27/27 5:00 PM	102
KPA.CTG2.GA0	Install - Tempering Air Ducts - Main Equip - SCR - Train 2	7	8/30/27 7:00 AM	9/8/27 5:00 PM	102
KPA.CTG2.GA0	Install - Tempering Air Duct Expansion Joints - Main Equip - SCF	1	9/9/27 7:00 AM	9/9/27 5:00 PM	102
BH CNN-KPJV-MAST-LIVE,40,T2,015 CONST - Train 2 - (GA015) SCR Filter House					
KPA.CTG2.GA0	Drive Pile - Filter House - Train 2 - Crane 1	7	3/12/27 7:00 AM	3/22/27 5:00 PM	13
KPA.CTG2.GA0	Install - (2) Inlet Filter House Transitions - Main Equip - SCR - Tra	6	10/4/27 7:00 AM	10/11/27 5:00 PM	97
KPA.CTG2.GA0	Install - Inlet Filter House Modules - Main Equip - SCR - Train 2	5	10/12/27 7:00 AM	10/18/27 5:00 PM	97
KPA.CTG2.GA0	Install - Inlet House Filters - Main Equip - SCR - Train 2	3	10/19/27 7:00 AM	10/21/27 5:00 PM	97
BH CNN-KPJV-MAST-LIVE,40,T2,017 CONST - Train 2 - (GA017) SCR Ammonia Flow Control Unit					
KPA.CTG2.GA0	Drive Pile - Ammonia Flow Control - Train 2 (GA017) - Crane 1	1	5/13/27 7:00 AM	5/13/27 5:00 PM	77
BH CNN-KPJV-MAST-LIVE,40,T2,018 CONST - Train 2 - (GA018) CEMS					
KPA.CTG2.GA0	Drive Pile - CEMS - Train 2 (GA018) - Crane 1	1	5/7/27 7:00 AM	5/7/27 5:00 PM	77
KPA.CTG2.GA0	Install - OFE Equipment Package - CEMS - Train 2 (GA018)	10	8/2/27 7:00 AM	8/13/27 5:00 PM	239
KPA.CTG2.GA0	Install - Equipment Electrical / Instrumentation - CEMS - Train 2	15	8/3/27 7:00 AM	8/23/27 5:00 PM	241
KPA.CTG2.GA0	Install - OFE Supplied Piping & Supports Packages - CEMS - Tr	15	8/5/27 7:00 AM	8/25/27 5:00 PM	239
BH CNN-KPJV-MAST-LIVE,40,T2,019 CONST - Train 2 - (GA019) Water Wash Skid (GE MLI E025)					
KPA.CTG2.GA0	Install - Water Wash Skid - Train 2 (GA019)	15	8/2/27 7:00 AM	8/20/27 5:00 PM	140
BH CNN-KPJV-MAST-LIVE,40,T2,020 CONST - Train 2 - (GA020) Gas Fuel Filtering Skid (GE MLI G015)					
KPA.CTG2.GA0	Install - GE Supplied Fuel Gas Filtering Skid - Train 2 (GA020)	15	12/1/27 7:00 AM	12/21/27 5:00 PM	55
BH CNN-KPJV-MAST-LIVE,40,T2,021 CONST - Train 2 - (GA021) Fuel Gas CTG Drain Tank					
KPA.CTG2.GA0	Install - Fuel Gas CTG Drain Tank - Train 2 (GA021)	15	12/1/27 7:00 AM	12/21/27 5:00 PM	55
BH CNN-KPJV-MAST-LIVE,40,T2,022 CONST - Train 2 - (GA022) Water Mist Fire Fighting Skid (GE MLI A273)					
KPA.CTG2.GA0	Install - GE Supplied Water Mist Fire Fighting Skid - Train 2 (GA	15	12/1/27 7:00 AM	12/21/27 5:00 PM	55
KPA.CTG2.GA0	Install - A/G Pipe - GE Water Mist Fire Fighting Skid - Train 2 (G/	160	6/16/27 7:00 AM	2/1/28 5:00 PM	27
BH CNN-KPJV-MAST-LIVE,40,T2,024 CONST - Train 2 - (GA024) Accessory Module (GE MLI A160)					
KPA.CTG2.GA0	Drive Pile - Accessory Module - Train 2 (GA024) - Crane 1	2	3/10/27 7:00 AM	3/11/27 5:00 PM	13
BH CNN-KPJV-MAST-LIVE,40,T2,026 CONST - Train 2 - (GA026) Lube Oil Conditioner (GE MLI F056)					
KPA.CTG2.GA0	Install - A/G Pipe - GE Lube Oil Conditioner - Train 2 (GA026)	182	4/30/27 7:00 AM	1/18/28 5:00 PM	37
BH CNN-KPJV-MAST-LIVE,40,T2,027 CONST - Train 2 - (GA027) AC Reactor (GE MLI A140)					
KPA.CTG2.GA0	Install - OFE Equipment Package - GE AC Reactor - Train 2 (GA	15	12/1/27 7:00 AM	12/21/27 5:00 PM	55
BH CNN-KPJV-MAST-LIVE,40,T2,028 CONST - Train 2 - (GA028) DC Link Reactor (GE MLI A140)					
KPA.CTG2.GA0	Install - OFE Equipment Package - GE DC Link Reactor - Train 2	15	12/1/27 7:00 AM	12/21/27 5:00 PM	55
BH CNN-KPJV-MAST-LIVE,40,T2,029 CONST - Train 2 - (GA029) Dehumidification Skid (GE MLI 1049)					
KPA.CTG2.GA0	Install - OFE Equipment Package - GE Dehumidification Skid - T	15	12/1/27 7:00 AM	12/21/27 5:00 PM	55
BH CNN-KPJV-MAST-LIVE,40,T2,030 CONST - Train 2 - (GA030) PEECC (GE MLI A059) / (GA031) LEC (GE MLI A192)					
KPA.CTG2.GA0	Drive Pile - PEECC/LEC - Train 2 (GA030) - Crane 1	2	3/8/27 7:00 AM	3/9/27 5:00 PM	13
BH CNN-KPJV-MAST-LIVE,40,T2,031 CONST - Train 2 - (GA031) LEC (GE MLI A192)					

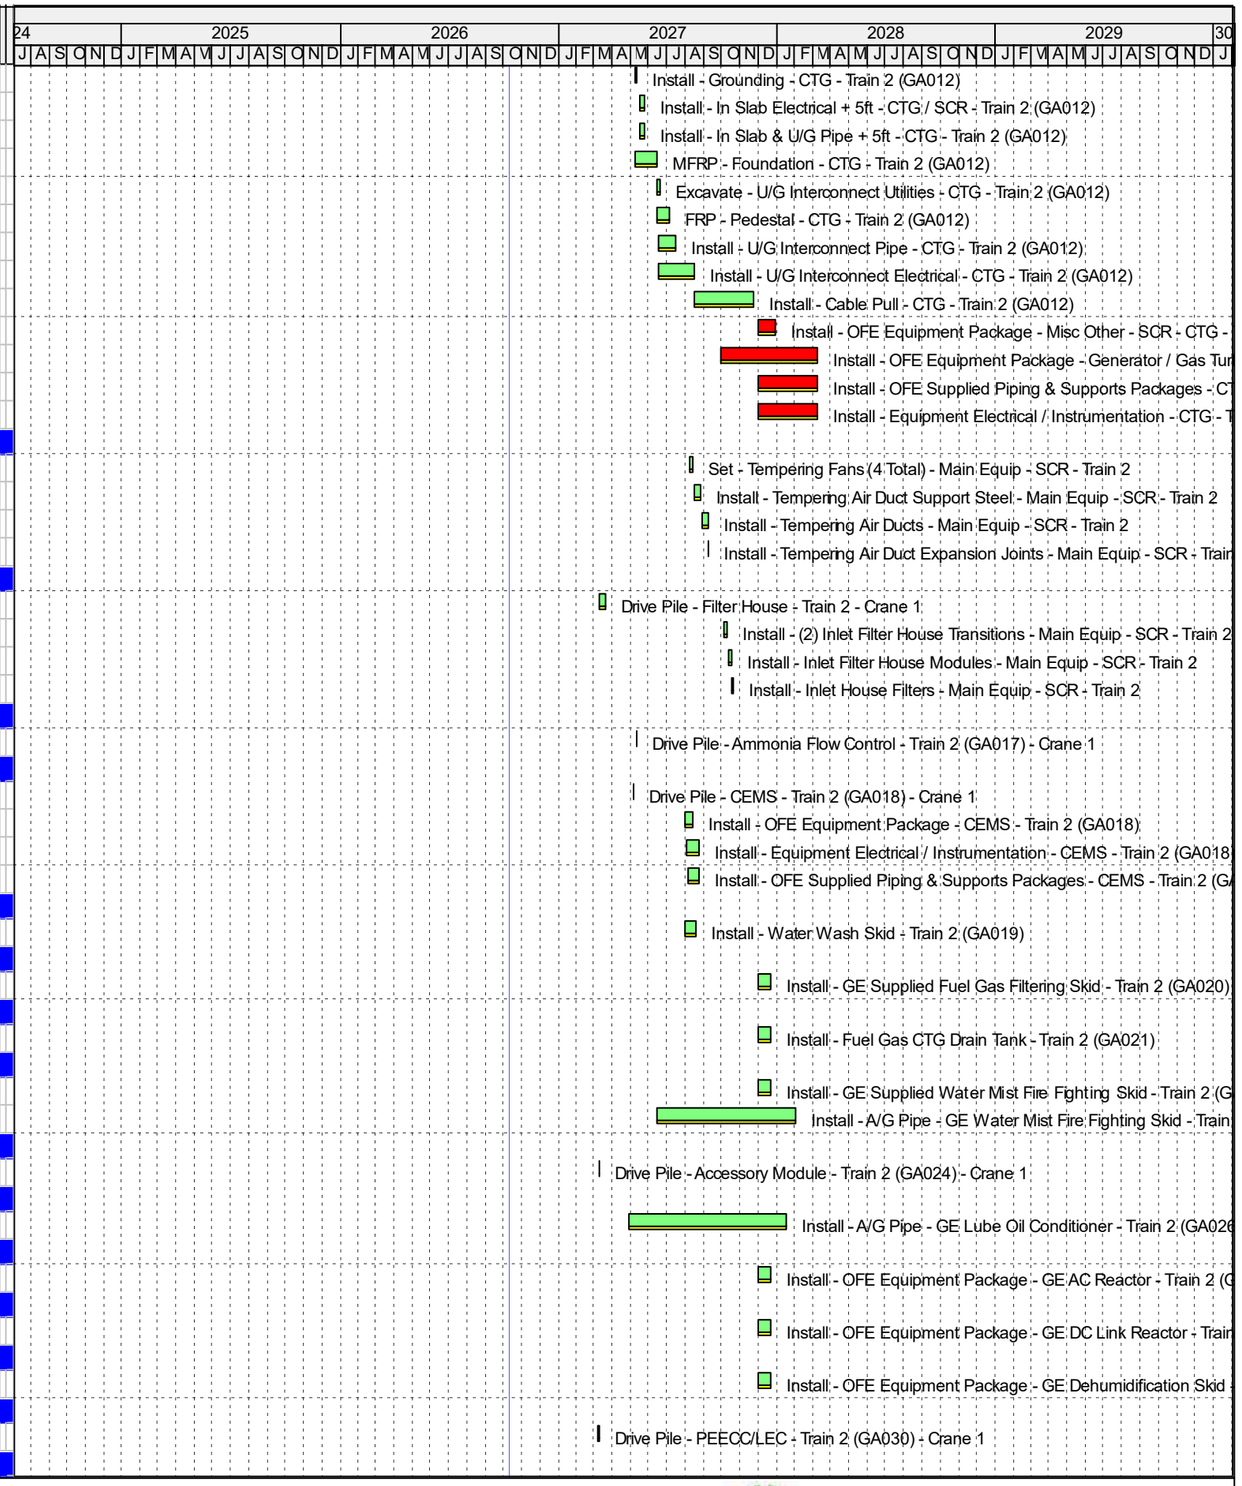

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.CTG2.GA0	Install - GE PEECC/LEC - Train 2 (GA030) / (GA031)	15	9/2/27 7:00 AM	9/23/27 5:00 PM	117
BH CNN-KPJV-MAST-LIVE,40,T2,032 CONST - Train 2 - (GA032) CT Excitation Transformer (GE MLI A150)					
KPA.CTG2.GA0	Install - OFE Equipment Package - GE CT Excitation Transforme	15	9/2/27 7:00 AM	9/23/27 5:00 PM	117
BH CNN-KPJV-MAST-LIVE,40,T2,033 CONST - Train 2 - (GA033) CT Isolation Transformer					
KPA.CTG2.GA0	Install - OFE Equipment Package - GE CT Isolation Transformer	15	12/1/27 7:00 AM	12/21/27 5:00 PM	55
BH CNN-KPJV-MAST-LIVE,40,T2,034 CONST - Train 2 - (GA034) CT Oil Containing Sump					
KPA.CTG2.GA0	Install - OFE Equipment Package - CT Oil Containing Sump - Tr	15	12/1/27 7:00 AM	12/21/27 5:00 PM	55
BH CNN-KPJV-MAST-LIVE,40,T2,041 CONST - Train 2 - (GA041) Power Distribution Center (PDC)					
KPA.CTG2.GA0	Drive Pile - Power Distribution Center (PDC) - Train 2 (GA041) - C	4	5/3/27 7:00 AM	5/6/27 5:00 PM	77
KPA.CTG2.GA0	MFRP - Foundation - Power Distribution Center (PDC) (GA041) -	6	5/7/27 7:00 AM	5/14/27 5:00 PM	116
KPA.CTG2.GA0	FRP - Piers - Power Distribution Center (PDC) (GA041) - Train 2	15	5/17/27 7:00 AM	6/7/27 5:00 PM	116
KPA.CTG2.GA0	Pick & Set - Power Distribution Center (PDC) (GA041) - Train 2	2	6/8/27 7:00 AM	6/9/27 5:00 PM	116
KPA.CTG2.GA0	Cable Pull - Power Distribution Center (PDC) (GA041) - Train 2	30	6/15/27 7:00 AM	7/27/27 5:00 PM	113
KPA.CTG2.GA0	Install - Electrical (Inside) - Power Distribution Center (PDC) (GA(	45	7/28/27 7:00 AM	9/29/27 5:00 PM	113
BH CNN-KPJV-MAST-LIVE,40,T2,042 CONST - Train 2 - (GA042) Secondary Unit Substation Transformer					
KPA.CTG2.GA0	Install - Secondary Unit Substation Transformer - Train 2 (GA04	15	12/1/27 7:00 AM	12/21/27 5:00 PM	55
BH CNN-KPJV-MAST-LIVE,40,T2,043 CONST - Train 2 - (GA043) Carbon Dioxide Bottle Manifold (GE MLI G1F0)					
KPA.CTG2.GA0	Install - A/G Pipe - GE Carbon Dioxide Bottle Manifold - Train 2 (	182	4/30/27 7:00 AM	1/18/28 5:00 PM	37
BH CNN-KPJV-MAST-LIVE,40,T2,045 CONST - Train 2 - (GA045) Air Processing Unit (APU) ((GE MLI A130)					
KPA.CTG2.GA0	Install - OFE Equipment Package - GE Air Processing Unit - Trai	15	12/1/27 7:00 AM	12/21/27 5:00 PM	55
BH CNN-KPJV-MAST-LIVE,40,T2,047 CONST - Train 2 - (GA047) Hydrogen Gas Dryer (GE ML G2MA)					
KPA.CTG2.GA0	Install - A/G Pipe - GE Hydrogen Gas Dryer - Train 2 (GA047)	140	4/23/27 7:00 AM	11/9/27 5:00 PM	84
BH CNN-KPJV-MAST-LIVE,40,T2,048 CONST - Train 2 - (GA048) CT Wastewater Sumps					
KPA.CTG2.GA0	Install - OFE Equipment Package - CT Wastewater Sumps - Tra	15	12/1/27 7:00 AM	12/21/27 5:00 PM	55
BH CNN-KPJV-MAST-LIVE,40,T2,050 CONST - Train 2 - (GA050) Water Wash/False Start Drains Tank					
KPA.CTG2.GA0	Install - CFE Equipment - False Start Drain Tank - CTG - Train 2	5	4/19/27 7:00 AM	4/23/27 5:00 PM	13
BH CNN-KPJV-MAST-LIVE,40,T2,051 CONST - Train 2 - (GA051) Cooling Water Module (GE MLI A076)					
KPA.CTG2.GA0	Drive Pile - Cooling Water Module - Train 2 (GA051) - Crane 1	3	5/10/27 7:00 AM	5/12/27 5:00 PM	77
KPA.CTG2.GA0	Install - OFE Equipment Package - Cooling Water Module - Trai	15	9/2/27 7:00 AM	9/23/27 5:00 PM	117
BH CNN-KPJV-MAST-LIVE,40,T2,082 CONST - Train 2 - (GA082) Aux Transformer					
KPA.CTG2.GA0	Install - OFE Equipment Package - Aux Transformer - Train 2 (G	10	3/8/27 7:00 AM	3/19/27 5:00 PM	248
BH CNN-KPJV-MAST-LIVE,40,T3 CONST - Train 3					
BH CNN-KPJV-MAST-LIVE,40,T3,009 CONST - Train 3 - (GA009) SCR & Exhaust Stack					
KPA.CTG3.GA0	Drive Pile - SCR & Stack - Train 3 (GA013) - Crane 1	15	2/2/27 7:00 AM	2/23/27 5:00 PM	2
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - SCR & Stack - Train 3	10	2/24/27 7:00 AM	3/9/27 5:00 PM	35
KPA.CTG3.GA0	MFRP - Foundation - SCR & Exhaust Stack - Train 3 (GA009)	25	4/26/27 7:00 AM	5/28/27 5:00 PM	2
KPA.CTG3.GA0	Verify / Survey / Layout - Main Equip - SCR - Train 3	9	6/1/27 7:00 AM	6/11/27 5:00 PM	167
KPA.CTG3.GA0	Fab - Section 1 (Breech Section) - Main Equip - SCR - Train 3	9	6/14/27 7:00 AM	6/24/27 5:00 PM	167
KPA.CTG3.GA0	Install - U/G Interconnect Pipe - SCR - Train 3 (GA013)	20	6/1/27 7:00 AM	6/28/27 5:00 PM	208
KPA.CTG3.GA0	Install - Bottom 49' Breech Stack Section - Main Equip - SCR - T	2	6/25/27 7:00 AM	6/28/27 5:00 PM	167
KPA.CTG3.GA0	Install - Inlet DSCR Duct Through Primary Duct A - Main Equip -	13	6/17/27 7:00 AM	7/6/27 5:00 PM	167
KPA.CTG3.GA0	Fab - Middle Stack Sections - Main Equip - SCR - Train 3	9	6/25/27 7:00 AM	7/8/27 5:00 PM	171
KPA.CTG3.GA0	Weld - Internal & External Ducts - Main Equip - SCR - Train 3	3	7/7/27 7:00 AM	7/9/27 5:00 PM	167
KPA.CTG3.GA0	Install - Middle Section Of 45' Stack - Main Equip - SCR - Train 3	2	7/9/27 7:00 AM	7/12/27 5:00 PM	171
KPA.CTG3.GA0	Fit & Weld - Lower Horizontal Stack Seam - Main Equip - SCR -	2	7/13/27 7:00 AM	7/14/27 5:00 PM	171
KPA.CTG3.GA0	Fab - Upper 45' Section Of Stack With Catwalk - Main Equip - S	7	7/12/27 7:00 AM	7/20/27 5:00 PM	167
KPA.CTG3.GA0	Install - Fan Outlet Dampers & Expansion Joints - Main Equip -	2	7/22/27 7:00 AM	7/23/27 5:00 PM	167
KPA.CTG3.GA0	Install - Upper Top Section Of Stack & Catwalk - Main Equip - S(	2	7/22/27 7:00 AM	7/23/27 5:00 PM	167
KPA.CTG3.GA0	Install - Fan Inlet Silencers - Main Equip - SCR - Train 3	3	7/26/27 7:00 AM	7/28/27 5:00 PM	167
KPA.CTG3.GA0	Install - U/G Interconnect Electrical - SCR - Train 3 (GA013)	42	6/1/27 7:00 AM	7/29/27 5:00 PM	116
KPA.CTG3.GA0	Weld - Top Horizontal Stack Seam - Main Equip - SCR - Train 3	2	7/29/27 7:00 AM	7/30/27 5:00 PM	167




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.CTG3.GA0	Install - All Inlet Duct Seam Insulation & Liner Plates - Main Equ	7	8/2/27 7:00 AM	8/10/27 5:00 PM	167
KPA.CTG3.GA0	Install - Internal Stack Insulation & Liners - Main Equip - SCR - T	4	8/5/27 7:00 AM	8/10/27 5:00 PM	167
KPA.CTG3.GA0	Install - Balance Of Inlet Duct Ladders & Platforms - Main Equip	3	9/7/27 7:00 AM	9/9/27 5:00 PM	157
KPA.CTG3.GA0	Install - OFE Supplied Piping & Supports Packages - SCR - Trai	100	6/1/27 7:00 AM	10/20/27 5:00 PM	128
KPA.CTG3.GA0	Install - Cable Pull - SCR - Train 3 (GA013)	70	7/30/27 7:00 AM	11/5/27 5:00 PM	116
KPA.CTG3.GA0	Install - Equipment Electrical / Instrumentation - SCR - Train 3 (G	150	6/1/27 7:00 AM	1/3/28 5:00 PM	78
KPA.CTG3.GA0	Load - All SCR Catalyst Blocks - Main Equip - SCR - Train 3	20	2/1/28 7:00 AM	2/29/28 5:00 PM	92
KPA.CTG3.GA0	LOE - Install - OFE Equipment Packages - Misc Major - SCR - Ti	228	6/1/27 7:00 AM	4/21/28 5:00 PM	0
BH CNN-KPJV-MAST-LIVE,40,T3,013 CONST - Train 3 - (GA013) CT Generator					
KPA.CTG3.GA0	Drive Pile - CT Generator - Train 3 (GA013) - Crane 1	18	1/7/27 7:00 AM	2/1/27 5:00 PM	2
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - CT Generator - Train 3	10	2/9/27 7:00 AM	2/23/27 5:00 PM	20
KPA.CTG3.GA0	Install - In Slab Electrical + 5ft - CTG / SCR - Train 3 (GA013)	5	3/30/27 7:00 AM	4/5/27 5:00 PM	131
KPA.CTG3.GA0	Install - In Slab & U/G Pipe + 5ft - CTG - Train 3 (GA013)	5	3/30/27 7:00 AM	4/5/27 5:00 PM	131
KPA.CTG3.GA0	MFRP - Foundation - CTG - Train 3 (GA013)	25	3/22/27 7:00 AM	4/23/27 5:00 PM	2
KPA.CTG3.GA0	Excavate - U/G Interconnect Utilities - CTG - Train 3 (GA013)	5	4/26/27 7:00 AM	4/30/27 5:00 PM	138
KPA.CTG3.GA0	FRP - Pedestal - CTG - Train 3 (GA013)	15	4/26/27 7:00 AM	5/14/27 5:00 PM	117
KPA.CTG3.GA0	Install - Grounding - CTG - Train 3 (GA013)	4	5/17/27 7:00 AM	5/20/27 5:00 PM	131
KPA.CTG3.GA0	Install - U/G Interconnect Pipe - CTG - Train 3 (GA013)	20	4/29/27 7:00 AM	5/26/27 5:00 PM	230
KPA.CTG3.GA0	Install - U/G Interconnect Electrical - CT Generator - Train 3 (GA(	42	4/29/27 7:00 AM	6/28/27 5:00 PM	138
KPA.CTG3.GA0	Install - Cable Pull - CTG - Train 3 (GA013)	70	6/29/27 7:00 AM	10/6/27 5:00 PM	138
KPA.CTG3.GA0	Install - OFE Equipment Package - Misc Other - SCR - CTG - Tra	20	1/3/28 7:00 AM	1/28/28 5:00 PM	0
KPA.CTG3.GA0	Install - OFE Equipment Package - Generator / Gas Turbine - C	120	11/1/27 7:00 AM	4/20/28 5:00 PM	0
KPA.CTG3.GA0	Install - OFE Supplied Piping & Supports Packages - CTG - Trai	79	1/3/28 7:00 AM	4/21/28 5:00 PM	0
KPA.CTG3.GA0	Install - Equipment Electrical / Instrumentation - CTG - Train 3 (G	103	11/26/27 7:00 AM	4/21/28 5:00 PM	0
BH CNN-KPJV-MAST-LIVE,40,T3,015 CONST - Train 3 - (GA015) SCR Filter House					
KPA.CTG3.GA0	Drive Pile - Filter House - Train 3 - Crane 1 (WEST SIDE)	3	10/26/26 7:00 AM	10/28/26 5:00 PM	2
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - SCR Filter House - Train :	10	10/29/26 7:00 AM	11/11/26 5:00 PM	341
KPA.CTG3.GA0	MFRP - Foundation - Filter House - Train 3 (GA015)	10	11/12/26 7:00 AM	11/25/26 5:00 PM	341
KPA.CTG3.GA0	Install - (2) Inlet Filter House Transitions - Main Equip - SCR - Tra	6	9/2/27 7:00 AM	9/10/27 5:00 PM	148
KPA.CTG3.GA0	Install - Inlet Filter House Modules - Main Equip - SCR - Train 3	5	9/13/27 7:00 AM	9/17/27 5:00 PM	148
KPA.CTG3.GA0	Install - Inlet House Filters - Main Equip - SCR - Train 3	3	9/20/27 7:00 AM	9/22/27 5:00 PM	148
BH CNN-KPJV-MAST-LIVE,40,T3,016 CONST - Train 3 - (GA016) SCR Tempering Air Fan					
KPA.CTG3.GA0	Set - Tempering Fans (4 Total) - Main Equip - SCR - Train 3	5	6/18/27 7:00 AM	6/24/27 5:00 PM	171
KPA.CTG3.GA0	Install - Tempering Air Duct Support Steel - Main Equip - SCR - T	8	6/29/27 7:00 AM	7/9/27 5:00 PM	167
KPA.CTG3.GA0	Install - Tempering Air Ducts - Main Equip - SCR - Train 3	7	7/12/27 7:00 AM	7/20/27 5:00 PM	167
KPA.CTG3.GA0	Install - Tempering Air Duct Expansion Joints - Main Equip - SCF	1	7/21/27 7:00 AM	7/21/27 5:00 PM	167
BH CNN-KPJV-MAST-LIVE,40,T3,017 CONST - Train 3 - (GA017) SCR Ammonia Flow Control Unit					
KPA.CTG3.GA0	Drive Pile - Ammonia Flow Control - Train 3 (GA017) - Crane 1	1	3/1/27 7:00 AM	3/1/27 5:00 PM	6
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - Ammonia Flow Control U	10	3/2/27 7:00 AM	3/15/27 5:00 PM	262
KPA.CTG3.GA0	MFRP - Foundation - Ammonia Flow Control Unit - Train 3 (GA0	10	3/16/27 7:00 AM	3/29/27 5:00 PM	262
KPA.CTG3.GA0	Install - OFE Equipment Package - Ammonia Flow Control Unit -	10	7/14/27 7:00 AM	7/27/27 5:00 PM	188
BH CNN-KPJV-MAST-LIVE,40,T3,018 CONST - Train 3 - (GA018) CEMS					
KPA.CTG3.GA0	Drive Pile - CEMS - Train 3 (GA018) - Crane 1	1	3/5/27 7:00 AM	3/5/27 5:00 PM	2
KPA.CTG3.GA0	Install - BoP U/G Electrical - CEMS - Train 3 (GA018)	5	3/8/27 7:00 AM	3/12/27 5:00 PM	283
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - CEMS - Train 3	10	3/8/27 7:00 AM	3/19/27 5:00 PM	324
KPA.CTG3.GA0	MFRP - Foundation - CEMS - Train 3 (GA048)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	324
KPA.CTG3.GA0	Install - OFE Equipment Package - CEMS - Train 3 (GA018)	10	8/2/27 7:00 AM	8/13/27 5:00 PM	241
KPA.CTG3.GA0	Install - OFE Supplied Piping & Supports Packages - CEMS - Tr	15	8/3/27 7:00 AM	8/23/27 5:00 PM	241
KPA.CTG3.GA0	Install - Equipment Electrical / Instrumentation - CEMS - Train 3	15	8/3/27 7:00 AM	8/23/27 5:00 PM	241
BH CNN-KPJV-MAST-LIVE,40,T3,020 CONST - Train 3 - (GA020) Gas Fuel Filtering Skid (GE MLI G015)					
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - Gas Fuel Filter Skid - Trai	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253

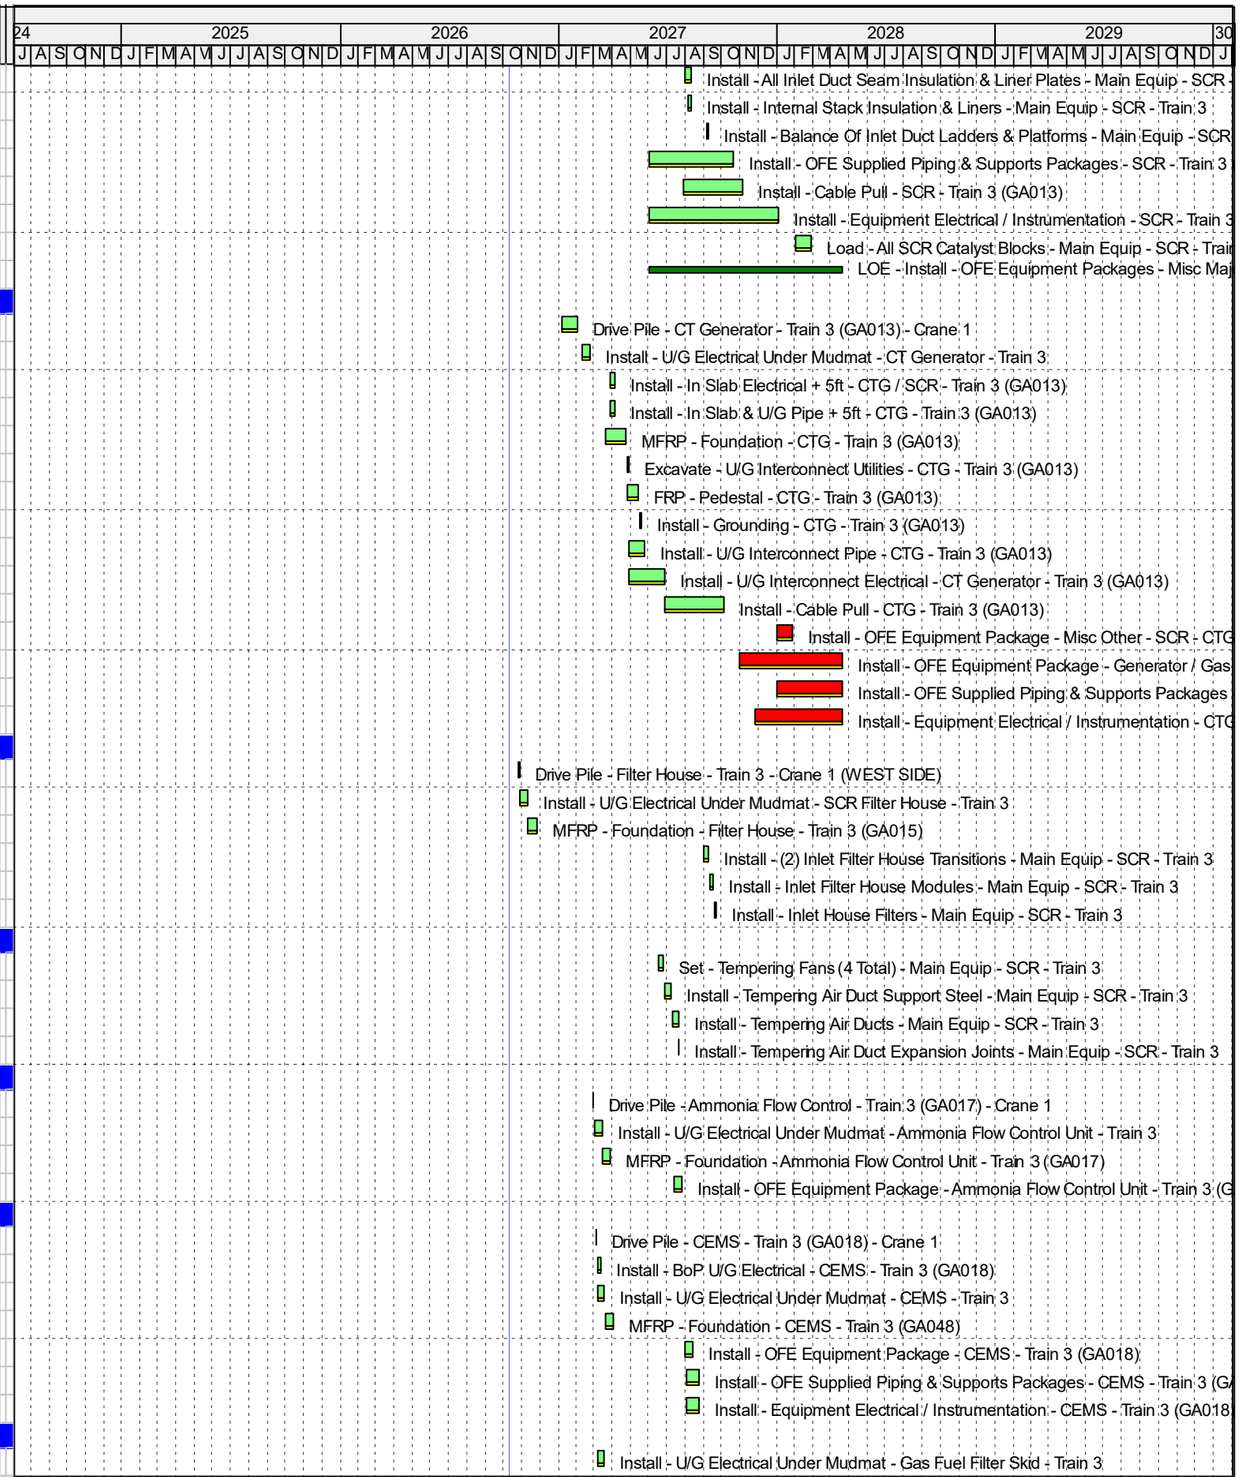

Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.CTG3.GA0:	MFRP - Foundation - Gas Fuel Filter Skid & Fuel Gas Drain Tank	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0:	Install - OFE Equipment Package - GE Fuel Gas Filtering Skid -	15	1/3/28 7:00 AM	1/21/28 5:00 PM	64
BH CNN-KPJV-MAST-LIVE,40,T3,021 CONST - Train 3 - (GA021) Fuel Gas CTG Drain Tank					
KPA.CTG3.GA0:	Install - ??? Equipment Package - Fuel Gas CTG Drain Tank - Ti	15	1/3/28 7:00 AM	1/21/28 5:00 PM	64
BH CNN-KPJV-MAST-LIVE,40,T3,022 CONST - Train 3 - (GA022) Water Mist Fire Fighting Skid (GE MLI A273)					
KPA.CTG3.GA0:	Install - U/G Electrical Under Mudmat - GE Water Mist Fire Fight	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0:	MFRP - Foundation - GE Water Mist Fire Fighting Skid- Train 3 (	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0:	Install - OFE Equipment Package - GE Supplied Water Mist Fire	15	8/3/27 7:00 AM	8/23/27 5:00 PM	169
KPA.CTG3.GA0:	Install - A/G Pipe - GE Water Mist Fire Fighting Skid - Train 3 (G/	160	6/16/27 7:00 AM	2/1/28 5:00 PM	57
BH CNN-KPJV-MAST-LIVE,40,T3,023 CONST - Train 3 - (GA023) Liquid Fuel Emulsion Control Skid (GE MLI A295)					
KPA.CTG3.GA0:	Install - U/G Electrical Under Mudmat - Liquid Fuel Emlusion Co	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0:	Install - OFE Equipment Package - Liquid Fuel Emlusion Contro	15	10/4/27 7:00 AM	10/22/27 5:00 PM	126
BH CNN-KPJV-MAST-LIVE,40,T3,024 CONST - Train 3 - (GA024) Accessory Module (GE MLI A160)					
KPA.CTG3.GA0:	Drive Pile - Accessory Module - Train 3 (GA024) - Crane 1 (WES	3	10/21/26 7:00 AM	10/23/26 5:00 PM	2
KPA.CTG3.GA0:	Install - U/G Electrical Under Mudmat - GE Accessory Module - T	10	10/26/26 7:00 AM	11/6/26 5:00 PM	343
KPA.CTG3.GA0:	MFRP - Foundation - GE Accessory Module - Train 3 (GA024)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0:	Install - OFE Equipment Package - GE Accessory Module - Trai	15	10/4/27 7:00 AM	10/22/27 5:00 PM	126
BH CNN-KPJV-MAST-LIVE,40,T3,026 CONST - Train 3 - (GA026) Lube Oil Conditioner (GE MLI F056)					
KPA.CTG3.GA0:	Install - U/G Electrical Under Mudmat - GE Lube Oil Conditioner	10	3/8/27 7:00 AM	3/19/27 5:00 PM	86
KPA.CTG3.GA0:	MFRP - Foundation - GE Lube Oil Conditioner - Train 3 (GA024)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	86
KPA.CTG3.GA0:	Install - OFE Equipment Package - GE Lube Oil Conditioner - Tr	15	4/5/27 7:00 AM	4/23/27 5:00 PM	86
KPA.CTG3.GA0:	Install - A/G Pipe - GE Lube Oil Conditioner - Train 3 (GA026)	182	4/30/27 7:00 AM	1/18/28 5:00 PM	67
BH CNN-KPJV-MAST-LIVE,40,T3,027 CONST - Train 3 - (GA027) AC Reactor (GE MLI A140)					
KPA.CTG3.GA0:	Install - U/G Electrical Under Mudmat - AC Reactor - Train 3	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0:	MFRP - Foundation - AC Reactor - Train 3 (GA027)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0:	Install - OFE Equipment Package - GE AC Reactor - Train 3 (GA	15	10/4/27 7:00 AM	10/22/27 5:00 PM	126
BH CNN-KPJV-MAST-LIVE,40,T3,028 CONST - Train 3 - (GA028) DC Link Reactor (GE MLI A140)					
KPA.CTG3.GA0:	Install - U/G Electrical Under Mudmat - DC Link Reactor - Train 3	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0:	MFRP - Foundation - DC Link Reactor - Train 3 (GA028)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0:	Install - OFE Equipment Package - GE DC Link Reactor - Train 3	15	1/3/28 7:00 AM	1/21/28 5:00 PM	64
BH CNN-KPJV-MAST-LIVE,40,T3,029 CONST - Train 3 - (GA029) Dehumidification Skid (GE MLI 1049)					
KPA.CTG3.GA0:	Install - U/G Electrical Under Mudmat - Dehumidification Skid - T	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0:	MFRP - Foundation - Dehumidification Skid - Train 3 (GA029)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0:	Install - OFE Equipment Package - GE Dehumidification Skid - T	15	10/4/27 7:00 AM	10/22/27 5:00 PM	126
BH CNN-KPJV-MAST-LIVE,40,T3,030 CONST - Train 3 - (GA030) PEECC (GE MLI A059) / (GA031) LEC (GE MLI A192)					
KPA.CTG3.GA0:	Drive Pile - PEECC/LEC - Train 3 (GA030) - Crane 1 (WEST SID	3	10/16/26 7:00 AM	10/20/26 5:00 PM	2
KPA.CTG3.GA0:	Install - U/G Electrical Under Mudmat - PEECC - Train 3	10	10/21/26 7:00 AM	11/3/26 5:00 PM	346
KPA.CTG3.GA0:	MFRP - Foundation - PEECC(GA030) / LEC(GA031) - Train 3	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0:	Install - OFE Equipment Package - GE PEECC - Train 3 (GA030	15	10/4/27 7:00 AM	10/22/27 5:00 PM	126
BH CNN-KPJV-MAST-LIVE,40,T3,031 CONST - Train 3 - (GA031) LEC (GE MLI A192)					
KPA.CTG3.GA0:	Install - U/G Electrical Under Mudmat - LEC - Train 3	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0:	Install - OFE Equipment Package - GE LEC - Train 3 (GA031)	15	10/4/27 7:00 AM	10/22/27 5:00 PM	126
BH CNN-KPJV-MAST-LIVE,40,T3,032 CONST - Train 3 - (GA032) CT Excitation Transformer (GE MLI A150)					
KPA.CTG3.GA0:	Install - U/G Electrical Under Mudmat - CT Excitation Transforme	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0:	MFRP - Foundation - CT Excitatiion Transformer - Train 3 (GA03	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0:	Install - OFE Equipment Package - GE CT Excitation Transforme	15	10/4/27 7:00 AM	10/22/27 5:00 PM	126
BH CNN-KPJV-MAST-LIVE,40,T3,033 CONST - Train 3 - (GA033) CT Isolation Transformer					
KPA.CTG3.GA0:	Install - U/G Electrical Under Mudmat - CT Isolation Transformer	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0:	MFRP - Foundation - CT Isolation Transformer - Train 3 (GA033)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0:	Install - OFE Equipment Package - GE CT Isolation Transformer	15	10/4/27 7:00 AM	10/22/27 5:00 PM	126
BH CNN-KPJV-MAST-LIVE,40,T3,034 CONST - Train 3 - (GA034) CT Oil Containing Sump					



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - CT Oil Containing Sump	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0	MFRP - Foundation - CT Oil Containing Sump - Train 3 (GA034)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0	Install - OFE Equipment Package - CT Oil Containing Sump - Tr	15	1/3/28 7:00 AM	1/21/28 5:00 PM	64
BH CNN-KPJV-MAST-LIVE,40,T3,035 CONST - Train 3 - (GA035) Isophase Bus/Generator Circuit Breaker Supports					
KPA.CTG3.GA0	Drive Pile - Isophase Bus Supports - Train 3 (GA035) - Crane 1	3	10/30/26 7:00 AM	11/3/26 5:00 PM	2
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - Isophase Bus - Train 3	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0	MFRP - Foundation - Isophase Bus Supports - Train 3 (GA035)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0	Install - OFE Equipment Package - Isophase Bus/Generator Cir	15	10/15/27 7:00 AM	11/4/27 5:00 PM	117
BH CNN-KPJV-MAST-LIVE,40,T3,036 CONST - Train 3 - (GA036) Unit Aux Transformer (1&3 Only)					
KPA.CTG3.GA0	Drive Pile - Unit Aux Transformer - Train 3 (GA036) - Crane 1	1	10/29/26 7:00 AM	10/29/26 5:00 PM	2
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - Unit Aux Transformer - Tr	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0	MFRP - Foundation - Unit Aux Transformer - Train 3 (GA036)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0	Install - BoP U/G Electrical - Unit Aux Transformer - Train 3 (GA0	5	4/5/27 7:00 AM	4/9/27 5:00 PM	258
KPA.CTG3.GA0	Install - U/G Pipe - Unit Aux Transformer - Train 3 (GA036)	5	4/12/27 7:00 AM	4/16/27 5:00 PM	258
KPA.CTG3.GA0	Install - OFE Equipment Package - Unit Aux Transformer - Train	4	1/3/28 7:00 AM	1/6/28 5:00 PM	64
KPA.CTG3.GA0	Install - OFE Supplied Piping & Supports Packages - Unit Aux Tr	15	1/3/28 7:00 AM	1/21/28 5:00 PM	64
KPA.CTG3.GA0	Install - Equipment Electrical / Instrumentation - Unit Aux Transf	15	1/3/28 7:00 AM	1/21/28 5:00 PM	64
BH CNN-KPJV-MAST-LIVE,40,T3,037 CONST - Train 3 - (GA037) Generator Step-up Transformer (1&3 Only)					
KPA.CTG3.GA0	Drive Pile - GSU Transformer - CTG - Train 3 (GA037) - Crane 1	4	10/12/26 7:00 AM	10/15/26 5:00 PM	2
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - GSU Transformer - Train	10	3/8/27 7:00 AM	3/19/27 5:00 PM	250
KPA.CTG3.GA0	MFRP - Foundation - GSU Transformer - CTG - Train 3 (GA037)	10	4/26/27 7:00 AM	5/7/27 5:00 PM	225
KPA.CTG3.GA0	Install - BoP U/G Electrical - GSU Transformer - CTG - Train 3 (G	5	5/10/27 7:00 AM	5/14/27 5:00 PM	238
KPA.CTG3.GA0	Install - U/G Pipe - GSU (Generator Step Up) Transformer - CTG	5	5/10/27 7:00 AM	5/14/27 5:00 PM	238
KPA.CTG3.GA0	Install - OFE Equipment Package - GSU (Generator Step Up) Tr	15	8/2/27 7:00 AM	8/20/27 5:00 PM	167
KPA.CTG3.GA0	Install - Equipment Electrical / Instrumentation - GSU Transform	15	8/3/27 7:00 AM	8/23/27 5:00 PM	169
KPA.CTG3.GA0	Install - OFE Supplied Piping & Supports Packages - GSU (Gen	15	8/5/27 7:00 AM	8/25/27 5:00 PM	167
BH CNN-KPJV-MAST-LIVE,40,T3,041 CONST - Train 3 - (GA041) Power Distribution Center (PDC)					
KPA.CTG3.GA0	Drive Pile - Power Distribution Center (PDC) - Train 3 (GA041) - C	2	3/3/27 7:00 AM	3/4/27 5:00 PM	2
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - PDC - Train 3	10	3/5/27 7:00 AM	3/18/27 5:00 PM	181
KPA.CTG3.GA0	MFRP - Foundation - Power Distribution Center (PDC) (GA041) -	6	3/19/27 7:00 AM	3/26/27 5:00 PM	181
KPA.CTG3.GA0	FRP - Piers - Power Distribution Center (PDC) (GA041) - Train 3	15	3/29/27 7:00 AM	4/16/27 5:00 PM	181
KPA.CTG3.GA0	Pick & Set - Power Distribution Center (PDC) (GA041) - Train 3	2	6/1/27 7:00 AM	6/2/27 5:00 PM	151
KPA.CTG3.GA0	Cable Pull - Power Distribution Center (PDC) (GA041) - Train 3	30	6/3/27 7:00 AM	7/15/27 5:00 PM	151
KPA.CTG3.GA0	Install - Electrical (Inside) - Power Distribution Center (PDC) (GA(	45	7/16/27 7:00 AM	9/17/27 5:00 PM	151
BH CNN-KPJV-MAST-LIVE,40,T3,042 CONST - Train 3 - (GA042) Secondary Unit Substation Transformer					
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - Secondary Unit Substati	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0	MFRP - Foundation - Secondary Unit Substation Transformer - T	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0	Install - OFE Equipment Package - Secondary Unit Substation T	15	1/3/28 7:00 AM	1/21/28 5:00 PM	64
BH CNN-KPJV-MAST-LIVE,40,T3,043 CONST - Train 3 - (GA043) Carbon Dioxide Bottle Manifold (GE MLI G1F0)					
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - GE Carbon Dioxide Bottl	10	3/8/27 7:00 AM	3/19/27 5:00 PM	2
KPA.CTG3.GA0	Install - OFE Equipment Package - GE Carbon Dioxide Bottle M	15	10/4/27 7:00 AM	10/22/27 5:00 PM	126
KPA.CTG3.GA0	Install - A/G Pipe - GE Carbon Dioxide Bottle Manifold - Train 3 (	182	4/30/27 7:00 AM	1/18/28 5:00 PM	67
BH CNN-KPJV-MAST-LIVE,40,T3,045 CONST - Train 3 - (GA045) Air Processing Unit (APU) ((GE MLI A130)					
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - APU - Train 3	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0	MFRP - Foundation - APC (Air Processing Unit) - Train 3 (GA045	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0	Install - OFE Equipment Package - GE Air Processing Unit - Trai	15	9/14/27 7:00 AM	10/4/27 5:00 PM	140
BH CNN-KPJV-MAST-LIVE,40,T3,046 CONST - Train 3 - (GA046) CT Compress Air Receiver					
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - CT Compressed Air Rece	10	3/8/27 7:00 AM	3/19/27 5:00 PM	258
KPA.CTG3.GA0	MFRP - Foundation - CT Compressed Air Receiver - Train 3 (GA	10	3/22/27 7:00 AM	4/2/27 5:00 PM	258
KPA.CTG3.GA0	Received - CHF - CT Compressed Air Receiver - Train 3	10	7/23/27 7:00 AM	8/5/27 5:00 PM	171
KPA.CTG3.GA0	Install - CH Equipment Package - CT Compressed Air Receiver -	10	8/6/27 7:00 AM	8/19/27 5:00 PM	171



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
BH CNN-KPJV-MAST-LIVE,40,T3,047 CONST - Train 3 - (GA047) Hydrogen Gas Dryer (GE ML G2MA)					
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - Hydrogen Gas Dryer - Tra	10	3/8/27 7:00 AM	3/19/27 5:00 PM	2
KPA.CTG3.GA0	Install - OFE Equipment Package - Hydrogen Gas Dryer - Train 3	15	10/4/27 7:00 AM	10/22/27 5:00 PM	126
KPA.CTG3.GA0	Install - A/G Pipe - GE Hydrogen Gas Dryer - Train 3 (GA047)	140	4/23/27 7:00 AM	11/9/27 5:00 PM	114
BH CNN-KPJV-MAST-LIVE,40,T3,048 CONST - Train 3 - (GA048) CT Wastewater Sumps					
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - CT Wastewater Sump/Pu	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0	MFRP - Foundation - CT Wastewater Sump/Pump - Train 3 (GA	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0	Install - OFE Equipment Package - CT Wastewater Sumps - Tra	15	1/3/28 7:00 AM	1/21/28 5:00 PM	64
BH CNN-KPJV-MAST-LIVE,40,T3,049 CONST - Train 3 - (GA049) CT Maintenance Area					
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - CT Maintaince Area - Tra	10	3/8/27 7:00 AM	3/19/27 5:00 PM	268
KPA.CTG3.GA0	MFRP - Foundation - CT Maintenance Area - Train 3 (GA049)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	268
BH CNN-KPJV-MAST-LIVE,40,T3,050 CONST - Train 3 - (GA050) Water Wash/False Start Drains Tank					
KPA.CTG3.GA0	Install - CFE Equipment - False Start Drain Tank - CTG - Train 3	5	2/2/27 7:00 AM	2/8/27 5:00 PM	20
BH CNN-KPJV-MAST-LIVE,40,T3,051 CONST - Train 3 - (GA051) Cooling Water Module (GE MLI A076)					
KPA.CTG3.GA0	Drive Pile - Cooling Water Module - Train 3 (GA051) - Crane 1	3	2/24/27 7:00 AM	2/26/27 5:00 PM	6
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - Cooling Water Module -	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0	MFRP - Foundation - Cooling Water Module - Train 3 (GA051)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0	Install - OFE Equipment Package - Cooling Water Module - Trai	15	10/4/27 7:00 AM	10/22/27 5:00 PM	126
BH CNN-KPJV-MAST-LIVE,40,T3,052 CONST - Train 3 - (GA052) Chemical Pot Feeder					
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - Chemical Pot Feeder - Tr	10	3/8/27 7:00 AM	3/19/27 5:00 PM	253
KPA.CTG3.GA0	MFRP - Foundation - Chemical Pot Feeder - Train 3 (GA051)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	253
KPA.CTG3.GA0	Install - OFE Equipment Package - Chemical Pot Feeder - Train	15	4/5/27 7:00 AM	4/23/27 5:00 PM	253
BH CNN-KPJV-MAST-LIVE,40,T3,082 CONST - Train 3 - (GA082) Aux Transformer					
KPA.CTG3.GA0	Install - U/G Electrical Under Mudmat - Aux Transformer - Train 3	10	3/8/27 7:00 AM	3/19/27 5:00 PM	258
KPA.CTG3.GA0	MFRP - Foundation - Aux Transformer - Train 3 (GA082)	10	3/22/27 7:00 AM	4/2/27 5:00 PM	258
KPA.CTG3.GA0	Install - OFE Equipment Package - Aux Transformer - Train 3 (G	10	4/5/27 7:00 AM	4/16/27 5:00 PM	258
BH CNN-KPJV-MAST-LIVE,40,34 CONST - Train 3 & Train 4 Roadway - Manholes & Duct Banks					
KPA.CTG4.ELED	Install - U/G Electrical Manhole (M402 to M401) & Duct Bank (D	5	11/2/26 7:00 AM	11/6/26 5:00 PM	315
KPA.CTG4.ELED	Install - U/G Electrical Duct Bank - (DB404)	5	11/9/26 7:00 AM	11/13/26 5:00 PM	358
KPA.CTG4.ELED	Install - U/G Electrical Manhole (M401 to M400) & Duct Bank (D	7	11/9/26 7:00 AM	11/17/26 5:00 PM	331
KPA.CTG4.ELED	Install - U/G Electrical Manhole (M400 to M403) & Duct Bank (D	5	12/14/26 7:00 AM	12/18/26 5:00 PM	320
KP.CTG3/4.CH.PI	Install - U/G Fire Protection Pipe - (Str A07 to Str A10) - South M	8	12/23/26 7:00 AM	1/5/27 5:00 PM	33
KP.CTG3/4.CH.PI	Install - U/G Process Pipe - (Str A07 to Str A10) - South Main - V	15	12/23/26 7:00 AM	1/14/27 5:00 PM	18
KP.CTG3/4.CH.PI	Install - U/G Process Pipe - (Str A09 to Str A19)	5	1/15/27 7:00 AM	1/21/27 5:00 PM	270
KP.CTG3/4.CH.PI	Install - U/G Fire Protection Pipe - (Str A10 to Str A13) - South M	7	1/15/27 7:00 AM	1/25/27 5:00 PM	26
KP.CTG3/4.CH.PI	Install - U/G Process Pipe - (Str A09 to Str A19 Branch)	5	1/22/27 7:00 AM	1/28/27 5:00 PM	298
KP.CTG3/4.CH.PI	Install - U/G Process Pipe - (Str B16 to Str B04)	5	1/22/27 7:00 AM	1/28/27 5:00 PM	303
KP.CTG3/4.CH.PI	Install - U/G Process Pipe - (Str A19 to Str B04)	5	1/29/27 7:00 AM	2/4/27 5:00 PM	298
KP.CTG3/4.CH.PI	Install - U/G Process Pipe - (Str B16 to Str B04 Branch)	5	1/29/27 7:00 AM	2/4/27 5:00 PM	303
KP.CTG3/4.CH.PI	Install - U/G Process Pipe - (Str A10 to Str A13) - South Main - M	15	1/15/27 7:00 AM	2/4/27 5:00 PM	18
KPA.CTG4.ELED	Install - U/G Electrical Duct Bank - (DB402A) - West Side of Trai	2	2/24/27 7:00 AM	2/25/27 5:00 PM	289
KP.CTG3/4.B.O.P	Install - U/G Fire Protectiion Pipe - (Str A13 to Str A15) - South M	5	3/4/27 7:00 AM	3/10/27 5:00 PM	168
KP.CTG3/4.CH.PI	Install - U/G Process Pipe - (Str A19 to Str B04 Branch)	5	3/5/27 7:00 AM	3/11/27 5:00 PM	279
KP.CTG3/4.CH.PI	Install - U/G Process Pipe - (Str A13 to Str A15) - South Main - E	10	3/4/27 7:00 AM	3/17/27 5:00 PM	163
KP.CTG3/4.CH.PI	Install - U/G Process Pipe - (CCW) - SCR - Train 4 - East Side	5	3/11/27 7:00 AM	3/17/27 5:00 PM	275
BH CNN-KPJV-MAST-LIVE,40,T4 CONST - Train 4					
KP.CTG4.GE.UG.	Install - U/G Electrical Duct Bank - (DB103, 103B, 103E, 103G)	9	3/18/27 7:00 AM	3/30/27 5:00 PM	265
KP.CTG4.GE.UG.	Install - U/G Electrical Manhole (M102)	1	3/31/27 7:00 AM	3/31/27 5:00 PM	265
BH CNN-KPJV-MAST-LIVE,40,T4,001 CONST - Train 4 - CTG Manholes & Duct Banks					
KP.CTG4.GE.UC	Install - U/G Electrical Duct Bank - (DB507) - Under Stormwater -	0	10/5/26 7:00 AM A	10/7/26 5:00 PM A	
KP.CTG4.GE.UC	Install - U/G Electrical Manhole (M405, M500, M406, & M407) &	15	11/2/26 7:00 AM	11/20/26 5:00 PM	18



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KP.CTG4.GE.UC	Install - U/G Electrical Manhole (M407 to M402) & Duct Bank (D	8	11/23/26 7:00 AM	12/4/26 5:00 PM	284
KP.CTG4.GE.UC	Install - U/G Electrical Duct Bank - (DB403A/C/D/E/G)	5	12/7/26 7:00 AM	12/11/26 5:00 PM	320
KP.CTG4.GE.UC	Install - U/G Electrical Manhole (M403 to M405) & Duct Bank (D	5	12/21/26 7:00 AM	12/28/26 5:00 PM	320
KP.CTG4.GE.UC	Install - U/G Electrical Duct Bank - (DB430, DB431, DB432, DB4	5	1/7/27 7:00 AM	1/13/27 5:00 PM	314
KP.CTG4.GE.UC	Install - U/G Electrical Duct Bank - (DB341) ****	20	1/7/27 7:00 AM	2/3/27 5:00 PM	69
KP.CTG4.GE.UC	Install - U/G Electrical Duct Bank - (DB303, 303B, 303E, 303G)	9	2/5/27 7:00 AM	2/18/27 5:00 PM	283
KP.CTG4.GE.UC	Install - U/G Electrical Manhole (M404) & Duct Bank (DB413, DE	15	2/4/27 7:00 AM	2/25/27 5:00 PM	191
KP.CTG4.GE.UC	Install - U/G Electrical Manhole - (M302)	1	3/1/27 7:00 AM	3/1/27 5:00 PM	277
KP.CTG4.GE.UC	Install - U/G Electrical Duct Bank - (DB406/A/B & DB420)	9	2/26/27 7:00 AM	3/10/27 5:00 PM	223
KP.CTG4.GE.UC	Install - U/G Electrical Duct Bank - (DB203, 203B, 203E, 203G)	9	3/2/27 7:00 AM	3/12/27 5:00 PM	277
KP.CTG4.GE.UC	Install - U/G Electrical Manhole - (M202)	1	3/15/27 7:00 AM	3/15/27 5:00 PM	277
KP.CTG4.GE.UC	Install - U/G Electrical Duct Bank - (DB422, DB412, DB412A, DE	10	3/11/27 7:00 AM	3/24/27 5:00 PM	265
KP.CTG4.GE.UC	Install - U/G Electrical Duct Bank - (DB407, DB407A, DB408) (G	5	3/25/27 7:00 AM	3/31/27 5:00 PM	265
BH CNN-KPJV-MAST-LIVE,40,T4,010 CONST - Train 4 - (GA010) SCR & SCR Exhaust Stack					
KPA.CTG4.GA0	Drive Pile - SCR & Stack - Train 4 (GA014) - Crane 1	0	8/26/26 7:00 AM A	9/21/26 5:00 PM A	
KPA.CTG4.GA0	Install - U/G Electrical Under Mudmat SCR - Train 4	0	10/7/26 7:00 AM A	10/13/26 5:00 PM	
KPA.CTG4.GA0	MFRP - Foundation - SCR & Exhaust Stack - Train 4 (GA010)	25	10/28/26 7:00 AM	12/3/26 5:00 PM	64
KPA.CTG4.GA0	Verify / Survey / Layout - Main Equip - SCR - Train 4	9	12/4/26 7:00 AM	12/16/26 5:00 PM	285
KPA.CTG4.GA0	Fab - Section 1 (Breech Section) - Main Equip - SCR - Train 4	9	2/16/27 7:00 AM	2/26/27 5:00 PM	245
KPA.CTG4.GA0	Install - Bottom 49' Breech Stack Section - Main Equip - SCR - T	2	3/1/27 7:00 AM	3/2/27 5:00 PM	245
KPA.CTG4.GA0	Install - Inlet DSCR Duct Through Primary Duct A - Main Equip -	13	2/19/27 7:00 AM	3/9/27 5:00 PM	245
KPA.CTG4.GA0	Fab - Middle Stack Sections - Main Equip - SCR - Train 4	9	3/1/27 7:00 AM	3/11/27 5:00 PM	249
KPA.CTG4.GA0	Weld - Internal & External Ducts - Main Equip - SCR - Train 4	3	3/10/27 7:00 AM	3/12/27 5:00 PM	245
KPA.CTG4.GA0	Install - Middle Section Of 45' Stack - Main Equip - SCR - Train 4	2	3/12/27 7:00 AM	3/15/27 5:00 PM	249
KPA.CTG4.GA0	Fit & Weld - Lower Horizontal Stack Seam - Main Equip - SCR -	2	3/16/27 7:00 AM	3/17/27 5:00 PM	249
KPA.CTG4.GA0	Fab - Upper 45' Section Of Stack With Catwalk - Main Equip - S	7	3/15/27 7:00 AM	3/23/27 5:00 PM	245
KPA.CTG4.GA0	Install - Fan Outlet Dampers & Expansion Joints - Main Equip -	2	3/25/27 7:00 AM	3/26/27 5:00 PM	245
KPA.CTG4.GA0	Install - Upper Top Section Of Stack & Catwalk - Main Equip - S	2	3/25/27 7:00 AM	3/26/27 5:00 PM	245
KPA.CTG4.GA0	Install - Fan Inlet Silencers - Main Equip - SCR - Train 4	3	3/29/27 7:00 AM	3/31/27 5:00 PM	245
KPA.CTG4.GA0	Weld - Top Horizontal Stack Seam - Main Equip - SCR - Train 4	2	4/1/27 7:00 AM	4/2/27 5:00 PM	245
KPA.CTG4.GA0	Install - All Inlet Duct Seam Insulation & Liner Plates - Main Equ	7	4/5/27 7:00 AM	4/13/27 5:00 PM	245
KPA.CTG4.GA0	Install - Internal Stack Insulation & Liners - Main Equip - SCR - T	4	4/8/27 7:00 AM	4/13/27 5:00 PM	245
KPA.CTG4.GA0	Install - U/G Interconnect Electrical - SCR - Train 4 (GA014)	42	4/5/27 7:00 AM	6/2/27 5:00 PM	1
KPA.CTG4.GA0	Install - Balance Of Inlet Duct Ladders & Platforms - Main Equip	3	8/4/27 7:00 AM	8/6/27 5:00 PM	175
KPA.CTG4.GA0	LOE - Install - OFE Equipment Packages - Misc Major - SCR - Ti	180	12/4/26 7:00 AM	8/19/27 5:00 PM	166
KPA.CTG4.GA0	Install - Cable Pull - SCR - Train 4 (GA014)	70	6/3/27 7:00 AM	9/10/27 5:00 PM	1
KPA.CTG4.GA0	Install - OFE Supplied Piping & Supports Packages - SCR - Trai	100	5/14/27 7:00 AM	10/5/27 5:00 PM	114
KPA.CTG4.GA0	Install - U/G Interconnect Pipe - SCR - Train 4 (GA014)	20	10/6/27 7:00 AM	11/2/27 5:00 PM	114
KPA.CTG4.GA0	Load - All SCR Catalyst Blocks - Main Equip - SCR - Train 4	20	2/1/28 7:00 AM	2/29/28 5:00 PM	107
KPA.CTG4.GA0	Install - A/G Equipment Electrical / Instrumentation - SCR - Train	150	9/13/27 7:00 AM	4/13/28 5:00 PM	1
BH CNN-KPJV-MAST-LIVE,40,T4,014C CONST - Train 4 - (GA014) CT Generator					
KPA.CTG4.GA0	Drive Pile - CTG - Train 4 (GA014) - Crane 1	18	12/10/26 7:00 AM	1/6/27 5:00 PM	2
KPA.CTG4.GA0	Install - In Slab & U/G Pipe + 5ft - CTG Only - Train 4 (GA014)	5	3/8/27 7:00 AM	3/12/27 5:00 PM	168
KPA.CTG4.GA0	Install - Grounding - CTG - Train 4 (GA014)	4	3/11/27 7:00 AM	3/16/27 5:00 PM	223
KPA.CTG4.GA0	MFRP - Foundation - CTG - Train 4 (GA014)	20	2/26/27 7:00 AM	3/25/27 5:00 PM	69
KPA.CTG4.GA0	Excavate - U/G Interconnect Utilities - CTG - Train 4 (GA014)	5	3/26/27 7:00 AM	4/1/27 5:00 PM	154
KPA.CTG4.GA0	FRP - Pedestal - CTG - Train 4 (GA014)	15	3/26/27 7:00 AM	4/15/27 5:00 PM	159
KPA.CTG4.GA0	Install - U/G Interconnect Pipe - CTG - Train 4 (GA014)	20	3/29/27 7:00 AM	4/23/27 5:00 PM	248
KPA.CTG4.GA0	Install - U/G Interconnect Electrical - CTG - Train 4 (GA014)	42	4/5/27 7:00 AM	6/2/27 5:00 PM	151
KPA.CTG4.GA0	Install - Cable Pull - CTG - Train 4 (GA014)	70	6/3/27 7:00 AM	9/10/27 5:00 PM	151




Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.CTG4.GA0	Install - OFE Equipment Package - Misc Other - SCR - CTG - Tra	20	2/1/28 7:00 AM	2/29/28 5:00 PM	0
KPA.CTG4.GA0	Install - OFE Equipment Package - Generator / Gas Turbine - C	95	12/1/27 7:00 AM	4/14/28 5:00 PM	0
KPA.CTG4.GA0	Install - OFE Supplied Piping & Supports Packages - CTG - Trair	53	2/1/28 7:00 AM	4/14/28 5:00 PM	0
KPA.CTG4.GA0	Install - Equipment Electrical / Instrumentation - CTG - Train 4 (G	53	2/1/28 7:00 AM	4/14/28 5:00 PM	0
BH CNN-KPJV-MAST-LIVE,40,T4,015 CONST - Train 4 - (GA015) SCR Filter House					
KPA.CTG4.GA0	Drive Pile - Filter House - Train 4 - Crane 1	0	9/22/26 7:00 AM A	10/5/26 5:00 PM A	
KPA.CTG4.GA0	Install - U/G Electrical - Filter House - Train 4	9	10/15/26 7:00 AM	10/27/26 5:00 PM	64
KPA.CTG4.GA0	MFRP - Foundation - Filter House - Train 4 (GA015)	15	12/4/26 7:00 AM	12/24/26 5:00 PM	317
KPA.CTG4.GA0	Install - (2) Inlet Filter House Transitions - Main Equip - SCR - Tra	6	8/2/27 7:00 AM	8/9/27 5:00 PM	166
KPA.CTG4.GA0	Install - Inlet Filter House Modules - Main Equip - SCR - Train 4	5	8/10/27 7:00 AM	8/16/27 5:00 PM	166
KPA.CTG4.GA0	Install - Inlet House Filters - Main Equip - SCR - Train 4	3	8/17/27 7:00 AM	8/19/27 5:00 PM	166
BH CNN-KPJV-MAST-LIVE,40,T4,016 CONST - Train 4 - (GA016) SCR Tempering Air Fan					
KPA.CTG4.GA0	Set - Tempering Fans (4 Total) - Main Equip - SCR - Train 4	5	2/22/27 7:00 AM	2/26/27 5:00 PM	249
KPA.CTG4.GA0	Install - Tempering Air Duct Support Steel - Main Equip - SCR - T	8	3/3/27 7:00 AM	3/12/27 5:00 PM	245
KPA.CTG4.GA0	Install - Tempering Air Ducts - Main Equip - SCR - Train 4	7	3/15/27 7:00 AM	3/23/27 5:00 PM	245
KPA.CTG4.GA0	Install - Tempering Air Duct Expansion Joints - Main Equip - SCF	1	3/24/27 7:00 AM	3/24/27 5:00 PM	245
BH CNN-KPJV-MAST-LIVE,40,T4,017 CONST - Train 4 - (GA017) SCR Ammonia Flow Control Unit					
KPA.CTG4.GA0	Drive Pile - Ammonia Flow Control- Train 4 (GA017) - Crane 1	0	10/5/26 7:00 AM A	10/8/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,40,T4,018 CONST - Train 4 - (GA018) CEMS					
KPA.CTG4.GA0	Drive Pile - CEMS - Train 4 (GA018) - Crane 1	0	9/15/26 7:00 AM A	9/15/26 5:00 PM A	
KPA.CTG4.GA0	Install - OFE Equipment Package - CEMS - Train 4 (GA018)	10	8/2/27 7:00 AM	8/13/27 5:00 PM	241
KPA.CTG4.GA0	Install - OFE Supplied Piping & Supports Packages - CEMS - Tr	15	8/3/27 7:00 AM	8/23/27 5:00 PM	241
KPA.CTG4.GA0	Install - Equipment Electrical / Instrumentation - CEMS - Train 4	15	8/3/27 7:00 AM	8/23/27 5:00 PM	241
BH CNN-KPJV-MAST-LIVE,40,T4,020 CONST - Train 4 - (GA020) Gas Fuel Filtering Skid (GE MLI G015)					
KPA.CTG4.GA0	Install - GE Supplied Fuel Gas Filtering Skid - Train 4 (GA020)	15	2/1/28 7:00 AM	2/22/28 5:00 PM	38
BH CNN-KPJV-MAST-LIVE,40,T4,021 CONST - Train 4 - (GA021) Fuel Gas CTG Drain Tank					
KPA.CTG4.GA0	Install - Fuel Gas CTG Drain Tank - Train 4 (GA021)	15	2/1/28 7:00 AM	2/22/28 5:00 PM	38
BH CNN-KPJV-MAST-LIVE,40,T4,022 CONST - Train 4 - (GA022) Water Mist Fire Fighting Skid (GE MLI A273)					
KPA.CTG4.GA0	Install - A/G Pipe - GE Water Mist Fire Fighting Skid - Train 4 (G	184	6/1/27 7:00 AM	2/18/28 5:00 PM	39
KPA.CTG4.GA0	Install - GE Supplied Water Mist Fire Fighting Skid - Train 4 (GA	15	2/1/28 7:00 AM	2/22/28 5:00 PM	38
BH CNN-KPJV-MAST-LIVE,40,T4,024 CONST - Train 4 - (GA024) Accessory Module (GE MLI A160)					
KPA.CTG4.GA0	Drive Pile - Accessory Module - Train 4 (GA024) - Crane 1	0	9/22/26 7:00 AM A	10/5/26 5:00 PM A	
BH CNN-KPJV-MAST-LIVE,40,T4,026 CONST - Train 4 - (GA026) Lube Oil Conditioner (GE MLI F056)					
KPA.CTG4.GA0	Install - A/G Pipe - GE Lube Oil Conditioner - Train 4 (GA026)	182	4/30/27 7:00 AM	1/18/28 5:00 PM	62
BH CNN-KPJV-MAST-LIVE,40,T4,027 CONST - Train 4 - (GA027) AC Reactor (GE MLI A140)					
KPA.CTG4.GA0	Install - OFE Equipment Package - GE AC Reactor - Train 4 (GA	15	2/1/28 7:00 AM	2/22/28 5:00 PM	38
BH CNN-KPJV-MAST-LIVE,40,T4,028 CONST - Train 4 - (GA028) DC Link Reactor (GE MLI A140)					
KPA.CTG4.GA0	Install - OFE Equipment Package - GE DC Link Reactor - Train 4	15	2/1/28 7:00 AM	2/22/28 5:00 PM	38
BH CNN-KPJV-MAST-LIVE,40,T4,029 CONST - Train 4 - (GA029) Dehumidification Skid (GE MLI 1049)					
KPA.CTG4.GA0	Install - OFE Equipment Package - GE Dehumidification Skid - T	15	2/1/28 7:00 AM	2/22/28 5:00 PM	38
BH CNN-KPJV-MAST-LIVE,40,T4,030 CONST - Train 4 - (GA030) PEECC (GE MLI A059) / (GA031) LEC (GE MLI A192)					
KPA.CTG4.GA0	Drive Pile - PEECC/LEC - Train 4 (GA030) - Crane 1	0	9/22/26 7:00 AM A	10/6/26 5:00 PM A	
KPA.CTG4.GA0	Install - U/G Electrical Conduit from PEECC/LEC to CTG Under I	25	1/21/27 7:00 AM	2/25/27 5:00 PM	69
KPA.CTG4.GA0	Install - GE PEECC/LEC - Train 4 (GA030) / (GA031)	15	11/2/27 7:00 AM	11/22/27 5:00 PM	100
BH CNN-KPJV-MAST-LIVE,40,T4,032 CONST - Train 4 - (GA032) CT Excitation Transformer (GE MLI A150)					
KPA.CTG4.GA0	Install - OFE Equipment Package - GE CT Excitation Transforme	15	11/2/27 7:00 AM	11/22/27 5:00 PM	100
BH CNN-KPJV-MAST-LIVE,40,T4,033 CONST - Train 4 - (GA033) CT Isolation Transformer					
KPA.CTG4.GA0	Install - OFE Equipment Package - GE CT Isolation Transformer	15	2/1/28 7:00 AM	2/22/28 5:00 PM	38
BH CNN-KPJV-MAST-LIVE,40,T4,034 CONST - Train 4 - (GA034) CT Oil Containing Sump					
KPA.CTG4.GA0	Install - OFE Equipment Package - CT Oil Containing Sump - Tr	15	2/1/28 7:00 AM	2/22/28 5:00 PM	38
BH CNN-KPJV-MAST-LIVE,40,T4,040 CONST - Train 4 - (GA040) 345kV Station Service Transformers (4 Only)					
KPA.CTG4.GA0	Drive Pile - 345kV Station Service Transformer - Train 4 (GA040	17	10/7/26 7:00 AM A	11/3/26 5:00 PM	62

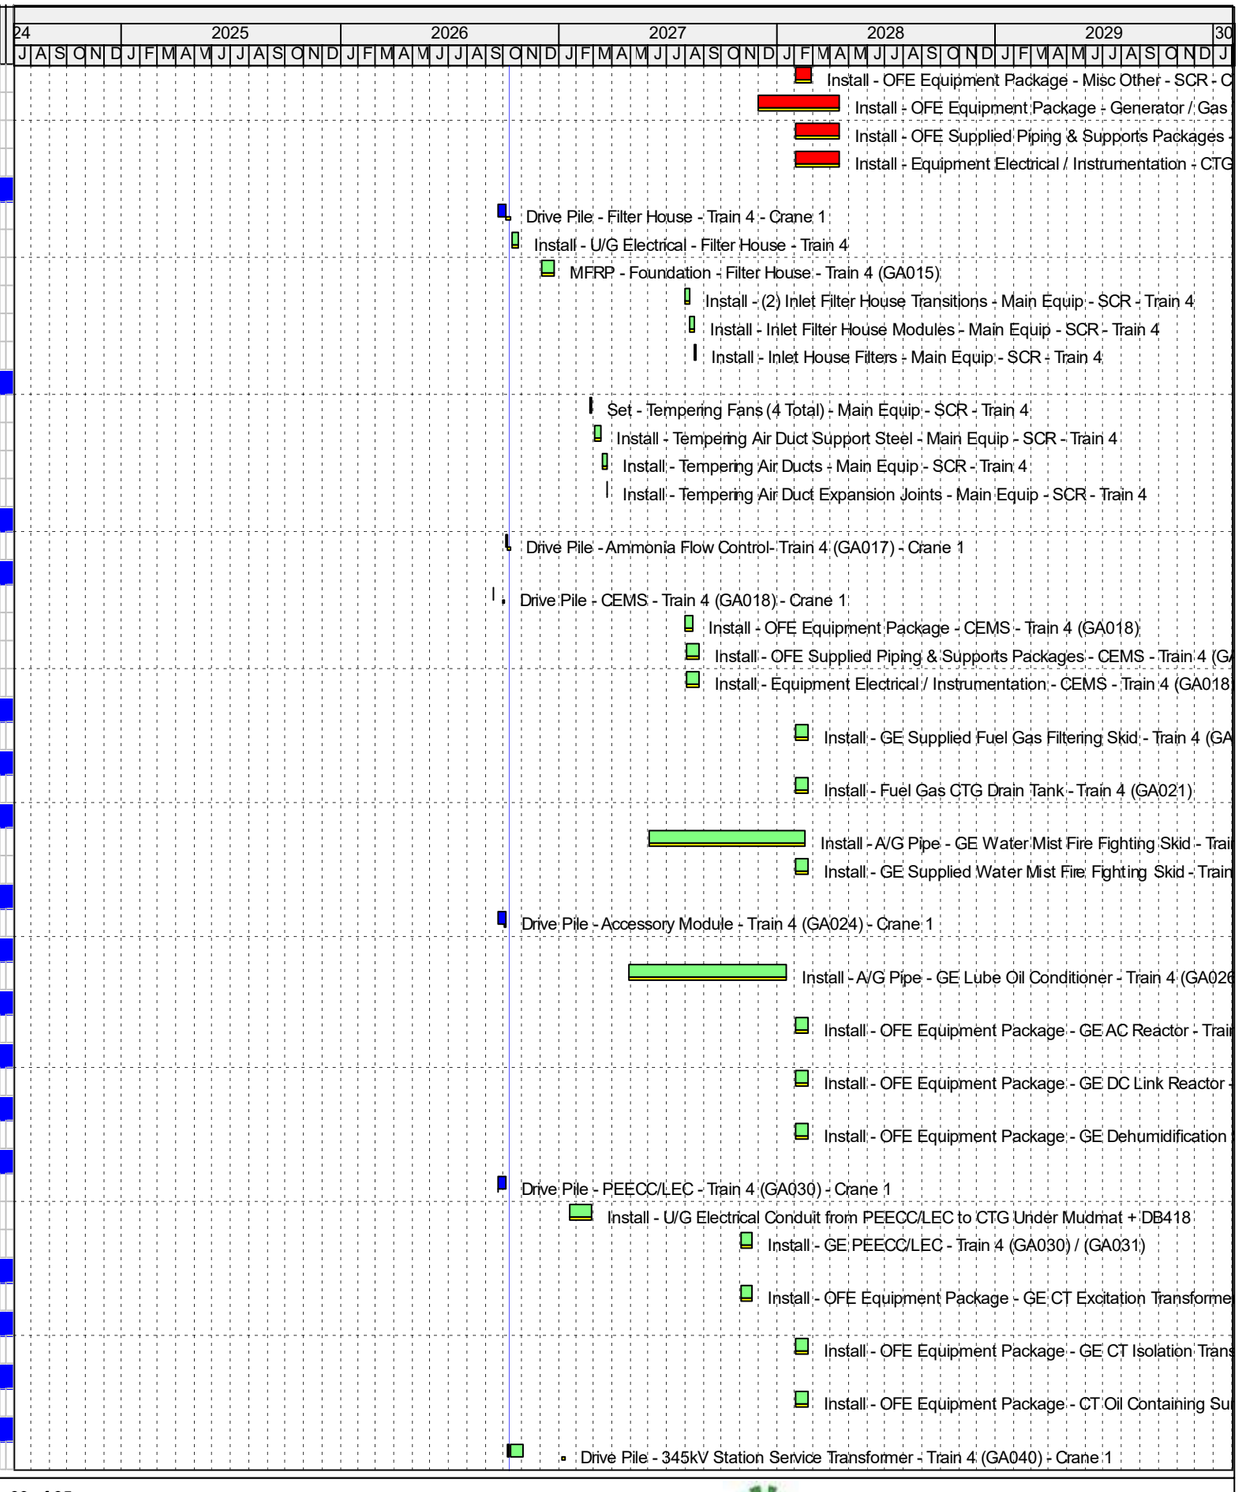


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.CTG4.GA0	MFRP - Foundation & Pedestal - 345kV Station Service Transfo	10	3/29/27 7:00 AM	4/9/27 5:00 PM	242
KPA.CTG4.GA0	Install - U/G Pipe - 345kV Station Service Transformer - Train 4 (	1	4/12/27 7:00 AM	4/12/27 5:00 PM	257
KPA.CTG4.GA0	Install - OFE Equipment Package - 345kV Station Service Trans	15	9/1/27 7:00 AM	9/22/27 5:00 PM	142
KPA.CTG4.GA0	Install - OFE Supplied Piping & Supports Packages - 345kV Sta	15	9/2/27 7:00 AM	9/23/27 5:00 PM	142
KPA.CTG4.GA0	Install - Equipment Electrical / Instrumentation - 345kV Station S	15	9/2/27 7:00 AM	9/23/27 5:00 PM	142
BH CNN-KPJV-MAST-LIVE,40,T4,041 CONST - Train 4 - (GA041) Power Distribution Center (PDC)					
KPA.CTG4.GA0	Drive Pile - Power Distribution Center (PDC) - Train 4 (GA041) - C	0	9/21/26 7:00 AM A	9/24/26 5:00 PM A	
KPA.CTG4.GA0	MFRP - Foundation - Power Distribution Center (PDC) - Train 4 (	6	2/26/27 7:00 AM	3/5/27 5:00 PM	191
KPA.CTG4.GA0	FRP - Piers - Power Distribution Center (PDC) - Train 4 (GA041)	15	3/8/27 7:00 AM	3/26/27 5:00 PM	191
KPA.CTG4.GA0	Pick & Set - Power Distribution Center (PDC) - Train 4 (GA041)	2	6/10/27 7:00 AM	6/11/27 5:00 PM	139
KPA.CTG4.GA0	Cable Pull - Power Distribution Center (PDC) - Train 4 (GA041)	30	6/14/27 7:00 AM	7/26/27 5:00 PM	139
KPA.CTG4.GA0	Install - Electrical (Inside) - Power Distribution Center (PDC) (GA(	45	7/27/27 7:00 AM	9/28/27 5:00 PM	139
BH CNN-KPJV-MAST-LIVE,40,T4,042 CONST - Train 4 - (GA042) Secondary Unit Substation Transformer					
KPA.CTG4.GA0	Install - Secondary Unit Substation Transformer - Train 4 (GA04	15	2/1/28 7:00 AM	2/22/28 5:00 PM	38
BH CNN-KPJV-MAST-LIVE,40,T4,043 CONST - Train 4 - (GA043) Carbon Dioxide Bottle Manifold (GE MLI G1F0)					
KPA.CTG4.GA0	Install - A/G Pipe - GE Carbon Dioxide Bottle Manifold - Train 4 (	182	4/30/27 7:00 AM	1/18/28 5:00 PM	62
BH CNN-KPJV-MAST-LIVE,40,T4,045 CONST - Train 4 - (GA045) Air Processing Unit (APU) ((GE MLI A130)					
KPA.CTG4.GA0	Install - OFE Equipment Package - GE Air Processing Unit - Trai	15	2/1/28 7:00 AM	2/22/28 5:00 PM	38
BH CNN-KPJV-MAST-LIVE,40,T4,047 CONST - Train 4 - (GA047) Hydrogen Gas Dryer (GE ML G2MA)					
KPA.CTG4.GA0	Install - A/G Pipe - GE Hydrogen Gas Dryer - Train 4 (GA047)	140	4/23/27 7:00 AM	11/9/27 5:00 PM	109
BH CNN-KPJV-MAST-LIVE,40,T4,048 CONST - Train 4 - (GA048) CT Wastewater Sumps					
KPA.CTG4.GA0	Install - OFE Equipment Package - CT Wastewater Sumps - Tra	15	2/1/28 7:00 AM	2/22/28 5:00 PM	38
BH CNN-KPJV-MAST-LIVE,40,T4,050 CONST - Train 4 - (GA050) Water Wash/False Start Drains Tank					
KPA.CTG4.GA0	Install - CFE Equipment - False Start Drain Tank - CTG - Train 4	5	1/7/27 7:00 AM	1/13/27 5:00 PM	99
BH CNN-KPJV-MAST-LIVE,40,T4,051 CONST - Train 4 - (GA051) Cooling Water Module (GE MLI A076)					
KPA.CTG4.GA0	Drive Pile - Cooling Water Module - Train 4 (GA051) - Crane 1	0	9/22/26 7:00 AM A	9/24/26 5:00 PM A	
KPA.CTG4.GA0	Install - OFE Equipment Package - Cooling Water Module - Trai	15	11/2/27 7:00 AM	11/22/27 5:00 PM	100
BH CNN-KPJV-MAST-LIVE,40,T4,082 CONST - Train 4 - (GA082) Aux Transformer					
KPA.CTG4.GA0	Install - OFE Equipment Package - Aux Transformer - Train 4 (G	10	3/8/27 7:00 AM	3/19/27 5:00 PM	273
BH CNN-KPJV-MAST-LIVE,40,08 CONST - Demobilization					
KPA.DEMOB.101	Demobilize - Site - Chattanooga (CBT)	10	10/25/27 7:00 AM	11/4/27 5:00 PM	340
KPA.DEMOB.102	Demobilize - Site - Madison Industrial (MI)	10	1/31/28 7:00 AM	2/11/28 5:00 PM	207
KPA.DEMOB.102	Demobilize - Site - Boyer (BRP)	10	1/31/28 7:00 AM	2/11/28 5:00 PM	207
KPA.DEMOB.103	Demobilize - Site - Corrigan Haberberger (CH)	10	1/31/28 7:00 AM	2/11/28 5:00 PM	207
KPA.DEMOB.103	Demobilize - Site - Guarantee Electric (GECO)	10	1/31/28 7:00 AM	2/11/28 5:00 PM	207
KPA.DEMOB.100	Restore - Construction - Site	80	8/9/28 7:00 AM	11/30/28 5:00 PM	3
KPA.DEMOB.101	Demobilize - Site - Kokosing Plocher II (KPII) [01/04/29]	20	12/1/28 7:00 AM	12/29/28 5:00 PM*	3
BH CNN-KPJV-MAST-LIVE,50 COMMISSIONING & STARTUP					
BH CNN-KPJV-MAST-LIVE,50,030 C&S - BoP					
KPA.CM.BOP.00(	Commission - (Placeholder) Task - BoP	137	12/14/27 7:00 AM	4/28/28 5:00 PM	107
BH CNN-KPJV-MAST-LIVE,50,010 C&S - CTG Train 1					
KPA.CM.CTG1.0(	Commission - Commission to First Fire - (Placeholder) Task - Tra	96	2/25/28 7:00 AM	5/30/28 5:00 PM	0
KPA.CM.CTG1.11	Commission - First Fire 05-31-2028 - Train 1	0	5/31/28 7:00 AM		0
KPA.CM.CTG1.11	Commission - First Fire to Commissioning Complete - Train 1	10	5/31/28 7:00 AM	6/9/28 5:00 PM	65
BH CNN-KPJV-MAST-LIVE,50,015 C&S - CTG Train 2					
KPA.CM.CTG2.0(	Commission - Commission to First Fire - (Placeholder) Task - Tra	104	3/11/28 7:00 AM	6/22/28 5:00 PM	0
KPA.CM.CTG2.2'	Commission - First Fire 06-23-2028 - Train 2	0	6/23/28 7:00 AM		0
KPA.CM.CTG2.2'	Commission - First Fire to Commissioning Complete - Train 2	10	6/23/28 7:00 AM	7/2/28 5:00 PM	42
BH CNN-KPJV-MAST-LIVE,50,020 C&S - CTG Train 3					
KPA.CM.CTG3.0(	Commission - Commission to First Fire - (Placeholder) Task - Tra	78	4/22/28 7:00 AM	7/8/28 5:00 PM	2
KPA.CM.CTG3.3'	Commission - First Fire 07-11-2028 - Train 3	0	7/9/28 7:00 AM		2

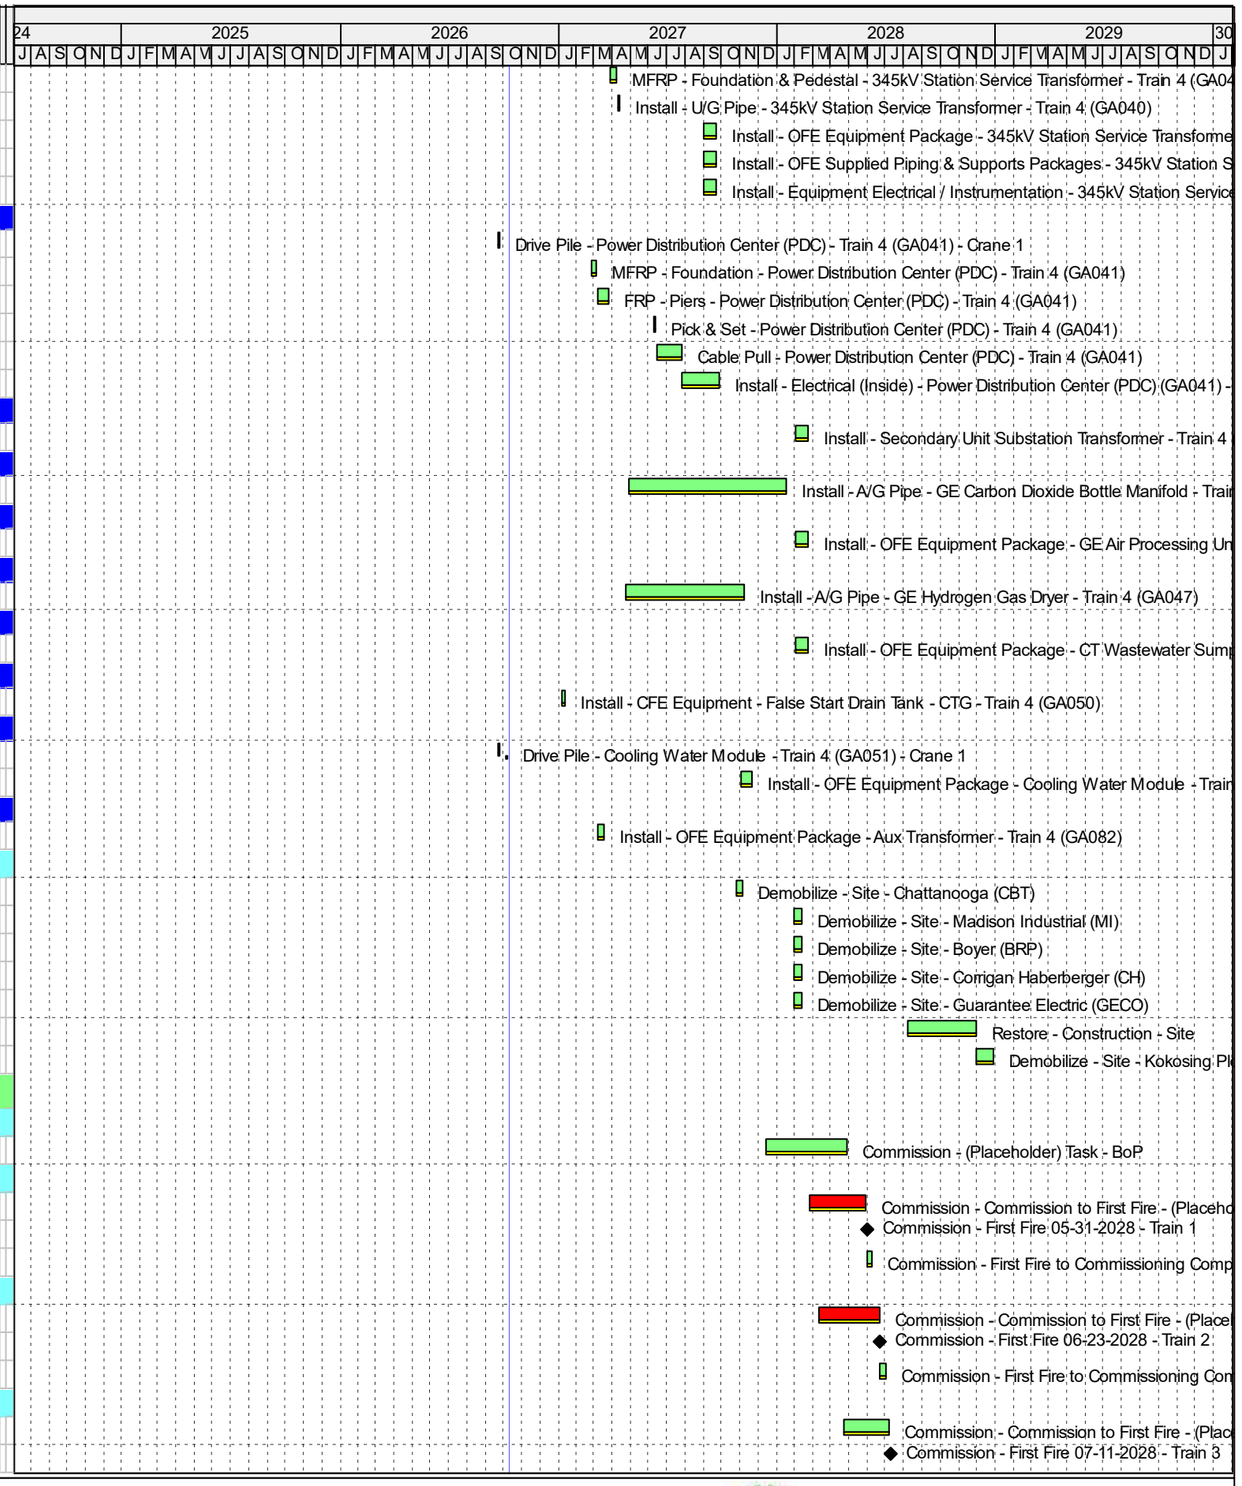


Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
Milestone

Ameren MISSOURI

Exhibit A

Activity ID	Activity Name	Remaining Duration	Start	Finish	Total Float
KPA.CM.CTG3.3	Commission - First Fire to Commissioning Complete - Train 3	10	7/9/28 7:00 AM	7/18/28 5:00 PM	26
BH CNN-KPJV-MAST-LIVE,50,025 C&S - CTG Train 4					
KPA.CM.CTG4.0(	Commission - Commission to First Fire - (Placeholder) Task - Tra	106	4/15/28 7:00 AM	7/29/28 5:00 PM	2
KPA.CM.CTG4.4	Commission - First Fire 08-01-2028 - Train 4	0	7/30/28 7:00 AM		2
KPA.CM.CTG4.4	Commission - First Fire to Commissioning Complete - Train 4	10	7/30/28 7:00 AM	8/8/28 5:00 PM	5



Remaining Level of Effort
Actual Level of Effort
Primary Baseline
Actual Work
Remaining Work
Critical Remaining Work
◆ Milestone

Ameren MISSOURI

Exhibit A
