

BESS Exhibit D


#	Activ ID	Activity Name	Dur	Start	Finish
1					
2		AMEREN - BIG HOLLOW BESS - 400MW 4hr	778	14-Aug-25	06-Sep-28
3		CONST DURATION SUMMARY	908	18-Aug-25	19-Apr-28
4		SUMMARY - MAKE READY / EARLY IMPORT (CAL DAYS)	145	18-Aug-25	15-Sep-26 A
5		SUMMARY - CONSTRUCTION (CAL DAYS)	750	01-Apr-26 A	19-Apr-28
6		PRECON / MAKE READY SUMMARY	213	14-Aug-25	04-Sep-26 A
7		SUMMARY - DESIGN RELEASE	80	14-Aug-25	09-Feb-26 A
8		SUMMARY - OWNER MAKE READY / COAL MITIGATION & IMPORT TO 406'	10	18-Aug-25	04-Sep-26 A
9		SUMMARY - DESIGN 30-90%	90	09-Feb-26 A	04-Sep-26 A
10		SUMMARY - PRECON	58	09-Feb-26 A	01-Apr-26 A
11		SUBSTATION SUMMARY	443	07-May-26	15-Feb-28
12		SUMMARY - SUBSTATION CONSTRUCTION	443	07-May-26	15-Feb-28
13		SUMMARY - SUBSTATION GSU I DELIV TO COMPLETION	115	01-Jul-27	14-Dec-27
14		SUMMARY - SUBSTATION GSU II DELIV TO COMPLETION	54	30-Nov-27	15-Feb-28
15		BESS PRODUCTION SUMMARY	407	01-Apr-26 A	16-Nov-27
16		SUMMARY - MOB & CIVIL EARLY IMPORT (FROM EL 406' TO BOT OF FTG)	0	01-Apr-26 A	15-Sep-26 A
17		SUMMARY - BESS - FOUNDATIONS	156	11-Sep-26 A	25-Mar-27
18		SUMMARY - UG ELECT - MVT CONDUIT	102	06-Oct-26 A	02-Mar-27
19		SUMMARY - UG ELECT - MV / FIBER / GROUNDING	113	06-Oct-26 A	29-Mar-27
20		SUMMARY - UG ELECT - GROUDING	93	19-Oct-26	02-Mar-27
21		SUMMARY - MVT EQUIP SET	16	12-May-27	03-Jun-27
22		SUMMARY - MVT TERMS	72	14-May-27	25-Aug-27
23		SUMMARY - LV FIBER CABLE	60	18-May-27	11-Aug-27
24		SUMMARY - DC TERMS ONLY*	69	11-Aug-27	16-Nov-27
25		SUMMARY - AUX EQUIP & TERMS	30	18-Aug-27	29-Sep-27
26		BESS BATTERY/CONTAINER SUMMARY	137	06-Aug-27	21-Feb-28
27		SUMMARY - BATTERIES SET	24	06-Aug-27	09-Sep-27
28		SUMMARY - TESLA BAT DELIV	20	06-Aug-27	02-Sep-27
29		SUMMARY - BATTERY SET TO MECH COMPLETION (CAL DAYS)	151	06-Aug-27	03-Jan-28
30		SUMMARY - BESS - BATTERY TERMS	69	11-Aug-27	16-Nov-27
31		SUMMARY - LAST BATTERY DELIV TO START OF ON-GRID (163CD'S)	161	08-Sep-27	15-Feb-28
32		SUMMARY - FEEDER MECH COMPLETION	77	13-Sep-27	03-Jan-28
33		SUMMARY - MPT SET TO START OF ON SITE (CAL DAYS)	84	30-Nov-27	21-Feb-28
34		TESLA / BESS CX / SUBST COMPL SUMMARY	172	06-Jan-28	06-Sep-28
35		SUMMARY - TESLA OFF-GRID SELF TESTING (BAT COLD CX - 28WD'S)	28	06-Jan-28	14-Feb-28
36		SUMMARY - TESLA GUARANTEED COMMISSIONING DUR (58WD'S)	58	06-Jan-28	27-Mar-28
37		SUMMARY - INTERCONNECTION / SYNC	4	02-Feb-28	07-Feb-28
38		SUMMARY - TESLA ON-GRID FUNCTIONAL & PERF TESTING	25	22-Feb-28	27-Mar-28
39		SUMMARY - SUBST COMPLETION	42	22-Feb-28	19-Apr-28
40		*MILESTONE: START OF TESLA HOT CX / ON-GRID	0	22-Feb-28	
41		SUMMARY - FINAL COMPLETION - FINAL COMPLETION (CAL DAYS)	140	20-Apr-28	06-Sep-28
42		PROJ MILESTONES	512	09-Feb-26 A	15-Feb-28
43		*MILESTONE: EPC / LNTP DESIGN	0		09-Feb-26 A
44		*MILESTONE: MOB / START MAKE READY	0	01-Apr-26 A	
45		*MILSTONE: PERMITTING COMPLETE	0		01-May-26
46		*MILESTONE: LNTP PROCUREMENT	0		10-Sep-26 A
47		*MILESTONE: OWNER MAKE READY SUBST COMPLETE	0		15-Sep-26 A
48		*MILESTONE: START DELIV OF MVT EQUIP (OWNER)	0		16-Apr-27
49		*MILESTONE: HV BREAKER #1 DELIV (OWNER)	0		13-May-27
50		*MILESTONE: OWNER BATTERY EARLIEST PERMITTED DELIVERY DATE (CAL DAYS)	0		01-Jun-27
51		*MILESTONE: HV BREAKER #2 DELIV (OWNER)	0		04-Jun-27
52		*MILESTONE: O&M BLDG COMPLETION	0		15-Jun-27
53		MILESTONE: BESS 1 MECH COMPLETION - GSU 1	0		01-Nov-27
54		*MILESTONE: SUBSTATION MECH COMPLETION - GSU I	0		21-Dec-27
55		*MILESTONE: SUBSTATION MECH COMPLETION - GSU II	0		15-Feb-28

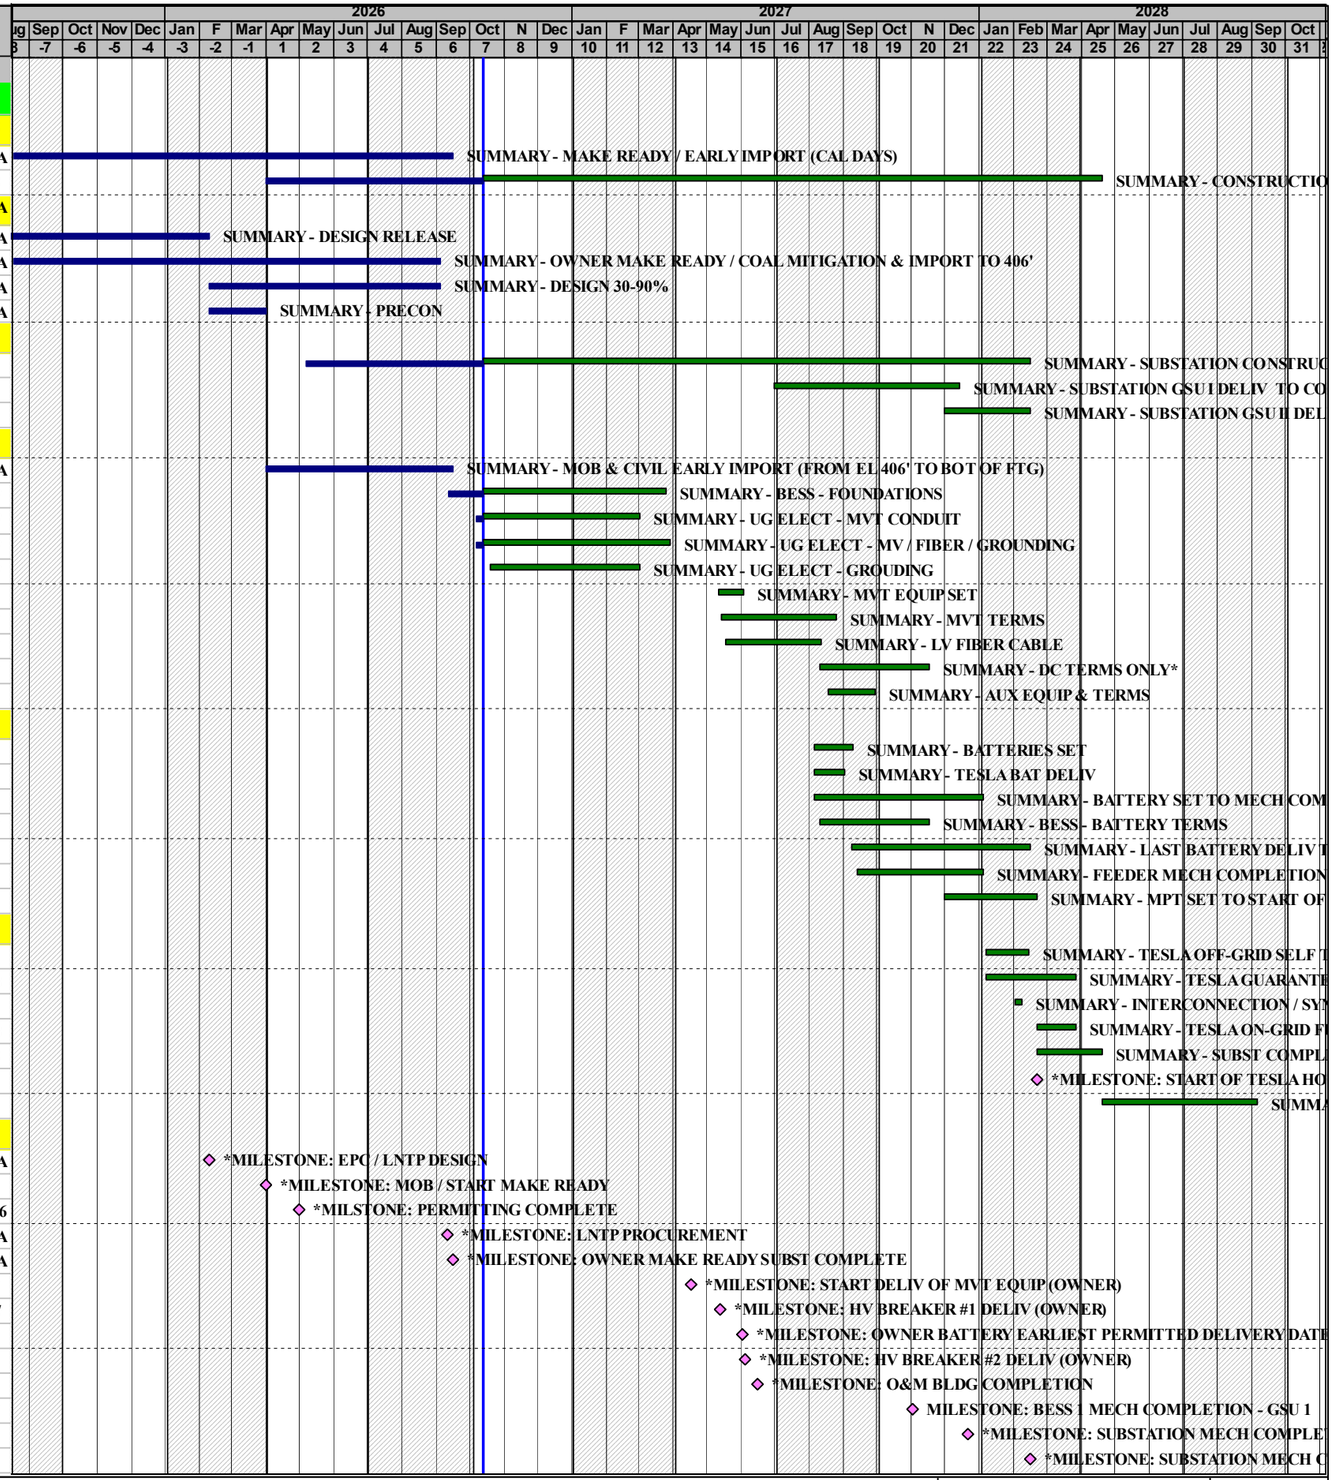


#	Activ ID	Activity Name	Dur	Start	Finish
56		CONTRACT MILESTONES	425	06-Jan-27	06-Sep-28
57		***MILESTONE: MVT CONC PADS COMPLETE (GSU#1 6/30/27)	0		06-Jan-27*
58		***MILESTONE: MVT CONC PADS COMPLETE (GSU#2 11/30/27)	0		13-Apr-27*
59		***MILESTONE: BAT CONC PADS COMPLETE (*6/1/27)	0		01-Jun-27*
60		*MILESTONE: OWNER GSU#1 DELIV	0		29-Jun-27
61		*MILESTONE: OWNER GSU#2 DELIV	0		29-Nov-27
62		MILESTONE: BESS MECH COMPLETION	0		03-Jan-28
63		*MILESTONE: SUBSTATION SUBSTANTIAL COMPLETION	0		15-Feb-28
64		***MILESTONE: GUARANTEED SUBSTANTIAL COMPLETION (*4/19/28)	0		19-Apr-28*
65		*MILESTONE: GUARANTEED FINAL COMPLETION (CAL DAYS)	0		06-Sep-28
66		PRECON - DESIGN / PERMITTING	778	14-Aug-25 A	06-Sep-28
67		CONTRACTING	275	14-Aug-25 A	10-Sep-26 A
68		LNTP	123	14-Aug-25 A	09-Feb-26 A
69		LNTP *2/9	67	14-Aug-25 A	09-Feb-26 A
70		*MILESTONE: LNTP DESIGN / EPC	0		09-Feb-26 A
71		RELEASE PROCUREMENT	74	08-May-26 A	10-Sep-26 A
72		PROCUREMENT RELEASE (INCL CCN)	5	08-May-26 A	10-Sep-26 A
73		*MILESTONE: LNTP PROCUREMENT	0		10-Sep-26 A
74		DESIGN	231	09-Feb-26 A	07-Jan-27
75		DESIGN - CIVIL	153	09-Feb-26 A	09-Sep-26 A
76		SURVEY - FINAL / GEOTECH	74	04-May-26 A	09-Sep-26 A
77		FINALIZE GEOTECH REPORT	5	04-May-26 A	06-Jun-26 A
78		FINAL SURVEY VERIFICATION	5	12-Jun-26 A	09-Sep-26 A
79		MILESTONE: FINAL GEOTECH	0		04-Sep-26 A
80		30% DESIGN	25	09-Feb-26 A	18-Mar-26
81		*MILESTONE: OWNER RELEASE DESIGN - CIVIL	0		09-Feb-26 A
82		CIVIL DESIGN - 30%	20	10-Feb-26 A	09-Mar-26
83		CIVIL DESIGN - GRADING PERMIT SUBMTL	5	10-Mar-26 A	18-Mar-26
84		60% DESIGN	30	10-Mar-26 A	01-May-26
85		CIVIL DESIGN - OWNER REVIEW 30%	10	10-Mar-26 A	23-Mar-26
86		CIVIL DESIGN - 60% (PERMITTING / CIVIL IMPORT)	25	17-Mar-26 A	01-May-26
87		90% DESIGN	25	04-May-26 A	19-Jun-26 A
88		CIVIL DESIGN - OWNER REVIEW 60%	15	04-May-26 A	26-May-26
89		CIVIL DESIGN - 90%	20	08-May-26 A	19-Jun-26 A
90		IFC	65	22-Jun-26 A	24-Aug-26
91		CIVIL DESIGN - OWNER REVIEW 90%	15	22-Jun-26 A	10-Jul-26 A
92		CIVIL DESIGN - IFC DOCUMENTS (100%)	10	13-Jul-26 A	03-Aug-26
93		CIVIL DESIGN -OWNER REVIEW IFC	5	04-Aug-26 A	11-Aug-26 A
94		*MILESTONE: FINAL SURVEY & GEOTECH COMPLETE	0		06-Aug-26
95		CIVIL DESIGN -REVISE IFC PER COMMENTS	5	18-Aug-26	24-Aug-26
96		*MILESTONE: CIVIL IFC DESIGN COMPLETE	0		24-Aug-26
97		DESIGN - ELECT	177	09-Feb-26 A	19-Oct-26
98		30% DESIGN	20	09-Feb-26 A	09-Mar-26
99		*MILESTONE: START DESIGN (LNTP)	0		09-Feb-26 A
100		BESS DESIGN - 30%	20	10-Feb-26 A	09-Mar-26
101		60% DESIGN	78	10-Mar-26 A	03-Jul-26 A
102		BESS DESIGN - OWNER REVIEW 30%	10	10-Mar-26 A	23-Mar-26
103		BESS DESIGN - 60% (PERMITTING/INV PROCUREMENT)	25	17-Mar-26 A	20-Apr-26 A
104		BESS DESIGN - 60% (REVISION 1)	6	11-May-26 A	03-Jul-26 A
105		90% DESIGN	79	20-Apr-26 A	11-Aug-26 A
106		BESS DESIGN - OWNER REVIEW 60%	15	20-Apr-26 A	08-May-26
107		BESS DESIGN - OWNER REVIEW 60% (REVISION 1)	14	06-Jul-26 A	28-Jul-26 A
108		BESS DESIGN - 90% (PROCUREMENT RELEASE)	9	29-Jul-26 A	11-Aug-26 A
109		IFC	49	11-Aug-26 A	19-Oct-26
110		BESS DESIGN - OWNER REVIEW 90%	15	11-Aug-26 A	04-Sep-26 A

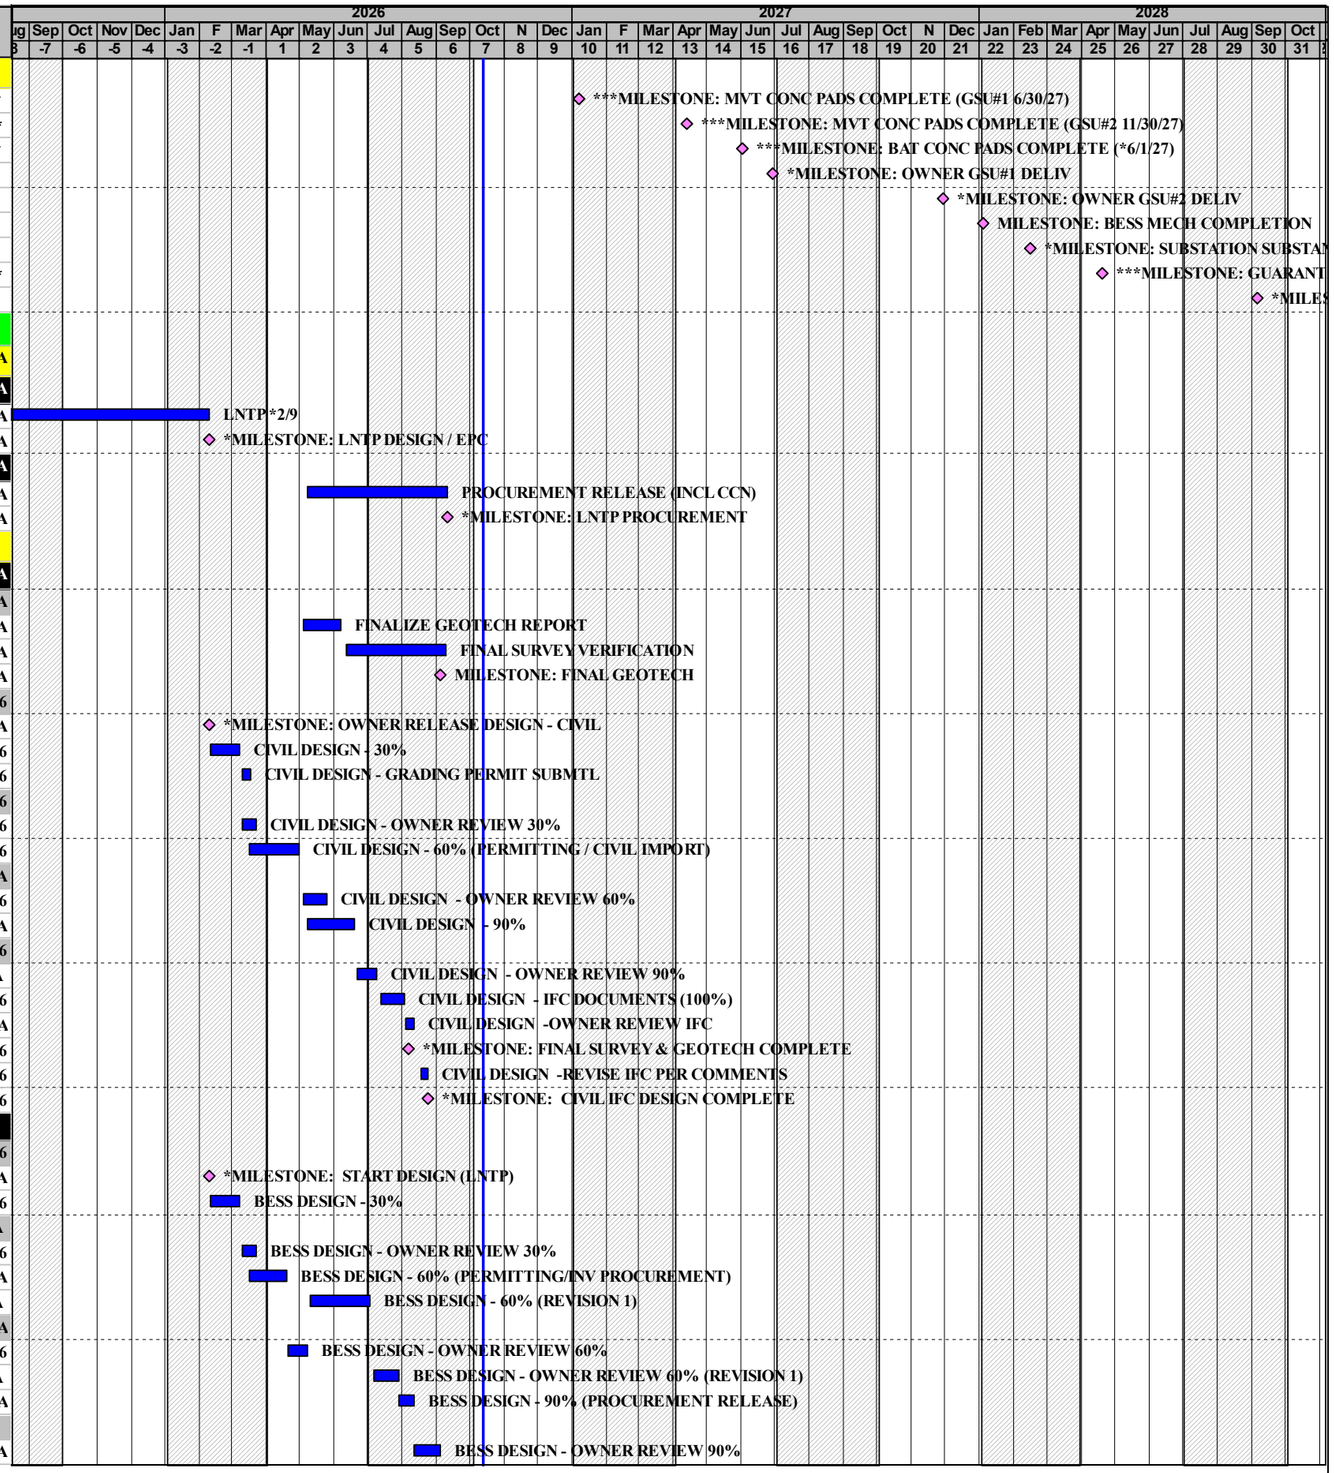


#	Activ ID	Activity Name	Dur	Start	Finish
111		BESS DESIGN - IFC DOCS (100% DD)	10	08-Sep-26 A	23-Sep-26 A
112		BESS DESIGN - OWNER REVIEW IFC	5	24-Sep-26 A	13-Oct-26
113		BESS DESIGN -REVISE IFC PER COMMENTS	5	13-Oct-26	19-Oct-26
114		*MILESTONE: ELECT IFC COMPLETE	0		19-Oct-26
115		**DESIGN - STRUCT**	147	09-Feb-26 A	04-Sep-26 A
116		30% DESIGN	20	09-Feb-26 A	09-Mar-26
117		*MILESTONE: START STRUCT DESIGN	0		09-Feb-26 A
118		BESS DESIGN - 30% STRUCT	20	10-Feb-26 A	09-Mar-26
119		EXECUTE STRUCT CONTRACT	5	10-Feb-26 A	16-Feb-26 A
120		60% DESIGN	30	10-Mar-26	20-Apr-26 A
121		BESS DESIGN - OWNER REVIEW 30% STRUCT (BESS PROCUREMENT)	10	10-Mar-26	23-Mar-26
122		BESS DESIGN - 60% STRUCT (PERMITTING)	25	17-Mar-26	20-Apr-26 A
123		90% DESIGN	25	20-Apr-26 A	24-Jun-26 A
124		BESS DESIGN - OWNER REVIEW 60% STRUCT	15	20-Apr-26 A	08-May-26
125		BESS DESIGN - 90% STRUCT	20	04-May-26	24-Jun-26 A
126		IFC	78	24-Jun-26 A	04-Sep-26 A
127		BESS DESIGN - OWNER REVIEW 90% STRUCT	15	24-Jun-26 A	17-Jul-26 A
128		BESS DESIGN - IFC DOCS STRUCT (100% DD)	10	18-Jul-26 A	03-Aug-26
129		BESS DESIGN - OWNER REVIEW IFC STRUCT	5	04-Aug-26	24-Aug-26
130		BESS DESIGN -REVISE IFC PER COMMENTS	5	25-Aug-26	04-Sep-26 A
131		*MILESTONE: STRUCT IFC COMPLETE	0		04-Sep-26 A
132		**DESIGN - SCADA**	103	05-Aug-26	31-Dec-26
133		30% DESIGN	14	05-Aug-26	12-Oct-26 A
134		CONTRACT - SCADA DESIGN - 30%	14	05-Aug-26	12-Oct-26 A
135		60% DESIGN	0	13-Oct-26	13-Oct-26
136		SCADA DESIGN - 60%	0	13-Oct-26	13-Oct-26
137		90% DESIGN	25	13-Oct-26	16-Nov-26
138		SCADA DESIGN - 60% OWNER REVIEW	15	13-Oct-26	02-Nov-26
139		SCADA DESIGN - 90%	10	03-Nov-26	16-Nov-26
140		IFC	30	17-Nov-26	31-Dec-26
141		SCADA DESIGN - 90% OWNER REVIEW	15	17-Nov-26	09-Dec-26
142		SCADA DESIGN - IFC	10	10-Dec-26	23-Dec-26
143		SCADA DESIGN - IFC OWNER REVIEW	5	24-Dec-26	31-Dec-26
144		*MILESTONE: SCADA DESIGN COMPLETE	0		31-Dec-26
145		**DESIGN - SUBSTATION**	231	09-Feb-26 A	07-Jan-27
146		30% DESIGN - CIVIL / ELECT	110	09-Feb-26 A	30-Jun-26 A
147		SUBSTATION EPC	0	09-Feb-26 A	10-Apr-26 A
148		*MILESTONE: OWNER RELEASE SUBSTATION DESIGN	0		10-Apr-26 A
149		CONTRACT - SUBSTATION DESIGN - 0-30% - CIVIL / ELECT	22	13-Apr-26 A	10-Jun-26 A
150		SUBSTATION DESIGN - 0-30% - CIVIL / ELECT	10	11-Jun-26 A	30-Jun-26 A
151		60% DESIGN - CIVIL / ELECT	97	01-Jul-26 A	29-Oct-26
152		SUBSTATION DESIGN - OWNER REVIEW 30% - CIVIL / ELECT	10	01-Jul-26 A	23-Jul-26 A
153		SUBSTATION DESIGN - 60% (PERMITTING) - CIVIL / ELECT	14	24-Jul-26 A	08-Oct-26 A
154		*MILESTONE: SUBSTATION STRUCT - PROCUREMENT RELEASE - (30%)	0		08-Oct-26 A
155		*MILESTONE: SUBSTATION PROCUREMENT RELEASE (STEEL)	0		29-Oct-26
156		90% DESIGN - CIVIL	15	09-Oct-26 A	29-Oct-26
157		SUBSTATION DESIGN - OWNER REVIEW 60% - CIVIL / ELECT	15	09-Oct-26 A	29-Oct-26
158		SUBSTATION DESIGN - 90% - CIVIL	10	13-Oct-26	26-Oct-26
159		IFC - CIVIL	41	27-Oct-26	24-Dec-26
160		SUBSTATION DESIGN - OWNER REVIEW 90% - CIVIL	15	27-Oct-26	16-Nov-26
161		SUBSTATION DESIGN - IFC PHYSICAL DESIGN DOCUMENTS (100%) - CIVIL	26	17-Nov-26	24-Dec-26
162		*MILESTONE: SUBSTATION IFC DESIGN COMPLETE - CIVIL	0		24-Dec-26
163		SUBSTATION - ELECT P&C DESIGN (50%-IFC)	46	30-Oct-26	07-Jan-27
164		90% DESIGN - ELECT	36	30-Oct-26	22-Dec-26
165		SUBSTATION DESIGN - 90% - ELECT	21	30-Oct-26	01-Dec-26
166		SUBSTATION DESIGN - OWNER REVIEW 90% - ELECT	15	02-Dec-26	22-Dec-26

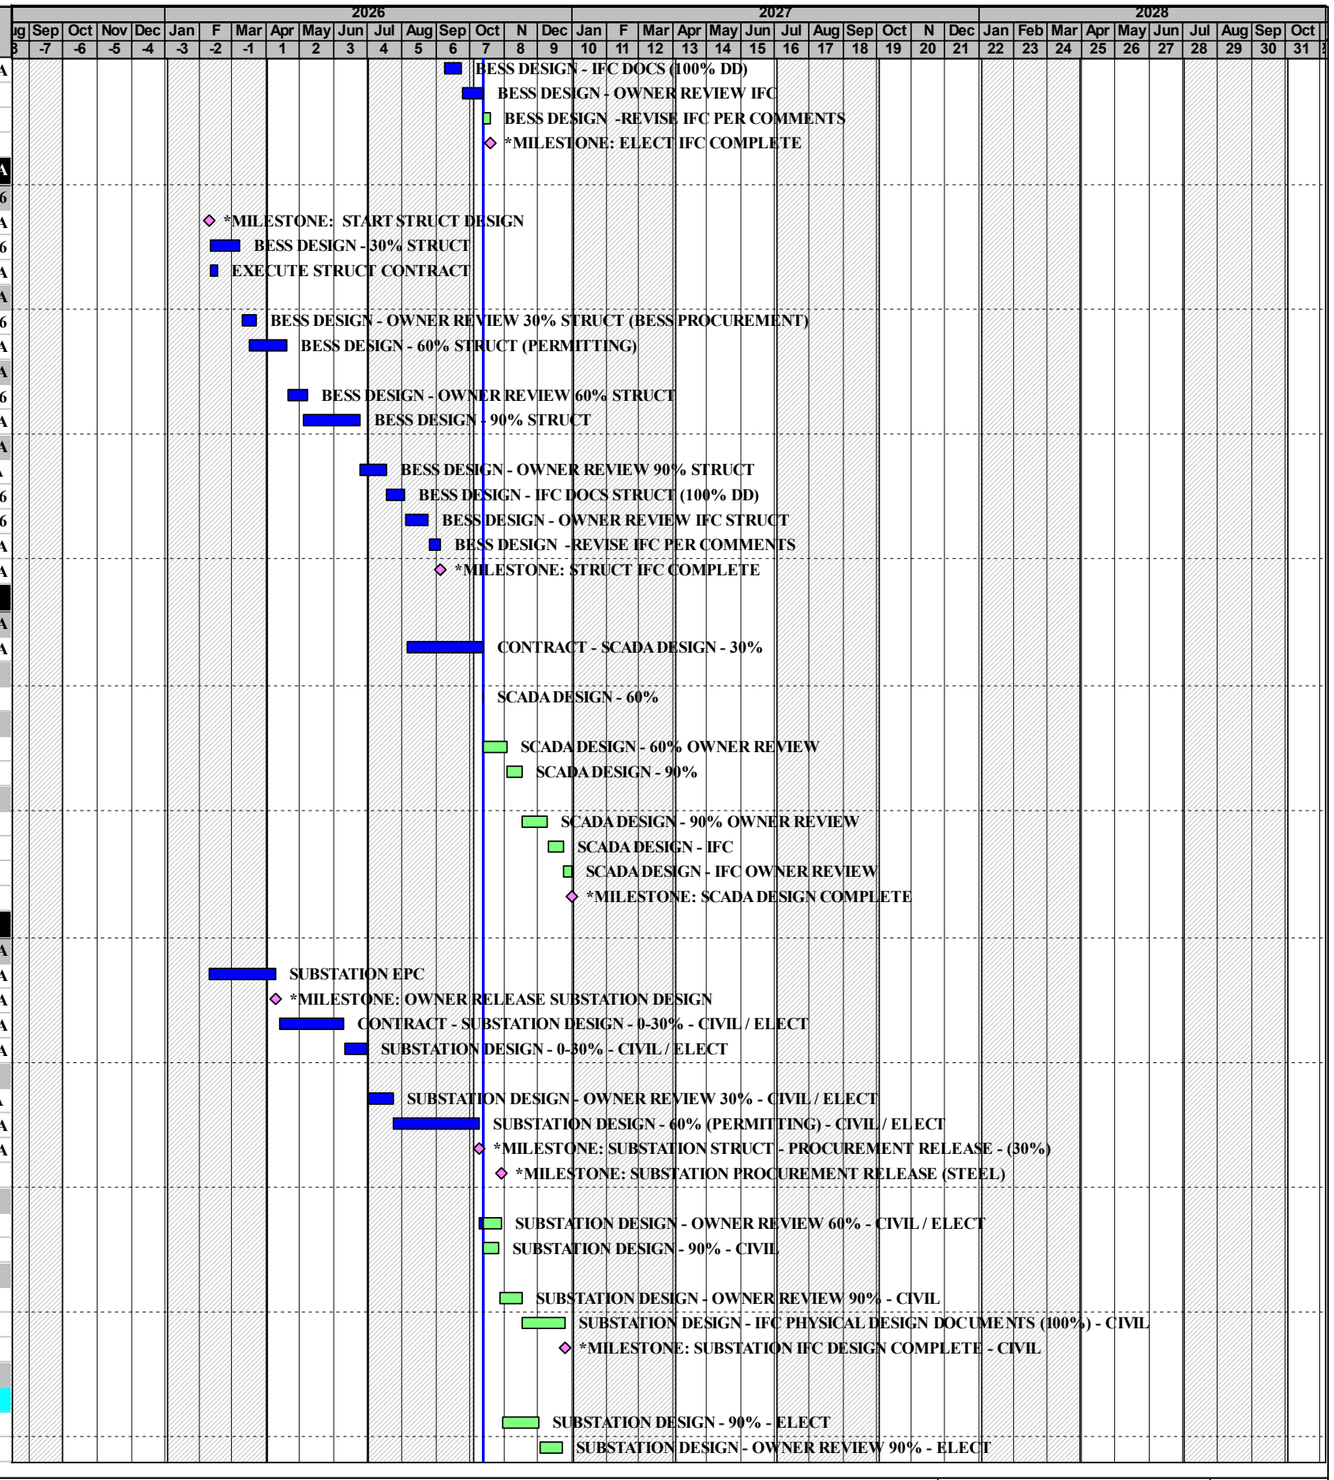


#	Activ ID	Activity Name	Dur	Start	Finish
167		IFC DESIGN - ELECT	10	23-Dec-26	07-Jan-27
168		SUBSTATION DESIGN - IFC ELECT DESIGN DOCUMENTS (100%)	10	23-Dec-26	07-Jan-27
169		*MILESTONE: SUBSTATION IFC DESIGN COMPLETE	0		07-Jan-27
170		PERMITTING	141	19-Mar-26 A	01-May-26 A
171		PERMITTING - 30% CIVIL (IMPORT SCOPE) CAL DAYS	10	19-Mar-26	02-Apr-26 A
172		DESIGN - PERMIT SUBMITAL (60% DESIGN) CAL DAYS	2	21-Apr-26 A	22-Apr-26 A
173		PERMITTING (BLDG) CAL DAYS	20	23-Apr-26 A	01-May-26
174		PROJECT PLANNING / SHARED SERVICES	638	05-Feb-26 A	06-Sep-28
175		PROCUREMENT	459	10-Feb-26 A	30-Nov-27
176		SCADA EQUIP	209	13-Oct-26	09-Aug-27
177		SCADA EQUIP - FAB LEAD TIME	207	13-Oct-26	05-Aug-27
178		RELEASE OF SCADA EQUIP (SUBSTATION)	7	13-Oct-26	21-Oct-26
179		FAB - SCADA EQUIP (SUBSTATION) 40WKS	200	22-Oct-26	05-Aug-27
180		DELIV - SCADA EQUIP - GSU I	2	06-Aug-27	09-Aug-27
181		DELIVER - SCADA EQUIP (SUBSTATION)	2	06-Aug-27	09-Aug-27
182		DELIV - SCADA EQUIP - GSU II	2	06-Aug-27	09-Aug-27
183		DELIVER - SCADA EQUIP (SUBSTATION)	2	06-Aug-27	09-Aug-27
184		AUX EQUIP	215	13-Oct-26	17-Aug-27
185		AUX EQUIP - FAB LEAD TIME	214	13-Oct-26	16-Aug-27
186		RELEASE FOR FAB ELECT AUX EQUIP	5	13-Oct-26	19-Oct-26
187		FAB - BESS ELECT AUX EQUIP	209	20-Oct-26	16-Aug-27
188		DELIV - AUX EQUIP - GSU I	1	17-Aug-27	17-Aug-27
189		DELIVER - BESS CIRC 1 - ELECT AUX EQUIP	1	17-Aug-27	17-Aug-27
190		DELIVER - BESS CIRC 2 - ELECT AUX EQUIP	1	17-Aug-27	17-Aug-27
191		DELIVER - BESS CIRC 3 - ELECT AUX EQUIP	1	17-Aug-27	17-Aug-27
192		DELIVER - BESS CIRC 4 - ELECT AUX EQUIP	1	17-Aug-27	17-Aug-27
193		DELIVER - BESS AUX 1 - ELECT AUX EQUIP	1	17-Aug-27	17-Aug-27
194		DELIV - AUX EQUIP - GSU II	1	17-Aug-27	17-Aug-27
195		DELIVER - BESS CIRC 5 - ELECT AUX EQUIP	1	17-Aug-27	17-Aug-27
196		DELIVER - BESS CIRC 6 - ELECT AUX EQUIP	1	17-Aug-27	17-Aug-27
197		DELIVER - BESS CIRC 7 - ELECT AUX EQUIP	1	17-Aug-27	17-Aug-27
198		DELIVER - BESS CIRC 8 - ELECT AUX EQUIP	1	17-Aug-27	17-Aug-27
199		DELIVER - BESS AUX 2 - ELECT AUX EQUIP	1	17-Aug-27	17-Aug-27
200		MV CABLE	295	10-Feb-26 A	07-Apr-27
201		MV CABLE - FAB LEAD TIME	270	10-Feb-26 A	31-Mar-27
202		RELEASE FOR FAB MV CABLE (60% DESIGN)	5	10-Feb-26 A	30-Sep-26 A
203		FAB LEAD TIME MV CABLE	106	01-Oct-26 A	31-Mar-27
204		DELIV - MV CABLE - GSU I	5	01-Apr-27	07-Apr-27
205		DELIVER MV CABLE	5	01-Apr-27	07-Apr-27
206		DELIV - MV CABLE - GSU II	5	01-Apr-27	07-Apr-27
207		DELIVER MV CABLE	5	01-Apr-27	07-Apr-27
208		MVT (OWNER 7ea/day)	333	10-Feb-26 A	01-Jun-27
209		MVT - FAB LEAD TIME (OWNER)	302	10-Feb-26 A	16-Apr-27
210		FAB - BESS MV EQUIP / MVT(52WKS) 112TOTAL (OWNER) *4/16/27	302	10-Feb-26 A	16-Apr-27
211		HOLD DELIVERY OF MVT TO JIT - 6/1 LATE FINISH (OWNER)	15	19-Apr-27	07-May-27
212		FAB - BESS MV EQUIP / MVT - HOLD TO JIT FOR A 6/1/27 LATE FINISH)	15	19-Apr-27	07-May-27
213		DELIV - MVT (OWNER)	16	10-May-27	01-Jun-27
214		SUMMARY - MVT DELIVERIES (107 EA @ 7 EA/DAY = 16 DAYS)	16	10-May-27	01-Jun-27
215		DELIV - MVT - GSU I	8	10-May-27	19-May-27
216		DELIVER - BESS CIRC 1 - MVT EQUIP / XFMR (6/DAY) 5/3 to 6/30	2	10-May-27	11-May-27
217		DELIVER - BESS CIRC 2 - MVT EQUIP / XFMR	2	12-May-27	13-May-27
218		DELIVER - BESS CIRC 3 - MVT EQUIP / XFMR	2	14-May-27	17-May-27
219		DELIVER - BESS CIRC 4 - MVT EQUIP / XFMR	2	18-May-27	19-May-27

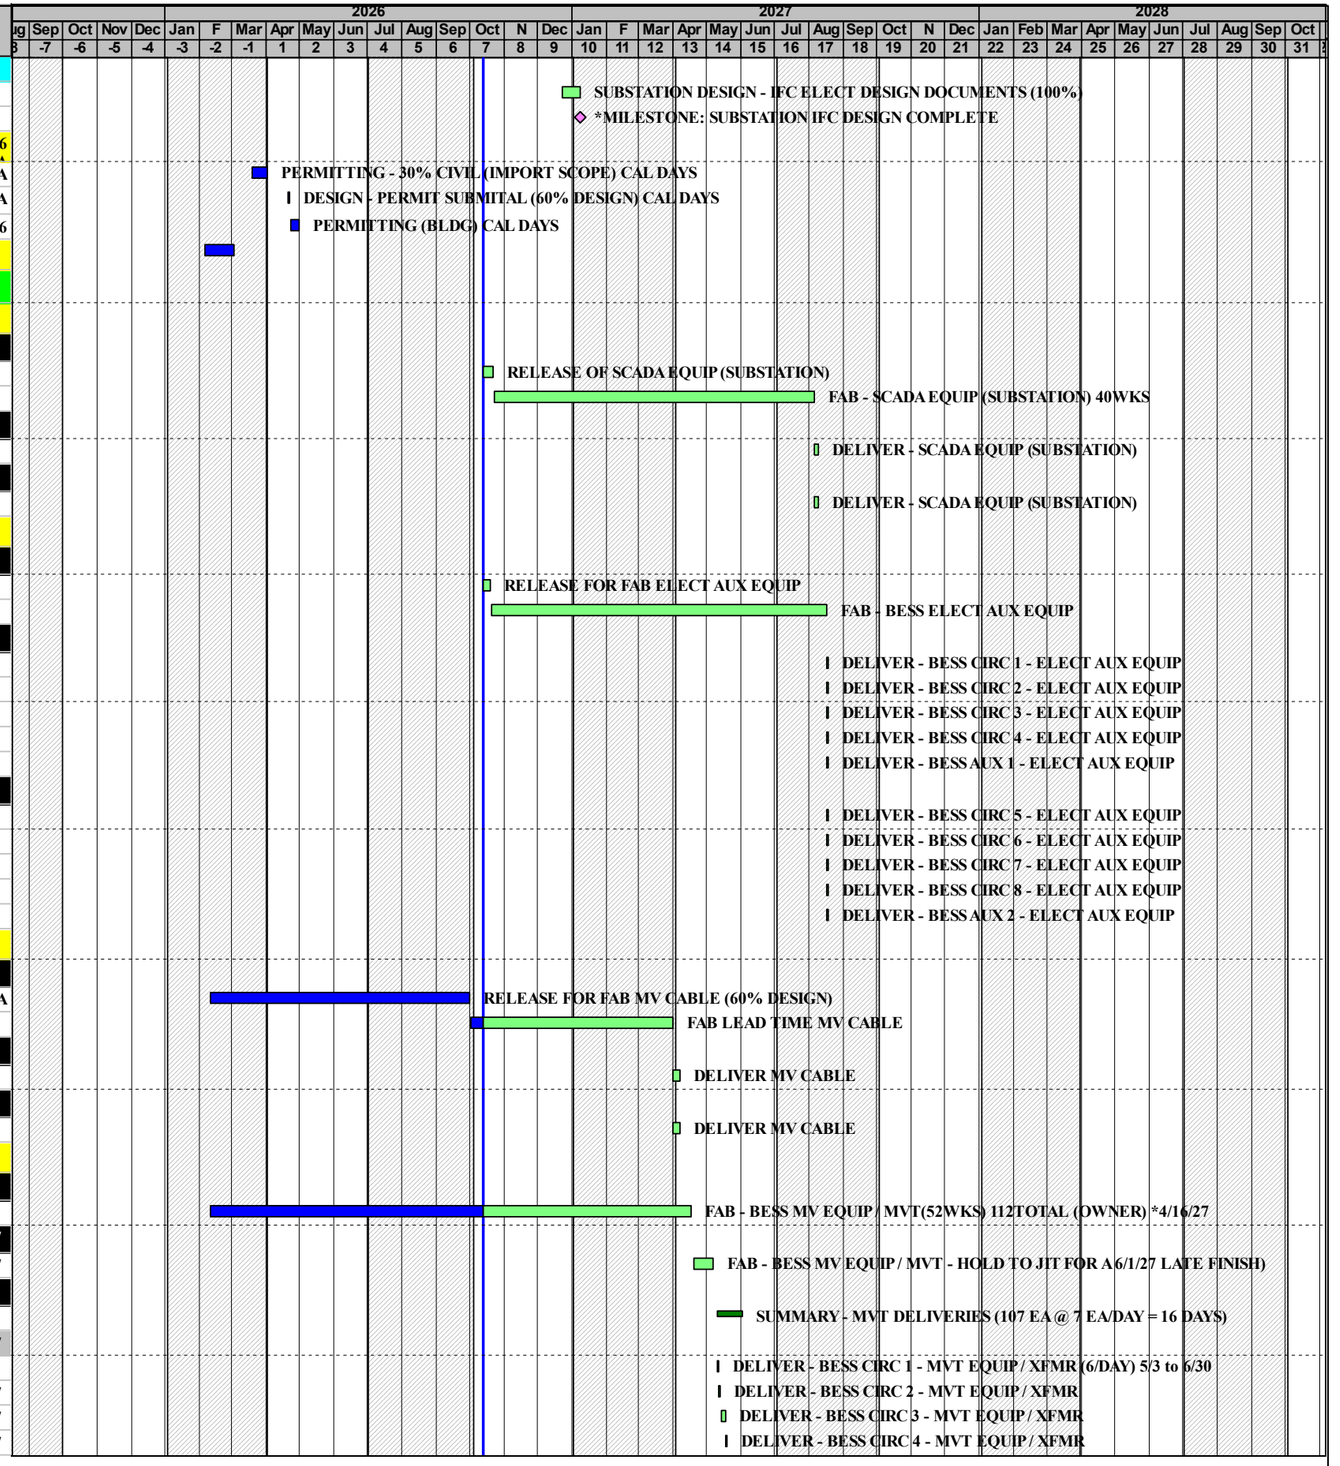


#	Activ ID	Activity Name	Dur	Start	Finish
220		DELIV - MVT - GSU II	8	20-May-27	01-Jun-27
221		DELIVER - BESS CIRC 5 - MVT EQUIP / XFMR	2	20-May-27	21-May-27
222		DELIVER - BESS CIRC 6 - MVT EQUIP / XFMR	2	24-May-27	25-May-27
223		DELIVER - BESS CIRC 7 - MVT EQUIP / XFMR	2	26-May-27	27-May-27
224		DELIVER - BESS CIRC 8 - MVT EQUIP / XFMR	2	28-May-27	01-Jun-27
225		SUBSTATION - GSU I & II	319	28-Aug-26	17-Nov-27
226		SUBSTATION - DISCONNECT SWITCHES - 35KV	150	30-Oct-26	03-Jun-27
227		SHOP DWGS / FAB LEAD TIME - SUBSTATION EQUIP - DISCONNECT SWITCHES 35 KV	150	30-Oct-26	03-Jun-27
228		DELIV - SUBSTATION EQUIP - DISCONNECT SWITCHES 35 KV	4	28-May-27	03-Jun-27
229		SUBSTATION - STATION SERVICE TRANSFORMER (XFMR)	95	08-Jan-27	20-May-27
230		SHOP DWGS / FAB LEAD TIME - SUBSTATION EQUIP - STATION SERVICE XFMR	95	08-Jan-27	20-May-27
231		DELIV - SUBSTATION EQUIP - STATION SERVICE XFMR	4	17-May-27	20-May-27
232		SUBSTATION - DISCONNECT SWITCHES - 345KV	305	08-Sep-26 A	17-Nov-27
233		SHOP DWGS / FAB LEAD TIME - SUBSTATION EQUIP - DISCONNECT SWITCHES - 345 KV	280	08-Sep-26 A	17-Nov-27
234		DELIV - SUBSTATION EQUIP - DISCONNECT SWITCHES - 345 KV	4	12-Nov-27	17-Nov-27
235		SUBSTATION - CIRCUIT BREAKERS - 35KV	150	30-Oct-26	03-Jun-27
236		SHOP DWGS / FAB LEAD TIME - SUBSTATION EQUIP - MV CIRCUIT BREAKERS - 35 KV	150	30-Oct-26	03-Jun-27
237		DELIV - SUBSTATION EQUIP - MV CIRCUIT BREAKERS - 35 KV	4	28-May-27	03-Jun-27
238		SUBSTATION - SURGE ARRESTERS	150	30-Oct-26	03-Jun-27
239		SHOP DWGS / FAB LEAD TIME - SUBSTATION EQUIP - SURGE ARRESTERS	150	30-Oct-26	03-Jun-27
240		DELIV - SUBSTATION EQUIP - SURGE ARRESTERS	4	28-May-27	03-Jun-27
241		SUBSTATION - BUS, CONNECTORS, & INSULATORS	90	08-Jan-27	13-May-27
242		SHOP DWGS / FAB LEAD TIME - SUBSTATION EQUIP - BUS, CONNECTORS, & INSULATORS	90	08-Jan-27	13-May-27
243		DELIV - SUBSTATION EQUIP - BUS, CONNECTORS, & INSULATORS	4	10-May-27	13-May-27
244		SUBSTATION - CONTROL ENCLOSURE & RELAY PANELS	275	28-Aug-26	16-Sep-27
245		SHOP DWGS / FAB LEAD TIME - SUBSTATION EQUIP - CONTROL ENCLOSURE	240	28-Aug-26	16-Sep-27
246		DELIV - SUBSTATION EQUIP - CONTROL ENCLOSURE	4	13-Sep-27	16-Sep-27
247		SUBSTATION - STEEL	200	30-Oct-26	13-Aug-27
248		SHOP DWGS / FAB LEAD TIME - SUBSTATION EQUIP - STEEL	200	30-Oct-26	13-Aug-27
249		DELIV - SUBSTATION EQUIP - STEEL	4	10-Aug-27	13-Aug-27
250		SUBSTATION - MPT GSU XFMR (OWNER)	459	10-Feb-26 A	30-Nov-27
251		FAB LEAD TIME - GSU I (OWNER)	354	10-Feb-26 A	30-Jun-27
252		FAB LEAD TIME - SUBSTATION EQUIP - MPT GSU XFMR (OWNER) GSU I (6/29/27)	353	10-Feb-26 A	29-Jun-27
253		DELIV - SUBSTATION EQUIP - MPT GSU XFMR (OWNER) 6/30//27 GSU I	1	30-Jun-27	30-Jun-27
254		FAB LEAD TIME - GSU II (OWNER)	459	10-Feb-26 A	30-Nov-27
255		FAB LEAD TIME - SUBSTATION EQUIP - MPT GSU XFMR (OWNER) GSU II (11/29/27)	458	10-Feb-26 A	29-Nov-27
256		DELIV - SUBSTATION EQUIP - MPT GSU XFMR (OWNER) 11/30//27	1	30-Nov-27	30-Nov-27
257		SUBSTATION - HV CIRCUIT BREAKERS (OWNER)	337	10-Feb-26 A	07-Jun-27
258		FAB LEAD TIME - BREAKER - GSU I	322	10-Feb-26 A	14-May-27
259		SHOP DWGS / FAB LEAD TIME - SUBSTATION EQUIP - HV CIRCUIT BREAKERS (GSU 1) (AVAIL 3/31/26)	61	10-Feb-26 A	13-May-27
260		DELIV - SUBSTATION EQUIP - HV CIRCUIT BREAKERS I (IN STORAGE)	1	14-May-27	14-May-27
261		FAB LEAD TIME - BREAKER - GSU II	337	10-Feb-26 A	07-Jun-27
262		SHOP DWGS / FAB LEAD TIME - SUBSTATION EQUIP - HV CIRCUIT BREAKERS (GSU II) (AVAIL 9/30/26)	189	10-Feb-26 A	04-Jun-27
263		DELIV - SUBSTATION EQUIP - HV CIRCUIT BREAKERS II (IN STORAGE)	1	07-Jun-27	07-Jun-27
264		BATTERIES (OWNER / TESLA MEGAPACK - 20ea/day)	401	10-Feb-26 A	07-Sep-27
265		BATTERIES - FAB LEAD TIME (OWNER/TESLA MEGAPACK) 6/1	333	10-Feb-26 A	01-Jun-27
266		RELEASE OF OFE BESS EQUIP - BATTERIES (OWNER)	10	10-Feb-26 A	23-Feb-26 A
267		MIN FAB LEAD TIME - BESS BATTERIES (6/1/27) 428EA	323	24-Feb-26 A	01-Jun-27
268		*MILESTONE: FRPS CONC PADS COMPLETE	0		15-Mar-27
269		BATTERIES - HOLD DELIV FOR JIT LATE FINISH OF 9/7	46	02-Jun-27	05-Aug-27
270		FAB - BESS BATTERIES (HOLD FOR JIT DELIV FOR LAST BAT FINISH OF 9/7)	46	02-Jun-27	05-Aug-27
271		BATTERIES - DELIV (22DAYS WITH 9/7 LATE FINISH)	22	06-Aug-27	07-Sep-27
272		SUMMARY - TESLA BAT DELIV	22	06-Aug-27	07-Sep-27
273		DELIV - BATTERIES - GSU I (OWNER/TESLA MEGAPACK)	12	06-Aug-27	23-Aug-27

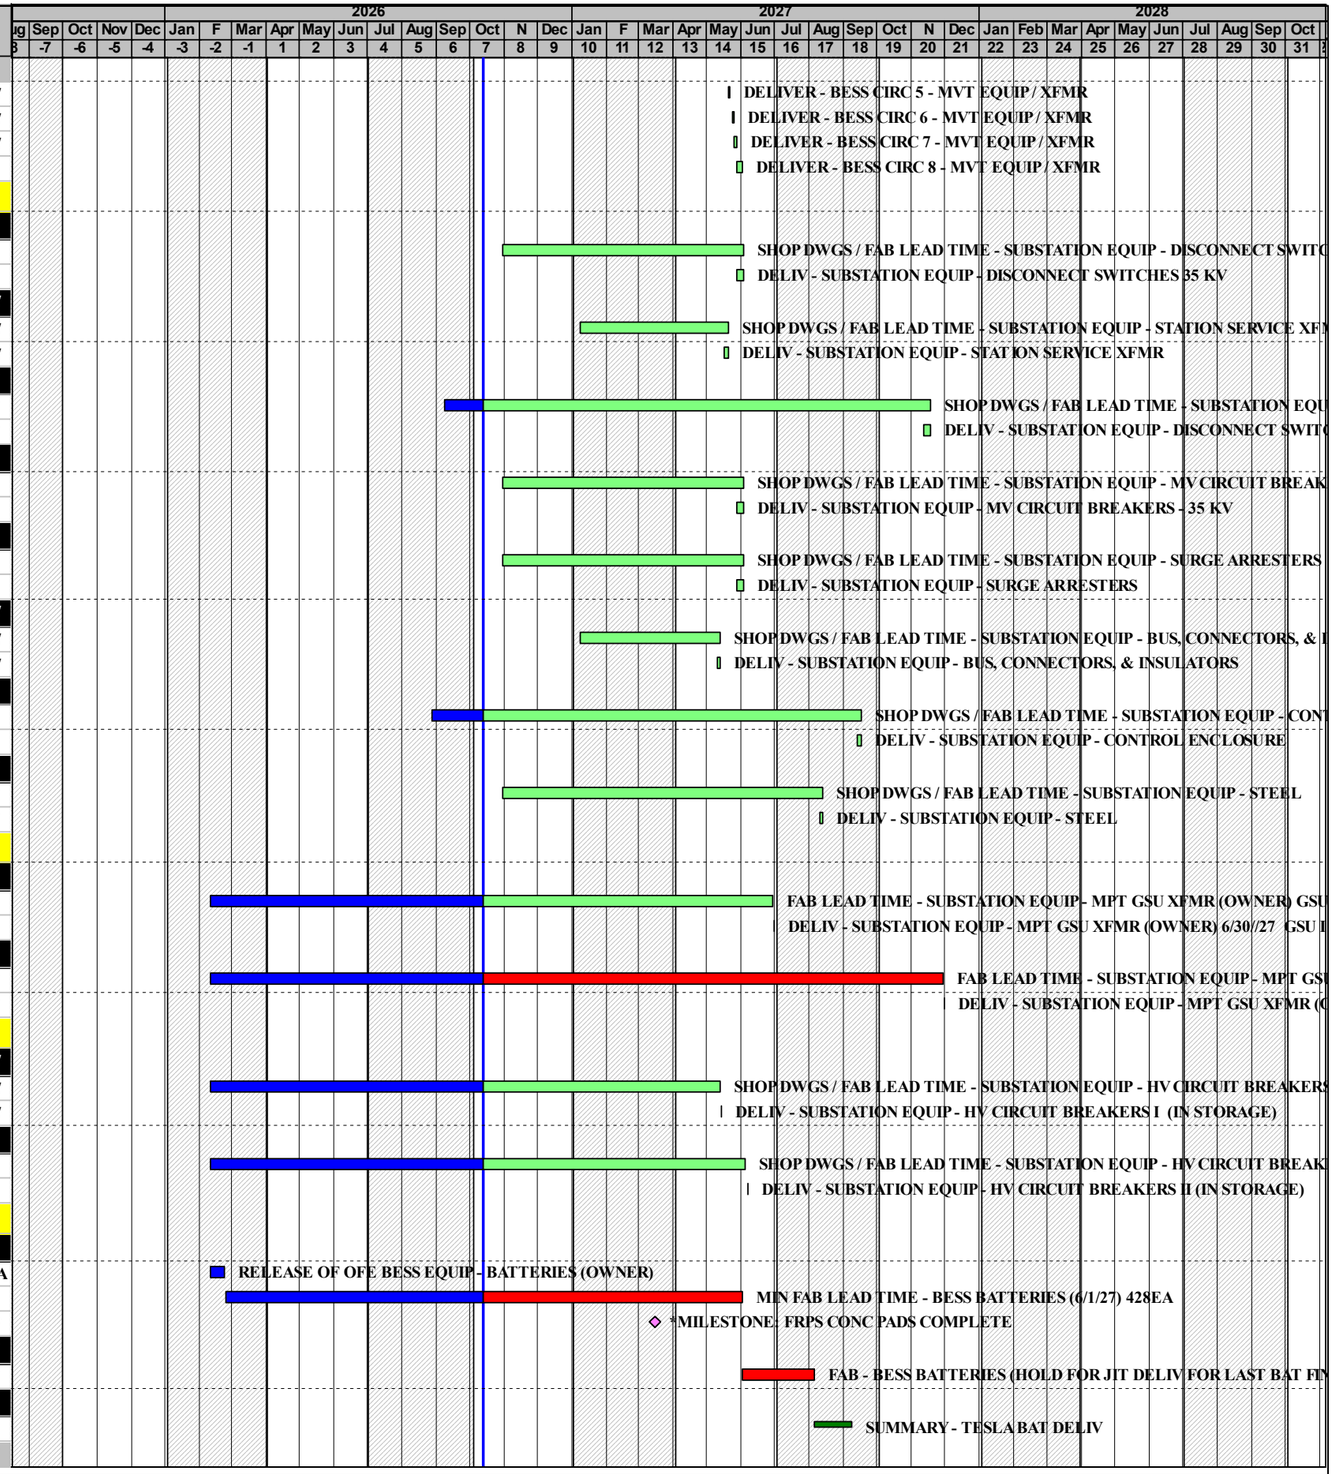


#	Activ ID	Activity Name	Dur	Start	Finish
274		DELIVER - BESS CIRC 1 - BATTERIES (428EA @ 20/day = 22DAY)	3	06-Aug-27	10-Aug-27
275		DELIVER - BESS CIRC 2 - BATTERIES	3	11-Aug-27	13-Aug-27
276		DELIVER - BESS CIRC 3 - BATTERIES	3	16-Aug-27	18-Aug-27
277		DELIVER - BESS CIRC 4 - BATTERIES	3	19-Aug-27	23-Aug-27
278		DELIV - BATTERIES - GSU II (OWNER/TESLA MEGAPACK)	10	24-Aug-27	07-Sep-27
279		DELIVER - BESS CIRC 5 - BATTERIES	3	24-Aug-27	26-Aug-27
280		DELIVER - BESS CIRC 6 - BATTERIES	3	27-Aug-27	31-Aug-27
281		DELIVER - BESS CIRC 7 - BATTERIES	2	01-Sep-27	02-Sep-27
282		DELIVER - BESS CIRC 8 - BATTERIES *9/7 late finish	2	03-Sep-27	07-Sep-27
283		CONSTRUCTION	719	15-Aug-25 A	06-Sep-28
284		OWNER MAKE READY - COAL MITIGATION & IMPORT TO EL 406'	197	15-Aug-25 A	04-Sep-26 A
285		MAKE READY - CONTRACTING (BY OWNER)	0	15-Aug-25	17-Aug-25
286		EARTHWORK - COAL REMOVAL & IMPORT TO EL 406' (BY OWNER) - 80%	99	18-Aug-25	01-Apr-26 A
287		EARTHWORK - COAL REMOVAL & IMPORT TO EL 406' (BY OWNER) - 100%	34	20-Jul-26 A	04-Sep-26 A
288		*MILESTONE: MAKE READY SUBST COMPLETE (BY OWNER) *3/30/26	0		04-Sep-26 A
289		MAKE READY / IMPORT	163	01-Apr-26 A	23-Dec-26
290		MAKE READY / EARTHWORK IMPORT	163	01-Apr-26 A	23-Dec-26
291		MOB - BESS	5	01-Apr-26 A	10-Apr-26 A
292		*MILESTONE: START MOB/SITE/ EARTHWORK BESS	0	01-Apr-26 A	
293		*MILESTONE: START MOB/SITE/EARTHWORK - SUBSTATION	0	06-Apr-26 A	
294		MOB - SUBSTATION	10	06-Apr-26 A	24-Apr-26 A
295		EARTHWORK - CIVIL (IMPORT AT BESS YARD/SUBSTATION/O&M)	50	07-May-26	13-Aug-26
296		EARTHWORK - CIVIL (IMPORT AT COAL PILE)	50	14-Sep-26 A	23-Dec-26
297		SUBSTATION	443	07-May-26	15-Feb-28
298		MOB / EARTHWORK	233	07-May-26	16-Apr-27
299		SUBSTATION - EARTHWORK / CIVIL / GRADING	11	07-May-26	02-Jun-26 A
300		MOBILIZE SUBSTATION INSTALLATION CREW	5	11-Jan-27	19-Jan-27
301		SUBSTATION - INSTALL FRPS CONC FOUNDATIONS	40	20-Jan-27	07-Apr-27
302		SUBSTATION - MILL CERT SUBMTL REVIEW	10	20-Jan-27	10-Feb-27
303		*MILESTONE: SUBSTATION MILL CERT SUBMTL	0	20-Jan-27	
304		SUBSTATION - FOUNDATION CURE	15	02-Apr-27	16-Apr-27
305		ERECTION / ELECTRICAL WORK	130	08-Apr-27	11-Oct-27
306		SUBSTATION - INSTALL CONDUIT	30	08-Apr-27	19-May-27
307		SUBSTATION - INSTALL GROUNDING	30	08-Apr-27	19-May-27
308		SUBSTATION - SET STEEL STRUCT	40	16-Aug-27	11-Oct-27
309		EQUIP INSTALL	59	17-Sep-27	10-Dec-27
310		SUBSTATION - INSTALL CONTROL ENCLOSURE & RELAY PANELS	5	17-Sep-27	23-Sep-27
311		SUBSTATION - GROUND COVER	4	24-Sep-27	29-Sep-27
312		SUBSTATION - PULL & TERM CABLE	28	24-Sep-27	02-Nov-27
313		SUBSTATION - INSTALL INSULATORS	5	12-Oct-27	18-Oct-27
314		SUBSTATION - INSTALL BUS, CONNECTORS	10	19-Oct-27	01-Nov-27
315		SUBSTATION - INSTALL PT'S & SURGE ARRESTORS	10	19-Oct-27	01-Nov-27
316		SUBSTATION - INSTALL DISCONNECT SWITCHES 35 KV	3	19-Oct-27	21-Oct-27
317		SUBSTATION - INSTALL MV CIRCUIT BREAKERS	5	19-Oct-27	25-Oct-27
318		SUBSTATION - INSTALL CCVT	5	02-Nov-27	08-Nov-27
319		SUBSTATION - INSTALL CTS	5	09-Nov-27	15-Nov-27
320		SUBSTATION - INSTALL STATION SERVICE XFRMR / ABG CONDUIT	5	09-Nov-27	15-Nov-27
321		SUBSTATION - INSTALL DISCONNECT SWITCHS - 345 KV	10	18-Nov-27	03-Dec-27
322		SUBSTATION - INSTALL YARD LIGHTING / ABG CONDUIT / EHS WIRE	5	06-Dec-27	10-Dec-27
323		O&M BUILDING	48	08-Apr-27	15-Jun-27
324		UG ELEC ROUGH-IN - O&M BLDG	10	08-Apr-27	21-Apr-27
325		STRUCT PAD - O&M BLDG	5	22-Apr-27	28-Apr-27
326		BLDG ERECT - O&M BLDG	5	29-Apr-27	05-May-27
327		BLDG / COMMUNICATION LOOP - O&M BLDG	20	06-May-27	03-Jun-27
328		INTERIOR BUILDOUT - O&M BLDG	10	06-May-27	19-May-27

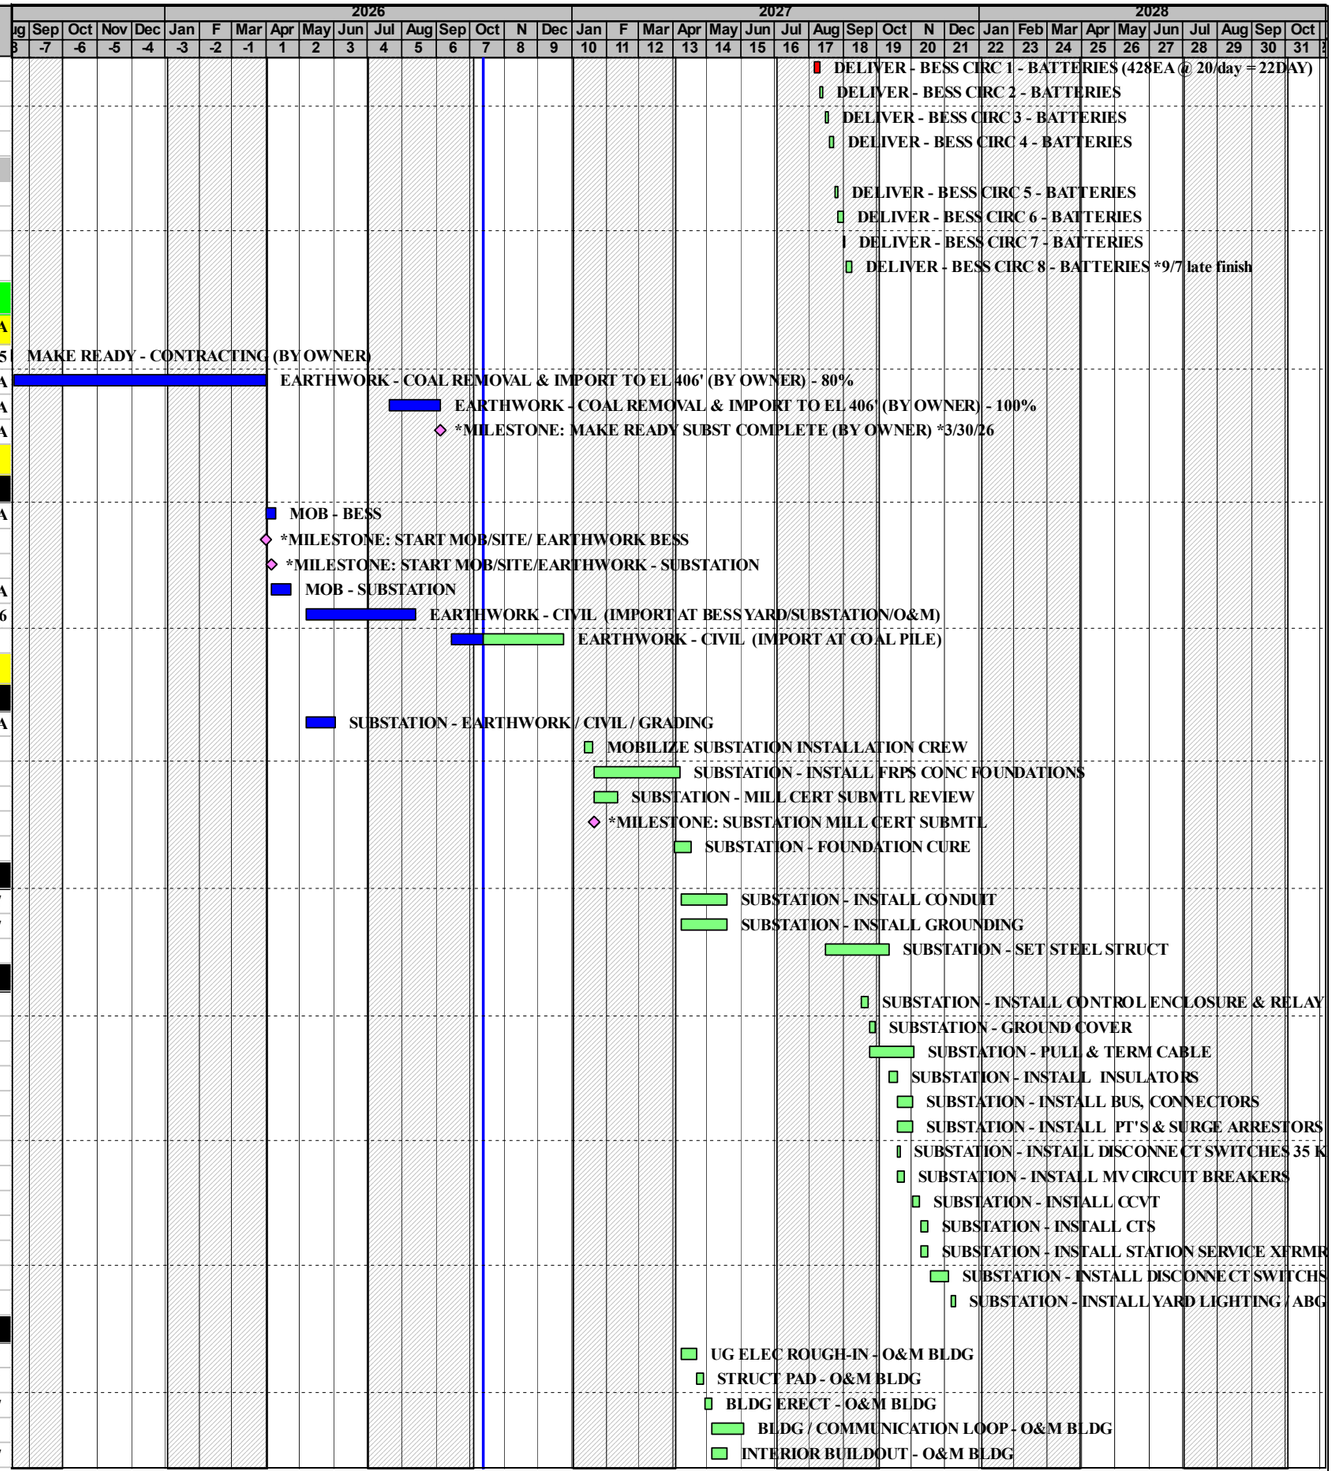


#	Activ ID	Activity Name	Dur	Start	Finish
329		COMMUNICATION BUILDOUT - O&M BLDG	10	20-May-27	03-Jun-27
330		QA / QC - O&M BLDG	3	04-Jun-27	08-Jun-27
331		CERTIFICATE OF OCCUPANCY - O&M BLDG	5	09-Jun-27	15-Jun-27
332		**SUBSTATION COMPLETION - GSU I**	120	01-Jul-27	21-Dec-27
333		SET / TIE-IN HV CIRC BREAKER	7	12-Oct-27	20-Oct-27
334		SUBSTATION - INSTALL HV CIRCUIT BREAKERS - GSU I	7	12-Oct-27	20-Oct-27
335		SET / TIE-IN MPT	51	01-Jul-27	13-Sep-27
336		SUBSTATION - OWNER SET/ ASSEMBLE/ OIL FILL / TEST - MAIN POWER TRANSFORMER - GSU I	44	01-Jul-27	01-Sep-27
337		SUBSTATION - TERM - MAIN POWER TRANSFORMER - GSU I	2	02-Sep-27	03-Sep-27
338		SUBSTATION - CONTROLS FINAL TERMS & CHECK-OUT - GSU I	5	07-Sep-27	13-Sep-27
339		TESTING & SUBST COMPLETION (GSU I)	24	16-Nov-27	21-Dec-27
340		SUBSTATION - UTILITY SIGN-OFF	2	16-Nov-27	17-Nov-27
341		SUBSTATION - MECH COMPLETION	2	13-Dec-27	14-Dec-27
342		*MILESTONE: SUBSTATION - GSU I BACKFEED (READY FOR SYNC)	0		14-Dec-27
343		SUBSTATION - MPT SOAK / BACKFEED	2	15-Dec-27	16-Dec-27
344		SUBSTATION - SUBMIT FOR COMPLETION	3	17-Dec-27	21-Dec-27
345		*MILESTONE: SUBSTATION COMPLETION - GSU I	0		21-Dec-27
346		**SUBSTATION COMPLETION - GSU II**	80	21-Oct-27	15-Feb-28
347		SET / TIE-IN HV CIRC BREAKER	7	21-Oct-27	29-Oct-27
348		SUBSTATION - INSTALL HV CIRCUIT BREAKERS - GSU II	7	21-Oct-27	29-Oct-27
349		SET / TIE-IN MPT	44	30-Nov-27	01-Feb-28
350		SUBSTATION - OWNER SET/ ASSEMBLE/ OIL FILL / TEST - MAIN POWER TRANSFORMER - GSU II	39	30-Nov-27	25-Jan-28
351		SUBSTATION - TERM - MAIN POWER TRANSFORMER - GSU II	2	26-Jan-28	27-Jan-28
352		SUBSTATION - CONTROLS FINAL TERMS & CHECK-OUT - GSU II	5	26-Jan-28	01-Feb-28
353		TESTING & SUBST COMPLETION (GSU II)	10	02-Feb-28	15-Feb-28
354		SUBSTATION - UTILITY SIGN-OFF	1	02-Feb-28	02-Feb-28
355		SUBSTATION - MECH COMPLETION	1	03-Feb-28	03-Feb-28
356		SUBSTATION - MPT SOAK / BACKFEED	2	04-Feb-28	07-Feb-28
357		*MILESTONE: SUBSTATION - GSU II BACKFEED (READY FOR SYNC)	0	07-Feb-28	
358		*MILESTONE: SUBSTATION - GSU II SYNC	0		07-Feb-28
359		SUBSTATION - SUBMIT FOR COMPLETION	6	08-Feb-28	15-Feb-28
360		*MILESTONE: SUBSTATION COMPLETION - GSU II	0		15-Feb-28
361		**BESS PRODUCTION**	341	17-Aug-26	03-Jan-28
362		**BESS PRODUCTION (GSU I)**	300	17-Aug-26	01-Nov-27
363		MOB / EARTHWORK (GSU I)	88	17-Aug-26	06-Jan-27
364		EARTHWORK	5	17-Aug-26	21-Aug-26
365		MOB / EARTHWORK - PAD CERTIFY	5	17-Aug-26	21-Aug-26
366		FENCING	15	11-Dec-26	06-Jan-27
367		PERMANENT FENCING (JIT TO EQUIP SET)	15	11-Dec-26	06-Jan-27
368		UG ELECT @ EQUIP PADS (GSU I)	49	06-Oct-26 A	11-Dec-26
369		UG ELECT - CIRC 1	16	06-Oct-26 A	23-Oct-26
370		BESS - UG ELECT ROUGH-IN/CONDUIT AT MVT (CIRC 1)	15	06-Oct-26 A	23-Oct-26
371		BESS - ELECT GROUNDING (CIRC 1)	5	19-Oct-26	23-Oct-26
372		UG ELECT - CIRC 2	10	26-Oct-26	06-Nov-26
373		BESS - UG ELECT ROUGH-IN/CONDUIT AT MVT (CIRC 2)	10	26-Oct-26	06-Nov-26
374		BESS - ELECT GROUNDING (CIRC 2)	5	02-Nov-26	06-Nov-26
375		UG ELECT - CIRC 3	10	09-Nov-26	20-Nov-26
376		BESS - UG ELECT ROUGH-IN/CONDUIT AT MVT (CIRC 3)	10	09-Nov-26	20-Nov-26
377		BESS - ELECT GROUNDING (CIRC 3)	5	16-Nov-26	20-Nov-26
378		UG ELECT - CIRC 4	10	23-Nov-26	08-Dec-26
379		BESS - UG ELECT ROUGH-IN/CONDUIT AT MVT (CIRC 4)	10	23-Nov-26	08-Dec-26
380		BESS - ELECT GROUNDING (CIRC 4)	5	02-Dec-26	08-Dec-26
381		UG ELECT - AUX	3	09-Dec-26	11-Dec-26
382		BESS - AUX POWER ELECT DUCT BANK	3	09-Dec-26	11-Dec-26
383		FOUNDATIONS - MVT EQUIP PADS (GSU I)	65	27-Aug-26	06-Jan-27
384		BESS MILL CERT SUBMTL	11	27-Aug-26	23-Sep-26 A

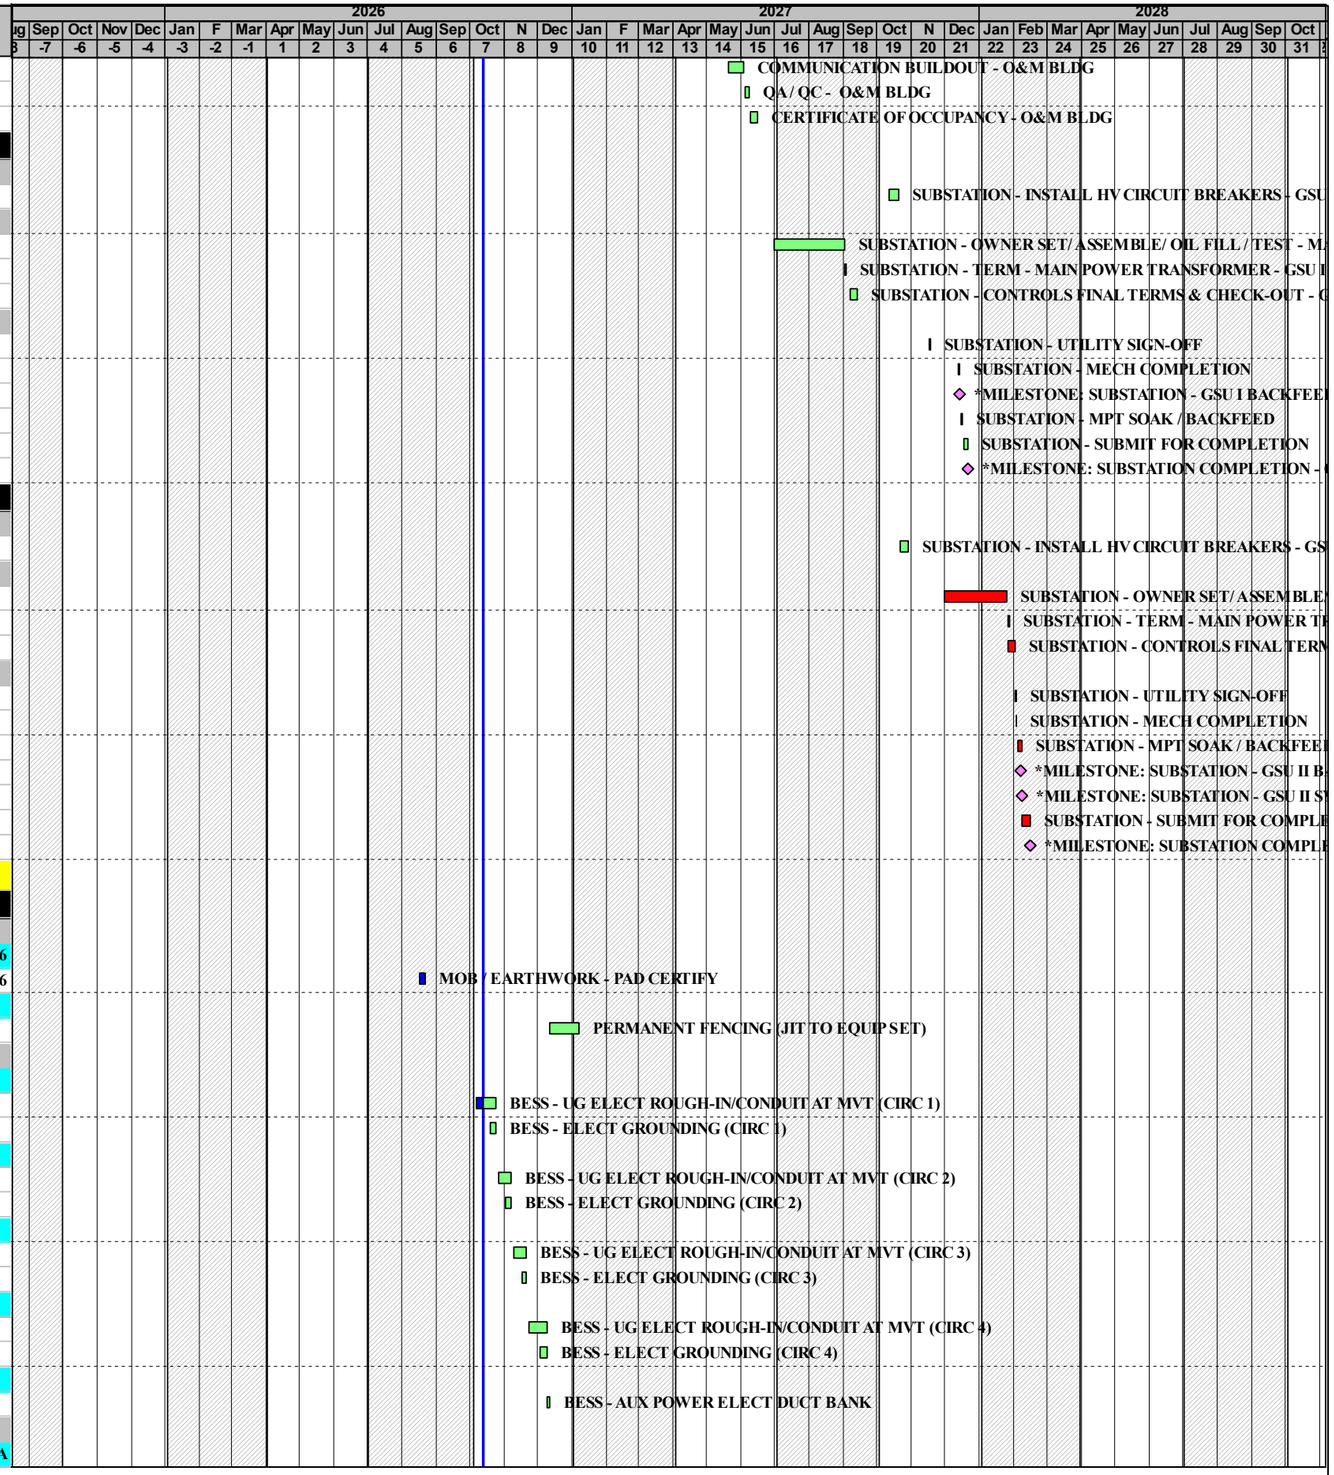


#	Activ ID	Activity Name	Dur	Start	Finish
385		BESS CIRC 1 - MILL CERT SUBMTL REVIEW	10	27-Aug-26	23-Sep-26 A
386		*MILESTONE: BESS CIRC 1 MILL CERT SUBMTL (GSU I)	0	10-Sep-26 A	
387		CONC FOUNDATIONS - MVT EQUIP PADS - CIRC 1	9	06-Nov-26	18-Nov-26
388		BESS - FRPS CONC MVT PADS (CIRC 1)	6	06-Nov-26	13-Nov-26
389		BESS - CURE CONC MVT PADS (CIRC 1)	5	14-Nov-26	18-Nov-26
390		CONC FOUNDATIONS - MVT EQUIP PADS - CIRC 2	8	23-Nov-26	05-Dec-26
391		BESS - FRPS CONC MVT PADS (CIRC 2)	4	23-Nov-26	30-Nov-26
392		BESS - CURE CONC MVT PADS (CIRC 2)	5	01-Dec-26	05-Dec-26
393		CONC FOUNDATIONS - MVT EQUIP PADS - CIRC 3	7	08-Dec-26	16-Dec-26
394		BESS - FRPS CONC MVT PADS (CIRC 3)	4	08-Dec-26	11-Dec-26
395		BESS - CURE CONC MVT PADS (CIRC 3)	5	12-Dec-26	16-Dec-26
396		CONC FOUNDATIONS - MVT EQUIP PADS - CIRC 4	8	21-Dec-26	02-Jan-27
397		BESS - FRPS CONC MVT PADS (CIRC 4)	4	21-Dec-26	28-Dec-26
398		BESS - CURE CONC MVT PADS (CIRC 4)	5	29-Dec-26	02-Jan-27
399		AUX FOUNDATIONS	5	29-Dec-26	06-Jan-27
400		BESS - AUX FRPS CONC PAD & QA/QC	5	29-Dec-26	06-Jan-27
401		FOUNDATIONS - BATT EQUIP PADS (GSU I)	86	24-Aug-26	11-Jan-27
402		CONC FOUNDATIONS - BATT EQUIP PADS - CIRC 1	54	24-Aug-26	25-Nov-26
403		BESS - FRPS CONC BATT PADS (CIRC 1) - ROAD ROW	15	24-Aug-26	11-Sep-26 A
404		BESS - CURE CONC BATT PADS (CIRC 1) - ROAD ROW	5	11-Sep-26 A	05-Oct-26 A
405		BESS - FRPS CONC BATT PADS (CIRC 1) - SWALE ROW	5	16-Nov-26	20-Nov-26
406		BESS - CURE CONC BATT PADS (CIRC 1) - SWALE ROW	5	21-Nov-26	25-Nov-26
407		CONC FOUNDATIONS - BATT EQUIP PADS - CIRC 2	67	14-Sep-26 A	12-Dec-26
408		BESS - FRPS CONC BATT PADS (CIRC 2) - ROAD ROW	7	14-Sep-26 A	21-Sep-26 A
409		BESS - CURE CONC BATT PADS (CIRC 2) - ROAD ROW	5	01-Oct-26 A	05-Oct-26 A
410		BESS - FRPS CONC BATT PADS (CIRC 2) - SWALE ROW	5	01-Dec-26	07-Dec-26
411		BESS - CURE CONC BATT PADS (CIRC 2) - SWALE ROW	5	08-Dec-26	12-Dec-26
412		CONC FOUNDATIONS - BATT EQUIP PADS - CIRC 3	62	23-Sep-26 A	23-Dec-26
413		BESS - FRPS CONC BATT PADS (CIRC 3) - ROAD ROW	6	23-Sep-26 A	28-Sep-26 A
414		BESS - CURE CONC BATT PADS (CIRC 3) - ROAD ROW	5	01-Oct-26 A	05-Oct-26 A
415		BESS - FRPS CONC BATT PADS (CIRC 3) - SWALE ROW	5	14-Dec-26	18-Dec-26
416		BESS - CURE CONC BATT PADS (CIRC 3) - SWALE ROW	5	19-Dec-26	23-Dec-26
417		CONC FOUNDATIONS - BATT EQUIP PADS - CIRC 4	73	29-Sep-26 A	11-Jan-27
418		BESS - FRPS CONC BATT PADS (CIRC 4) - ROAD ROW	6	29-Sep-26 A	05-Oct-26 A
419		BESS - CURE CONC BATT PADS (CIRC 4) - ROAD ROW	5	06-Oct-26 A	13-Oct-26
420		BESS - FRPS CONC BATT PADS (CIRC 4) - SWALE ROW	5	29-Dec-26	06-Jan-27
421		BESS - CURE CONC BATT PADS (CIRC 4) - SWALE ROW	5	06-Jan-27	11-Jan-27
422		MV ELECT / FIBER TRENCHING/WIRE/BACKFILL (GSU I)	36	16-Nov-26	18-Jan-27
423		MV ELECT/FIBER TRENCHING/WIRE/BACKFILL - CIRC 1	15	16-Nov-26	08-Dec-26
424		BESS - MV ELECT / FIBER TRENCHING & CONDUIT- CIRC 1	15	16-Nov-26	08-Dec-26
425		MV ELECT/FIBER TRENCHING/WIRE/BACKFILL - CIRC 2	7	09-Dec-26	17-Dec-26
426		BESS - MV ELECT / FIBER TRENCHING & CONDUIT- CIRC 2	7	09-Dec-26	17-Dec-26
427		MV ELECT/FIBER TRENCHING/WIRE/BACKFILL - CIRC 3	7	18-Dec-26	30-Dec-26
428		BESS - MV ELECT / FIBER TRENCHING & CONDUIT- CIRC 3	7	18-Dec-26	30-Dec-26
429		MV ELECT/FIBER TRENCHING/WIRE/BACKFILL - CIRC 4	7	04-Jan-27	18-Jan-27
430		BESS - MV ELECT / FIBER TRENCHING & CONDUIT- CIRC 4	7	04-Jan-27	18-Jan-27
431		EQUIP - MVT/SCADA/AUX (GSU I)	98	12-May-27	29-Sep-27
432		CIRC EQUIP 1 - MVT/SCADA/AUX (GSU I)	77	12-May-27	30-Aug-27
433		MV EQUIP & TERMS	14	12-May-27	01-Jun-27
434		BESS - SET ELECT MVT/ XFMR EQUIP (CIRC 1) 12EA	2	12-May-27	13-May-27
435		BESS - MVT/ XFMR EQUIP WIRE PULL & TERMS	10	14-May-27	27-May-27
436		BESS - MV WIRE TEST (VLF/PD) (CIRC 1)	2	28-May-27	01-Jun-27
437		SCADA EQUIP / TERMS	7	14-May-27	24-May-27
438		BESS - SET SCADA EQUIP (CIRC 1)	2	14-May-27	17-May-27
439		BESS - SCADA EQUIP WIRE PULL / TERMINATION (CIRC 1)	5	18-May-27	24-May-27
440		FIBER / TESTING	2	28-May-27	01-Jun-27

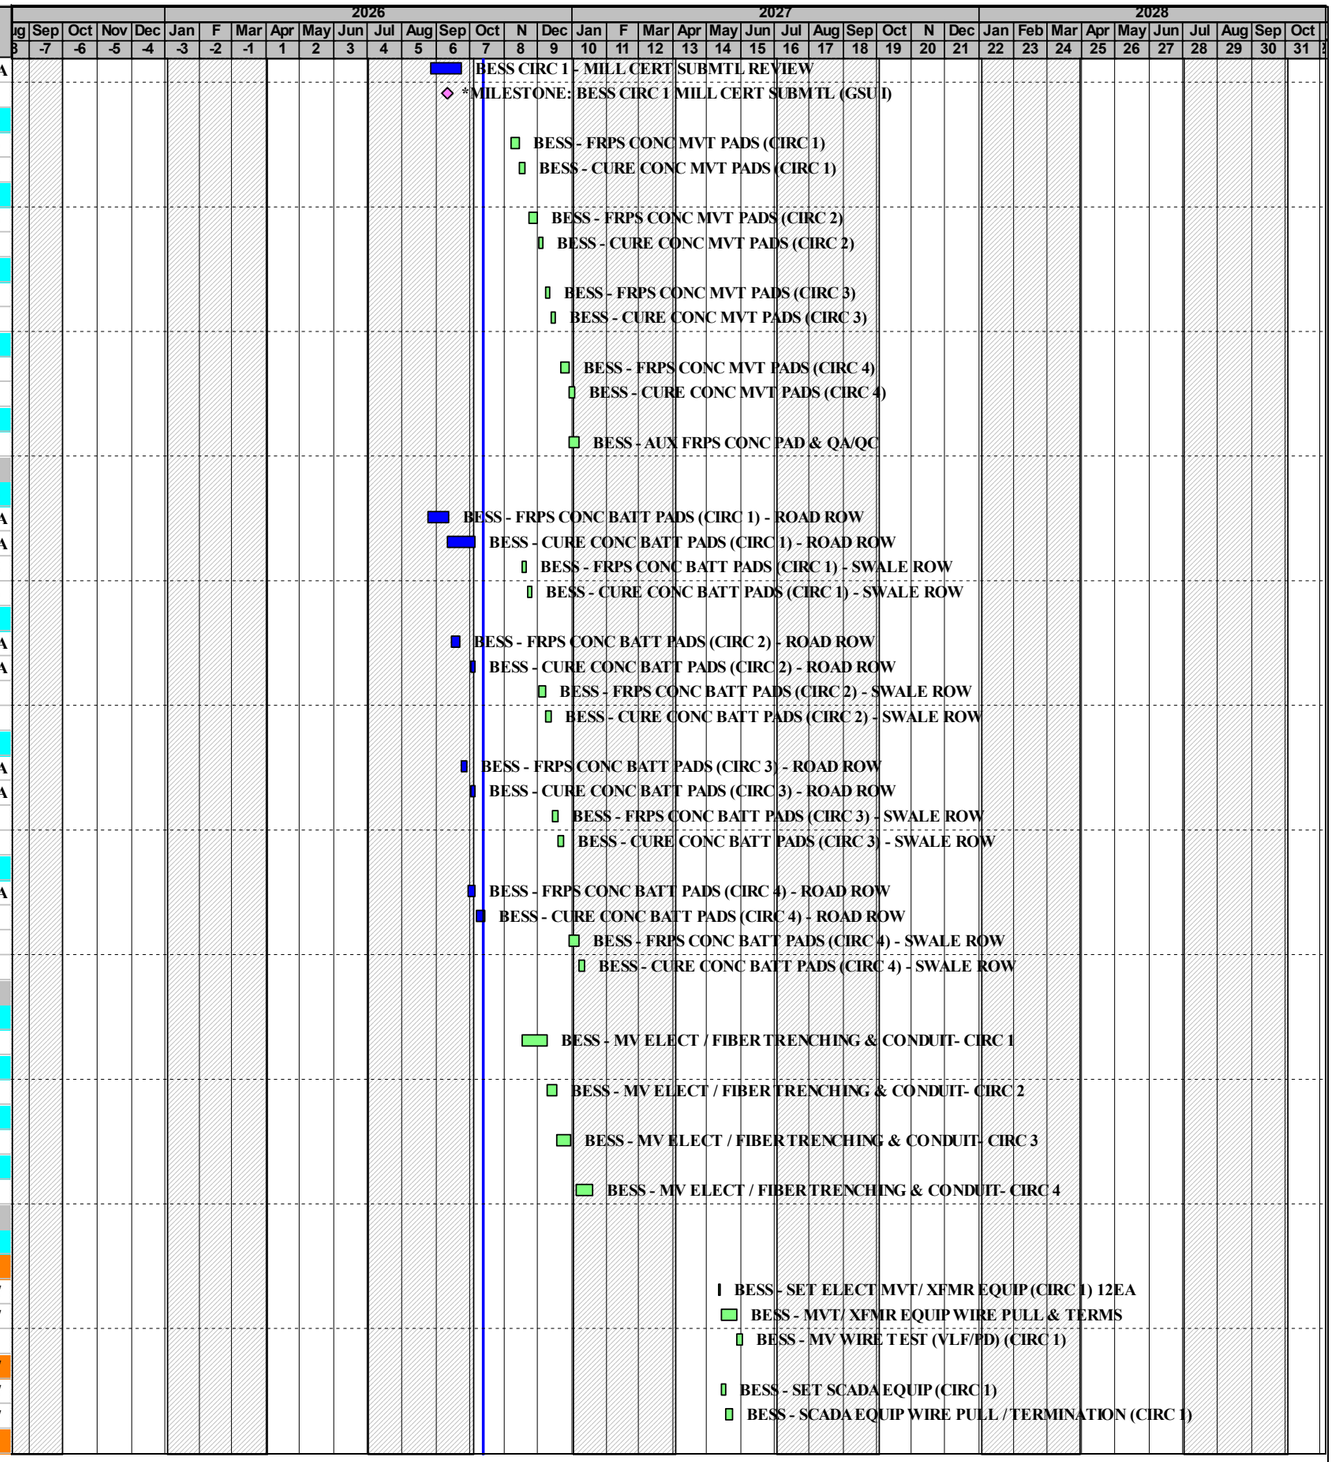


#	Activ ID	Activity Name	Dur	Start	Finish
441		BESS - FIBER OTDR TEST (CIRC 1)	2	28-May-27	01-Jun-27
442		AUX EQUIP / TERMS	9	18-Aug-27	30-Aug-27
443		BESS - SET ELECT AUX EQUIP (CIRC 1)	2	18-Aug-27	19-Aug-27
444		BESS - AUX WIRE PULL / TERMINATION / TESTING (CIRC 1)	7	20-Aug-27	30-Aug-27
445		CIRC EQUIP 2 - MVT/SCADA/AUX (GSU I)	82	14-May-27	09-Sep-27
446		MV EQUIP & TERMS	22	14-May-27	15-Jun-27
447		BESS - SET ELECT MVT/ XFMR EQUIP (CIRC 2) 12EA	2	14-May-27	17-May-27
448		BESS - MVT/ XFMR EQUIP/XFMR TERMINATION (CIRC 2)	10	28-May-27	11-Jun-27
449		BESS - MV WIRE TEST (VLF/PD) (CIRC 2)	2	14-Jun-27	15-Jun-27
450		SCADA EQUIP / TERMS	10	18-May-27	01-Jun-27
451		BESS - SET SCADA EQUIP (CIRC 2)	2	18-May-27	19-May-27
452		BESS - SCADA EQUIP WIRE PULL / TERMINATION (CIRC 2)	5	25-May-27	01-Jun-27
453		FIBER / TESTING	2	14-Jun-27	15-Jun-27
454		BESS - FIBER OTDR TEST (CIRC 2)	2	14-Jun-27	15-Jun-27
455		AUX EQUIP / TERMS	14	20-Aug-27	09-Sep-27
456		BESS - SET SCADA EQUIP (CIRC 2)	2	20-Aug-27	23-Aug-27
457		BESS - AUX WIRE PULL / TERMINATION / TESTING (CIRC 2)	7	31-Aug-27	09-Sep-27
458		CIRC EQUIP 3 - MVT/SCADA/AUX (GSU I)	87	18-May-27	20-Sep-27
459		XFMR EQUIP & TERMS	28	18-May-27	25-Jun-27
460		BESS - SET ELECT MVT/ XFMR EQUIP (CIRC 3) 12EA	2	18-May-27	19-May-27
461		BESS - MVT/ XFMR EQUIP/XFMR TERMINATION (CIRC 3)	10	10-Jun-27	23-Jun-27
462		BESS - MV WIRE TEST (VLF/PD) (CIRC 3)	2	24-Jun-27	25-Jun-27
463		SCADA EQUIP / TERMS	18	20-May-27	15-Jun-27
464		BESS - SET SCADA EQUIP (CIRC 3)	2	20-May-27	21-May-27
465		BESS - SCADA EQUIP WIRE PULL / TERMINATION (CIRC 3)	5	09-Jun-27	15-Jun-27
466		FIBER / TESTING	2	24-Jun-27	25-Jun-27
467		BESS - FIBER OTDR TEST (CIRC 3)	2	24-Jun-27	25-Jun-27
468		AUX EQUIP / TERMS	19	24-Aug-27	20-Sep-27
469		BESS - SET ELECT AUX EQUIP (CIRC 3)	2	24-Aug-27	25-Aug-27
470		BESS - AUX WIRE PULL / TERMINATION / TESTING (CIRC 3)	7	10-Sep-27	20-Sep-27
471		CIRC EQUIP 4 - MVT/SCADA/AUX (GSU I)	92	20-May-27	29-Sep-27
472		XFMR EQUIP & TERMS	34	20-May-27	08-Jul-27
473		BESS - SET ELECT MVT/ XFMR EQUIP (CIRC 4) 12EA	2	20-May-27	21-May-27
474		BESS - MVT/ XFMR EQUIP WIRE PULL & TERMS (CIRC 4)	10	22-Jun-27	06-Jul-27
475		BESS - MV WIRE TEST (VLF/PD) (CIRC 4)	2	07-Jul-27	08-Jul-27
476		SCADA EQUIP / TERMS	26	24-May-27	29-Jun-27
477		BESS - SET SCADA EQUIP (CIRC 4)	2	24-May-27	25-May-27
478		BESS - SCADA EQUIP WIRE PULL / TERMINATION (CIRC 4)	5	23-Jun-27	29-Jun-27
479		FIBER / TESTING	2	07-Jul-27	08-Jul-27
480		BESS - FIBER OTDR TEST (CIRC 4)	2	07-Jul-27	08-Jul-27
481		AUX EQUIP / TERMS	24	26-Aug-27	29-Sep-27
482		BESS - SET ELECT AUX EQUIP (CIRC 4)	2	26-Aug-27	27-Aug-27
483		BESS - AUX WIRE PULL / TERMINATION / TESTING (CIRC 4)	7	21-Sep-27	29-Sep-27
484		AUX	11	30-Aug-27	14-Sep-27
485		AUX EQUIP / TERMS	10	30-Aug-27	13-Sep-27
486		BESS - SET ELECT AUX EQUIP	5	30-Aug-27	03-Sep-27
487		BESS - AUX WIRE PULL / TERMINATION / TESTING	5	07-Sep-27	13-Sep-27
488		AUX TESTING / COMPLETION	1	14-Sep-27	14-Sep-27
489		BESS - AUX TESTING	1	14-Sep-27	14-Sep-27
490		SCADA EQUIP INSTALL - SUBSTATION / COMM BLDG (GSU I)	15	07-Sep-27	27-Sep-27
491		BESS - SCADA EQUIPMENT/RACK INSTALL (SUBSTATION)	15	07-Sep-27	27-Sep-27
492		EQUIP - BATTERIES (GSU I)	44	06-Aug-27	07-Oct-27
493		CIRC 1 - 48 BATTERIES (GSU I)	18	06-Aug-27	31-Aug-27
494		BATTERIES / TERMS	18	06-Aug-27	31-Aug-27
495		BESS - SET BATTERIES (CIRC 1) SET 20EA	3	06-Aug-27	10-Aug-27
496		BESS - ELECT WIRE PULL / TERMINATION (FROM MVT TO BATTERY) (CIRC 1)	15	11-Aug-27	31-Aug-27

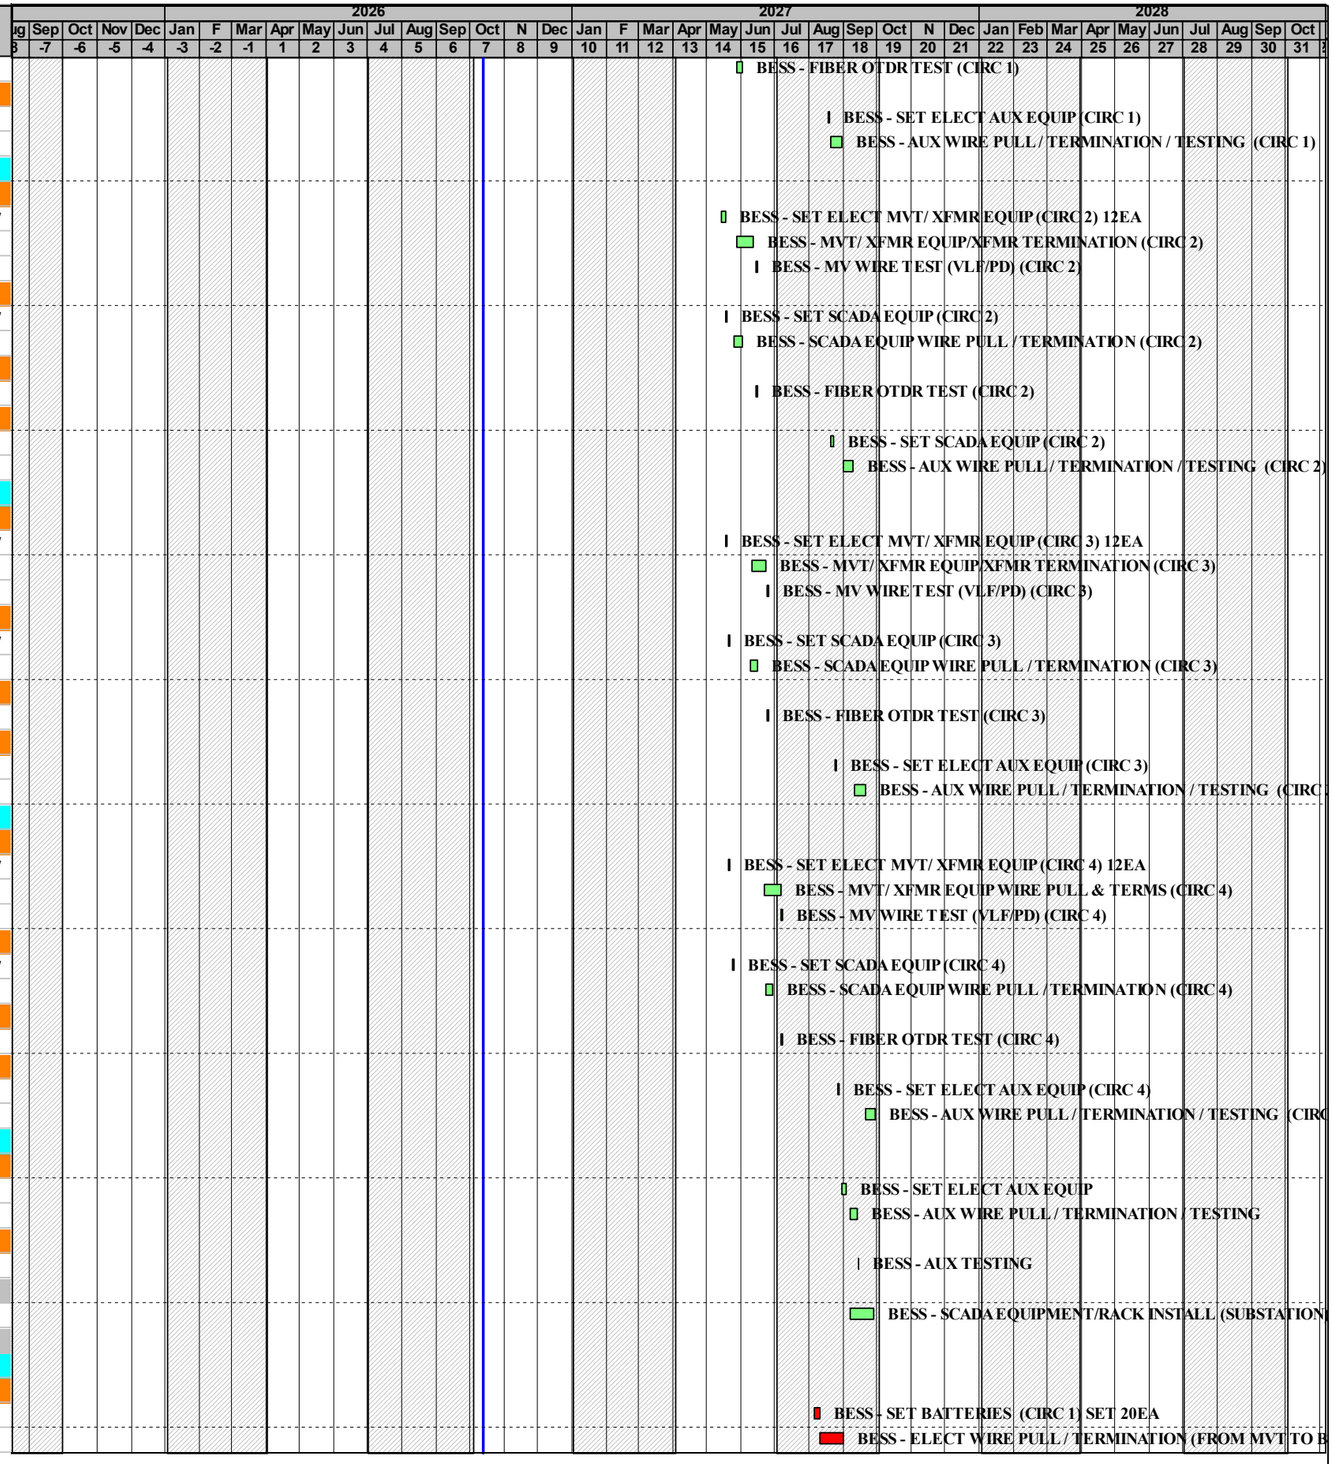


#	Activ ID	Activity Name	Dur	Start	Finish
497		BESS - MVT CABLE TRAY TO BATTERY (CIRC 1)	10	11-Aug-27	24-Aug-27
498		CIRC 2 - 48 BATTERIES (GSU I)	27	11-Aug-27	17-Sep-27
499		BATTERIES / TERMS	27	11-Aug-27	17-Sep-27
500		BESS - SET BATTERIES (CIRC 2)	2	11-Aug-27	12-Aug-27
501		BESS - MVT CABLE TRAY TO BATTERY (CIRC 2)	8	25-Aug-27	03-Sep-27
502		BESS - ELECT WIRE PULL / TERMINATION (FROM MVT TO BATTERY) (CIRC 2)	12	01-Sep-27	17-Sep-27
503		CIRC 3 - 48 BATTERIES (GSU I)	31	16-Aug-27	28-Sep-27
504		BATTERIES / TERMS	31	16-Aug-27	28-Sep-27
505		BESS - SET BATTERIES(CIRC 3)	2	16-Aug-27	17-Aug-27
506		BESS - MVT CABLE TRAY TO BATTERY (CIRC 3)	7	07-Sep-27	15-Sep-27
507		BESS - ELECT WIRE PULL / TERMINATION (FROM MVT TO BATTERY) (CIRC 3)	7	20-Sep-27	28-Sep-27
508		CIRC 4 - 48 BATTERIES (GSU I)	35	19-Aug-27	07-Oct-27
509		BATTERIES / TERMS	35	19-Aug-27	07-Oct-27
510		BESS - SET BATTERIES(CIRC 4)	2	19-Aug-27	20-Aug-27
511		BESS - MVT CABLE TRAY TO BATTERY (CIRC 4)	7	16-Sep-27	24-Sep-27
512		BESS - ELECT WIRE PULL / TERMINATION (FROM MVT TO BATTERY) (CIRC 4)	7	29-Sep-27	07-Oct-27
513		TESTING / MECH COMPLETION (GSU I)	45	30-Aug-27	01-Nov-27
514		MECH COMPLETION (GSU I)	45	30-Aug-27	01-Nov-27
515		CIRC 1	9	30-Aug-27	10-Sep-27
516		EARTHWORK - FINAL GRADING(CIRC 1)	2	30-Aug-27	31-Aug-27
517		BESS - QA-QC (CIRC 1)	5	01-Sep-27	08-Sep-27
518		BESS - MV EQUIP TESTING (CIRC 1)	3	01-Sep-27	03-Sep-27
519		BESS - COMPLETION LIST / CORRECTIONS (CIRC 1)	2	09-Sep-27	10-Sep-27
520		BESS SCADA COLD COMMISSIONING (CIRC 1)	1	09-Sep-27	09-Sep-27
521		*MILESTONE: FEEDER COMPLETION (CIRC 1)	0		10-Sep-27
522		CIRC 2	19	01-Sep-27	28-Sep-27
523		EARTHWORK - FINAL GRADING(CIRC 2)	2	01-Sep-27	02-Sep-27
524		BESS - QA-QC (CIRC 2)	3	20-Sep-27	22-Sep-27
525		BESS - MV EQUIP TESTING (CIRC 2)	3	20-Sep-27	22-Sep-27
526		BESS - COMPLETION LIST / CORRECTIONS (CIRC 2)	2	23-Sep-27	24-Sep-27
527		*MILESTONE: FEEDER COMPLETION (CIRC 2)	0		24-Sep-27
528		BESS SCADA COLD COMMISSIONING (CIRC 2)	1	28-Sep-27	28-Sep-27
529		CIRC 3	22	03-Sep-27	05-Oct-27
530		EARTHWORK - FINAL GRADING(CIRC 3)	2	03-Sep-27	07-Sep-27
531		BESS - QA-QC (CIRC 3)	3	29-Sep-27	01-Oct-27
532		BESS SCADA COLD COMMISSIONING (CIRC 3)	1	29-Sep-27	29-Sep-27
533		BESS - MV EQUIP TESTING (CIRC 3)	3	29-Sep-27	01-Oct-27
534		BESS - COMPLETION LIST / CORRECTIONS (CIRC 3)	2	04-Oct-27	05-Oct-27
535		*MILESTONE: FEEDER COMPLETION (CIRC 3)	0		05-Oct-27
536		CIRC 4	26	08-Sep-27	13-Oct-27
537		EARTHWORK - FINAL GRADING(CIRC 4)	2	08-Sep-27	09-Sep-27
538		BESS SCADA COLD COMMISSIONING (CIRC 4)	1	30-Sep-27	30-Sep-27
539		BESS - QA-QC (CIRC 4)	2	08-Oct-27	11-Oct-27
540		BESS - COMPLETION LIST / CORRECTIONS (CIRC 4)	2	12-Oct-27	13-Oct-27
541		*MILESTONE: FEEDER COMPLETION (CIRC 4)	0		13-Oct-27
542		PROJ MECH COMPLETION (GSU I)	37	10-Sep-27	01-Nov-27
543		EARTHWORK - FINAL ROADS	7	10-Sep-27	20-Sep-27
544		ISSUE MECH COMPLETION	1	14-Oct-27	14-Oct-27
545		WEATHER ALLOWANCE (MECH)	12	15-Oct-27	01-Nov-27
546		MILESTONE: BESS 1 MECH COMPLETION (GSU I)	0		01-Nov-27
547		BESS PRODUCTION (GSU II)	319	17-Aug-26	03-Jan-28
548		EARTHWORK (GSU II)	94	17-Aug-26	15-Mar-27
549		EARTHWORK	5	17-Aug-26	21-Aug-26
550		EARTHWORK - PAD CERTIFY	5	17-Aug-26	21-Aug-26
551		FENCING	84	13-Oct-26	15-Mar-27
552		TEMP FENCING (INCL. LAYOUT)	10	13-Oct-26	26-Oct-26

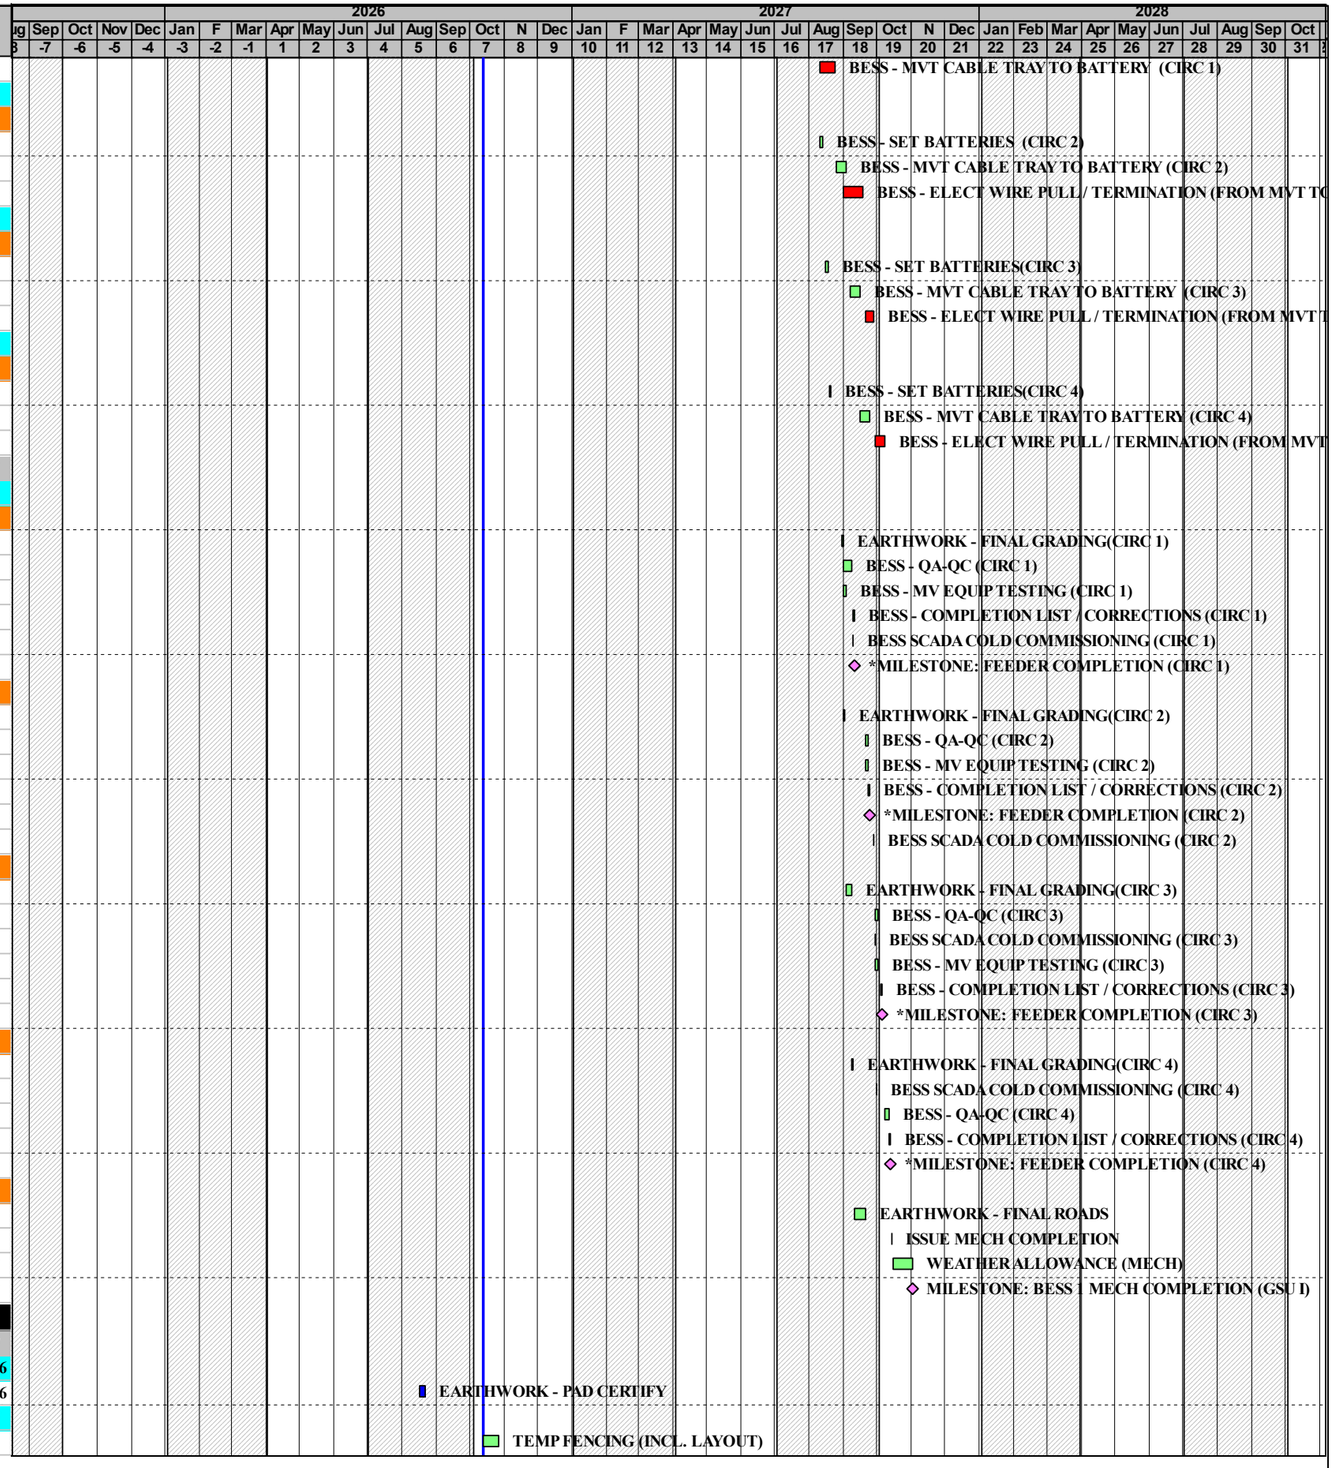


#	Activ ID	Activity Name	Dur	Start	Finish
553		PERMANENT FENCING (JIT TO EQUIP SET)	15	09-Feb-27	15-Mar-27
554		UG ELECT @ EQUIP PADS (GSU II)	43	09-Dec-26	09-Mar-27
555		UG ELECT - CIRC 5	10	09-Dec-26	22-Dec-26
556		BESS - UG ELECT ROUGH-IN/CONDUIT AT MVT (CIRC 5)	10	09-Dec-26	22-Dec-26
557		BESS - ELECT GROUNDING (CIRC 5)	5	16-Dec-26	22-Dec-26
558		UG ELECT - CIRC 6	10	23-Dec-26	13-Jan-27
559		BESS - UG ELECT ROUGH-IN/CONDUIT AT MVT (CIRC 6)	10	23-Dec-26	13-Jan-27
560		BESS - ELECT GROUNDING (CIRC 6)	5	05-Jan-27	13-Jan-27
561		UG ELECT - CIRC 7	10	18-Jan-27	08-Feb-27
562		BESS - UG ELECT ROUGH-IN/CONDUIT AT MVT (CIRC 7)	10	18-Jan-27	08-Feb-27
563		BESS - ELECT GROUNDING (CIRC 7)	5	27-Jan-27	08-Feb-27
564		UG ELECT - CIRC 8	10	09-Feb-27	02-Mar-27
565		BESS - UG ELECT ROUGH-IN/CONDUIT AT MVT (CIRC 8)	10	09-Feb-27	02-Mar-27
566		BESS - ELECT GROUNDING (CIRC 8)	5	22-Feb-27	02-Mar-27
567		UG ELECT - AUX	3	03-Mar-27	09-Mar-27
568		BESS - AUX POWER ELECT DUCT BANK	3	03-Mar-27	09-Mar-27
569		MV ELECT / FIBER TRENCHING & CABLE (GSU II)	34	19-Jan-27	29-Mar-27
570		MV ELECT/FIBER TRENCHING/WIRE/BACKFILL - CIRC 5	7	19-Jan-27	02-Feb-27
571		BESS - MV ELECT / FIBER TRENCHING & CONDUIT- CIRC 5	7	19-Jan-27	02-Feb-27
572		MV ELECT/FIBER TRENCHING/WIRE/BACKFILL - CIRC 6	7	09-Feb-27	23-Feb-27
573		BESS - MV ELECT / FIBER TRENCHING & CONDUIT- CIRC 6	7	09-Feb-27	23-Feb-27
574		MV ELECT/FIBER TRENCHING/WIRE/BACKFILL - CIRC 7	7	02-Mar-27	16-Mar-27
575		BESS - MV ELECT / FIBER TRENCHING & CONDUIT- CIRC 7	7	02-Mar-27	16-Mar-27
576		MV ELECT/FIBER TRENCHING/WIRE/BACKFILL - CIRC 8	7	19-Mar-27	29-Mar-27
577		BESS - MV ELECT / FIBER TRENCHING & CONDUIT- CIRC 8	7	19-Mar-27	29-Mar-27
578		FOUNDATIONS - MVT EQUIP PADS (GSU II)	67	11-Jan-27	13-Apr-27
579		CONC FOUNDATIONS - MVT EQUIP PADS - CIRC 5	10	11-Jan-27	23-Jan-27
580		BESS - FRPS CONC MVT PADS (CIRC 5)	4	11-Jan-27	18-Jan-27
581		BESS - CURE CONC MVT PADS (CIRC 5)	5	19-Jan-27	23-Jan-27
582		CONC FOUNDATIONS - MVT EQUIP PADS - CIRC 6	10	01-Feb-27	13-Feb-27
583		BESS - FRPS CONC MVT PADS (CIRC 6)	4	01-Feb-27	08-Feb-27
584		BESS - CONC PAD QA-QC / CURE (CIRC 6)	5	09-Feb-27	13-Feb-27
585		CONC FOUNDATIONS - MVT EQUIP PADS - CIRC 7	10	22-Feb-27	06-Mar-27
586		BESS - FRPS CONC MVT PADS (CIRC 7)	4	22-Feb-27	01-Mar-27
587		BESS - CONC PAD QA-QC / CURE (CIRC 7)	5	02-Mar-27	06-Mar-27
588		CONC FOUNDATIONS - MVT EQUIP PADS - CIRC 8	7	15-Mar-27	23-Mar-27
589		BESS - FRPS CONC MVT PADS (CIRC 8)	4	15-Mar-27	18-Mar-27
590		BESS - CONC PAD QA-QC / CURE (CIRC 8)	5	19-Mar-27	23-Mar-27
591		AUX FOUNDATIONS	30	03-Mar-27	13-Apr-27
592		BESS - AUX FRPS CONC PAD & QA-QC	5	03-Mar-27	15-Mar-27
593		BESS - WEATHER (MECH PAD COMPLETE)	21	16-Mar-27	13-Apr-27
594		*MILESTONE: MVT CONC PADS COMPLETE	0		13-Apr-27
595		FOUNDATIONS - BATT EQUIP PADS (GSU II)	125	06-Oct-26 A	30-Mar-27
596		CONC FOUNDATIONS - BATT EQUIP PADS - CIRC 5	84	06-Oct-26 A	01-Feb-27
597		BESS - FRPS CONC BATT PADS (CIRC 5) - ROAD ROW	6	06-Oct-26 A	09-Oct-26 A
598		BESS - CURE CONC BATT PADS (CIRC 5) - ROAD ROW	5	10-Oct-26 A	15-Oct-26
599		BESS - FRPS CONC BATT PADS (CIRC 5) - SWALE ROW	5	19-Jan-27	27-Jan-27
600		BESS - CURE CONC BATT PADS (CIRC 5) - SWALE ROW	5	28-Jan-27	01-Feb-27
601		CONC FOUNDATIONS - BATT EQUIP PADS - CIRC 6	99	12-Oct-26 A	22-Feb-27
602		BESS - FRPS CONC BATT PADS (CIRC 6) - ROAD ROW	6	12-Oct-26 A	20-Oct-26
603		BESS - CURE CONC BATT PADS (CIRC 6) - ROAD ROW	5	21-Oct-26	25-Oct-26
604		BESS - FRPS CONC BATT PADS (CIRC 6) - SWALE ROW	5	09-Feb-27	17-Feb-27
605		BESS - CURE CONC BATT PADS (CIRC 6) - SWALE ROW	5	18-Feb-27	22-Feb-27
606		CONC FOUNDATIONS - BATT EQUIP PADS - CIRC 7	100	21-Oct-26	15-Mar-27
607		BESS - FRPS CONC BATT PADS (CIRC 7) - ROAD ROW	6	21-Oct-26	28-Oct-26
608		BESS - CURE CONC BATT PADS (CIRC 7) - ROAD ROW	5	29-Oct-26	02-Nov-26

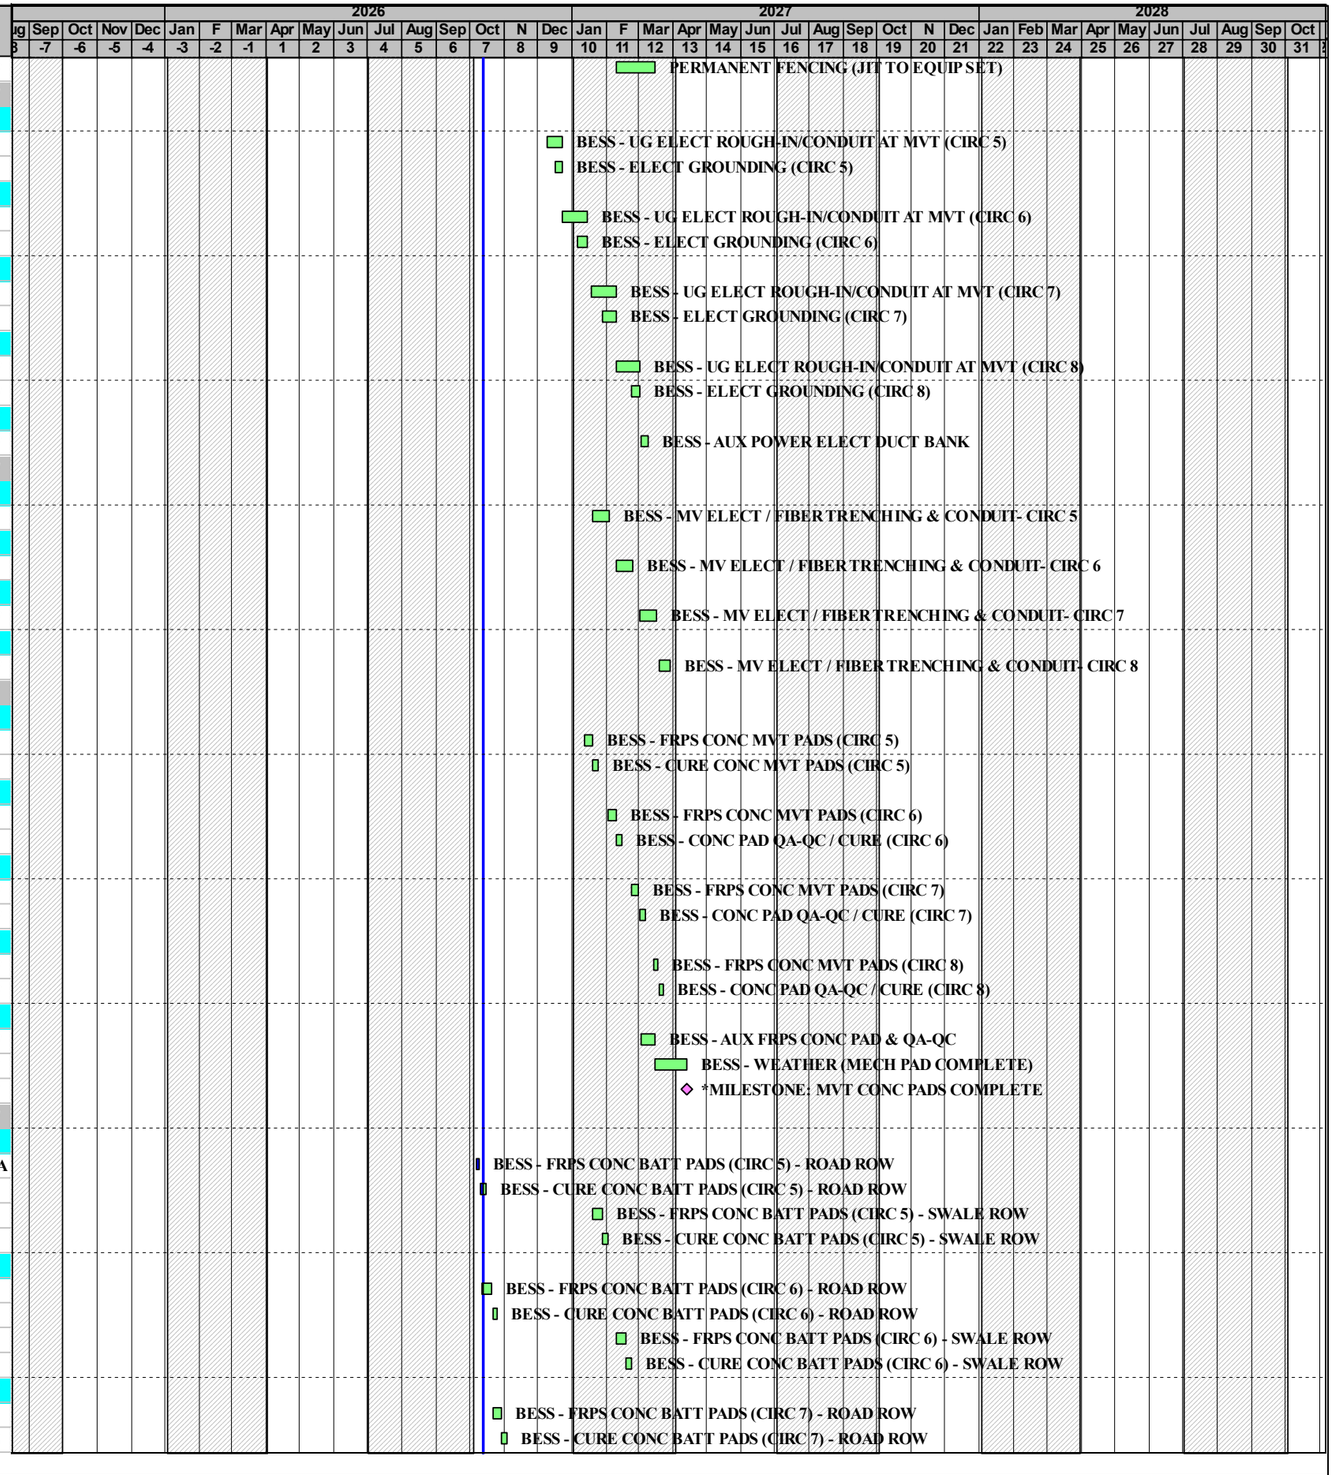

#	Activ ID	Activity Name	Dur	Start	Finish
609		BESS - FRPS CONC BATT PADS (CIRC 7) - SWALE ROW	5	02-Mar-27	10-Mar-27
610		BESS - CURE CONC BATT PADS (CIRC 7) - SWALE ROW	5	11-Mar-27	15-Mar-27
611		CONC FOUNDATIONS - BATT EQUIP PADS - CIRC 8	105	29-Oct-26	30-Mar-27
612		BESS - FRPS CONC BATT PADS (CIRC 8) - ROAD ROW	6	29-Oct-26	05-Nov-26
613		BESS - CURE CONC BATT PADS (CIRC 8) - ROAD ROW	5	06-Nov-26	10-Nov-26
614		BESS - FRPS CONC BATT PADS (CIRC 8) - SWALE ROW	5	19-Mar-27	25-Mar-27
615		BESS - CURE CONC BATT PADS (CIRC 8) - SWALE ROW	5	26-Mar-27	30-Mar-27
616		EQUIP - MVT/SCADA/AUX (GSU II)	90	24-May-27	29-Sep-27
617		CIRC EQUIP 5 - MVT/SCADA/AUX (GSU II)	69	24-May-27	30-Aug-27
618		MV EQUIP & TERMS	42	24-May-27	22-Jul-27
619		BESS - SET ELECT MVT/ XFMR EQUIP 14EA	2	24-May-27	25-May-27
620		BESS - MVT/ XFMR EQUIP WIRE PULL & TERMS (CIRC 5)	10	07-Jul-27	20-Jul-27
621		BESS - MV WIRE TEST (VLF/PD) (CIRC 5)	2	21-Jul-27	22-Jul-27
622		SCADA EQUIP / TERMS	29	26-May-27	07-Jul-27
623		BESS - SET SCADA EQUIP (CIRC 5)	2	26-May-27	27-May-27
624		BESS - SCADA EQUIP WIRE PULL / TERMINATION (CIRC 5)	5	30-Jun-27	07-Jul-27
625		FIBER / TESTING	2	21-Jul-27	22-Jul-27
626		BESS - FIBER OTDR TEST (CIRC 5)	2	21-Jul-27	22-Jul-27
627		AUX EQUIP / TERMS	9	18-Aug-27	30-Aug-27
628		BESS - SET ELECT AUX EQUIP (CIRC 5)	2	18-Aug-27	19-Aug-27
629		BESS - AUX WIRE PULL / TERMINATION / TESTING (CIRC 5)	7	20-Aug-27	30-Aug-27
630		CIRC EQUIP 6 - MVT/SCADA/AUX (GSU II)	74	26-May-27	09-Sep-27
631		MV EQUIP & TERMS	50	26-May-27	05-Aug-27
632		BESS - SET ELECT MVT/ XFMR EQUIP (CIRC 6) 14EA	2	26-May-27	27-May-27
633		BESS - MVT/ XFMR EQUIP WIRE PULL & TERMS (CIRC 6)	10	21-Jul-27	03-Aug-27
634		BESS - MV WIRE TEST (VLF/PD) (CIRC 6)	2	04-Aug-27	05-Aug-27
635		SCADA EQUIP / TERMS	32	28-May-27	14-Jul-27
636		BESS - SET SCADA EQUIP (CIRC 6)	2	28-May-27	01-Jun-27
637		BESS - SCADA EQUIP WIRE PULL / TERMINATION (CIRC 6)	5	08-Jul-27	14-Jul-27
638		FIBER / TESTING	2	04-Aug-27	05-Aug-27
639		BESS - FIBER OTDR TEST (CIRC 6)	2	04-Aug-27	05-Aug-27
640		AUX EQUIP / TERMS	14	20-Aug-27	09-Sep-27
641		BESS - SET ELECT AUX EQUIP (CIRC 6)	2	20-Aug-27	23-Aug-27
642		BESS - AUX WIRE PULL / TERMINATION / TESTING (CIRC 6)	7	31-Aug-27	09-Sep-27
643		CIRC EQUIP 7 - MVT/SCADA/AUX (GSU II)	79	28-May-27	20-Sep-27
644		XFMR EQUIP & TERMS	56	28-May-27	17-Aug-27
645		BESS - SET ELECT MVT/ XFMR EQUIP (CIRC 7) 14EA	2	28-May-27	01-Jun-27
646		BESS - MVT/ XFMR EQUIP WIRE PULL & TERMS (CIRC 7)	10	02-Aug-27	13-Aug-27
647		BESS - MV WIRE TEST (VLF/PD) (CIRC 7)	2	16-Aug-27	17-Aug-27
648		SCADA EQUIP / TERMS	40	02-Jun-27	28-Jul-27
649		BESS - SET SCADA EQUIP (CIRC 7)	2	02-Jun-27	03-Jun-27
650		BESS - SCADA EQUIP WIRE PULL / TERMINATION (CIRC 7)	5	22-Jul-27	28-Jul-27
651		FIBER / TESTING	2	16-Aug-27	17-Aug-27
652		BESS - FIBER OTDR TEST (CIRC 7)	2	16-Aug-27	17-Aug-27
653		AUX EQUIP / TERMS	19	24-Aug-27	20-Sep-27
654		BESS - SET ELECT AUX EQUIP (CIRC 7)	2	24-Aug-27	25-Aug-27
655		BESS - AUX WIRE PULL / TERMINATION / TESTING (CIRC 7)	7	10-Sep-27	20-Sep-27
656		CIRC EQUIP 8 - MVT/SCADA/AUX (GSU II)	84	02-Jun-27	29-Sep-27
657		XFMR EQUIP & TERMS	62	02-Jun-27	27-Aug-27
658		BESS - SET ELECT MVT/ XFMR EQUIP (CIRC 8) 12EA	2	02-Jun-27	03-Jun-27
659		BESS - MVT/ XFMR EQUIP WIRE PULL & TERMS (CIRC 8)	10	12-Aug-27	25-Aug-27
660		BESS - MV WIRE TEST (VLF/PD) (CIRC 8)	2	26-Aug-27	27-Aug-27
661		SCADA EQUIP / TERMS	48	04-Jun-27	11-Aug-27
662		BESS - SET SCADA EQUIP (CIRC 8)	2	04-Jun-27	07-Jun-27
663		BESS - SCADA EQUIP WIRE PULL / TERMINATION (CIRC 8)	5	05-Aug-27	11-Aug-27
664		FIBER / TESTING	2	26-Aug-27	27-Aug-27

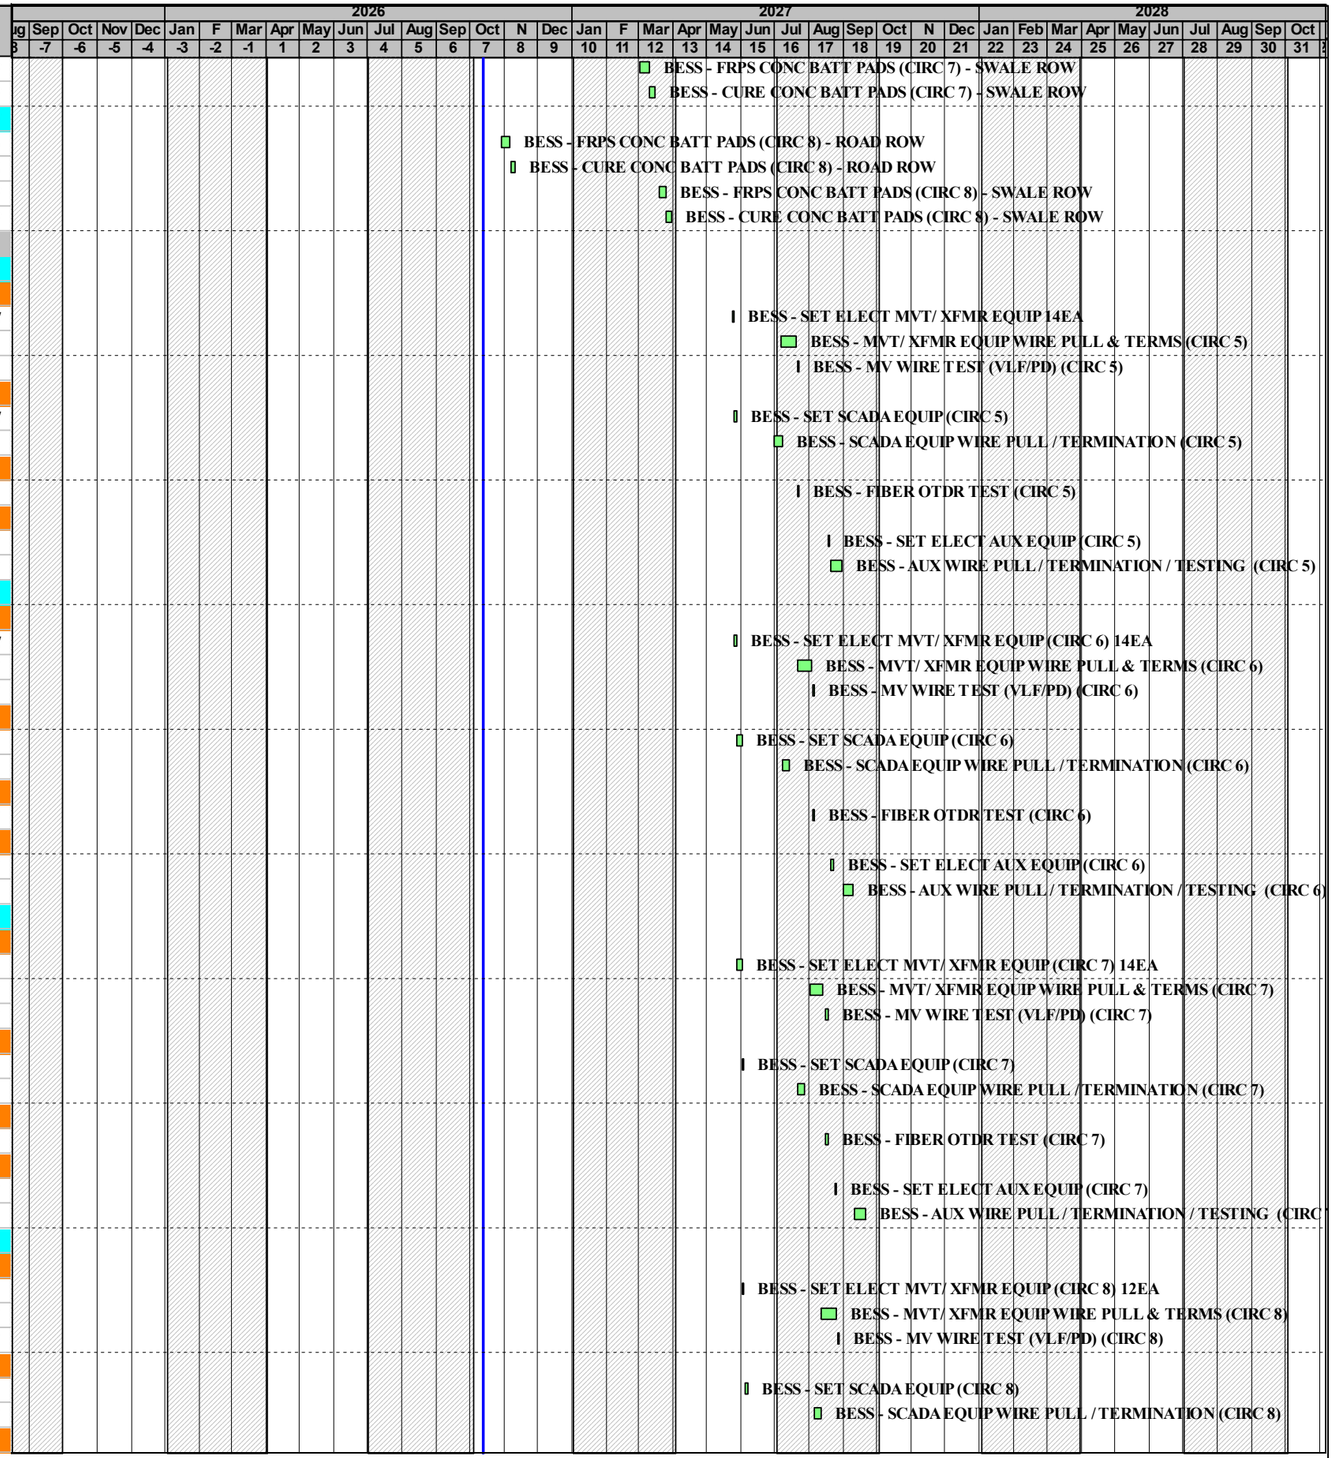

#	Activ ID	Activity Name	Dur	Start	Finish
665		BESS - FIBER OTDR TEST (CIRC 8)	2	26-Aug-27	27-Aug-27
666		AUX EQUIP / TERMS	24	26-Aug-27	29-Sep-27
667		BESS - SET ELECT AUX EQUIP (CIRC 8)	2	26-Aug-27	27-Aug-27
668		BESS - AUX WIRE PULL / TERMINATION / TESTING (CIRC 8)	7	21-Sep-27	29-Sep-27
669		AUX (GSU II)	12	30-Aug-27	15-Sep-27
670		AUX EQUIP / TERMS	10	30-Aug-27	13-Sep-27
671		BESS - SET ELECT AUX EQUIP	5	30-Aug-27	03-Sep-27
672		BESS - AUX WIRE PULL / TERMINATION / TESTING	5	07-Sep-27	13-Sep-27
673		AUX TESTING / COMPLETION	2	14-Sep-27	15-Sep-27
674		BESS - AUX TESTING	2	14-Sep-27	15-Sep-27
675		SCADA EQUIP INSTALL - SUBSTATION / COMM BLDG (GSU II)	15	07-Sep-27	27-Sep-27
676		BESS - SCADA EQUIPMENT/RACK INSTALL (SUBSTATION)	15	07-Sep-27	27-Sep-27
677		EQUIP - BATTERIES (GSU II)	60	24-Aug-27	16-Nov-27
678		CIRC EQUIP 5 - 48 BATTERIES (GSU II)	39	24-Aug-27	18-Oct-27
679		BATTERIES / TERMS	39	24-Aug-27	18-Oct-27
680		BESS - SET BATTERIES (CIRC 5)	2	24-Aug-27	25-Aug-27
681		BESS - MVT CABLE TRAY TO BATTERY (CIRC 5)	7	27-Sep-27	05-Oct-27
682		BESS - ELECT WIRE PULL / TERMINATION (FROM MVT TO BATTERY) (CIRC 5)	7	08-Oct-27	18-Oct-27
683		CIRC EQUIP 6 - 48 BATTERIES (GSU II)	43	27-Aug-27	27-Oct-27
684		BATTERIES / TERMS	43	27-Aug-27	27-Oct-27
685		BESS - SET BATTERIES (CIRC 6)	2	27-Aug-27	30-Aug-27
686		BESS - MVT CABLE TRAY TO BATTERY (CIRC 6)	5	06-Oct-27	12-Oct-27
687		BESS - ELECT WIRE PULL / TERMINATION (FROM MVT TO BATTERY) (CIRC 6)	7	19-Oct-27	27-Oct-27
688		CIRC EQUIP 7 - 48 BATTERIES (GSU II)	47	01-Sep-27	05-Nov-27
689		BATTERIES / TERMS	47	01-Sep-27	05-Nov-27
690		BESS - SET BATTERIES(CIRC 7)	2	01-Sep-27	02-Sep-27
691		BESS - MVT CABLE TRAY TO BATTERY (CIRC 7)	5	13-Oct-27	19-Oct-27
692		BESS - ELECT WIRE PULL / TERMINATION (FROM MVT TO BATTERY) (CIRC 7)	7	28-Oct-27	05-Nov-27
693		CIRC EQUIP 8 - 48 BATTERIES (GSU II)	50	08-Sep-27	16-Nov-27
694		BATTERIES / TERMS	50	08-Sep-27	16-Nov-27
695		BESS - SET BATTERIES(CIRC 8)	2	08-Sep-27	09-Sep-27
696		BESS - MVT CABLE TRAY TO BATTERY (CIRC 8)	5	20-Oct-27	26-Oct-27
697		BESS - ELECT WIRE PULL / TERMINATION (FROM MVT TO BATTERY) (CIRC 8)	7	08-Nov-27	16-Nov-27
698		TESTING / MECH COMPLETION (GSU II)	53	15-Oct-27	03-Jan-28
699		MECH COMPLETION (GSU II)	53	15-Oct-27	03-Jan-28
700		CIRC 5	6	15-Oct-27	22-Oct-27
701		EARTHWORK - FINAL GRADING(CIRC 5)	2	15-Oct-27	18-Oct-27
702		BESS - QA-QC (CIRC 5)	2	19-Oct-27	20-Oct-27
703		BESS - MV EQUIP TESTING (CIRC 5)	3	19-Oct-27	21-Oct-27
704		BESS - SUBMIT FEEDER COMPLETION (CIRC 5)	2	21-Oct-27	22-Oct-27
705		BESS SCADA COLD COMMISSIONING (CIRC 5)	1	21-Oct-27	21-Oct-27
706		*MILESTONE: FEEDER COMPLETION (CIRC 5)	0		22-Oct-27
707		CIRC 6	11	19-Oct-27	02-Nov-27
708		EARTHWORK - FINAL GRADING(CIRC 6)	2	19-Oct-27	20-Oct-27
709		BESS SCADA COLD COMMISSIONING (CIRC 6)	1	22-Oct-27	22-Oct-27
710		BESS - QA-QC (CIRC 6)	2	28-Oct-27	29-Oct-27
711		BESS - MV EQUIP TESTING (CIRC 6)	3	28-Oct-27	01-Nov-27
712		BESS - SUBMIT FEEDER COMPLETION (CIRC 6)	2	01-Nov-27	02-Nov-27
713		*MILESTONE: FEEDER COMPLETION (CIRC 6)	0		02-Nov-27
714		CIRC 7	16	21-Oct-27	11-Nov-27
715		EARTHWORK - FINAL GRADING(CIRC 7)	2	21-Oct-27	22-Oct-27
716		BESS SCADA COLD COMMISSIONING (CIRC 7)	1	25-Oct-27	25-Oct-27
717		BESS - QA-QC (CIRC 7)	2	08-Nov-27	09-Nov-27
718		BESS - MV EQUIP TESTING (CIRC 7)	3	08-Nov-27	10-Nov-27
719		BESS - SUBMIT FEEDER COMPLETION (CIRC 7)	2	10-Nov-27	11-Nov-27
720		*MILESTONE: FEEDER COMPLETION (CIRC 7)	0		11-Nov-27

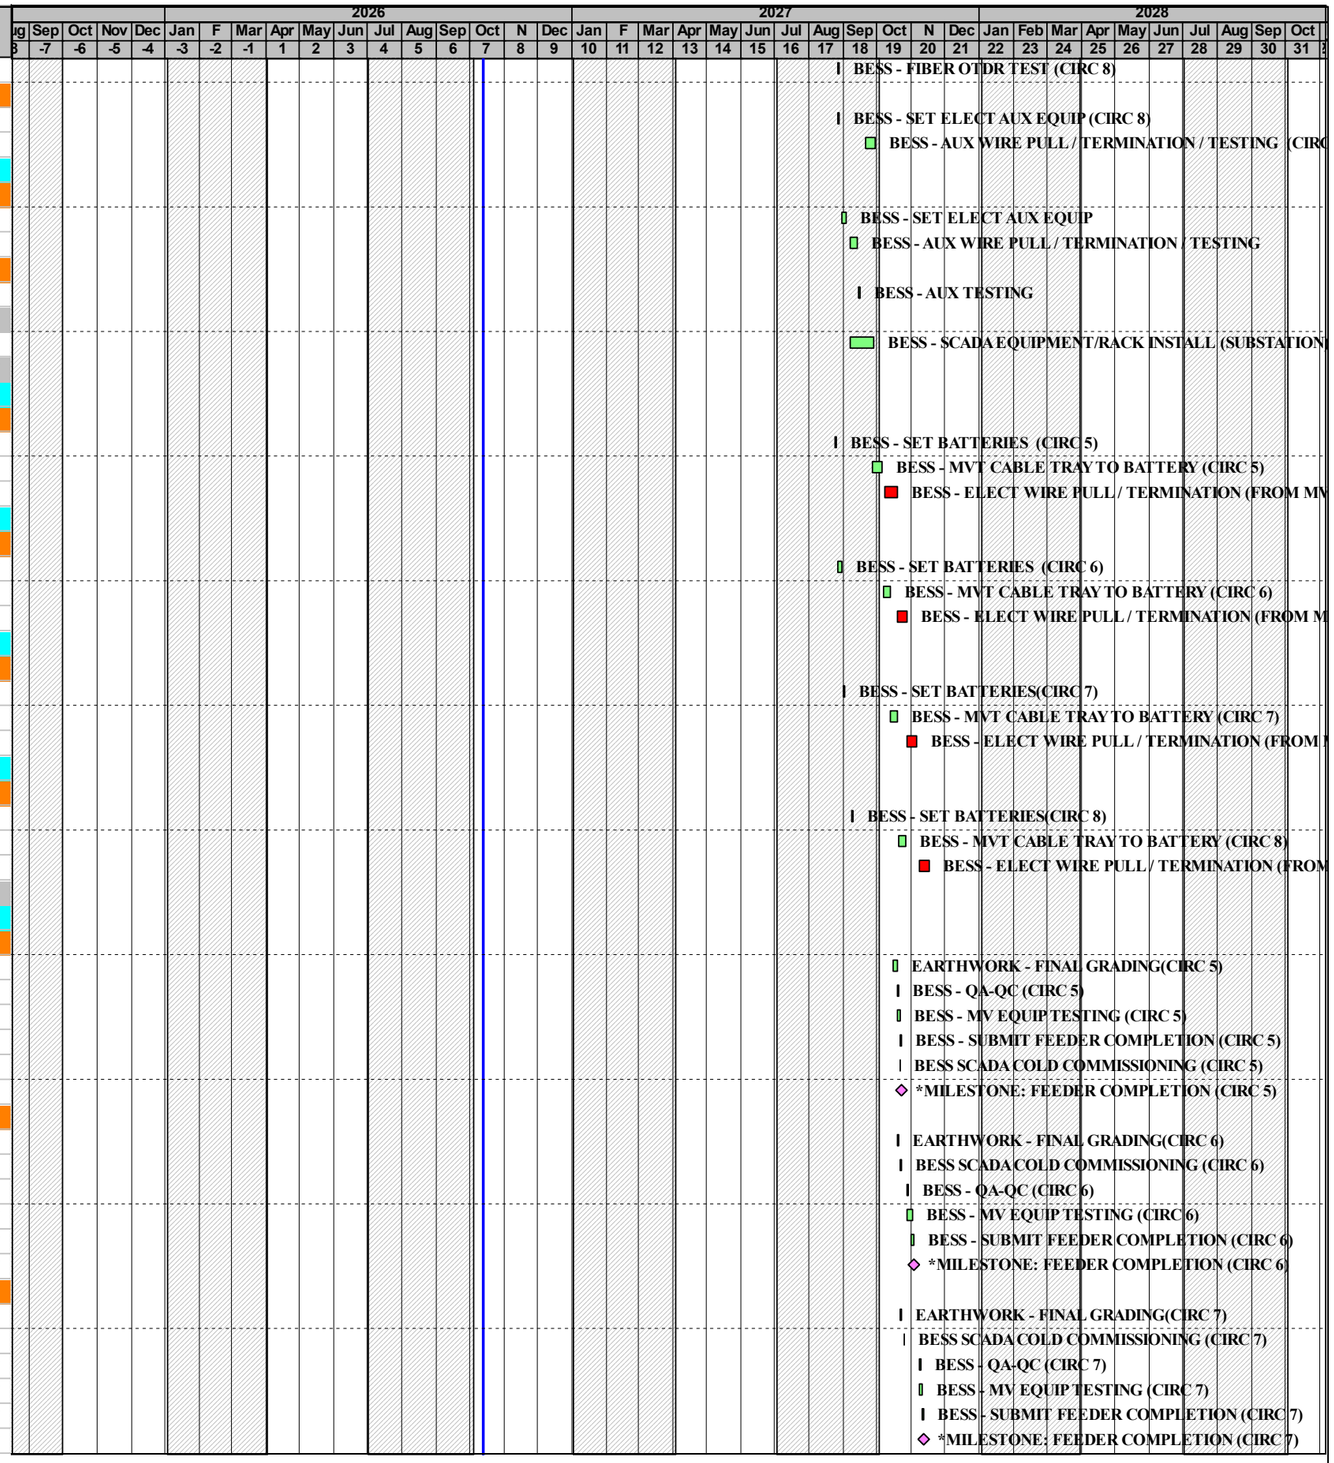

#	Activ ID	Activity Name	Dur	Start	Finish
721		CIRC 8	33	25-Oct-27	10-Dec-27
722		EARTHWORK - FINAL GRADING(CIRC 8)	2	25-Oct-27	26-Oct-27
723		BESS SCADA COLD COMMISSIONING (CIRC 8)	1	26-Oct-27	26-Oct-27
724		BESS - MV EQUIP TESTING (CIRC 8)	3	17-Nov-27	19-Nov-27
725		BESS - QA-QC (CIRC 8)	12	22-Nov-27	09-Dec-27
726		BESS - SUBMIT FEEDER COMPLETION (CIRC 8)	1	10-Dec-27	10-Dec-27
727		*MILESTONE: FEEDER COMPLETION (CIRC 8)	0		10-Dec-27
728		PROJ MECH COMPLETION (GSU II)	21	02-Dec-27	03-Jan-28
729		EARTHWORK - FINAL ROADS	7	02-Dec-27	10-Dec-27
730		ISSUE MECH COMPLETION	1	13-Dec-27	13-Dec-27
731		WEATHER ALLOWANCE (MECH)	13	14-Dec-27	03-Jan-28
732		MILESTONE: MECH COMPLETION (GSU II)	0		03-Jan-28
733		BESS COMMISSIONING / SUBST COMPLETION	77	04-Jan-28	19-Apr-28
734		BESS - TESLA OFF-GRID (OWNER)	30	04-Jan-28	14-Feb-28
735		BATTERY OFF-GRID (GSU I)	16	04-Jan-28	25-Jan-28
736		BESS - TESLA OFF-GRID SELF TESTNG (HOLD FOR JIT)	2	04-Jan-28	05-Jan-28
737		BESS - TESLA OFF-GRID SELF TESTNG (BAT COLD CX - CIRC 1) JIT	4	06-Jan-28	11-Jan-28
738		BESS - TESLA OFF-GRID SELF TESTNG (BAT COLD CX - CIRC 2)	4	12-Jan-28	17-Jan-28
739		BESS - TESLA OFF-GRID SELF TESTNG (BAT COLD CX - CIRC 3)	3	18-Jan-28	20-Jan-28
740		BESS - TESLA OFF-GRID SELF TESTNG (BAT COLD CX - CIRC 4)	3	21-Jan-28	25-Jan-28
741		BATTERY OFF GRID (GSU II)	14	26-Jan-28	14-Feb-28
742		BESS - TESLA OFF-GRID SELF TESTNG (BAT COLD CX - CIRC 5) JIT	4	26-Jan-28	31-Jan-28
743		BESS - TESLA OFF-GRID SELF TESTNG (BAT COLD CX - CIRC 6)	4	01-Feb-28	04-Feb-28
744		BESS - TESLA OFF-GRID SELF TESTNG (BAT COLD CX - CIRC 7)	4	07-Feb-28	10-Feb-28
745		BESS - TESLA OFF-GRID SELF TESTNG (BAT COLD CX - CIRC 8)	2	11-Feb-28	14-Feb-28
746		SUBST COMPLETION	47	15-Feb-28	19-Apr-28
747		INTERCONNECTION / MVT SOAK	5	15-Feb-28	21-Feb-28
748		BESS - INTERCONNECTION / MVT SOAK	2	15-Feb-28	16-Feb-28
749		BESS - TESLA INSTALLATION COMPLETION NOTICE	5	15-Feb-28	21-Feb-28
750		BESS - OWNER/TESLA BATTERY ON-GRID TESTING	25	22-Feb-28	27-Mar-28
751		BESS - TESLA ON-GRID FUNCTIONAL & PERF TESTING (HOT CX)	25	22-Feb-28	27-Mar-28
752		SUBST COMPLETION	17	28-Mar-28	19-Apr-28
753		BESS - PLANT CONTROLLER CX	10	28-Mar-28	10-Apr-28
754		BESS - PERFORMANCE TESTING / REPORTING	5	11-Apr-28	17-Apr-28
755		BESS - SUBMIT FOR SUBSTANTIAL	2	18-Apr-28	19-Apr-28
756		*MILESTONE: PROJ SUBSTANTIAL	0		19-Apr-28
757		PROJ FINAL COMPLETION / CLOSEOUT	140	20-Apr-28	06-Sep-28
758		FINAL CORRECTIONS / TESTING (CAL DAYS)	58	20-Apr-28	16-Jun-28
759		SUBMIT FOR PROJ FINAL COMPLETION (CAL DAYS)	2	17-Jun-28	18-Jun-28
760		*MILESTONE: PROJ FINAL COMPLETION (CAL DAYS)	0		06-Sep-28

